

District Report

Sindhuli

4 – 17 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Municipal Level Orientation Meeting	4 th January 2019	35	2	Er. Lekhnath Paudel Sachin Malego Er. Kiran Mahat (M&E DLPIU-Building) Dinesh Sanjel (DSE) Praveen Kumar Thakur (Engineer) Santosh Kapar (Engineer) Dinesh Sardar (Sub-Engineer)	Meeting Minutes Photos
Support to National IM team for draft design of Municipal Level website (Recovery and Resilience)	Ongoing since 10 th January 2019			Sachin Malego	Prototype Designs
ToT training at Dulikhel, Kavreplanchowk	7 th – 12 th January 2019			Lekhnath Paudel	
Meeting with DLPIU (Building), Swisscontact and DLPIU/GMaLI for the discussion of training on light timber structure manual	17 th January 2019			Lekhnath Paudel	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
1. Palika Level Meeting at Kamalamai Municipality	If possible at all ward levels	HRRP-Nepal	Lekhnath Paudel Sachin Malego
2. 5W Workshop to PO's	Planned not finalized	HRRP-Nepal	Lekhnath Paudel Sachin Malego
3. District Coordination Meeting	Planned not finalized	HRRP-Nepal	Lekhnath Paudel Sachin Malego

News & Updates




Er. Lekhnath Paudel (DTC-Sindhuli) during an interview at Radio Siddhababa. He was interviewed about the construction of timber houses and its feasibility and robustness.

Tranche Status

Rural /Municipality	Dudhauri Municipality	Ghanglekh RM	Golanjor RM	Hariharpurghadi RM	Kamalimai Municipality	Marin RM	Phikkal RM	Sunkoshi RM	Tinpatan RM
Total HHs Surveyed	14607	2834	4330	5046	15479	5465	3474	5745	7935
Total HHs Eligible	4650	2068	2779	2392	7863	3340	2173	4723	4281
Total HHs Enrolled	4646	2068	2098	2392	7850	3340	2173	4237	4281
First Tranche	4646	2068	2098	2392	7850	3340	2173	4237	4281
Second Tranche	2615	1357	2421	1916	4588	2173	2007	4162	4109
Third Tranche	855	871	1741	338	2024	823	1358	2697	1579
Total HH Constructed	612	865	1607	308	1738	786	1274	2344	1352
Grievance Registered	11157	785	1614	2531	7018	2303	1294	1067	5491
Grievance Addressed	9449	781	1598	2487	6831	2235	1292	1045	4827
RF HH Eligible	3493	530	667	1538	1768	1266	923	327	2499
RF HH Enrolled	288	97	95	0	278	59	6	0	316
RF 1 st Tranche	288	97	95	0	278	59	6	0	316
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	13	8	11	8	10	4	6	5	11
Non-Compliance Addressed	0	4	0	0	0	0	0	2	3


Graph of Tranche Status:

Tranche Status of Sindhuli

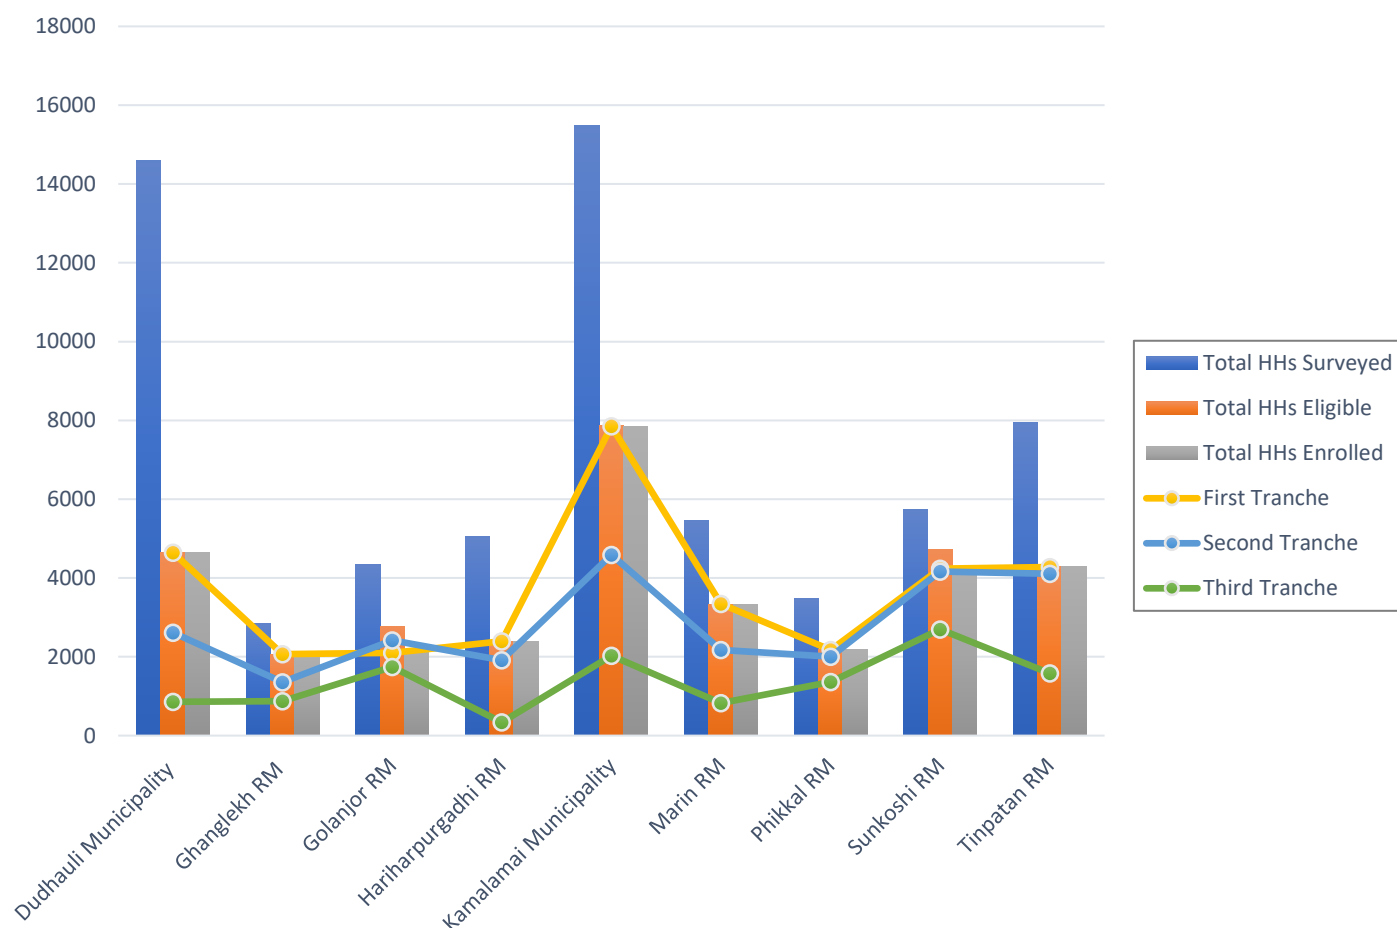


Graph for Retrofitting Status:

Retrofitting Status of Sindhuli

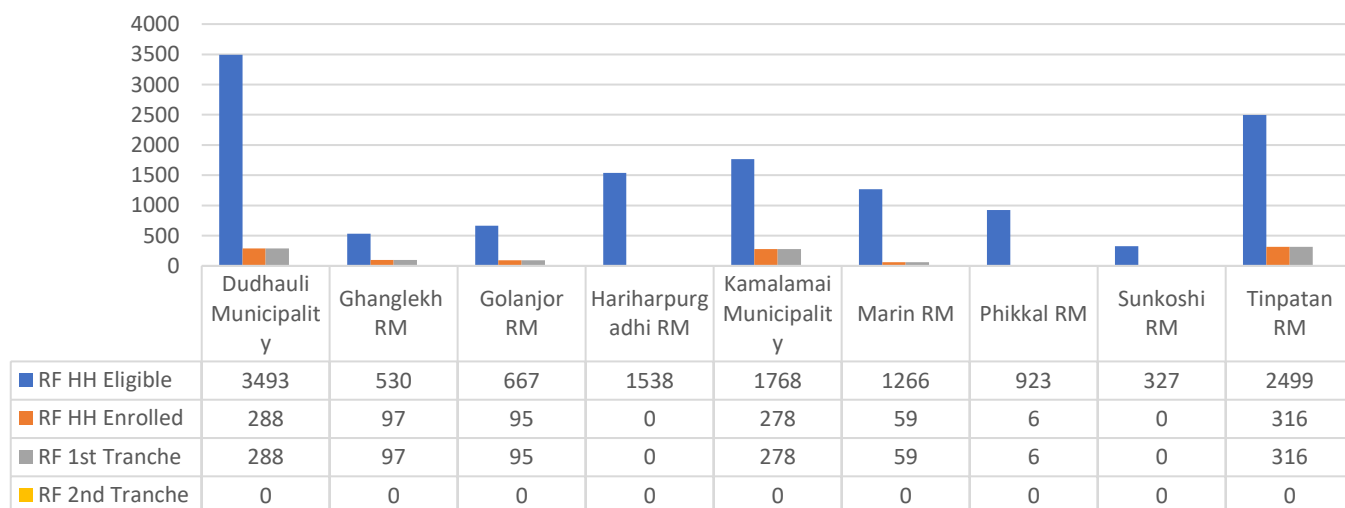

Graph for Grievance Status:

Grievance Status

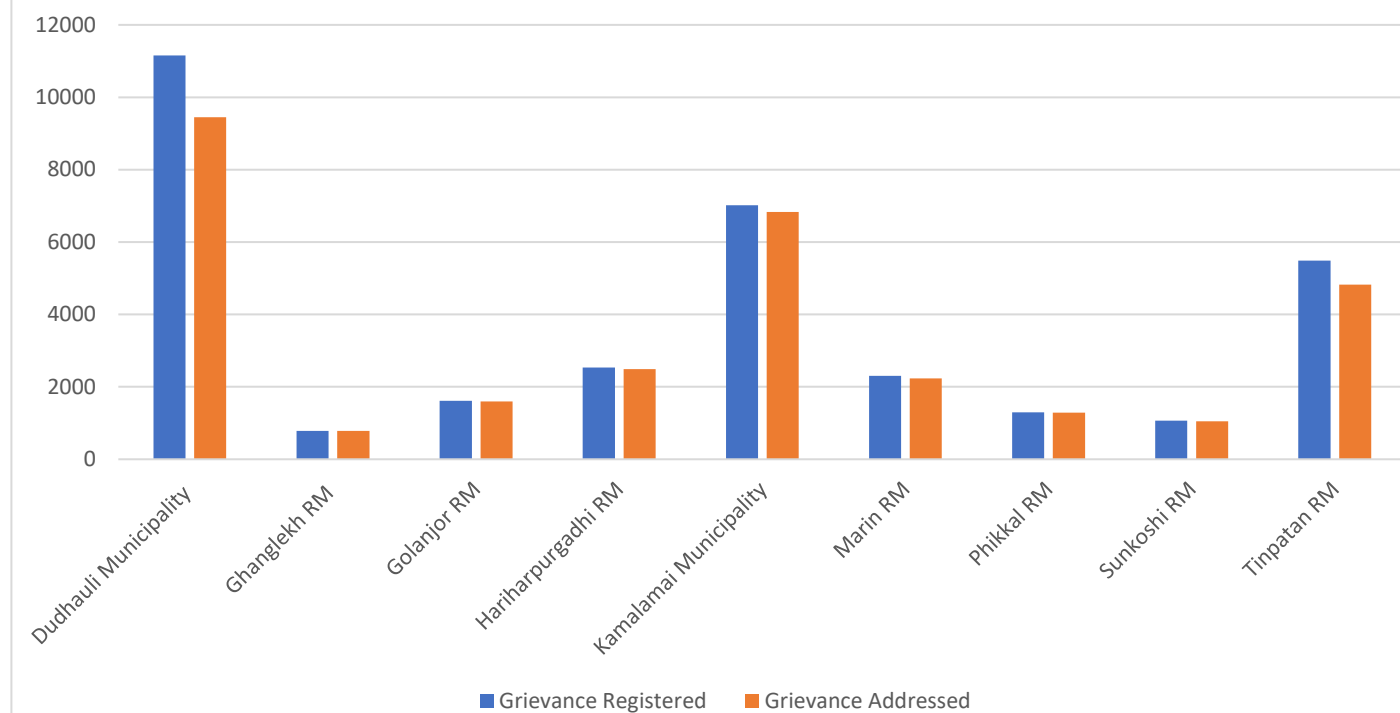

Light Timber/Steel Frame Structure Manual Training

Name of Training Program	Engineers Training on “Light Timber/Steel Frame Structure Manual”				
Training Venue, Location	Hotel Sindhuli Inn, Sindhulimadhi, Sindhuli				
	GPS	27.252°N		85.97°E	
Date	26-12-2018 to 27-12-2018				
Organizing Partners	1. National Reconstruction Authority, CLPIU (Building)				
	2. National Reconstruction Authority, DLPIU (Building), Sindhuli				
	3. Swisscontact- Swiss Foundation for Technical Cooperation				
	4. Housing Recovery and Reconstruction Platform (HRRP)-Nepal				
Type of Training/Program (Tick in appropriate box)	Mason	Engineers	Social Mobilizers	Orientation	Other
		√			
No. of Participants (Mention Types and No. eg. Engineer, Mason, Carpenter etc.)	Type and No. of Participant				
	Social Mobilizer	Technical person	DC/IM officer	Others	Total
		36			36
Geographical Coverage	Sindhuli District				
Resource Persons	Coordinator:		Lekhanath Paudel (HRRP)		
	Team Members:		Kuber Bogati (HRRP)		
			Prayash Malla (NSET)		
			Sabika Mastron (JICA)		
			Animesh Bajracharya (JICA)		
			Sagun Ranjitkar (ASF NEPAL)		
			Rajiv Kumar Sah (DSE)		
		Sachin Malego (HRRP)			
Guest Speaker	Er. Dev Narayan Prasad Yadav, Acting Project Chief, DLPIU/GMaLI, Sindhuli		Email: nra.sindhuli@gmail.com Contact No.: 9852029429		

	Er. Prabhakar Lal Karna, Project Chief, DLPIU (Building), Sindhuli	Email: maxplk26@gmail.com Contact No.: 9841507715
Daily Activities and Observations		
Day	Activity	Remarks
1	- Welcome and participants Introduction and Expectation Collection of expectation along with group formation, pre-test and course introduction - Non- compliance issues of light timber construction - Failure Modes and Damage Grade classification of Light Timber Buildings - Seismic Evaluation of (Structural System (mechanism of loading)) of light timber building - Technical Specification of Timber Building - Frame action: Calculation of Bracing and its' Balancing	The first day of the training focused mainly on the theoretical, design and calculation part of the manual. The training was observed to be equally important for the technical staffs of Government as well as the POs working in the field of reconstruction.
2	- Field visit to Inspection site - Group Work for Inspection and Presentations - In-situ Wood Treatment - Correction Measures for existing building - Evaluation/Closing	The second day of the training was focused on the field visit to inspection site. In-situ Wood Treatment procedure was also done for each group. For the group activities, all the participants were divided into groups of 6. Each group was given a topic and 10 minutes for the group presentation on the second day of the training. The evaluation of the presentation was done based on the group participation, presentation content, time management.

Field Visit /Joint Field Monitoring Visit Reports

Visit: Dudhouli Municipality

Date	Location	Participants from HRRP and stakeholders
01 Jan 2019 to 05 Jan 2019	Dudhouli Municipality	Er. Kiran Kumar Mahat (M&E), Er. Dinesh Sanjel (DSE), Er. Pravin Kumar Thakur (Engineer- DLPIU), Er. Lekhanath Paudel (DTC-HRRP), Mr. Sachin Malego (DIMO-HRRP)
Objective(s)	Reconstruction Update/ Housing Reconstruction issues, Challenges Interaction between local government agencies, implementing partners and local people (beneficiaries) Collection of Typologies of Houses	
Summary	Joint monitoring and field visit was conducted by HRRP Sindhuli along with NRA-CLPIU M&E (Kiran Mahat), DSE (Dinesh Sanjel), DLPIU-Building Engineer (Prabin Kumar Thakur). The field visit gave an opportunity to NRA-CLPIU/DLPIU and HRRP to observe, supervise and monitor ongoing construction of Houses (<i>Compliance & Non-Compliance houses</i>) at Dudhouli, Sirthouli, Harsahi and Arunthakur wards of Dudhouli Municipality. ➤ In Dudhouli ward no. 7 of Dudhouli Municipality about 80% HHs are in Elani land so still not started reconstruction. ➤ Due to unavailability of Hybrid Structure inspection form beneficiaries constructing hybrid structure houses could not receive 3rd tranche of GON housing grant. ➤ Beneficiary with timber framed houses have not received 3rd tranche of GON housing grant. ➤ After visiting those houses DSE had advised DLPIU Engineers for the inspection of those completed timber frame houses for releasing 3rd tranche. ➤ In Harsahi ward no. 06, of Dudhouli Municipality 98 beneficiaries had signed PA agreement, among them only 25 beneficiaries had started reconstruction, others are in Elani land problem. ➤ In Arunthakur ward no. 13 of Dudhouli Municipality most of the constructed houses are non-compliance since 5" (5 inch) brick wall is constructed as partition wall in load bearing masonry structure. Almost houses of Dudhouli Municipality are timber framed hybrid structure with ground floor stone/brick masonry and first floor constructed with light material, however, some houses were load bearing structures (Stone Masonry in Cement/Mud Mortar, Brick Masonry in Cement Mortar). On 4th January 2019 the palika level meeting was conducted in presence of all wards chairperson and ward level DLPIU Engineers/Sub-Engineers. All the ward chairperson shared the reconstruction updates/housing reconstruction issues, problems and challenges. Some key points are: ❖ Beneficiaries having PA agreement in Elani land could not start reconstruction yet ❖ Re-survey is carried out in some places but not covered overall wards ❖ Still grievance not addressed beneficiaries are in dilemma ❖ Insufficient number of field technical staffs	

- ❖ No exact retrofitting model, hence beneficiaries are in big trouble

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Elani land	Higher level decision	GON, NRA	As soon as possible
Grievance	Re-survey for missed HHs	NRA, GMAI	As soon as possible

Photos



Dudhouli Municipality Mayer Mr. Ghanashyam Raut sharing information regarding reconstruction issues and challenges



Participants (ward chairpersons and ward level DLPIU technical staff) at palika level meeting

Housing Typology Report



The house belongs to Mrs. Manamaya Ghimire, permanent residence of Dudhouli ward no 08, Dudhouli Municipality, Sindhuli district. She has received 3rd tranche of GON housing grant. The house was load bearing brick in cement mortar but after receiving 3rd




The house belongs to Mrs. Bhabamaya Ghimire, permanent residence of Dudhouli ward no 07, Dudhouli Municipality, Sindhuli district. She has received 2nd tranche of GON housing grant. The house is load bearing structure with brick in cement mortar. The

tranche the owner now modified house by constructing RRC frame structure which seems non-compliance.



The house belongs to Mr. Padam Bahadur Tamang, permanent residence of Madubani ward no. 11, Dudhouli Municipality, Sindhuli district. He has received 2nd tranche of GON housing grant. The house is load bearing structure with brick in cement mortar (BMC) and is non-compliance due to 5-inch wall, band discontinuous and not in proper spacing. According to beneficiary he had constructed this house before deployment of DLPIU-Engineers.

house is non-compliance since opening percentage is larger. During the visit our team had advised her to construct wall in the opening area to meet the standard.

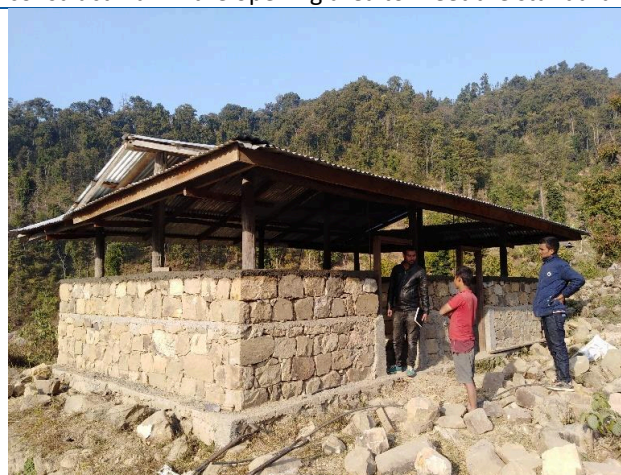

The house belongs to Mr. Bam Bahadur Tamang, permanent residence of Arunthakur war no. 13, Dudhouli Municipality, Sindhuli district. He has received 2nd tranche of GON housing grant. The house is timber frame structure with ground floor stone in mud mortar (SMM) with RC band. Vertical timber post is in plane of masonry wall which seems there is no connection of timber post and masonry wall. During the visit our team advised masons for correction.

Case Study

Sl. No.	Beneficiary Name	Owner Name	VDC	Ward	GP/No	Ward No	Area No	PA No	Recommendation	Remarks
10900	Purung	Purung	2	Dudhouli	Municipality	13	97207	G-20-2-0-001	Beneficiary	Partial beneficiary
10901	Indra Bdr. Khatri	Indra Bdr. Khatri	5	Dudhouli	Municipality	13	97208	G-20-2-0-002	Beneficiary	Partial beneficiary

Sl. No.	Beneficiary Name	Owner Name	VDC	Ward	GP/No	Ward No	Area No	PA No	Recommendation	Remarks
10906	Ratna Bdr. Lamichhane	Ratna Bdr. Lamichhane	अमर	१	दुधौली	१३	९७६११	९-२०-२-०-००१	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10907	Tanka Bdr. Damai	Tanka Bdr. Damai	अमर	१	दुधौली	१३	९७६१२	९-२०-२-०-००२	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10908	Ambar Bdr. Khatri	Ambar Bdr. Khatri	अमर	४	दुधौली	१३	९७६१३	९-२०-२-०-००३	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10909	Narayan Bdr. Khadka	Narayan Bdr. Khadka	अमर	४	दुधौली	१३	९७६१४	९-२०-२-०-००४	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10910	Tek Bdr. Khadka	Tek Bdr. Khadka	अमर	४	दुधौली	१३	९७६१५	९-२०-२-०-००५	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10911	Abak Bdr. Khatri	Abak Bdr. Khatri	अमर	४	दुधौली	१३	९७६१६	९-२०-२-०-००६	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10912	Omaya Khatri	Omaya Khatri	अमर	४	दुधौली	१३	९७६१७	९-२०-२-०-००७	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10913	Rudra Bdr. Rayachhetri	Rudra Bdr. Rayachhetri	अमर	४	दुधौली	१३	९७६१८	९-२०-२-०-००८	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10914	Gyan Bdr. Prasad	Gyan Bdr. Prasad	अमर	४	दुधौली	१३	९७६१९	९-२०-२-०-००९	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10915	Hem Singh Tamang	Hem Singh Tamang	अमर	७	दुधौली	१३	९७६२०	९-२०-२-०-०१०	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10916	Kamal Bdr. Alamgar	Kamal Bdr. Alamgar	अमर	७	दुधौली	१३	९७६२१	९-२०-२-०-०११	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही

Sl. No.	Beneficiary Name	Owner Name	VDC	Ward	GP/No	Ward No	Area No	PA No	Recommendation	Remarks
10917	Yadu Bdr. Magar	Yadu Bdr. Magar	अमर	७	दुधौली	१३	९७६२२	९-२०-२-०-०१२	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10918	Yashu Maya Tamang	Yashu Maya Tamang	अमर	७	दुधौली	१३	९७६२३	९-२०-२-०-०१३	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10919	Dhokan Bdr. Sarki	Dhokan Bdr. Sarki	अमर	७	दुधौली	१३	९७६२४	९-२०-२-०-०१४	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10920	Indra Bdr. Larki	Indra Bdr. Larki	अमर	७	दुधौली	१३	९७६२५	९-२०-२-०-०१५	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10921	Surya Maya Tamang	Surya Maya Tamang	अमर	७	दुधौली	१३	९७६२६	९-२०-२-०-०१६	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10922	Krona Bdr. Tamang	Krona Bdr. Tamang	अमर	७	दुधौली	१३	९७६२७	९-२०-२-०-०१७	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10923	Hem Bdr. Tamang	Hem Bdr. Tamang	अमर	७	दुधौली	१३	९७६२८	९-२०-२-०-०१८	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10924	Rudra Bdr. Khatri	Rudra Bdr. Khatri	अमर	७	दुधौली	१३	९७६२९	९-२०-२-०-०१९	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही
10925	Krishna Bdr. Magar	Krishna Bdr. Magar	अमर	८	दुधौली	१३	९७६३०	९-२०-२-०-०२०	प्रतिकरण लाभग्राही	प्रतिकरण लाभग्राही

During our field visit to Dudhouli Municipality's ward no. 13 we came up with an unusual case of 21 earthquake beneficiaries who still had not received their first tranche since PA agreement.

It was disappointing to see the negligence and lack of knowledge and co-ordination between the Local Level government bodies and Government bodies at District Level. When enquired it was stated that, the ward secretary once took the PA agreement files to NRA Office in Sindhuli but due to some unknown reason the files were not accepted and no proper explanation from NRA was provided on why those files were returned. Since, then the files remain with in the confinement of ward secretary and due to other official work, no initiative was taken either from the local level to forward those files. Now the scenario is that all District Level NRA has been dissolved to GMAI and GMAI does not have proper information about those files since it never came under their radar.

Ward No. 13 is at one of the most remote places of Dudhouli Municipality and can take up to a day to reach. Development infrastructure is next to negligible and the 21 beneficiaries are still living in the hope of receiving tranche and reconstructing and retrofitting their homes.

*Above are the list of beneficiaries 1 for RCB (Reconstruction Beneficiary) and the next 20 RTB (Retrofitting Beneficiary).

Note: HRRP is soon going to organize a meeting regarding this with GMAI and delegates from Dudhouli to bring it to a conclusion.
