

District Report

Sindhuli

25 May - 7 June 2018

Activity Summary

Activity	Contact Person	Reference Document
Info Pack, District Profile Distribution to Sunkoshi Rural Municipality and collection of Feedback.	techcord.sindhuli@hrrpnepal.org	
Conducted joint monitoring and field visit in Bhimsthan, Dudhauli Urban Municipality, respective wards and ward office from 7 th June 2018 to 10 th June 2018 jointly with M&E, DSE and DLPIU Engineer.	techcord.sindhuli@hrrpnepal.org	

Upcoming Events & Meetings

	Date, Time, and Location	Contact Person
Planning to conduct Orientation/training on light timber/steel framed structural manual for DLPIU Engineers and POs.	On 21 st and 22 nd June 2018, at DCC Meeting Hall, from 10:00 AM to 5:00 PM.	techcord.sindhuli@hrrpnepal.org

News & Updates

- Orientation/training on light timber/steel framed structure manual
- Build Change is going to organize 4 days retrofitting training for Engineers

Field Visit Reports


Date	Location	Participants
7 th June 2018 – 10 th June 2018	Bhimsthan, Dudhauli Urban Municipality Sindhuli	• Er. Kiran Mahat (M&E) Consultant, Er. Lekhanath Paudel (HRRP), Er. Rajiv Shah (DSE), Er. English Yadav (DLPIU Engineer)
Objective(s)	• Visit with Ward President and monitoring owner- driven households of Bhimasthan and Dudhauli Urban Municipality. • Discussion about the problem related with reconstruction, tranche received by the beneficiaries, policies made by respective ward president, upcoming events by NRA, etc.	
Summary	The field visit was conducted by NRA/HRRP joint monitoring with M&E CLPIU, DSE and DLPIU Engineer Sindhuli from 7th June 2018 to 10th June 2018 in Bhimasthan and Dudhauli Urban Municipality. • On 7th June 2018 we visited with the president, beneficiaries of ward no 3, Bhimsthan of Tinpatan Rural Municipality and discussed on the problems and challenges in the reconstruction, most of the beneficiaries of ward no 3 were waiting for the design manual for timber framed structure, due that some houses constructed recently after the Gorkha Earthquake and must be corrected.	

- On 8th June 2018 we visited with the chief administrative officer, beneficiaries of ward no 9, Dudhauli of Dudhauli Municipality and discussed on the problems and challenges in the reconstruction. Most of the houses had got government 2nd tranche. We found some under construction non-compliance RCC building there.
- On 9th June 2018 we visited with the beneficiaries of ward no. 7 of Dudhauli Urban Municipality and discussed on the issues and challenges regarding reconstruction. Most of the beneficiary were waiting for design of timber framed structure manual so that that manual will meet their design requirement and get government 3rd tranche.
- In Dudhauli Urban Municipality most of the houses are timber framed structure so all the technical staff are waiting for training on timber framed structure manual.

Reconstruction Progress Report of Dudhauli Urban Municipality

S. N	Name of Ward	Total Beneficiaries	1 st Tranche Received	2 nd Tranche Received	3 rd Tranche Received	Remarks
1	Hatpate	844	693	300	33	
2	Nipane	209	24	1	0	
3	Sirhauli	596	450	255	65	
4	Harshahi	98	65	40	0	
5	Dudhauli	1642	1325	601	136	
6	Jinakhu	227	224	50	20	
7	Arunthakur	675	663	625	30	
8	Kukurthakur	362	340	237	0	
	Total	4653	3704	2109	284	

Source: Dudhauli Urban Municipality Office, Dudhauli 2075/02/25.

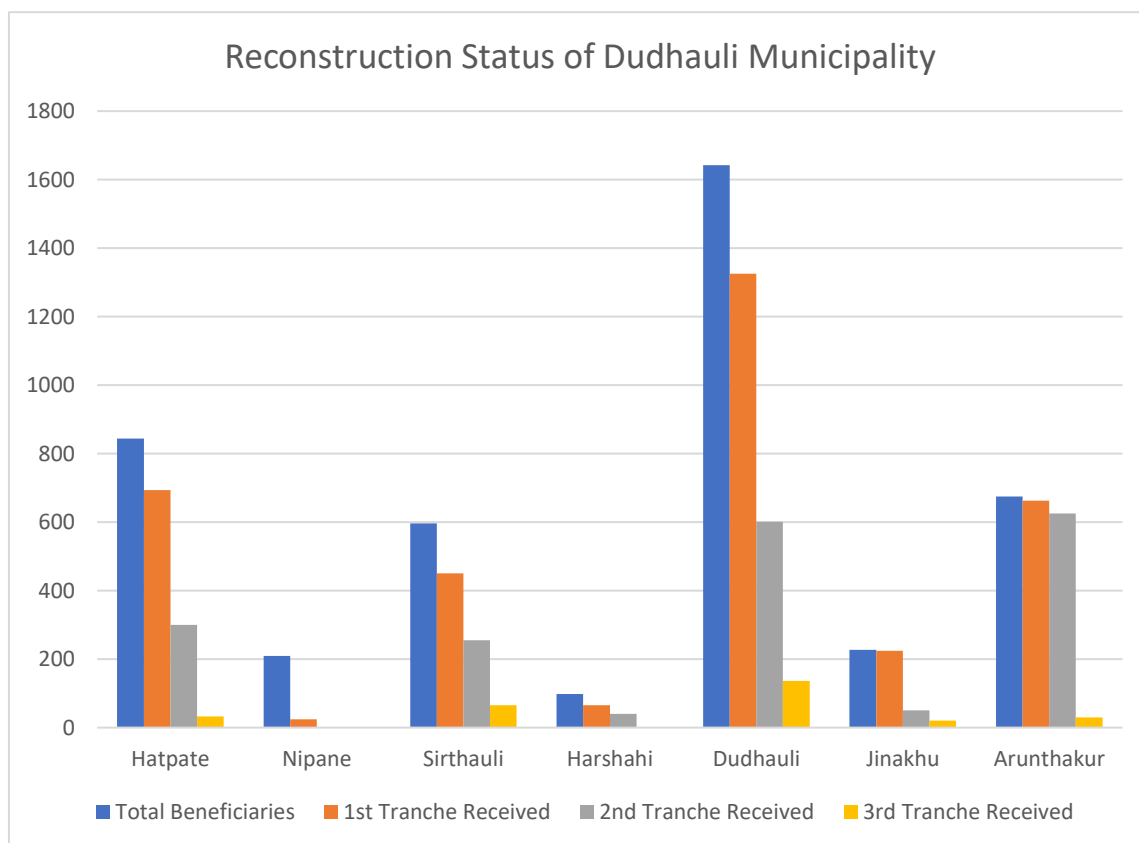

Challenges / Issues Identified	Action Required	Responsible	Timeframe
➤ Non-compliant houses	Control over	DLPIU Engineers	As soon as possible
➤ Scarcity of Skilled mason	Mason Training	DUDBC, CLPIU, NRA	As soon as possible
➤ Unavailability of DLPIU Engineers	Regular Monitoring	DLPIU, CLPIU, NRA	Quick
➤ Problems regarding timber houses	Training	NRA, DLPIU	As soon as possible

Photos



Timber framed structure house located in Dudhauli ward no – 09 of Dudhauli Urban Municipality, Sindhuli district. This house was built recently after the Gorkha Earthquake, it is L-shaped so, we provided some correction measures to the house owner during visit. House owner is waiting for government 3rd tranche.



Timber framed structure house located in Bhimasthan Ward no – 03 of Tinpatan Rural Municipality, Sindhuli district. This house was built recently after the Gorkha Earthquake, before the deployment of DLPIU Engineers. Few corrections are required to make compliance so that house owner would get government 3rd tranche.



Brick Masonry building located in Bhimasthan ward no – 03 of Tinpatan Rural Municipality, Sindhuli district. This house is in the stage of under construction, it seems non-compliance because RCC column with single reinforce bar. The house owner has received government 2nd tranche.



RCC building located in Dudhauli ward no – 09 of Dudhauli Urban Municipality, Sindhuli district. According to DLPIU Engineer, the house owner has started reconstruction without design and drawing approval from Municipality and the shape of building is C. The house owner has only received government 1st tranche.



Timber framed structure house located in ward no – 07 of Dudhauri Municipality, Sindhuli district. The house is in the stage of under construction. We suggested house owner to extend the ground floor wall up to vertical timber post and in the first floor to use light construction material to make compliance. House owner has received government 2nd tranche and waiting for 3rd tranche.



RCC framed structure building located in Bhimsthan ward no – 03 of Tinpatan Rural Municipality, Sindhuli district. The house was non-compliance so DSE providing technical support to beneficiary so that she/he can receive government 3rd tranche.
