

Monthly District Report

Dolakha, Ramechhap, Sindhuli

12 July - 22 August 2019

Summary of events during this period					
Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Dolakha	Meal reporting of July 2019	5-Aug-2019		prabin.gautam@hrrpnepal.org	
	Palika Level Coordination Meeting on Reconstruction	20-Aug-2019	Baiteshwor RM	prabin.gautam@hrrpnepal.org	GD link
	Ward Level Coordination Meeting on Reconstruction	21-Aug-2019	Jiri Municipality, ward no.: 6	prabin.gautam@hrrpnepal.org	GD link
	Palika Level Coordination Meeting on Reconstruction	23-Aug-2019	Tamakoshi RM	prabin.gautam@hrrpnepal.org	GD link
	Palika profile link upload at Palika website	till 26-Aug-2019	District-palikas	prabin.gautam@hrrpnepal.org	8 out of 9 completed.
Ramechhap	Ward Level Coordination Meeting on Reconstruction	06-Aug-2019	Manthali Municipality-4	Pranjal Bhandari	GD Link to the meeting minutes
	Ward Level Coordination Meeting on Reconstruction	07-Aug-2019	Manthali Municipality-3	Pranjal Bhandari	GD Link to the meeting minutes
	Palika Level Coordination Meeting on Reconstruction	08-Aug-2019	Ramechhap Municipality	Pranjal Bhandari	GD Link to the meeting minutes
	Ward Level Coordination Meeting on Reconstruction	09-Aug-2019	Ramechhap-7	Pranjal Bhandari	GD Link to the meeting minutes
Sindhuli	Joint Monitoring field visit to Golanjor Gauplaika	6 th Aug 2019	Golanjor Gauplaika	Tulasi Ram Lamichhane; Tulasi.lamichhane@hrrpnepal.org	
	Joint Monitoring field visit to Marin Gauplaika	8 th Aug 2019	Marin Gauplaika	Tulasi Ram Lamichhane; Tulasi.lamichhane@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
POs Coordination Meeting	28 Jun 2019, Ramechhap, Manthali	HRRP	Pranjal Bhandari
Field Visit to Sunapati RM	02-06 Jul, 2019, Sunapati, Ramechhap	HRRP	Pranjal Bhandari

News & Updates


- The solution to 1800 beneficiaries living in ailani land has been provided by the team led by Member of Parliament Ganesh pahadi on 5th August 2019. The program was conducted in DCC hall. The committee consisted two member of parliaments from district, DCC chief, CDO and the GMALI Chief.

Tranche Status (Dolakha)


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Baiteshwor Gaunpalika	6392	8359	8204	7772	7295	6941	342	54	54	0
Bhimeshwor Nagarpalika	10796	12515	11617	11188	8995	7797	353	179	179	0
Bigu Gaunpalika	5758	6733	6358	6292	5813	5496	35	8	8	0
Gaurishankar Gaunpalika	5405	6876	6697	6553	5835	5633	134	51	51	0
Jiri Nagarpalika	4764	5850	5665	5100	4328	3697	171	77	77	0
Kalinchok Gaunpalika	7527	8916	8534	8491	8027	7733	32	21	21	0
Melung Gaunpalika	7006	7685	7207	6653	6153	5754	476	262	262	0
Sailung Gaunpalika	6800	8424	7308	7080	6234	5424	918	213	213	0
Tamakoshi Gaunpalika	6191	7461	6979	6932	6496	6041	115	41	41	0

Graph of Tranche Status:

Reconstruction- Tranche Status

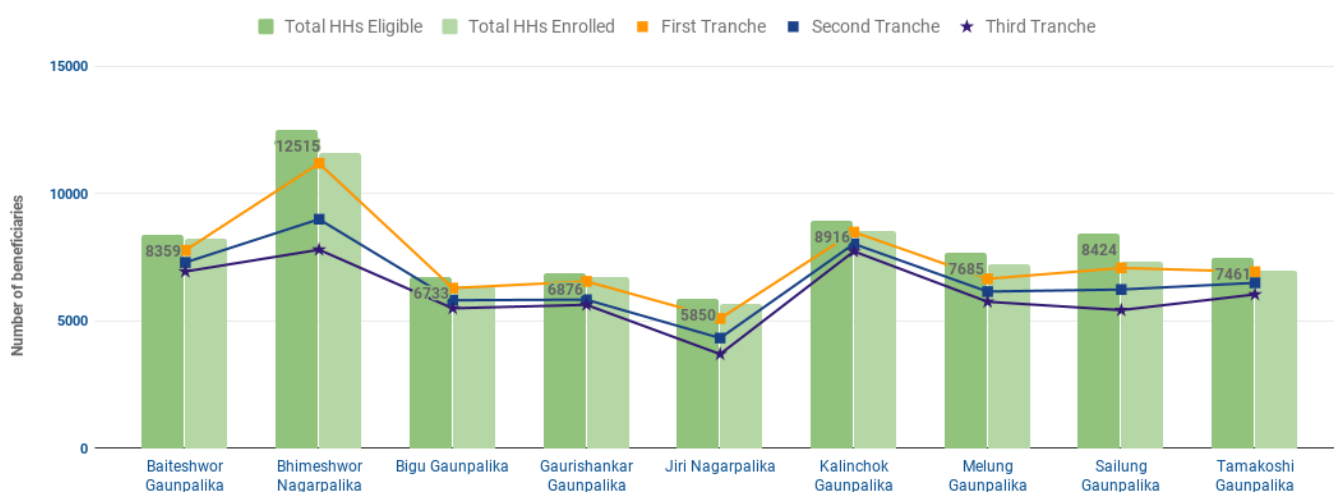


Reconstruction - Retrofitting Status

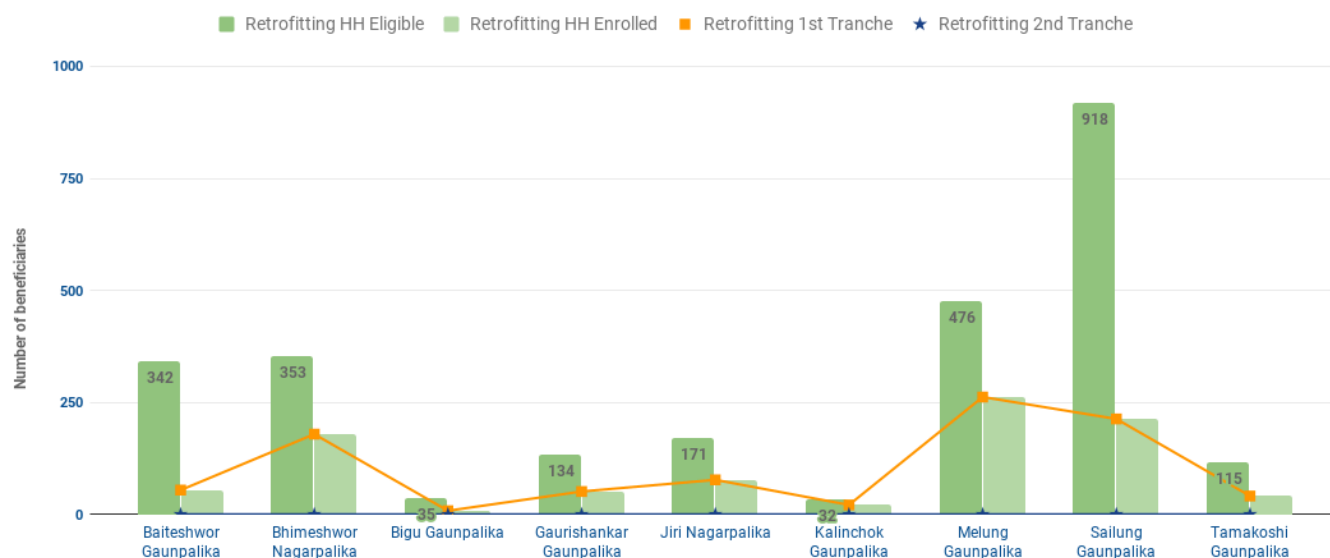


Tranche Status (Sindhuli)

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Dudhouli Nagarpalika	15002	5179	4692	4692	2275	842	3531		804	0
Ghanglekh Gaunpalika	3032	2244	2139	2139	1662	1148	530		118	0
Golanjor Gaunpalika	4835	3231	2992	2992	2372	1774	667		97	0
Hariharpurgadhi Gaunpalika	5176	2601	2296	2296	1746	326	1538		0	0
Kamalamai Nagarpalika	15659	8537	7799	7799	4528	2610	1788		376	0
Marin Gaunpalika	5717	5011	3690	3685	2455	1257	1266		896	0
Phikkal Gaunpalika	4072	2666	2171	2171	2005	1699	932		8	0
Sunkoshi Gaunpalika	6393	5032	4858	4858	3554	1685	327		0	0
Tinpatan Gaunpalika	8863	4701	4671	4671	3986	3234	2499		543	0

Graph of Tranche Status:

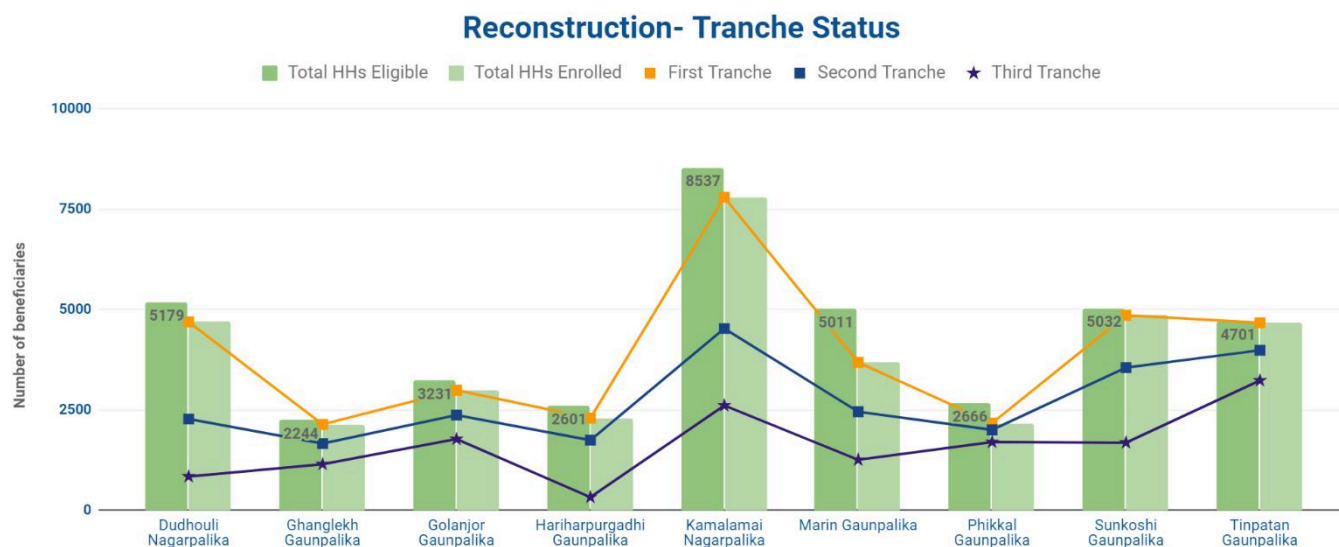

Graph for Retrofitting Status:

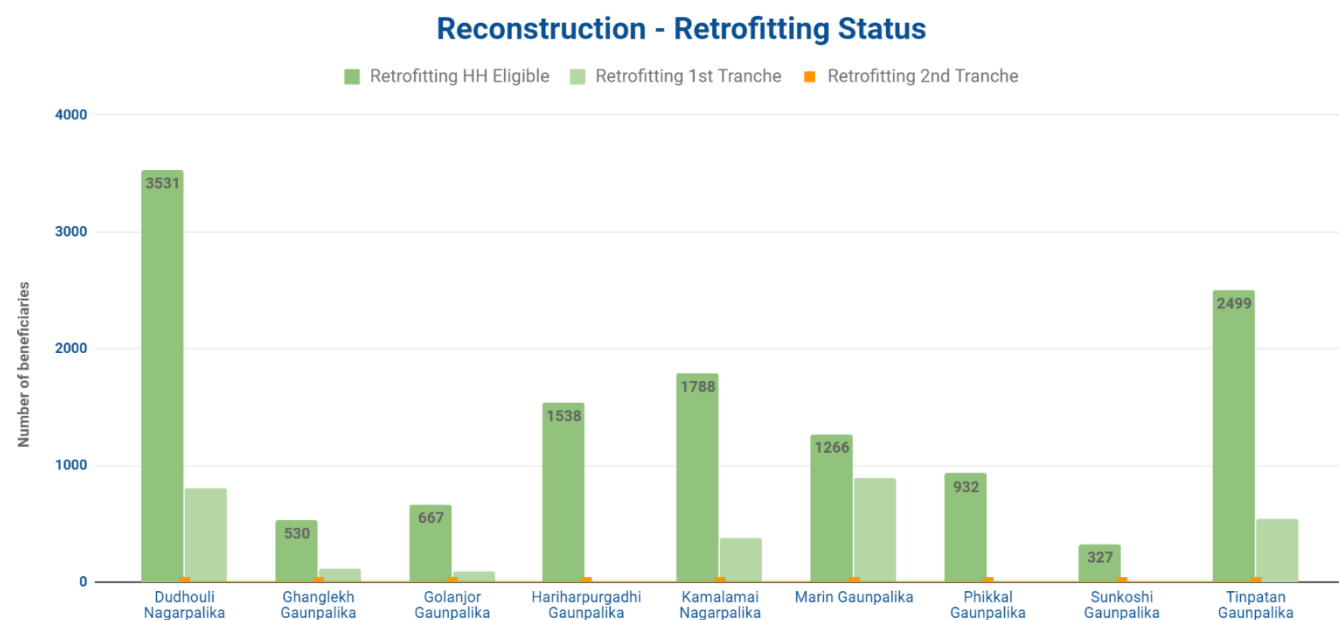


Tranche Status (Ramechhap)


Tranche Status Table:

Palika Name	Total Eligible HHs	PA Signed	Tranche I	Tranche II	Tranche III	Retrofit Eligible	Retrofit Tranche I	Retrofit Tranche II
Doramba Gaunpalika	5275	4855	4849	4115	3449	1076	83	0
Gokulganga Gaunpalika	6377	6129	6124	5489	4822	347	13	0
Khadadevi Gaunpalika	5223	5128	5128	4848	4452	1317	222	0
Likhu Gaunpalika	5688	5570	5570	5226	4857	1010	26	0
Manthali Nagarpalika	11123	10800	10796	9913	8953	1271	132	0
Ramechhap Nagarpalika	6555	6424	6424	5939	5551	960	7	0
Sunapati Gaunpalika	3697	3563	3561	3206	2614	821	21	0
Umakunda Gaunpalika	4997	4643	4643	4205	3301	343	10	0

Graph of Tranche Status:

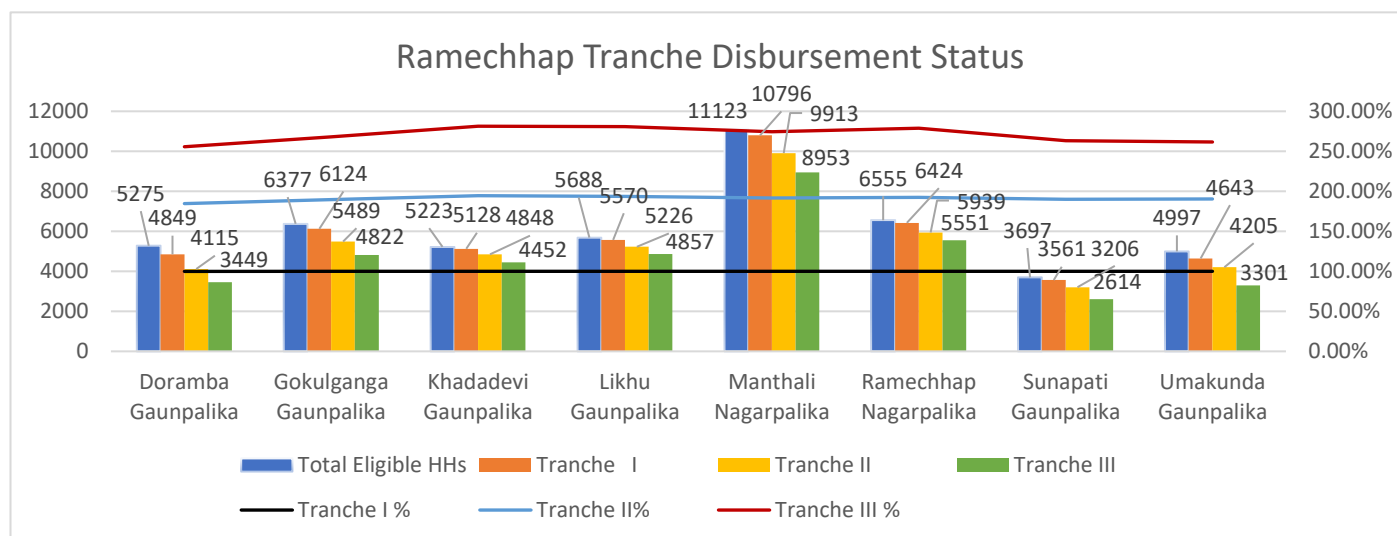

Graph for Retrofitting Status:

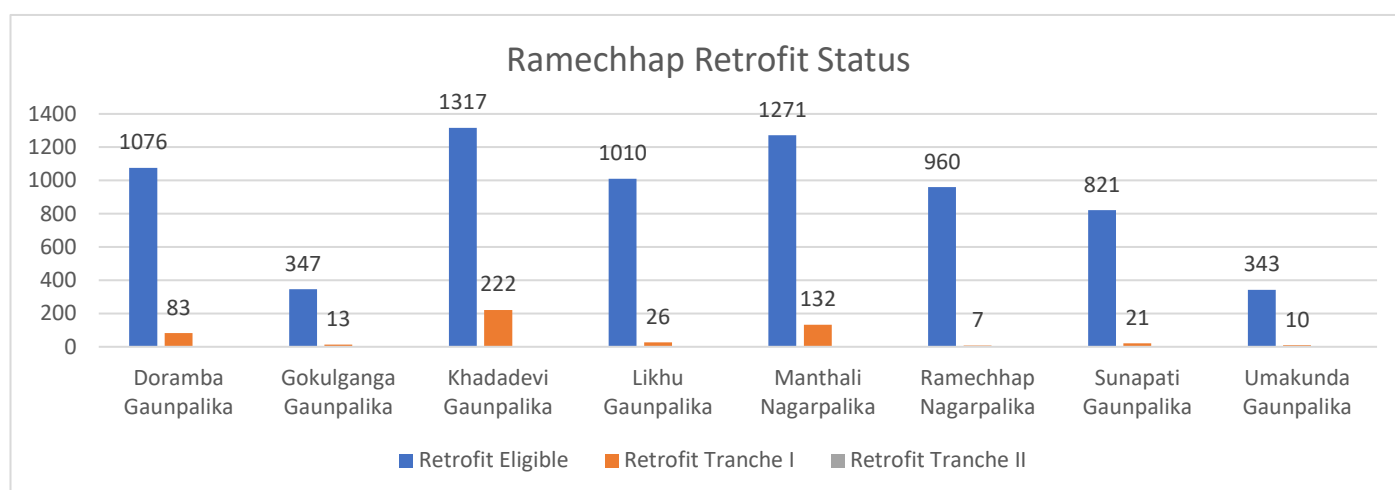

Field Visit Reports (Dolakha)

Visit 1

Visit 1

Date	Location	Participants
(19 – 23) August 2019	Baiteshwor RM, Jiri Municipality and Tamakoshi RM	- Umesh Raut (DLPIU) - Prabin Gautam (HRRP) - Sabita Basnet (DLPIU) - Subhash Shah (DLPIU)
Objective(s)	- Retrofit case stories. - Palika level coordination meetings. - Conduct palika capacity assessment survey. - Housing Typology Survey collection. - Ward level reconstruction coordination meetings.	
Why was the visit carried out in this location?		
In these Palikas, there are issues on reconstruction as most of the beneficiaries listed under retrofit list do not want to retrofit their houses but wants to rebuild a new home instead.		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		

Summary		
Field Visit: - No. of HHs visited:7 - No. of meetings with engineers: 3 - No. of meetings with local officials: 2		
During the field visit and palika/ward level meeting, most of the stakeholders either beneficiary or government authorities were seemed to have a mix understanding of retrofit technique. Government authorities and ward officials view retrofit as a weak process of repair work in which houses would be plastered with cement mortar, the cracks made due to earthquake will just be covered and thus, it is not suitable for shelter purpose. On the other hand, beneficiary compare retrofit as 1 lakh eligible grant receiver with that of full grade 3 lakhs grant receivers/beneficiary. Instead of repairing and retrofitting their bigger houses for settlement purpose, they seem very eager to receive 3 lakhs government grant in order to reconstruct new house. NRA field engineers have constantly communicated with the beneficiary regarding the benefits of retrofitting their old house as it contains more space for storage of grains, rooms for living and conserving the ancient culture of the locality.		

Following meetings were completed during the field visit:

- [Baiteshwor Rural Municipality, Palika level coordination meeting 190820](#)
- [Jiri Municipality, Palika level coordination meeting 190821](#)
- [Tamakoshi Rural Municipality, Palika level coordination meeting 190823](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Lack of practical experience among beneficiary has lowered retrofitting of houses.	In order to get experience on retrofit technique, they were suggested to visit neighboring palika's retrofitted house.	NRA and partner organizations should focus retrofit with more resources available.	Beneficiary, NRA, Plaika/Ward and POs	
Understanding of retrofit among palika/ward officials is very low.		Orientation on retrofit technique should be provided.	NRA and POs	
Retrofit beneficiary wants to be listed under full grade damage scale in order to receive 3 lakhs government grant.	RTB beneficiary can be converted to RCB only through recommendation of NRA field engineers and palika/ward officials to central NRA.			

Photos



Photo: Palika level meeting at Baiteshwor rural municipality



Photo: interaction with retrofit beneficiary and NRA engineer.

Field Visit Reports (Ramechhap)

Visit 1

Date	Location	Participants
06-Aug-2019	Manthali Municipality	Pranjal Bhandari (IM, HRRP), Prabin Gautam (DC, HRRP), Keshab Raj Pandey (DSE, DLPIU Building), Suman Bohora (Coordinator, Scott Wilson), Jagadish Chand (Engineer, Scott Wilson)
07-Aug-2019	Manthali Municipality	Pranjal Bhandari (IM, HRRP), Prabin Gautam (DC, HRRP), Keshab Raj Pandey (DSE, DLPIU Building), Suman Bohora (Coordinator, Scott Wilson), Jagadish Chand (Engineer, Scott Wilson)
08-Aug-2019	Ramechhap Municipality	Pranjal Bhandari (IM, HRRP), Prabin Gautam (DC, HRRP), Keshab Raj Pandey (DSE, DLPIU Building), Suman Bohora (Coordinator, Scott Wilson), Jagadish Chand (Engineer, Scott Wilson)

09-Aug-2019	Ramechhap Municipality	Pranjal Bhandari (IM, HRRP), Prabin Gautam (DC, HRRP), Keshab Raj Pandey (DSE, DLPIU Building), Suman Bohora (Coordinator, Scott Wilson), Jagadish Chand (Engineer, Scott Wilson)		
Objective(s)	- To understand the status of reconstruction, to solve the non-compliance issues at the field level, to interact with the field engineers. - To understand the resurvey and reverification. - To understand the challenges facing the retrofitting.			
Why was the visit carried out in this location?				
- Reported non-compliant issues reported in the location. - Priority Palikas for Joint Monitoring visit. - Large number of Retrofitting beneficiaries that have not done PA agreement with the government.				
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'				
Summary				
Field Visit: - No. of HHs visited:10 - No. of meetings with engineers: 2 - No. of meetings with local officials: 4 Meeting: put a link to meeting minute (if Municipal/Ward level meetings held) Meeting Minutes Ward Level Meeting, Manthali-4, Salu Meeting Minutes Ward Level Meeting Manthali Municipality-3 Meeting Minutes Ward Level Meeting Ramechhap Municipality-7, Sukajor Meeting Minutes Palika Level Coordination Meeting, Ramechhap Municipality				
Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Large number of Retrofit Beneficiaries has not signed the PA with the government	The ward should take the initiative and encourage the beneficiaries in signing the PA	-	Ward Office, Field Engineers	As soon as possible
In Manthali Municipality, there is a general belief amongst the beneficiaries that retrofit is a costly process and is not strong enough.	There is a need of a demo house on retrofit that is necessary to clear the understanding of the beneficiaries on retrofit	-	Palika Office in coordination with the Partner organization.	As soon as possible
Photos				



Cluster 10 D.C Mr. Prabin Gautam observing the retrofit house at Manthali Municipality



Palika Level Meeting ongoing at Ramechhap Municipality.



Meeting and update sharing with DLPIU Building Chief Mr. Prabhakar Lal Karn.



Interaction with Retrofit Beneficiary at Likhu Tamakoshi Municipality.

Field Visit Reports (Sindhuli)

Visit 1

Date	Location	Participants
6 th August 2019	Golanjor Gaupalika	• Surya Prakash Bista, GMALI Chief • Dinesh Sanjel, DSE, DLPIU Building • Tara Lamichhane, SDS, GMALI • Bhola Basnet, CSRC • Ganga Ghimire, Trasnparency International • Tulasi Ram Lamichhane, HRRP
Objective(s)	• To interact with the people’s representatives regarding reconstruction • To discuss regading the PA digitization • To conduct the municipal capacity assessment • To inform about palika profile	
Why was the visit carried out in this location?		
• The reconstruction rate has been low in the gaupalika. • About 570 PA books still needs to be digitized		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
N/A		
Summary		
Field Visit: • No. of HHs visited: 0 • No. of meetings with engineers: 1 • No. of meetings with local officials: 1		
The interaction program with the elected representatives was conducted in 6th August 2019. The program was organized by HRRP/GMALI with the logistics support from Transparency International and Durable Solutions. The program was chaired by Puspa Bahadur Karki, Chairperson of the gaupalika. The Chief guest of the program was Surya Prakash Bista, Act. Chief of GMALI. SDS Tara Lamichhane and DSE Dinesh Sanjel were the guests. The program was facilitated by Ganga Ghimire, representative of TI Nepal. The Act Chief of GMALI stated that the reconstruction has been affected by retrofitting. About 9000 beneficiaries out of 14000 retrofitting beneficiaries have only done agreement but no one have taken the second tranche yet in the district. He also stated that 570 PA books still requires digitization, so he requested the ward chairperson to assist the PA book collector assigned for the digitization. He also requested the people’s representatives to support in speeding the retrofitting work. DSE Dinesh Sanjel stated that the deadline to submit the list of houses constructed before the arrival of engineers is 15th of Bhadra. Also, the resurvey has to completed by 24th of sharwan. He also said that UNOPS has been working in the retrofitting sector and will be retrofitting one model house in the palika. SDS Tara Lamichhane stated that the ESMP conducted by GMALI is to support the reconstruction work. It deals with the structures affected during reconstruction and directly support the reconstruction. It deals with the plantation if timber has been extracted from the community forest, construction of water schemes if scarcity of water is the reason behind the delay in the reconstruction.		

District Technical Coordinator of HRRP stated about the palika profile being made and its importance. He also requested the palika chairperson for its regular update in the website.

Bhola Basnet of Durable Solutions stated that there are 8 landless issues registered in the GMALI which has been addressed and if any missing he requested the ward chairpersons to proceed with the registration process in GMALI with self-declaration, ward recommendation, and other forms made available in ward office.

The Chairperson of Gaupalika ended the program with his closing remarks. He said that the reconstruction works has to be completed in time and urged the ward chairperson to involve in development activities after the completion of reconstruction. He also committed to support the beneficiaries in the livelihood program of gaupalika to enhance the economic status of the beneficiaries.

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
What is the process for completion certificate	The forms has to be filled by the engineers in the provided format. And the distribution ceremony will be organized in gaupalika to distribute for bulk numbers	Dinesh Sanjel DSE		
The houses reconstructed are vulnerable after the landslide during this monsoon	The NRA has assigned the DLPIUs to collect such beneficiaries list and send to central NRA	N/A	NRA	ASAP

Photos



Interaction with peoples representatives and public



Act Chief of NRA giving the update of reconstruction in the program.

Visit 2

Date	Location	Participants
8 th August 2019	Marin Gaupalika	- Surya Prakash Bista, GMALI Chief - Dinesh Sanjel, DSE, DLPIU Building - Tara Lamichhane, SDS, GMALI - Bhola Basnet, CSRC - Ganga Ghimire, Transparency International - Tulasi Ram Lamichhane, HRRP
Objective(s)	To interact with the people's representatives regarding reconstruction	

	• To discuss regarding the PA digitization • To conduct the municipal capacity assessment • To inform about palika profile			
Why was the visit carried out in this location?				
• The reconstruction rate has been low in the gaupalika. • About 570 PA books still needs to be digitized				
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'				
N/A				
Summary				
The interaction program with the elected representatives was conducted in 8th August 2019. The program was organized by HRRP/GMALI with the logistics support from Transparency International and Durable Solutions. The program was chaired by Pani Raj Bamjan, Chairperson of the gaupalika. The Chief guest of the program was Surya Prakash Bista, Act. Chief of GMALI. SDS Tara Lamichhane ,DSE Dinesh Sanjel and Executive Officer Nawaraj Baral were the guests. The program was facilitated by Ganga Ghimire, representative of TI Nepal. The Act Chief of GMALI stated that the reconstruction. Out of 5011 beneficiaries 1257 have received the third tranche and no beneficiaries have received second tranche of retrofitting. He also stated that 962 PA books still requires digitization, so he requested the ward chairperson to assist the PA book collector assigned for the digitization. He also requested the people’s representatives to support in speeding the retrofitting work. Besides this he stated that the solution for 264 beneficiaries living in ailani land was provided with solution. DSE Dinesh Sanjel stated that the deadline to submit the list of houses constructed before the arrival of engineers is 15th of Bhadra. Also, the resurvey has to completed by 24th of Sharwan. He also said that UNOPS has been working in the retrofitting sector and will be retrofitting one model house in the palika. Bhola Basnet of Durable Solutions stated that there are 1800 landless issues were solved by the committee on coordination of the member of parliament out of which 264 were from Marin Gaupaliaka. If any beneficiaries are missing, he requested the ward chairpersons to proceed with the registration process in GMALI with self-declaration, ward recommendation, and other forms made available in ward office. The Chairperson of Gaupalika ended the program with his closing remarks. He said that the gaupalika will support with full effort to complete the reconstruction in allocated time. He also thanked GMALI for easing the reconstruction process for the landless people.				
Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)				
Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
The timber houses are not receiving the third tranche	Necessary corrections must be done as suggested by Engineer	DSE	DSE	ASAP
After agreement has been done the documents has been lost of the beneficiaries and he is not receiving the tranche	Find the digital copy of the beneficiary and give the print copy	GMALI Chief	MIS Expert	ASAP

Photos				
				
Act Chief of GMALI giving the update of reconstruction in the program		Gaupalika chairperson giving the closing remarks.		

Housing Typology Report



The House Belongs to Mr Bal Kumari Thapa and is situated at Manthali Municipality-4 Salu. The house is a SMM structure. The house owner has received all three tranches from the government. The total cost of the house is estimated at 6.5 Lakhs Rupees out of which 3.5 lakhs was borrowed from the local lenders according to the owner.



The house belongs to Mrs. Maili Thapa and is situated in Manthali Municipality-4, Salu. The house is a SMM structure. The houseowner has received all the three tranches from the government. The estimated cost of the house is 6 Lakhs.

Case Study

Name: Mr. Tolak Bahadur Karki

PA number: R-21-9-1-0-005

Damage grade scale: Grade 3

Technical solution required: Minor repair (Retrofit)

Longitude: 86.055382

Latitude: 27.43795

He is from Manthali Municipality-2, Kathajor village. His house sustained several cracks during 2015 earthquake. He recalls that there were plenty of confusions early regarding retrofitting technique. He came to know that a Partner Organization (PO) named Build Change (in support of Scott Wilson) who conducts repair and retrofit of minor damaged houses. Thus, one of the local from Manthali municipality coordinated with the PO to visit the house of Tolak Bahadur Karki to retrofit his house.

He visited to Build Change office at Manthali and told that they can process for retrofitting of his house. The technical staffs from the organization came to examine the house and informed him of the technicalities that they would need to go through. Such technicalities were as removing the number of the windows(openings), penetrating the walls to insert the rods, removing some extra cracks and filling them, etc. He appreciates the technique of retrofitting of old house very much and was convinced that the columns added to the existing structure would amply support the structure. He realized that the retrofitted houses would preserve the ancestral outer structure and design of house.

The engineers informed him of the amount of cost with materials that would be needed to retrofit the house. He was advised to procure 700kg of rods, 85 sacks of cement, 2 tractors of sand, 1 truck of aggregate. Initially, the agreement was that the materials be procured by the houseowner while the labor costs be borne by the organization. However, the house owner was not able to procure all required materials as his wife was sick and had kidney failure which required an immediate operation. Thus, it created economic crisis within the family. After knowing about his family problem, the organization agreed to bear the cost of the materials as well.

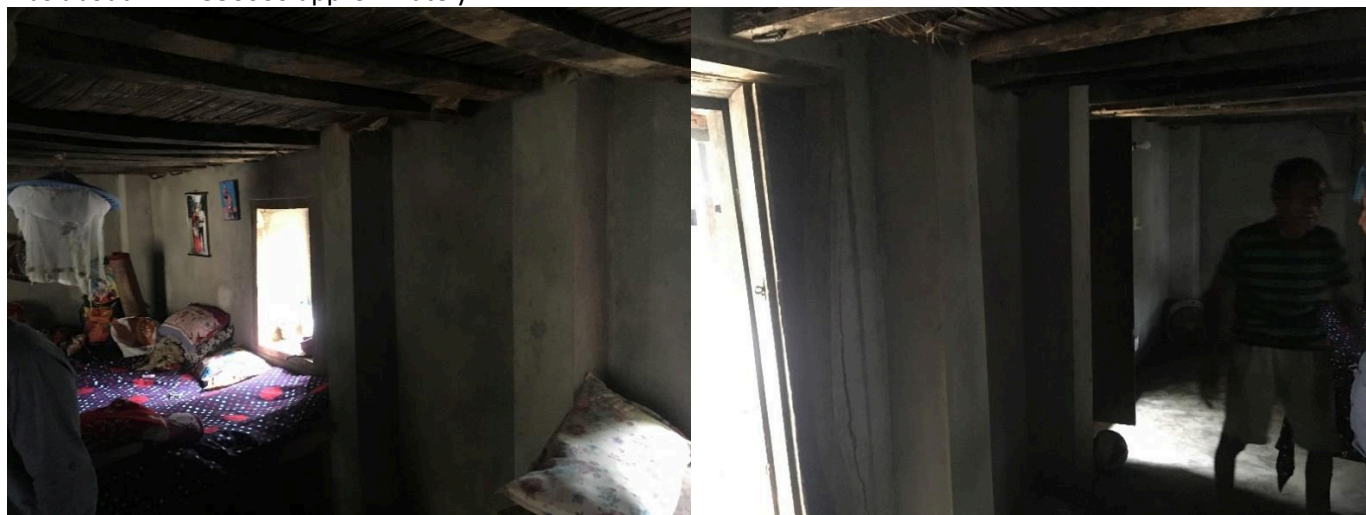


Photo: Tolak Bahadur Karki (Retrofit Beneficiary, Manthali Municipality-2, Kathajor)



Pic: The Retrofitted house Belonging to Tolak Bahadur Karki, Manthali Municipality-2, Kathajor village.

It took about 50 days for the organization to complete retrofitting of Tolak Bahadur's house and the cost incurred was about NPR. 550000 approximately.



Pic: The Interiors of Tol Bahadur's house

Tolak Bahadur is well satisfied with his house been retrofitted and the work carried out by the organization. He thinks that the house has become more stronger than before. He counts himself lucky as he did not have to bear the costs which was well above head of the grant provided by the government. This is also one of the main reasons which he believes that most of the retrofit beneficiaries do not prefer to undergo through it. After the completion of retrofitting work of his house, several beneficiaries visited to see examine the retrofitting technique but most of them turned off by knowing that the costs associated with it is much higher than that supported by the government.
