


[FAQs](#) | [Briefing Pack](#) | [Meeting & Events](#) | [5W](#) | [Housing Progress](#) | [Housing Typologies](#)



As of the beginning of May, the HRRP has moved to [a new district coordination structure](#). There are now 11 district coordination teams, with each team covering a group of districts, and some teams also providing remote support to some of the 18 moderately affected districts.

Featured Technical Staff Person

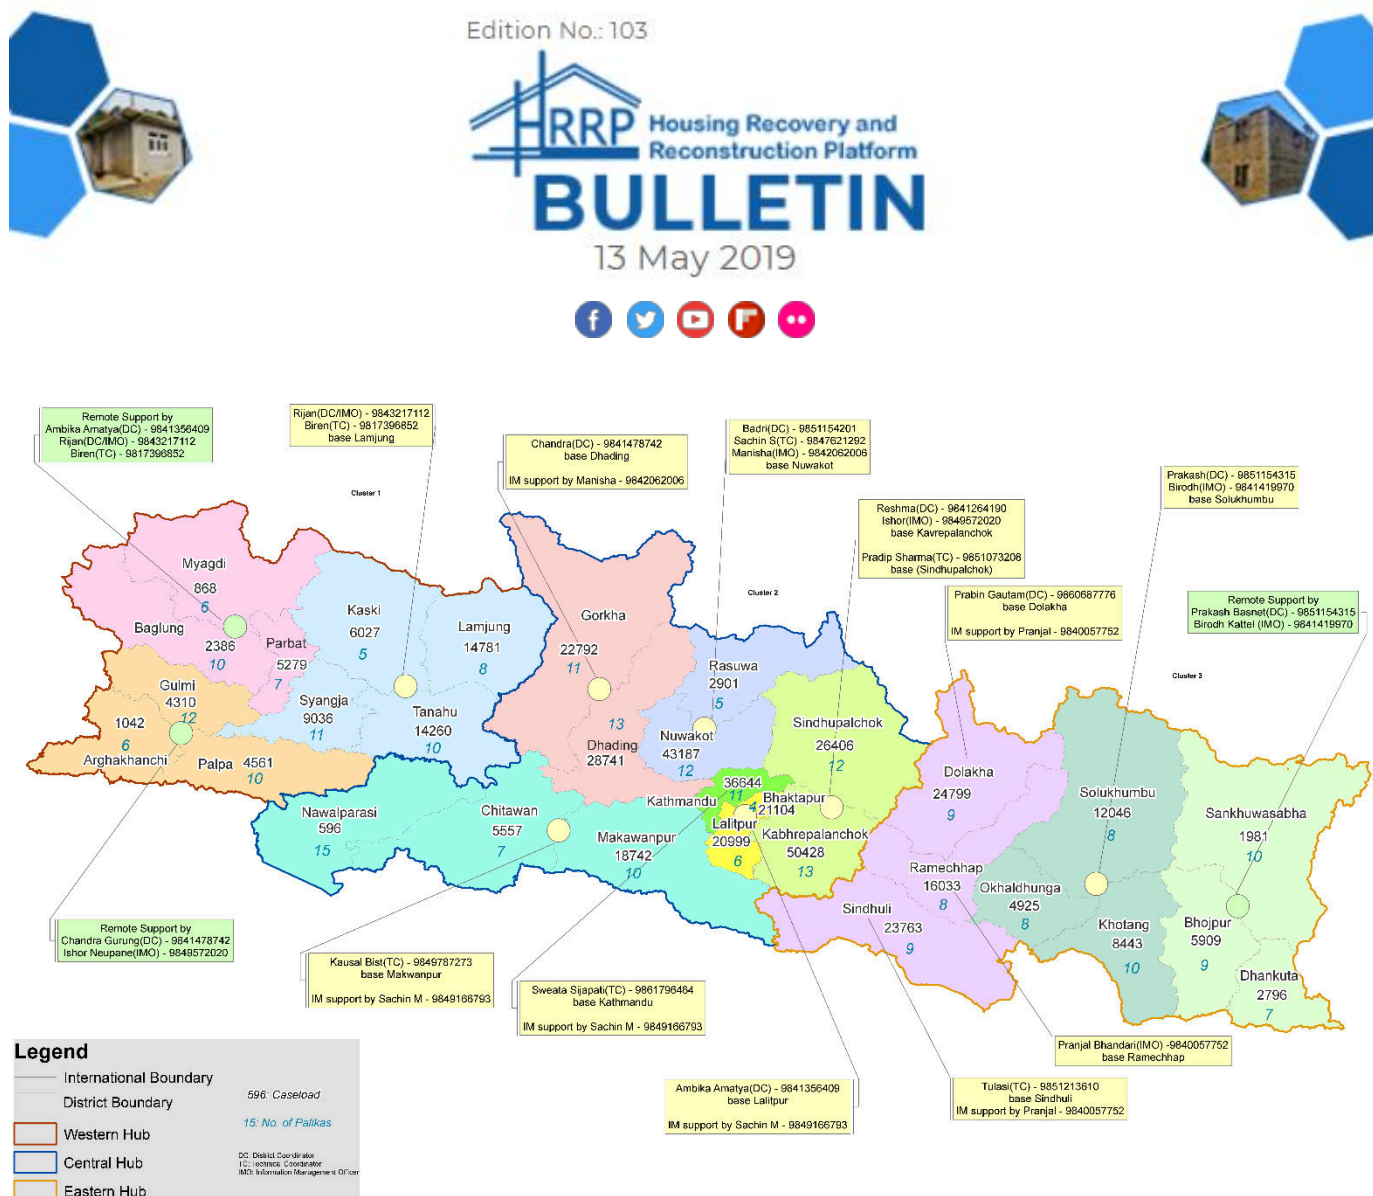

Suraj Shrestha
Engineer, Bhaktapur, DLPIU Building

This month's featured technical staff person is Suraj Shrestha. Suraj is from Ward No. 2, Tumbewa Rural Municipality, Panchthar district and has been working in Bhaktapur since June 2018. He was initially deployed as a ward engineer for wards 5, 6, and 7 of Gorkha Municipality, Gorkha in June 2016.

Suraj shares about his experience working in Gorkha and Bhaktapur as well as reflecting on how the training that he has been provided with since starting to work on the reconstruction has enhanced his knowledge and made it easier to deliver his work effectively. He has found people to be very receptive and open to information and guidance on safer reconstruction.


Highlights

- Update from the most recent meeting of the Vulnerable Support Working Group (VSWG) on 9 May
 - Summary of Technical Sharing Session on Joint Monitoring Field Visit, 23 April
 - In **Ward 7, Godawari Municipality, Lalitpur** one engineer will now be deployed twice a week at the ward office to facilitate and support households in safer reconstruction. This decision was taken after most of the houses constructed used columns with 4 vertical reinforcement bars in each corner where one vertical bar would be sufficient. This has been due to untimely information flow to households.
 - [The Path to Housing Recovery, Nepal Earthquake 2015 Housing Reconstruction, Fourth Anniversary Edition](#)
 - [5W products](#), prepared based on the latest round of 5W data from 25 March 2019
-

National Updates

NRA, CLPIU GMALI and Building, Grant Disbursement Data, as of 13 May:

Reconstruction Grant	18 March	15 April	13 May
Total No. Eligible HHs	818,851	824,452	825,633
HHs Enrolled	756,127	761,445	763,598
HHs Received 1 st Tranche	751,986	756,214	759,138
HHs Applied for 2 nd Tranche	574,043	578,835	585,529
HHs Received 2 nd Tranche	554,775	564,820	573,974
Non-compliant at 2 nd Tranche	4,519	4,326	4,405
HHs Applied for 3 rd Tranche	416,491	422,951	429,951
HHs Received 3 rd Tranche	390,448	403,561	418,417
Non-compliant at 3 rd Tranche	2,327	2,363	2,355
Houses Completed	378,935	382,112	386,527
HHs with Completion Certificate	7,465	8,390	9,008
Retrofit Grant	18 March	15 April	13 May
Total No. Eligible HHs	63,019	63,693	65,977
HHs Enrolled	18,342	20,106	20,291
HHs Received 1 st Tranche	17,437	19,170	19,528
HHs Received 2 nd Tranche	27	27	41

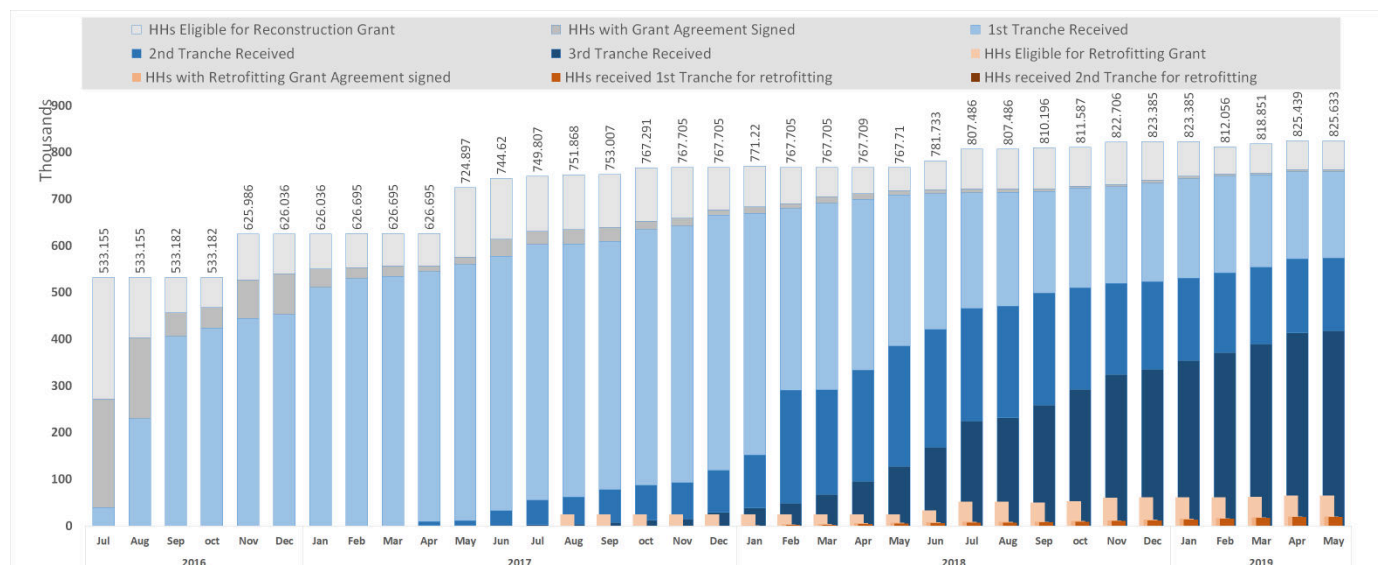

Progress with the disbursement of the GoN housing reconstruction and retrofit grants based on NRA, GMALI CLPIU, and Building CLPIU data from July 2016 to 13 May 2019.

HRRP3 Review and Reflection Meeting, 29-30 April: the objective of the event was to review HRRP activities and to set priorities for the HRRP3 extension period from (March-July 2019). The event was also an opportunity to prepare for the [new HRRP district coordination structure](#). During the event, HRRP National Coordinator, Loren Lockwood and representatives from HRRP implementing Partner Organisations (POs) (CRS, OXFAM, Caritas Nepal, Plan International, and NSET) acknowledged and appreciated the work of HRRP team members. Everyone expressed their commitment to enhance coordination, collaboration, and partnership with the reconstruction stakeholders to move forward aimed at accomplishing reconstruction goals of building safer, stronger, and resilient communities.

Vulnerable Support Working Group (VSWG) Meeting, 9 May: the meeting was chaired by Dr. Chandra Shrestha (NRA Executive Committee Member) and included participants from ASF, Habitat for Humanity, CRS, Lutheran World Relief, HRRP, and NARMIN as well as representatives from various NRA sections. The meeting included presentations on the contents of a vulnerable support handbook currently being prepared, the capacity building process for Senior Engineers, Social Mobilisers, and Mobile Masons, case load verification survey update, and urban reconstruction issues. It was decided that the draft vulnerable support hand book and questionnaire for case load verification survey will be shared with all VSWG members for feedback and comments by today (13 May) after which the document will be submitted to the NRA Executive Committee for approval by 14 May. In addition, a four-member working group led by Under Secretary, Shankar Hari Acharya (Coordinator), was formed to work on urban reconstruction.

Consultation meeting on Camp Coordination and Camp Management (CCCM) Contingency Plan, 9 May: IOM organised the event to share the draft CCCM cluster contingency plan with cluster co-leads and humanitarian partners and to collect and discuss feedback on the plan. Participants included UN Women, Save the Children, UNFPA, WFP, DCA, IFRC, Nepal Army Disaster Unit, Nepal Police Disaster Unit, and the Armed Police Force Disaster Unit. The participants took part in different group work activities on disaster scenarios for earthquakes and floods, as well as providing feedback on cross cutting issues, GESI, and supporting vulnerable households. The IOM CCCM team will incorporate all the feedback received before presenting the plan to DUDBC (CCCM cluster lead) for endorsement.

Sharing of DRRM Needs and Capacity Assessment Report of 14 Selected Municipalities across Seven Provinces, 10 May: the session was organised by the CBDRM platform and the study was financially supported by IOM. The major objective of the sharing session was to have an open discussion on the findings from the study. The study started in October 2018 with the aim of identifying the strengths and major capacity gaps of the municipalities in DRRM. This is a first step in the process to build municipal capacity on DRRM as per the DRM Act. The study team presented the key findings from the report including that municipal officials overall have limited knowledge and understanding of DRRM, the DRM Act has had limited impact on planning and activities at municipal officials, neighbouring municipalities are not coordinating or collaborating on DRM planning or activities, and the study did not find any evidence of engaging vulnerable groups in a structured way in DRM. The study did find however that in municipalities where post-earthquake reconstruction is on-going, municipalities have an increased knowledge and awareness of resilience and risk mitigation. The study found that municipalities need training on light search and rescue, capacity building efforts for municipal officials on DRM, communication, and information management, and that there is a need to establish platforms and mechanisms for inter-governmental collaboration, knowledge sharing, and learning.

UK Shelter Forum and Technical Workshop on Health and Shelter, 9 and 10 May: the events covered a wide range of topics and areas of interest and concern, including issues that relate to both psychological and physical health and well-being. The forum and technical workshop considered issues of shelter from a health sector perspective and discussed how this could influence the way the shelter sector works. A recording of the UK shelter forum is available [here](#).

World Reconstruction Forum, Geneva, 13-14 May: this is a global forum that provides a platform to collect, assess, and share experiences in disaster recovery and reconstruction and take forward the policy dialogue. This is the fourth World Reconstruction Conference (WRC) and the theme is “Inclusion for Resilient Recovery,” building on the recognition and consensus of previous WRCs that recovery can risk reinforcing existing inequalities; that a resilient recovery is imperative to sustainable development and poverty reduction; and that to be resilient, recovery must build back better.

Global Platform for Disaster Risk Reduction, Geneva, 13-17 May: this is a biennial multi-stakeholder forum established by the UN General Assembly to review progress, share knowledge and discuss the latest developments and trends in reducing disaster risk. The event is a critical component of the monitoring and implementation process of the Sendai Framework for Disaster Risk Reduction (2015-2030). The outcomes of the Global Platform will

inform the deliberations of the High-Level Political Forum on Sustainable Development and the UN 2019 Climate Summit from a disaster risk reduction perspective.

Promoting Safer Building Working Group Meeting, London, 20 and 21 May: this working group, which is under the Global Shelter Cluster, will meet next week in London. The agenda for the meeting includes the piloting in Mozambique of the Informing Choice for Better Shelter Protocol, an update and analysis of the evidence for self-recovery after Cyclone Idai from the CARE team, advances on the Tonga Country Profile and other work by CRAterre, discussion to advance tools and guidance for implementation of a supporting self-recovery shelter programming, follow up from the UK Shelter Forum and the implications of 'shelter & health' for a self-recovery approach, developing research ideas in advance of an [Academic/ Practitioner Forum on 7 June](#), and next steps for the working group, including the development of effective communication.

District & Municipal Updates

Technical Sharing Session on Joint Monitoring Field Visit, 23 April: the Central Level Project Implementation Unit (CLPIU)/Building and Housing Recovery and Reconstruction Platform (HRRP) organised a half day technical sharing session on joint monitoring field visits. HRRP and CLPIU-Building started the joint monitoring visits in the 14 most earthquake affected districts from February 2018. So far, 215 visits have been conducted by Monitoring and Evaluation (M&E) Consultants of Building CLPIU and HRRP district teams covering 118 Municipalities across the 14 affected districts. During the session, Mr. Navaraj Pyakurel, Project Director, CLPIU -Building highlighted the effectiveness of joint monitoring in addressing the field level issues and challenges in reconstruction. He further highlighted issues related to houses constructed immediately after the 2015 earthquake and misconception between repair and retrofit. He added that joint monitoring could be a good platform to determine the number houses constructed after the earthquake to devise policies to address them and to increase awareness on retrofitting among local representatives and households.

7-day Training of Trainers on Earthquake Resistant Building Construction, 19-25 April, Pokhara, Kaski: the training was jointly organised by the Central Level Project Implementation Unit (CLPIU)/Building and District Level Project Implementation Unit (DLPIU)/Building. HRRP and NSET provided technical support during the training. 70 newly recruited Engineers attended the training from the moderately earthquake affected districts Kaski, Syangja, Baglung, Parbat, and Myagdi.

HRRP District and Municipal Coordination Meetings, 12 April – 9 May 2019: during this period district coordination meetings took place in Makwanpur (11 April), Sindhuli (17 April), Sindhupalchok (23 April), and Dhading (25 April). Municipal level meetings took place in municipalities and wards across Gorkha, Kavrepalanchok, Lalitpur, Okhaldhunga, Ramechhap, Rasuwa, and Sindhupalchok. Some of the highlights from these meetings include:

- In **Makwanpur**, the meeting focused on landless issues, but few decisions were made. Where households are unable to submit their electricity or drinking water bill, the meeting agreed to accept other documents such as voter's card, voter name list, and public pleadings as evidence to facilitate the process of housing reconstruction. Based on the report from the sub-committee formed for the investigation of housing lands proposed to be purchased for different groups of landless beneficiaries, the meeting decided to urge relevant offices to initiate the process to release grants for purchase of land to all applicants. The meeting highlighted the need for households to have submitted all required documents prior to receiving the second tranche. The meeting also decided to support households who have submitted complete documents for the land they been living on for a long time and would like to build new houses.
- In **Sindhuli**, the DLPIU Building Chief noted that 223 households from Hariharpurgadhi Rural Municipality have not opened bank accounts, and no files have been received by DLPIU Building. NRCS noted that it has almost completed its reconstruction project and all that remains is the distribution of completion certificates. Mercy Corps is providing 50,000 NPRs top up support to 35 vulnerable households, and 31 of these have completed their reconstruction and received the third tranche but the completion certificates

still need to be distributed. CSRC conducted an orientation on land issues in its working areas. The orientation was focused on ailani land (government land) which is a major issue in the district. CSRC has received a list of 1,549 households who are living on ailani land. Twenty of these households want to relocate to other places and 6 of them have already been approved for relocation.

- In **Sindhupalchok**, the GMALI Chief raised concerns that issues related to the reconstruction process for landless households who have constructed houses on other people's land have not been addressed yet. Ward chairpersons were requested to take extra caution while dealing with issues with fake beneficiaries as many are appealing through grievance. DLPIU Building noted a slow CS entry process despite a good progress in reconstruction in the district. Partner Organisations were requested to support field engineers for regular CS entry. In case of 169 households with double PA number in JICA's working area, GMALI Chief requested them to draft a letter from the ward to remove those households from one of the lists. GMALI will then correspond to NRA for further removal process.
- In **Dhading**, a programme was organised in memory of the Gorkha earthquake. The DLPIU Building Chief highlighted the importance of working together and creating earthquake resilient communities in view of the frequent disasters occurring in the country. District GMALI provided an update on the tranche disbursement progress; of the 4,711 households eligible for the retrofit grant, 565 have signed the partnership agreement and received the first tranche and none have received the second tranche. NSET Baliyo Ghar shared that 19,371 households have benefitted through various types of technical assistance activities. Purnima Project supported by DFID and Mott MacDonald are focused on community infrastructure and are working with various organisations; WFP on foot trails, OXFAM and DCA on water supply, and GEOC providing engineering support for schools and suspension bridge.
- **Ward 1, Aamachhodingmo Rural Municipality (10 April) & Ward 3, Gosaikunda Rural Municipality (11 April), Rasuwa**: in both wards, 80% households have received the third tranche, but completion certificate distribution has not started. Retrofitting of masonry structures was discussed during the meeting, as well as issues and challenges related to non-compliant houses. Housing typologies prevalent in the wards include timber structures, hybrid structures, and load bearing brick masonry structures. In Ward 3, Gosaikunda, only two sub engineers are deployed so they are facing difficulty handling complex non-compliant cases.
- **Ward 7, Dharche Rural Municipality (17 April), Gorkha**: the ward chief provided an update on the reconstruction progress. They also discussed the issues and challenges in the ward including retrofitting, people having houses in other places, and resurvey and reverification process.
- **Ward 10, Panauti Municipality (24 April), Kavrepalanchok**: the list of 22 households who reconstructed their houses immediately after the earthquake has been prepared and forwarded to DLPIU Building and documents of 24 households requesting to switch from retrofit to full reconstruction grant has been forwarded to NRA. Grievances are the major issue in the ward. The earlier round of resurvey and reverification missed a total of 496 grievances from two previous wards which are now included in ward 10. These will be covered in the current ongoing resurvey and reverification along with other grievances filed at the ward. Another challenge in reconstruction is the communication gap. Most information, such as notices and policies of NRA, reach the ward after the deadline. Orientations on policies are mostly done at municipal level, but it is at ward level where these orientations are required.
- **Ward 10, Champadevi Rural Municipality (25 April), Okhaldhunga**: the ward chief raised concerns regarding households switching from the retrofit to full reconstruction grant without demolishing their damaged house. They also raised requests to complete the resurvey and reverification process as soon as possible. They also shared that the technical person was accused of taking money from households was found not guilty.
- **Ward 8, Manthali Municipality (25 April), Ramechhap**: out of 25 households listed on the NRA vulnerable list, 15 have not started reconstruction. 35 households have been identified as eligible for the retrofit grant but none of them have done the partnership agreement as they wish to switch to the full reconstruction grant. An integrated settlement of 21 households was planned but due to delays in decisions from NRA,

these households have constructed houses by purchasing land on their own. SW Nepal has been providing socio technical support to the households.

- **Ward 7, Lalitpur Metropolitan City (6 May), Lalitpur:** with support from Maya Foundation, Pilachhen Reconstruction Project has reconstructed 84 houses so far. The main reconstruction issues in the area are lack of land ownership papers among the multiple households living in a single house. The poor economic condition of some households and difficulty in transporting construction materials in core areas are also challenges to reconstruction. The Ward Chief insisted on providing grants on an area wise basis to the households.
- **Ward 9, Godawari Municipality (6 May), Lalitpur:** the majority of the houses constructed are RCC and load bearing with brick in cement mortar. Many of the households in the ward wish to build RCC structures but because the reconstruction grant doesn't cover the full cost they are unsure whether to rebuild their houses or return the first tranche. The ward office will prepare a list of households who reconstructed houses before the endorsement of NRA guidelines and the deployment of engineers in the field. These houses will be again inspected by the engineers for any correction measures to be applied to bring these households into the reconstruction grant process. The ward office was requested to prepare a list of landless households and submit to DLPIU GMALI Lalitpur to facilitate further process of rebuilding their houses.
- **Ward 7, Godawari Municipality (7 May), Lalitpur:** most of the houses constructed in the area are stone and mud mortar, it was reported that many of these houses have used columns with 4 vertical reinforcement bars in each corner where one vertical bar would be sufficient. This has been due to untimely information flow to households. One engineer will now be deployed twice a week at the ward office to facilitate and support households in safer reconstruction. The main issue is with ailani land (government land) where people have been living for many years, but they do not have any land ownership certificates. So, they have not been able to sign a partnership agreement. The Ward Chief was informed that some of these issues could be solved through documentation and public inquiry deed process. They were also told to avoid conducting documentation process of houses that fall in the right of way. The Ward Chief mentioned that houses included on the retrofit list are not in a condition to be retrofitted due to their damage level.
- **Temal Rural Municipality (8 May), Kavrepalanchok:** the reconstruction progress is quite slow; migration to urban areas and water scarcity have been the major challenges of reconstruction. It was reported that the NRA deadline for reconstruction and policies to return tranche if houses are not constructed have encouraged reconstruction in the municipality. Initially, reconstruction coordination meetings used to be held in the presence of all the ward chiefs, but this could not continue due to difficulty in accessibility for all the wards. Information on newly assigned focal person and their ToR was shared during the meeting. It was also decided to increase retrofit awareness programme using a demo retrofit house.
- **Bhotekoshi Rural Municipality (7 May), Barhabise Municipality (8 May) & Tripurasundari Rural Municipality (9 May), Sindhupalchok:** grievance settlement has been the main issue in these municipalities. The grievance list provided by the NRA to the engineers does not include all the names of households recommended by the wards. Municipalities have decided to resurvey all the houses recommended by the wards. Presence of technical persons was found to be low, so the municipalities were informed that action would be taken if anyone is found absent from their duty station. The municipalities further decided that engineers need to complete the CS entry backlog by Baisakh 2076 (mid May 2019).

HRRP District Coordination Team Dhading, Weekly District Report, 12 April – 9 May 2019



Ward 4, Siddhalekh Rural Municipality, Dhading: single storey, hollow concrete blocks with cement mortar, RCC bands and flexible roof. The floor area is less than 1,000 sqft, with strength of block 6.9 N/mm² and building size 23' x 25'. The home owner has received all three tranches of the GoN housing reconstruction grant.

HRRP District Coordination Team Kathmandu, Weekly District Report, 12 April – 9 May 2019



Ward No. 9, Godawari Municipality, Lalitpur: single storey, four room load bearing brick and cement mortar masonry house. The house was initially two roomed but after receiving the first tranche, two more rooms were added, thus, was considered non-compliant. The household is currently applying correction measures. The approximate cost of construction is 1,200,000 NPRs. The home owner said reconstruction of the house was delayed due to shortage of water.

HRRP District Coordination Team Kavrepalanchok, Weekly District Report, 12 April – 9 May 2019



Ward No. 5, Temal Rural Municipality, Kavrepalanchok: Demo retrofit house carried out as part of the DFID funded retrofit project implemented by a consortium of UNOPS, Build Change, and BBC Media Action. Two male and three female masons are being trained under two head masons and an engineer.

HRRP District Coordination Team Makwanpur, Weekly District Report, 12 April – 9 May 2019



Ward No. 5, Thaha Municipality, Makwanpur: single storey, two room, load bearing brick and cement mortar masonry house with flexible roof. The home owner has received all tranches of the GoN housing reconstruction grant. The total cost of construction was 700,000 NPRs.

HRRP District Coordination Team Ramechhap, Weekly District Report, 12 April – 9 May 2019



Ward No. 8, Manthali Municipality, Ramechhap: two room, stone and mud mortar masonry house with RCC bands. The home owner added a room for kitchen using light materials. The home owner has received all three tranches of the GoN housing reconstruction grant.

HRRP District Coordination Team Rasuwa, Weekly District Report, 12 April – 9 May 2019



Ward No. 3, Gosaikunda Rural Municipality, Rasuwa: two storey hybrid structure with ground floor stone and cement mortar masonry and first floor in brick and cement mortar masonry. The home owner has received all three tranches of the GoN housing reconstruction grant. The total cost of construction is 2,100,000 NPRs.

HRRP District Coordination Team Sindhupalchok, Weekly District Report, 12 April – 9 May 2019



Ward No. 4, Bhotekoshi Rural Municipality, Sindhupalchok: timber frame structure. The home owner has received second tranche of the GoN housing reconstruction grant. The house is non-compliant due to lack of stud battens so, the home owner was suggested to apply stud battens to be eligible for third tranche.

Case Studies

Featured technical staff person, Suraj Shrestha: Suraj is from Ward No. 2, Tumbewa Rural Municipality, Panchthar district and has been working in Bhaktapur since June 2018. He was initially deployed as a ward engineer for wards 5, 6, and 7 of Gorkha Municipality, Gorkha in June 2016. Suraj shared that the main reconstruction issues in Bhaktapur are:

1. **Building Permit Process & Consultancy Services:** a municipal building permit is required for all buildings but the process to get the permit is lengthy and can be challenging for home owners. Private consultancies are providing design and supervision services for the buildings, but in some places these consultants are providing poor advice to people which affects the quality and ultimately the strength of building.
2. **Design vs. Implementation:** Suraj has found that it is the contractor's judgement and local practices that are followed in the construction, and not what is prescribed in the structural detailing in the house design.
3. **Construction of Additional Floors:** after completing construction, some people have added additional floors making the house non-compliant under the building code and in contravention of the building permit.
4. **One Room Houses:** some people are still choosing to construct one room houses just to access the housing reconstruction grant.
5. **Retrofitting Guidelines:** NRA have only provided retrofitting guidelines for some type-design buildings but in reality, every building is different and for retrofitting needs a specific solution. Many buildings do not meet the criteria given by NRA, so people are still waiting for the proper solution to retrofit their house.

Suraj feels that the major issue in the reconstruction is communication gaps between key stakeholders. In Suraj's experience every household wants to build a safe and resilient house, but most people get their information on how to rebuild from local contractors and neighbours and not from the engineers. Suraj hopes that in the coming days the engineers will be able to bridge the information gap. It is important to highlight that Suraj has taken part in

6 trainings since he was deployed, but none have been on communication skills. If the engineers are going to be able to communicate effectively with households they will need to have training in this area.

Bibi Maya Ghalan is a widow, whose husband died 9 years ago. She has three daughters, two of whom are married. Her ten year old daughter lives with her in ward no 4, Hattirdada, Nallu, Konjyosom Rural Municipality. Bibi's house was severely damaged by the earthquake but she stayed living in the damaged house for about two years because she didn't have enough money to start rebuilding. Bibi was waiting for the housing reconstruction grant from the government but she is illiterate and found the associated paper work and bank procedures very challenging. The Rural Institution for Community Development (RICOD) is an organisation that works in Bibi's ward and they supported her to get through the grant process. RICOD also provided Bibi with the bricks for building her house, as top up support for the reconstruction of her home. Bibi also took part in agricultural training provided by RICOD, as well as receiving seeds and other materials. Bibi is now planning to build a polytunnel where she can grow tomatoes to increase her income.



Bibi stands outside her new house, built with support from RICOD.

HRRP Products

The Path to Housing Recovery, Nepal Earthquake 2015 Housing Reconstruction, Fourth Anniversary Edition: this document presents a timeline of key points so far in the housing recovery, as well as including a pre-earthquake section in an attempt to highlight the decades of work on earthquake preparedness and response in Nepal which preceded 25 April 2015. It is hoped that this timeline has already contributed to and will continue to contribute to increased awareness and understanding of the huge number of policies, procedures, and guidelines that have been developed for the recovery process. Any feedback or suggestions for improvement can be shared with Minar Thapa Magar, HRRP Deputy National Coordinator, minar@hrrpnepal.org.

5W Products are prepared based on the [latest round of 5W data, as of 25 March 2019](#). **Housing reconstruction progress maps** are prepared based on Building CLPIU data as of 5 April 2019.



Technical Assistance for Housing Reconstruction - Coverage of Activities

[5 TA Activities-32 districts](#)
[7 TA Activities-32 districts](#)
[Short Training Coverage](#)
[Vocational Training Coverage](#)
[Community & HHs Orientation](#)
[Demonstration Construction](#)
[Door to Door Technical Assistance](#)
[Helpdesks/Tech. Resource Centres](#)



Sector Wise Maps of EQ affected districts

[Disaster Risk Management](#)
[Education](#)
[Employment and Livelihood](#)
[Gender Equality and Social Inclusion](#)
[Health](#)
[Nutrition](#)
[Agriculture, Livestock Development, and Irrigation](#)
[Social Protection](#)
[Water, Sanitation, and Hygiene](#)
[Number of POs in each ward](#)
[Number of sectors in each ward](#)



Housing Reconstruction Progress Maps

[PA agreement between HHs and GoN](#)
[Construction Started](#)
[1st tranche received](#)
[Compliance rate 2nd tranche](#)
[Compliance rate 3rd tranche](#)
[Construction completed](#)

Partner Products

[Engagement pathways and MEAL for Promoting Safer Building and Supporting Self-Recovery, Scoping Review, December 2018:](#) prepared as part of the Promoting Safer Building (PSB) Working Group (WG), under the Global Shelter Cluster, this scoping review examines what has been documented about knowledge engagement and communication for safer reconstruction, what is known amongst practitioners about what should be done and what is actually being done in practice. This exercise will inform potential future steps that the PSB WG could take to overcome the challenges facing the shelter sector in communication and knowledge engagement.

[Milijuli Nepali, Episode 1202:](#) this is an on-location programme from Karlim, Baglung. The programme starts with a poem on disaster risk reduction by Runmaya Gadel. The first story is of Bishnu Gadel, a Female Community Health Volunteer, who shares ways to be safe during pregnancy. The second story is about Nandu Subedi, a shopkeeper who shares about the things that a person should keep in mind while operating a shop. The third story is of Gaurishankar Sharma, a teacher, who shares the importance and benefits of living in traditional houses. He also explains the process of retrofitting and its importance. The fourth story is about Suntali Shahi, a farmer. She says that most houses are now empty as most families have migrated. Only nine houses in the village are now being used. The programme closes with Runmaya encouraging people to seek an engineer's support if they are retrofitting a house.

[First Advance Estimate of 2019 Wheat Production in Nepal:](#) the estimate was prepared using the CCAFS Regional Agricultural Forecasting Toolbox (CRAFT). The total wheat production in 2019 is forecasted to be 1,950,946 MT, a 1.13 percent decrease compared to the production level of 1,973,151 MT in 2018. The expected yield rate of wheat is expected to be 2.88 MT per hectare. Furthermore, the forecasted figure is a 3.5 percent increase compared to the average production level of the last five years. The report includes province wise wheat production data too.

[FAQs](#) | [Briefing Pack](#) | [Meeting & Events](#) | [5W](#) | [Housing Progress](#) | [Housing Typologies](#)



CONTACT US

HRRP Nepal Office

Jawagal, Lalitpur, Nepal

Tel: (+977) - 01 - 5544149

Email: info@hrrpnepal.org
