

Monthly District Report

Dolakha, Ramechhap, Sindhuli

22 October – 21 November 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Dolakha	District Coordination Meeting with World Bank, Palika focal engineers, GMaLI and HRRP organized by DLPIU/Building.	6-Nov-2019	DLPIU/Building office, Charikot, Dolakha.	prabin.gautam@hrrp.nepal.org	GD link to Minute.
	Palika profile data updated at GD.	12-Nov, 2019	-	prabin.gautam@hrrp.nepal.org	GD link
	Work on vulnerable beneficiary list of NRA for relocation with GMaLI.	15-Nov, 2019	-	prabin.gautam@hrrp.nepal.org	-
	Support GMaLI for compilation of INGOs tranche released detail.	19-Nov, 2019	-	prabin.gautam@hrrp.nepal.org	-
	Planning of joint monitoring field visit with retrofit task group at DLPIU/Building.	21-Nov, 2019	-	prabin.gautam@hrrp.nepal.org	-
Ramechhap	Field visit Ramechhap Municipality	18 Nov-22 Nov	Ramechhap Municipality-1,2,3,6,7,8,9	Pranjal Bhandari	
	Ward Level Coordination Meeting, Ramechhap-9	19-Nov-2019	Ramechhap Municipality-9	Pranjal Bhandari	Meeting Highlights
	Ward Level coordination Meeting, Ramechhap-8	20-Nov-2019	Ramechhap Municipality-8	Pranjal Bhandari	Meeting Highlights
	Ward Level Coordination Meeting, Ramechhap-7	21-Nov-2019	Ramechhap Municipality-7	Pranjal Bhandari	Meeting Highlights

Summary of events during this period

Sindhuli	Joint Monitoring field visit to ward no 3 and 5 of Dudhuli Municipality	12 Nov 2019	Sindhuli, Dudhuli Municipality	Tulasi Ram Lamichhane; Tulasi.lamichhane@hrrpnepal.org	Refer field visit Section
	Joint Monitoring field visit to ward no 3 Hariharpurgadhi	14 Nov 2019	Sindhuli, Hariharpurgadhi Rural Municipality	Tulasi Ram Lamichhane; Tulasi.lamichhane@hrrpnepal.org	Refer field visit Section

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Partners Coordination Meeting	Dec-5, 2019	HRRP	Pranjal Bhandari
Field Visit Doramba RM and Sunapati RM	Dec-23-27, 2019	HRRP	Pranjal Bhandari
Joint monitoring field visit	25 to 29 Nov, 2019 at Sailung and Jiri Palika	HRRP	prabin.gautam@hrrpnepal.org

News & Updates

Dolakha:

DLPIU/Building conducted coordination meeting in presence of representative from World Bank, NRA palika focal engineers, GMaLI and HRRP on 6th November 2019 at its meeting hall.

The meeting was focused on following topics:

1. Retrofit working group

a. Collection of retrofit beneficiary status with data.

b. Collection of lists of beneficiaries who are willing to retrofit their house within each Palika. DLPIU/Building is planning to conduct retrofit of at least 5 retrofitting houses within each palika.



2. PA Collection

a. Few numbers of PA card need to be collected by NRA field engineers and be submitted to GMaLI.

b. Digitization of PA will be carried out by GMaLI.

3. Verification of HHs supported by POs to avoid duplication of tranche

a. HRRP and GMaLI requested focal persons to coordinate with Palika and POs to verify if its beneficiaries have received support from POs so that GMaLI can minimize the risk of duplication of tranche.

The verified data must be listed in a written palika form.

4. Enrollment of HHs who are listed as beneficiary under following NRA criteria:

- a. Beneficiaries added through grievance
- b. Beneficiaries of vulnerable areas
- c. Landless beneficiaries
- d. Beneficiaries residing in public land approved by DCC
- e. Beneficiaries listed from Punaravedan
- f. Beneficiaries converted from RTB to RCB and vice-versa.
- g. All Retrofit beneficiaries

For the enrollment, beneficiary must provide following documents:

- I. Acceptance letter with confirmation of housing construction within NRA deadline.
- II. Partnership Agreement (PA) card.
- III. Ward level approval letter for tranche disbursement.

5. GMaLI to circulate detail status of individual Palika and ward level beneficiary data to palika focal person so that NRA field engineers, beneficiaries, Palika/Ward officials and POs can know the real scenario of each beneficiary.


Sindhuli

- Interaction with the staff of UNOPs regarding retrofitting and update of the activities in the 5W database on 19th Nov 2019.
- Participation in the interaction with the stakeholders of reconstruction organized by transparency Nepal on 19th Nov 2019.
- Participation in the ToT on Earthquake Building Construction in Dhankuta for Engineers.


Tranche Status (Dolakha)

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Baiteshwor Gaunpalika	6392	8359	8204	7826	7341	7015	342	54	54	0
Bhimeshwor Nagarpalika	10796	12515	11617	11371	9173	8216	353	179	179	0
Bigu Gaunpalika	5758	6733	6358	6303	5899	5639	35	8	8	0
Gaurishankar Gaunpalika	5405	6876	6697	6604	5895	5714	134	51	51	0
Jiri Nagarpalika	4764	5850	5665	5177	4383	3864	171	77	77	0
Kalinchok Gaunpalika	7527	8916	8534	8513	8120	7871	32	21	21	0
Melung Gaunpalika	7006	7685	7207	6922	6203	5861	476	262	262	0
Sailung Gaunpalika	6800	8424	7308	7293	6352	5756	918	213	213	0
Tamakoshi Gaunpalika	6191	7461	6979	6981	6564	6193	115	41	41	0

Reconstruction- Tranche Status

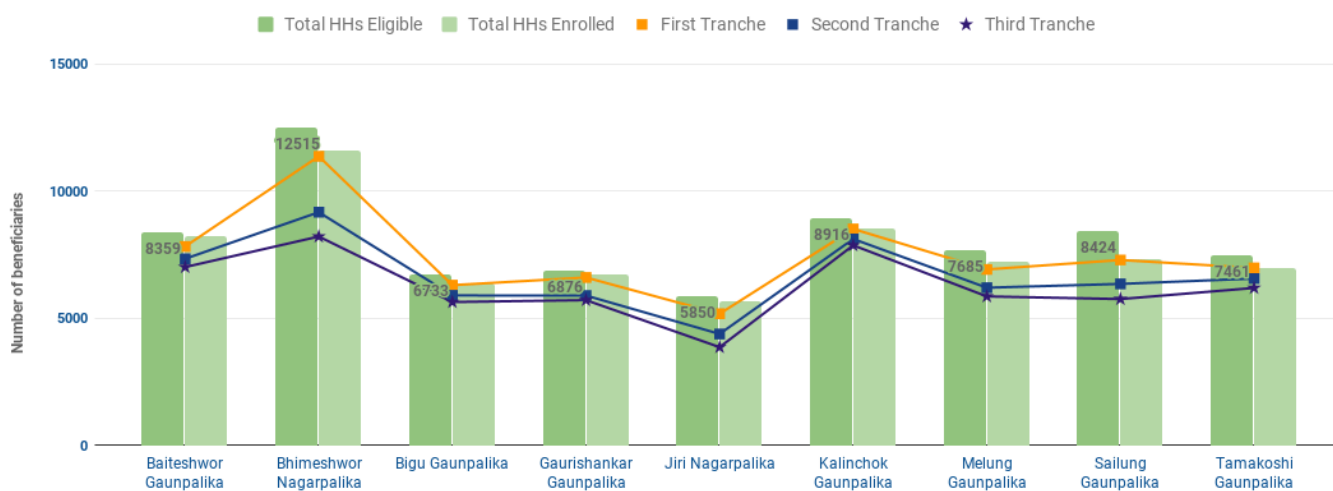

Reconstruction - Retrofitting Status

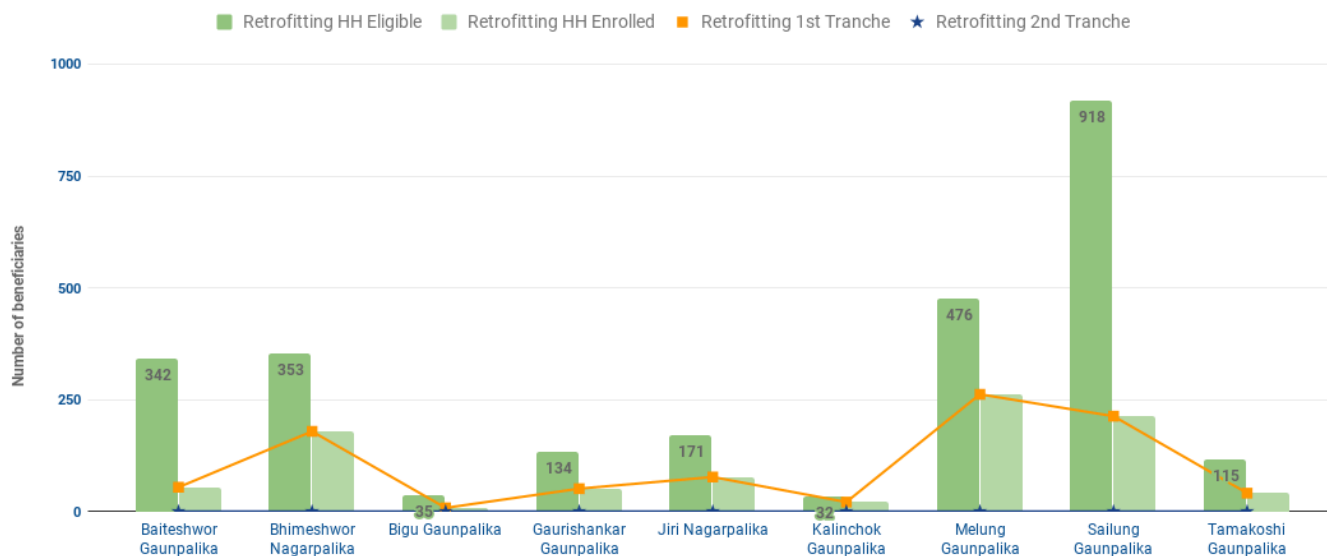


Tranche Status (Ramechhap)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Doramba Gaunpalika	5838	5275	4855	4849	4123	3471	1076	83	83	0
Gokulganga Gaunpalika	6037	6377	6129	6124	5498	4849	347	13	13	0
Khadadevi Gaunpalika	7084	5223	5128	5128	4862	4518	1317	222	222	0
Likhu Gaunpalika	6982	5688	5570	5570	5235	4887	1010	26	26	0
Manthali Nagarpalika	12388	11123	10800	10796	9957	9043	1271	132	132	0
Ramechhap Nagarpalika	8221	6555	6424	6424	5945	5599	960	7	7	0
Sunapati Gaunpalika	5625	3697	3563	3561	3210	2645	821	21	21	0
Umakunda Gaunpalika	6437	4997	4643	4643	4233	3390	343	10	10	0

Graph of Tranche Status:

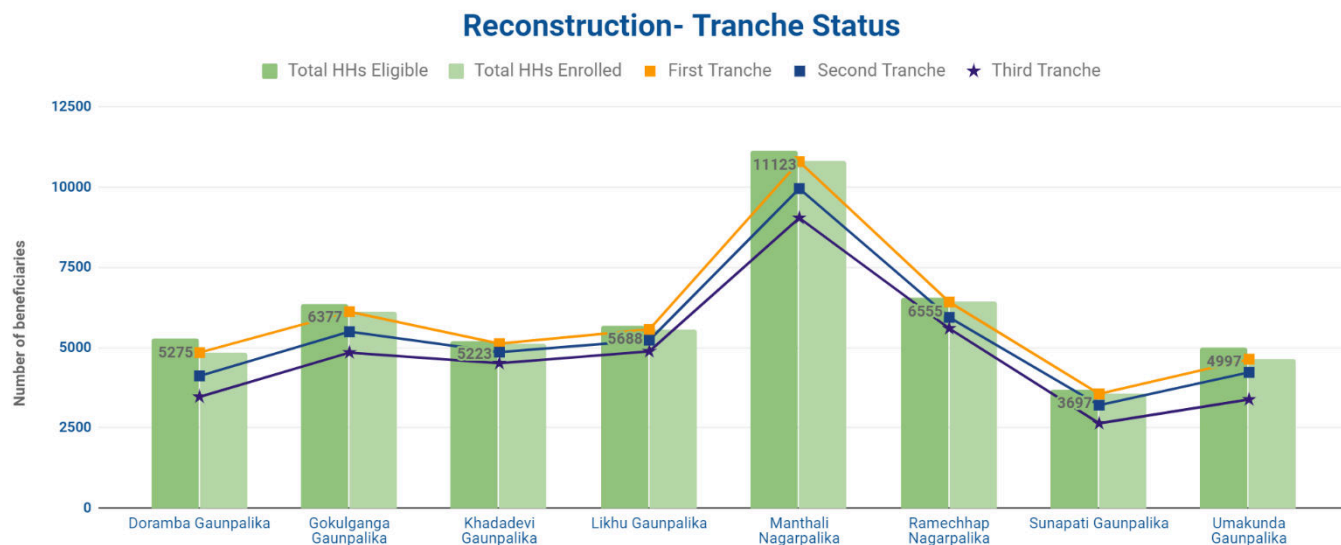

Graph for Retrofitting Status:

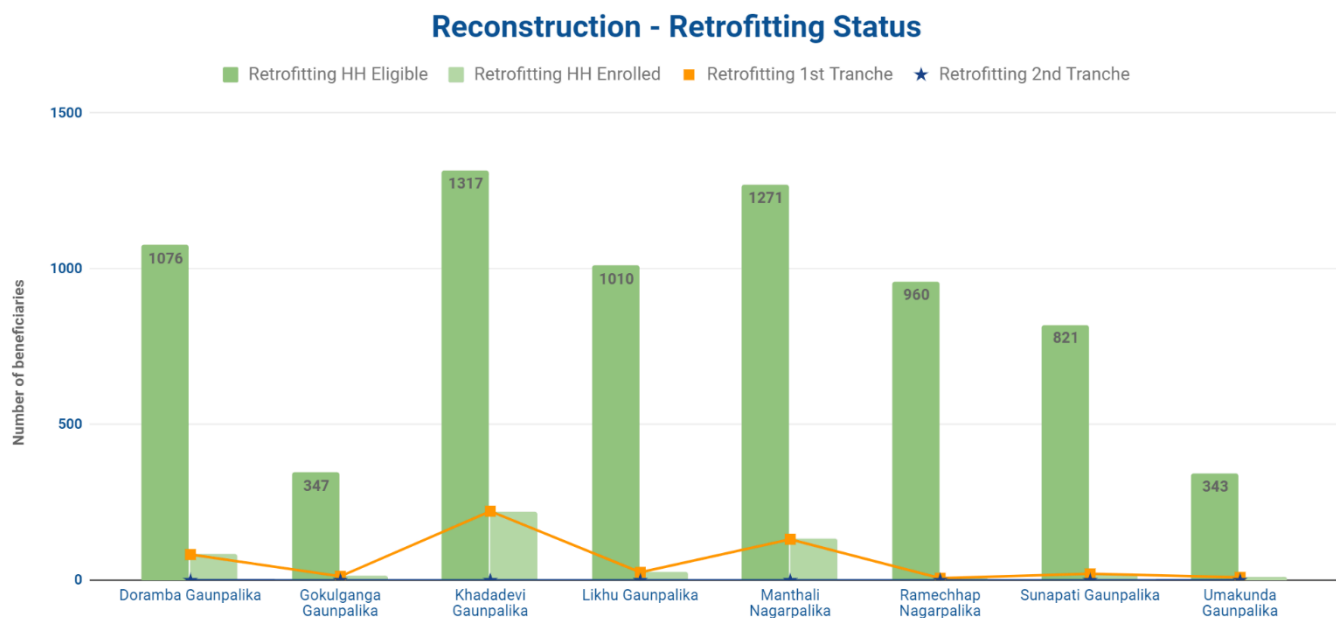


Tranche Status (Sindhuli)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Dudhouli Nagarpalika	15002	5203	5203	4494	2698	1213	3910		2480	0
Ghanglekh Gaunpalika	3032	2247	2247	2135	1879	1500	533		406	0
Golanjor Gaunpalika	4835	3235	3235	3116	2818	2481	683		234	0

Graph of Tranche Status:

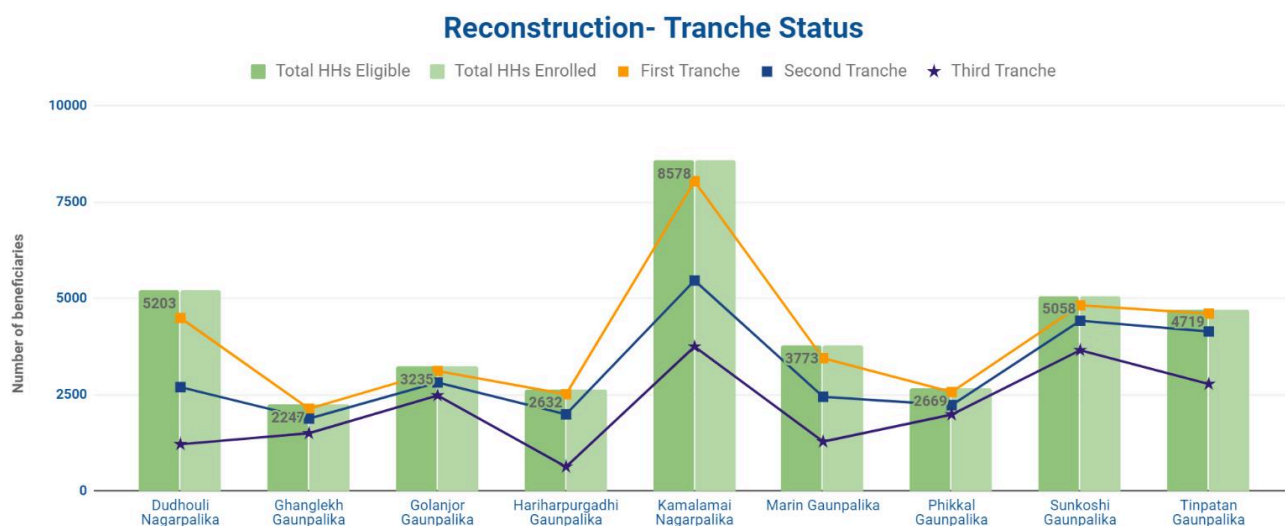

Graph for Retrofitting Status:

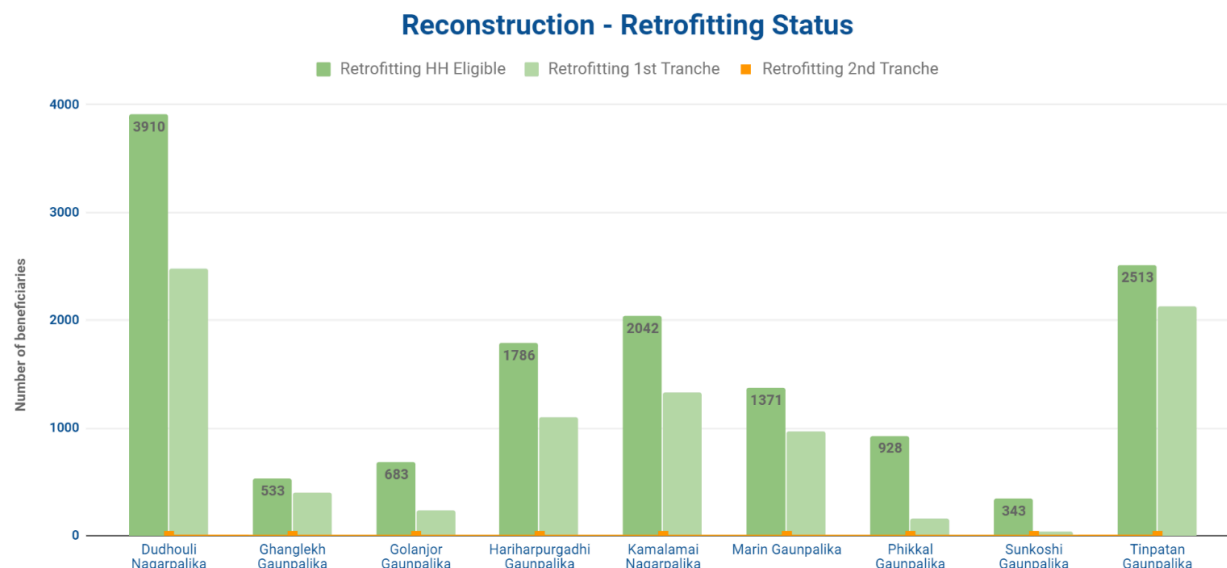

Field Visit Reports (Ramechhap)

Visit 1

Date	Location	Participants		
18-22 Nov, 2019	Ramechhap Municipality	Pranjal Bhandari (IMO, HRRP), Nikesh Maharjan (DSE, DLPIU-Building), Nabin Sharma (MIS Officer, DLPIU-Building), Suman Bohora, (Field Coordinator, SW Nepal), Ujjwal Ghimire		
Objective(s)	- To conduct Ward/Palika Level Coordination Meeting - Distribute HRRP Infopacks - Interaction with the elected officials on retrofit, understand the critical constraining factors and devise way forward. - Conduct housing Typology survey. - To assess the status of the Vulnerable Beneficiaries.			
Why was the visit carried out in this location? Priority wise, Write any other reason				
- The Municipality has the lowest retrofit enrolment rate amongst the municipalities in the district. - To observe a demo-house being retrofitted by Build Change/UNOPS - To monitor the presence of engineers in the ward. - To understand the status of the large number of vulnerable HHs in the Municipality. - To observe the non-compliant houses and provide the engineers with necessary feedbacks				
'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.				
Previous Issues		Current Issues		
Summary				
Field Visit: - No. of HHs visited: 22 - No. of meetings/interaction with engineers: 5 - No. of engineers interacted with: 10 - No. of meetings/interaction with local officials: 3 - No. of local officials interacted with: 7				
Meeting: put a link to meeting minute (if Municipal/Ward level meetings held) Meeting Highlights Ramechhap-9 191119 Meeting Highlights Ramechhap-8 191120 Meeting Highlights Ramechhap-7, 191121				
Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Majority of the HHs who are retrofit eligible have not signed the PA with the government.	The ward office should conduct a door to door campaigns to encourage the beneficiaries to sign the PA	The ward office should conduct a door to door campaigns to encourage the beneficiaries to sign the PA	Ward Office	ASAP
Large Number of the Retrofit Enrolled HHs have filed for the	The Field engineers were provided with the form		Field engineers	ASAP

change in beneficiary type, additional information on the status of which is lacking at the DLPIU Building.	detailing the information status of the retrofit which the engineers has to fill and submit to the DLPIU Building			
The grievances should be addressed at the earliest			NRA	ASAP

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)

- Due to the lack of understanding about strength of the retrofitted house, cost associated, the beneficiaries and the elected representatives are not convinced about retrofit as a result majority of the retrofit eligible have filed for the change in beneficiary type.
- Many of the retrofit eligible HHs have constructed a new house within the NRA standards. Some have dismantled their old house while others haven't.
- There is need of demo retrofit house in each wards of the district in order to scale up retrofitting. Build change/UNOPS are currently retrofitting demo houses in each of the Palika in the district but it is not enough to spur retrofit in the district.

Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)

Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)

- Majority of the vulnerable beneficiaries in Ramechhap Municipality have completed reconstruction. However, they have not received any additional support from the government or Partner Organizations.

Photos



Ward Level Coordination Meeting ongoing at Ramechhap Municipality-8



The DLPIU Building Officials observing the under-progress retrofitting being done by Build Change/UNOPS at Ramechhap Bazar.

Field Visit Reports (Sindhuli)

Visit 1

Date	Location	Participants		
12 th Nov 2019	Ward 3 Office, Dudhauri Municipality	• Dinesh Sanjel (DSE) • Pramod Sah (Focal Person) • Bibek Kumar Karn (Engineer) • Tulasi Ram Lamichhane (Technical Coordinator/HRRP) • Diraj Sardar (Engineer) •		
Objective(s)	• To discuss regarding retrofitting • To discuss regarding reconstruction • To discuss regarding landless issues			
Why was the visit carried out in this location? Priority wise, Write any other reason				
The field visit was carried out to discuss and interact regarding retrofitting issues in the ward. The field visit was carried out jointly by District retrofitting task force team and HRRP.				
If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.				
Previous Issues	Current Issues: The beneficiaries residing in ailani land but having numberi land in vulnerable settlement (near the kamala river) are unable to reconstruct the house due to the land issues.			
Summary				
Field Visit: • No. of HHs visited: 4 • No. of meetings/interaction with engineers: 1 • No. of engineers interacted with: 6 • No. of meetings/interaction with local officials: 1 • No. of local officials interacted with: 1 The meeting was chaired by Chairperson of Ward office. DSE and member of retrofitting task force team and Technical Coordinator of HRRP were present in the program. The discussion was focused in the reconstruction and retrofitting works undergoing in the ward. The ward Engineer Siddhartha Sonu Karn updated the tranche status of the ward and stated that Retrofitting works have been initiated by UNOPS/Build Change in the ward. DSE Dinesh Sanjel stated that NRA has given preference to the retrofitting and he requested the ward representatives to aware the beneficiaries for the retrofitting works. He also instructed the engineers to submit the details of retrofitting within the end of the month of Kartik. He also stated about the deadline for the second tranche which is end of month of kartik. HRRP Technical Coordinator handed the Palika profile and tranche maps to the ward chairperson. Ward Chairperson thanked the team for visiting the ward and requested for the frequent visit in the ward so that the information can be disseminated in the ward. He stated that there has been gap in the sharing of information between the district level office and the ward offices. He stated that reconstruction have been almost completed however the cases related to the ailani land, grievances have been delaying the reconstruction. The case of ailani land with numberi lands have been not solved yet which is leaving the reconstruction beneficiaries not able to reconstruct the houses. He requested the team to forward this issue to the national level.				
Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)				

Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
The issues regarding the beneficiaries having numberi land in vulnerable settlement and residing in ailani land has not been included in the tranche process.	The geological study must be done in numberi land stating vulnerable settlement and then the house owner is provided with the option to reside in the same ailani land or purchase land with 2 lakhs provided	N/A	NRA	ASAP
What will happen to the beneficiaries who have not received the 1 st tranche, beneficiaries of grievances and the ailani land beneficiaries in the second tranche deadline	The deadline is not applicable for such beneficiaries. However, they must take the completion certificate within the month of Asar 2077. NRA must perform the speedy process for such beneficiaries.	N/A	NRA/ GMALI	ASAP

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)

UNOPS have been doing retrofitting works in the ward. They have been retrofitting 5 houses.

Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)

Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)


Photos



Field Visit Reports (Sindhuli)

Visit 2

Date	Location	Participants		
12 th Nov 2019	Ward 5 Office, Dudhauri Municipality	• Dinesh Sanjel (DSE) • Pramod Sah (Focal Person) • Bibek Kumar Karn (Engineer) • Tulasi Ram Lamichhane (Technical Coordinator/HRRP) • Diraj Sardar (Engineer) •		
Objective(s)	• To discuss regarding retrofitting • To discuss regarding reconstruction • To discuss regarding landless issues			
Why was the visit carried out in this location? Priority wise, Write any other reason				
The field visit was carried out to discuss and interact regarding retrofitting issues and reconstruction in the ward. The field visit was carried out jointly by District retrofitting task force team and HRRP.				
If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.				
Previous Issues	Current Issues: The beneficiaries residing in ailani land but having numberi land in vulnerable settlement (near the kamala river) are unable to reconstruct the house due to the land issues.			
Summary				
Field Visit: • No. of HHs visited: 2 • No. of meetings/interaction with engineers: 1 • No. of engineers interacted with: 6 • No. of meetings/interaction with local officials: 1 • No. of local officials interacted with: 1 The meeting was chaired by Chairperson of Ward office. DSE and member of retrofitting task force team and Technical Coordinator of HRRP were present in the program. The discussion was focused in the reconstruction and retrofitting works undergoing in the ward. DSE Dinesh Sanjel stated that NRA has given preference to the retrofitting and he requested the ward representatives to aware the beneficiaries for the retrofitting works. He also instructed the engineers to submit the details of retrofitting within the end of the month of Kartik. HRRP Technical Coordinator handed the Palika profile and tranche maps to the ward chairperson. Ward Chairperson thanked the team for visiting the ward and requested for the frequent visit in the ward so that the information can be disseminated in the ward. He stated that the cases related to the ailani land, grievances have been delaying the reconstruction. The case of ailani land with numberi lands have been not solved yet which is leaving the reconstruction beneficiaries not able to reconstruct the houses. Also, he stated the dilemma about the retrofitting as not a single house has been retrofitted in the ward. He stated the need of retrofitting model house which could be sample for the beneficiaries. He requested the team to forward this issue to the national level. Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)				

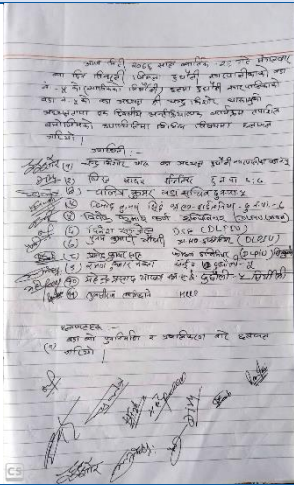Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)				
Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)				
Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)				
Photos				
				
Meeting at ward no 5 Dudhauri Municipality		Minutes of meeting		

Field Visit Reports (Sindhuli)

Visit 3

Date		Location	Participants
12 th Nov 2019		Ward 3 Office, Hariharpurgadhi Rural Municipality	• Rajib Sah (DSE) • Tulasi Ram Lamichhane (Technical Coordinator/HRRP) • Mohan Shrestha (Sub Engineer)
Objective(s)	• To discuss regarding retrofitting • To discuss regarding reconstruction		
Why was the visit carried out in this location? Priority wise, Write any other reason			

The field visit was carried out to discuss and interact regarding the low construction and retrofitting in the ward. The field visit was carried out jointly by District retrofitting task force team and HRRP.

'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.

Previous Issues	Current Issues: The beneficiaries residing in ailani land but having numberi land in vulnerable settlement (near the kamala river) are unable to reconstruct the house due to the land issues.
------------------------	---

Summary

Field Visit:

- No. of HHs visited: 2
- No. of meetings/interaction with engineers: 1
- No. of engineers interacted with: 4
- No. of meetings/interaction with local officials: 1
- No. of local officials interacted with: 1

The meeting was chaired by Chairperson of Ward office. DSE and member of retrofitting task force team and Technical Coordinator of HRRP were present in the program. The ward engineer told that the rate of reconstruction will rise as he have send 200 files for second tranche and 100 files for third tranche. The discussion was focused in the reconstruction and retrofitting works undergoing in the ward. DSE Dinesh Sanjel stated that NRA has given preference to the retrofitting and he requested the ward representatives to aware the beneficiaries for the retrofitting works. He also instructed the engineers to submit the details of retrofitting within the end of the month of Kartik. HRRP Technical Coordinator handed the Palika profile and tranche maps to the ward chairperson.

The ward chairperson stated that the ailani land issues in the ward has not been solved yet. He stated that the reconstruction will rise up if such issues will be solved. He requested to put the issues to concerned authority.

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Issues of ailani land has not been addressed in the ward	Collection of data and addressal by the district authority for the ailani land issues	N/a	CSRC, GMALI	ASAP

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)


Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)

Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)

Photos



Meeting at ward no 3 Hariharpurgadhi Municipality

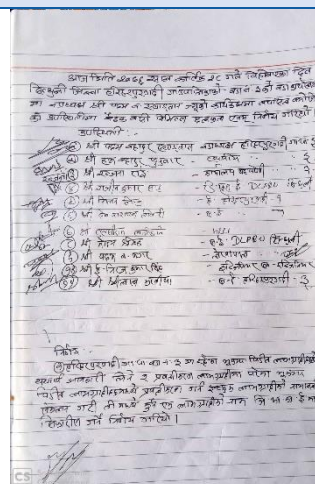

Minutes of meeting

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
How effective would it be to retrofit the SMM houses particularly the ones that are more than 15 years old?	Samir Karki, Ward Chief – Ramechhap 7	It depends on the level of damage the house has sustained. Even on the old houses, retrofit can be done by replacing the weak and feeble wooden posts with new ones. (Nikesh Maharjan, DSE)
When would the NRA address the grievances?	Kedar Karki, Ward Chief -Ramechhap 8	The NRA are on process of addressing grievances. It would be done at the earliest. (Nikesh Maharjan, DSE)
What is the process of releasing the third tranche to a beneficiary who have constructed his house in neighboring district?	Chandra Bahadur Shrestha, Ward Chief- Ramechhap-9	The engineers of the neighboring district to which the beneficiary has migrated must perform CS entry of the beneficiary's house but by choosing Ramechhap district from the drop-down. It would then show in the MIS of Ramechhap and the process of tranche release can be initiated. (Nabin Sharma, MIS Officer)
