

District Report

Kathmandu Valley

12 April – 9 May 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
The ward level general coordination meeting was conducted at Ward no 7, Pilachhen Tole of Lalitpur Metropolitan City. The coordination meeting was attended by Ward Chief, Ward Member, engineer of Lalitpur Metropolitan City and HRRP Kathmandu Valley Team member. The main objective of the meeting was to discuss on reconstruction progress taking place in areas of Ward no. 7 Pilachhen.	16 April 2019	2	2	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
A field monitoring visit was conducted at Ward no. 7 and 17 of Lalitpur Metropolitan City. The visit team included engineer from Lalitpur Metropolitan City and Kathmandu valley team member. Building typology of 3 houses was collected in Kobo Collect Mobile App.	16 April 2019		2	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
Joint M & E Visit was conducted at Ward no. 9, Champi of Godawari Municipality by HRRP Lalitpur District Coordination Team along with M & E Consultant (CLPIU Building), M & E Specialist, EHRP/DLPIU GMALI Lalitpur, DLPIU Engineer and technical personnel from Godawari Municipality.	6 May 2019	2	3	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
Joint M & E Visit was conducted at Ward no. 7, Devichaur of Godawari Municipality by HRRP Lalitpur District Coordination Team along with M & E Consultant (CLPIU Building), M & E Specialist (EHRP/DLPIUGMALI Lalitpur), DLPIU Engineer, technical personnel from Godawari Municipality and Ward Member of Devichaur Ward Office	7 May 2019	4	4	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
A general ward coordination meeting was conducted at Ward no. 9, Champi, Godawari Municipality. The meeting was attended by Ward Chief of Ward no. 9 and Joint M & E visit team members from DLPIU Building Lalitpur, DLPIU GMALI Lalitpur and HRRP Lalitpur District Coordination Team. The coordination meeting was focused on discussing the reconstruction issues in Champi. Preparation of beneficiaries' list who have reconstructed houses before placement of technical personnel were stressed in the meeting.	6 May 2019	3	3	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	

Summary of events during this period

A general ward coordination meeting was conducted at Ward no. 7, Devichaur, Godawari Municipality. The meeting was attended by Ward Chief of Ward no. 7 and Joint M & E visit team members from DLPIU Building Lalitpur, DLPIU GMAI Lalitpur, HRRP Lalitpur District Coordination Team, Reconstruction technical personnel of Godawari Municipality. The coordination meeting was focused on discussing the reconstruction issues in Devichaur. The process of documentation and public inquiry deed was emphasized during the meeting.	7 May 2019	5	4	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
Update of the housing typology in GD and Flickr	12April-9 May 2019			Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org	
Upload of training database, update in 5W and contact list update.	12April-9 May 2019			Ms. Manisha Rai IM Officer HRRP Kathmandu Valley im.ktm@hrrpnepal.org Contact: 9842062006	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Joint M & E visit to observe reconstruction efforts of beneficiaries in Lalitpur and Bhaktapur districts	10 May- 6 June 2019	HRRP Lalitpur and Bhaktapur district team	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409
Joint M & E visit to observe reconstruction efforts of beneficiaries in Kathmandu district	10 May- 6 June 2019	HRRP Kathmandu district team	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org

News & Updates

- Er. Krishna Lal Piya has been appointed as Chief of DLPIU NRA GMALI Lalitpur.
- Hari Prasad Sharma has been appointed as Chief of DLPIU NRA GMALI Kathmandu.
- The structure of HRRP Kathmandu Valley team has been modified as of May 1, 2019.

Tranche Update

Kathmandu Reconstruction Update as of 22 April 2019

Municipality	Kageshwori Manahara	KMC	Kritipur	Gokarneshwor	Chandragiri	Tokha	Tarakeshwor	Dakshinkali	Nagarjun	Budanilkhantha	Shankharpur
Total HHs Eligible	3677	7561	3227	2939	5906	1749	6174	4087	4447	2694	6102
Total HHs Enrolled	3290	5993	2489	2543	4876	1588	5228	3799	4108	2076	5553
1st Tranche	3290	5993	2489	2543	4761	1588	5228	3799	4108	2076	5553
2nd Tranche	1757	1428	935	1474	1380	680	2004	1531	1489	1008	2695
3rd Tranche	1048	1153	765	1145	1188	540	1632	943	1135	803	1718
Total HH Constructed	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Grievance Registered	N/A	N/A	1275	1962	1291	369	2493	1096	851	547	1665
Grievance Addressed	N/A	N/A	208	1158	695	335	2186	753	545	308	340
RF HH Eligible	75	173	44	20	128	48	107	52	38	11	110
RF HH Enrolled	24	33	16	7	46	26	32	31	5	0	40
RF 1st Tranche	24	33	16	7	46	26	32	31	5	0	40
RF 2nd Tranche	0	0	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Non-Compliance Addressed	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A

Bhaktapur Reconstruction Update as of 12 April 2019


Rural /Municipality	Bhaktapur NP	Changunarayan NP	Madhyapur Thimi NP	Suryabinayak NP
Total HHs Eligible	7622	10937	2333	7416
Total HHs Enrolled	5607	9712	2059	6969
First Tranche	5607	9712	2059	6969
Second Tranche	1617	3086	661	2499
Third Tranche	1431	2841	613	2319
Total HH Constructed	N/A	N/A	N/A	N/A
Grievance Registered	1592	2096	2407	1926
Grievance Addressed	1542	1692	1431	1665
RF HH Eligible	148	212	101	233

RF HH Enrolled	42	88	56	101
RF 1st Tranche	42	88	56	101
RF 2nd Tranche	0	0	0	0
Non-Compliance Registered	N/A	N/A	N/A	N/A
Non-Compliance Addressed	N/A	N/A	N/A	N/A


Lalitpur Reconstruction Update as of 12 April 2019

Rural /Municipality	Lalitpur MPC	Godawari UM	Mahalaxmi UM	Mahankal RM	Bagmati RM	Konjyosom RM
Total HHs Eligible	7373	9597	3662	2271	3370	2154
Total HHs Enrolled	6322	7988	3096	2236	3084	2058
First Tranche	6300	7907	3068	2235	3072	2050
Second Tranche	1228	2517	839	1736	2494	1731
Third Tranche	765	1992	690	985	1695	1301
Total HH Constructed	N/A	N/A	N/A	N/A	N/A	N/A
Grievance Registered	3229	2405	927	549	883	927
Grievance Addressed	2296	1777	822	294	713	514
RF HH Eligible	275	325	90	61	252	372
RF HH Enrolled	123	66	21	52	89	257
RF 1st Tranche	117	66	19	51	85	245
RF 2nd Tranche	0	0	0	0	0	0
Non-Compliance Registered	N/A	N/A	N/A	N/A	N/A	N/A
Non-Compliance Addressed						

Graph of Reconstruction Status in Kathmandu as of 22 April 2019:

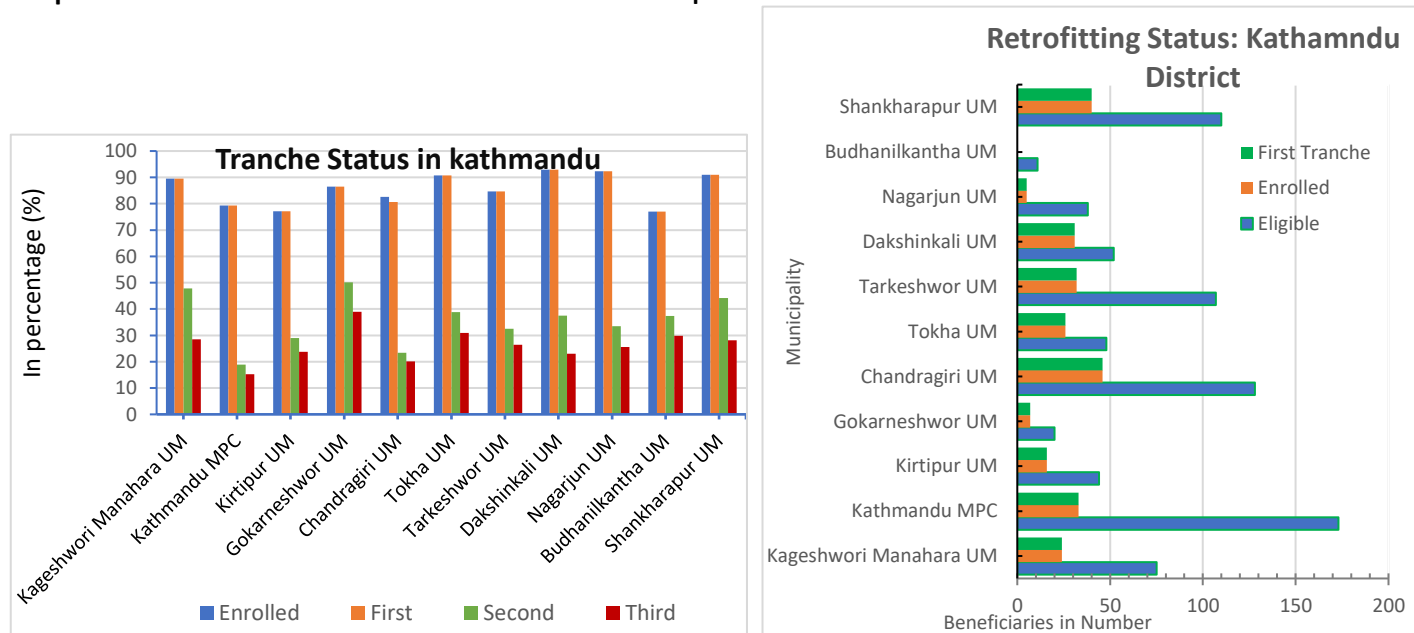


GRIEVANCE STATUS: KATHMANDU DISTRICT

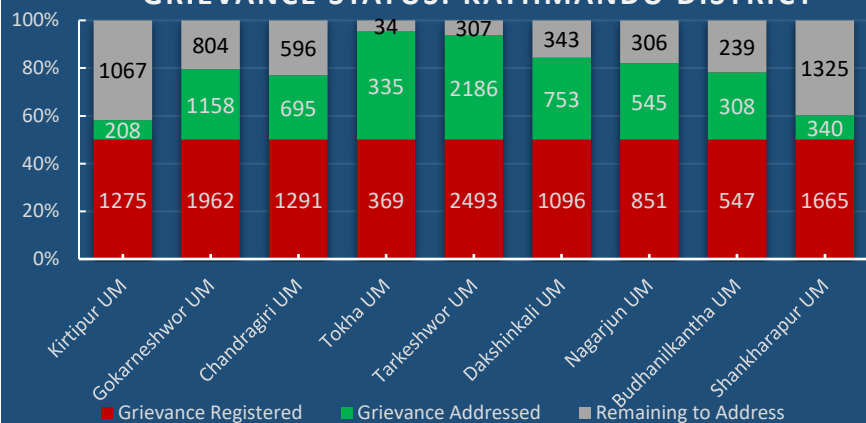


Bhaktapur Reconstruction Update as of 12 April 2019


Tranche Status: Bhaktapur District

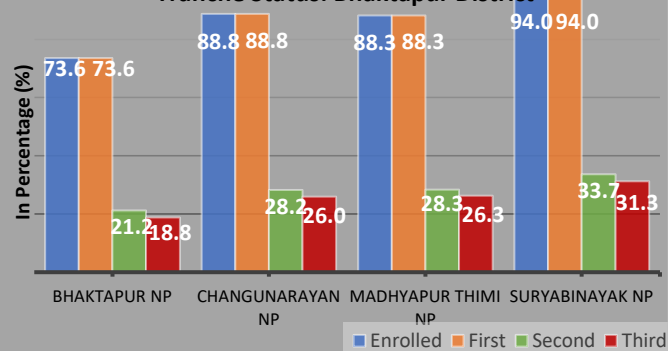

GRIEVANCE STATUS: BHAKTAPUR DISTRICT

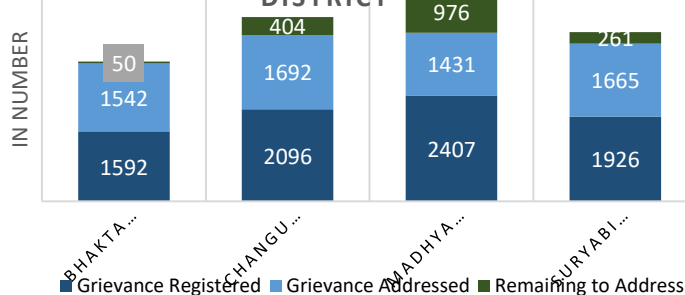


RETROFITTING STATUS: BHAKTAPUR DISTRICT

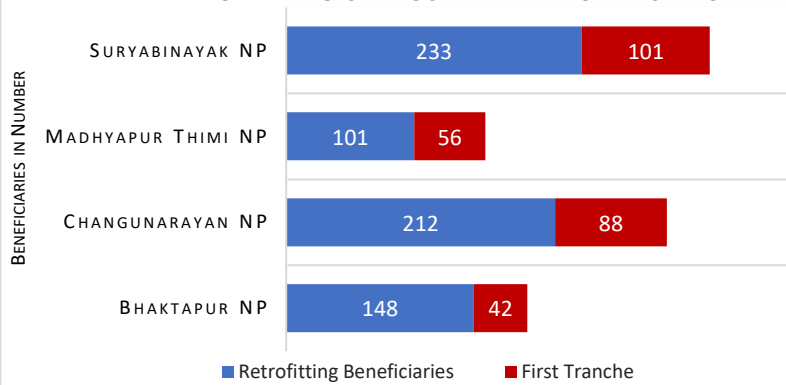


Lalitpur Reconstruction Update as of 12 April 2019


RETROFITTING STATUS: LALITPUR DISTRICT

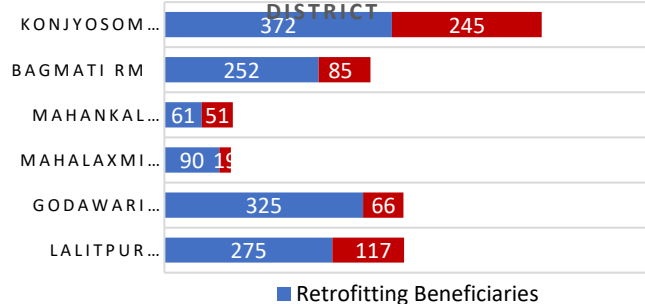

Tranche Status in Lalitpur District

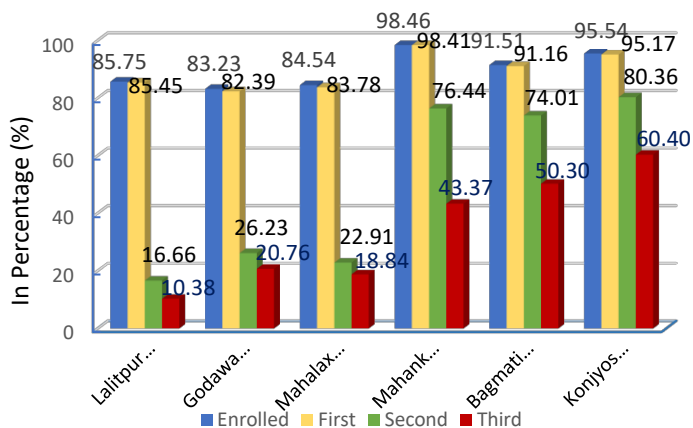

GRIEVANCE STATUS: LALITPUR DISTRICT

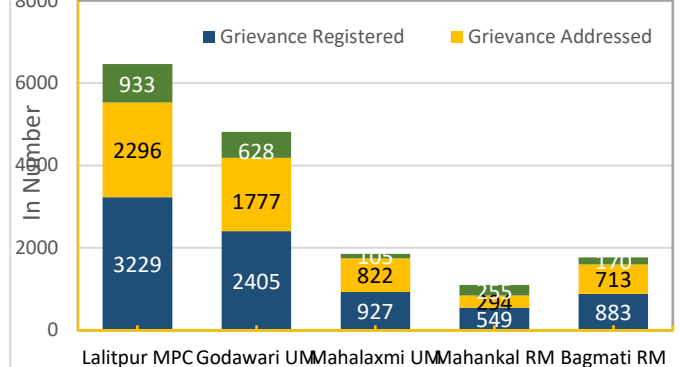

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
16 April 2019	Ward no. 7 Pilachhen and Ward no. 17 Lukhushi, Lalitpur Metropolitan City, Lalitpur district	- Ambika Amatya, HRRP Kathmandu Valley District Team - Jyoti Bastola, Engineer, Lalitpur Metropolitan City
Objective(s)		Objectives - To interact with elected ward officials about shelter reconstruction taking place in Ward no 7. - To conduct 3rd inspection of the houses that have been reconstructed. - To take building typology on KoBo Collect App. - To interact with beneficiaries and provide relevant suggestions further.

Summary	HRRP Kathmandu valley team along DLPIU Engineer from Lalitpur Metropolitan City conducted brief field visit Ward no 7 and 17 of Lalitpur Metropolitan City. The field visit team observed 3 houses in total (2 houses from Ward no. 7 and 1 house from Ward no 17). The observed houses have already received 2 nd tranche and 3 rd tranche has been applied. The houses were found to be complaint.		
	Meeting with Mr. Kul Bahadur Maharjan, Ward Chief, Ward no .7, Pilachhen The total beneficiaries in Ward no 7 is 355, 1s tranche taken by 332, 2 nd tranche taken by 99 and 3 rd tranche by 56 beneficiaries only. 44 beneficiaries have shown interests to go into retrofitting list. The field visit team met Mr. Kul Bahadur Maharjan, Ward Chief, Ward no. 7, Pilachhen Tole, Lalitpur Metropolitan City and conducted ward coordination meeting. Through support from Maya Foundation, Pilachhen Reconstruction Project has managed to reconstruct 84 houses altogether till now. The key reconstruction issues identified were lack of land ownership papers among the multiple beneficiaries who are living on single house with multiple family members. Also, the poor economic condition of beneficiaries is another problem that has delayed the reconstruction. The Ward Chief highlighted the need of revision of NRA's policy to provide grant to beneficiaries, as due to differences in prices of construction materials in various earthquake affected districts have hindered them to stay back from reconstructing their houses. The Ward Chief insisted for need of providing grants on area-wise basis.		
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Majority of beneficiaries have not yet started reconstructing their houses though they have received 1 st tranche from government.	Ward office should play constructive role in motivating beneficiaries to reconstruct houses. Ward-based engineers should be deployed so that beneficiaries can get technical assistance in rebuilding safe houses. If beneficiaries not intending to reconstruct houses, then Ward office should lobby with them to return the 1 st tranche amount.	Ward office, Municipality office, DLPIU Engineers	As soon as possible
There is likely of addition of storeys after beneficiaries receives 3 rd tranche in face of risk towards houses constructed on small parcel land in core areas.	Ward office along with municipality office should conduct appropriate monitoring so that addition of storeys will be reduced. Further, Ward office should inform beneficiaries about risk of adding storeys on houses that are constructed on small land.	Ward office, Municipality office	As soon as possible
Photos			



Beneficiary name: Mrs. Krishna Kumari Maharjan, Lukhushi Ward no 17, Lalitpur Metropolitan City. RCC structure with 5.5 stories has 6 rooms in total. The house is complaint and has received all three tranches from government.



Beneficiary name: Mr. Rajbhai Maharjan, Ward no. 7, Sakho Tole, Pilachhen, Lalitpur Metropolitan City. RCC structure with 4.5 stories and 6 number of rooms. The house is complaint and has received all three tranche from government.

Visit 2

Date	Location	Participants from HRRP and stakeholders
6 May 2019	Ward no. 9, Champi, Godawari Municipality, Lalitpur district	- Roshan Raj Giri, M & E Consultant, NRA CLPIU Building - Yamnath Giri, M & E Specialist, EHRP/DLPIU GMaLI Lalitpur - Ambika Amatya, District Coordinator, HRRP Lalitpur and Bhaktapur District Team - Bidya Baral, Engineer, DLPIU Building Lalitpur - Sabita Dangol, Engineer, Godawari Municipality
Objective(s)	- To interact with elected ward officials about shelter reconstruction taking place in Champi areas. - To observe the reconstruction status of the houses. - To interact with beneficiaries and provide relevant suggestions further. - To take building typology on KoBo Collect App.	

Summary

HRRP Lalitpur District Coordination Team along with M & E Consultant (DLPIU Building Kathmandu and Lalitpur), M & E Specialist (EHRP/DLPIU GMALI Lalitpur), DLPIU Engineer and technical personnel from Godawari Municipality conducted field visit Ward no 9, Champi of Godawari Municipality. The field visit team observed 6 houses in total. One house were undergoing correction phase, while other 3 houses were in non-complaint category.

Meeting with Mr. Atmaram Thapa Chhetri, Ward Chief, Ward no. 9, Champi, Godawari Municipality

The total beneficiaries at Ward no. 9 is 916, enrolled in PA is 818, 1st tranche received- 814, 2nd tranche received- 237 and 3rd tranche received- 145. Majority of housing typology in practice at areas of Champi includes RCC and load bearing with BMC.

It was revealed that majority of beneficiaries are perplexed about whether to return 1st tranche and to rebuild house as well as they have yet not reconstructed their houses. Majority of beneficiaries intends to rebuild RC houses, but the tranche amount provided by government were found to be insufficient to reconstruct such housing typology.

M & E Consultant stressed and requested Ward Chief for preparation of list of beneficiaries who have reconstructed house before the endorsement of NRA's guidelines and before placement of engineers. Further, Ward Chief was informed that such houses can be inspected again by engineers and correction methods can be applied to bring such houses into mainstream of reconstruction and grant process.

Nominal number of landless beneficiaries have been identified in Ward no. 9. Ward Chief were requested to prepare and submit list of landless beneficiaries to DLPIU GMALI Lalitpur office so that further processes of rebuilding houses for them can be coordinated and facilitated.

Challenges / Issues Identified

Beneficiaries are not much aware of reconstructing safe and sound houses by following design catalogues

Action Required

Ward based engineer should be deployed so that technical assistance and support can be provided to beneficiaries in selecting housing typologies from design catalogues.

Responsible

Ward office, Municipality office, DLPIU Engineers, CLPIU

Timeframe

As soon as possible

Photos



Beneficiary name: Mr. Rajan Baniya, Ward no. 9, Etaeti Tole, Champi, Godawari Municipality. 1 storey, 4 roomed load bearing BMC house is currently going through correction phase whereby keeping sil, lintel and corner stitch bands. Previously, beneficiary had only 2 rooms constructed during time of earthquake. After agreement done with government, 2 rooms were added by the beneficiary. The house was considered non-compliant during inspection therefore in suggestion from engineers correction of the house is in process from past 1.5 months. Upto now Rs 10 lakh has been spend including correction process too. Beneficiary is expected to spend upto 12 lakh with all the remaining works. Water shortage is a huge problem in this area. A small natural well (kuwa) is 20 minutes far, the water flow of which is very low from the tap. Nearly 6 hours is spend daily (morning and evening) to collect sufficient amount of water necessary for reconstruction purpose and for household purpose too. Beneficiary claims that reconstruction of his house has delayed due to shortage of water.

Beneficiary name: Mr. Krishna Kumar Bista, Ward no. 9, Champi, Godawari Municipality. 1 storey 4 roomed wall system house is made of interlocking bricks. The house has 23 feet length and 20 feet breadth with floor to floor height is 9 feet. Nearly 7 months was utilized to reconstruct this house. Further, around Rs 1500000 amount was spend by the beneficiary to reconstruct the house. The beneficiary has received upto 2nd tranche, however the house has been declared non-compliant. M & E Consultant insisted for some further discussion about this type of houses which could result in suggestion of applying correction methods for this house.

Visit 3

Date	Location	Participants from HRRP and stakeholders
7 May 2019	Ward no. 7, Devichaur, Godawari Municipality, Lalitpur district	- Roshan Raj Giri, M & E Consultant, NRA CLPIU Building - Yamnath Giri, M & E Specialist, EHRP/DLPIU GMAI Lalitpur - Monika Bajimaya, DMT IM Coordinator, HRRP - Ambika Amatya, District Coordinator, HRRP Lalitpur and Bhaktapur District Team - Bidya Baral, Engineer, DLPIU Building Lalitpur - Jeena Shrestha, Engineer, Godawari Municipality - Dinesh Prasad Joshi, Sub Engineer, Godawari Municipality - Tulasi Prasad Timilsina, Ward Member, Ward no. 7, Devichaur, Godawari Municipality

Objective(s)

- To interact with elected ward officials about shelter reconstruction taking place in Devichaur areas.
- To observe the reconstruction status of the houses.
- To interact with beneficiaries and provide relevant suggestions further
- To take building typology on KoBo Collect App.

Summary

A Joint M & E visit was conducted by HRRP Lalitpur District Coordination Team along with M & E Consultant (DLPIU Lalitpur and Kathmandu), M & E Specialist, EHRP/DLPIU GMAI Lalitpur, DLPIU Engineer, technical personnel from Godawari Municipality and Ward member of Ward no. 7, Devichaur, Godawari Municipality. The field visit team observed 8 houses in total. The dominated housing typology in various parts of Devichaur includes mainly of load bearing stone masonry and mud mortar (SMM) with rigid roof. Some of the beneficiaries have reconstructed RCC and BMC structures too. In SMM houses, beneficiaries have kept vertical and horizontal bands and raised upto .5 attic. Many of the observed houses have received 2nd tranche and were found complaint during the visit. M & E consultant suggested to apply addition of RC roof bands to some beneficiaries so that house remains safe and become eligible for 3rd tranche.

Meeting with Mr. Giri Prasad Timilsina, Ward Chief, Ward no. 7, Devichaur

The total beneficiaries in Ward no. 7 is 632, 1st tranche were received by nearly 550 beneficiaries, 2nd tranche by 160 and 3rd tranche by around 90. The ward coordination meeting was focused on the vast differences in beneficiaries taking 2nd and 3rd tranche.

	Handful of people in Devichaur areas who are residing on Aelani land (government owned public land) since many years have been declared as beneficiaries but they havenot been enrolled in PA due to disputes in land ownership cases. Ward Chief were informed that through documentation and public inquiry deed process, couple of land issues cases can be solved. Ward Chief was emphasized about to avoid conducting documentation process on houses that falls in Right of Way. The coordination meeting come up with a plan of deploying one engineer in Ward office of Devichaur twice a week so that technical assistance and support to beneficiaries will be ensured in rebuilding safe houses.
--	---

Challenges / Issues Identified	Action Required	Responsible	Timeframe
The land ownership issues of beneficiaries residing on aelani land have been not solved yet.	NRA have issued relevant guidelines and processes to solve various kinds of land issues of earthquake affected beneficiaries. Ward office should actively take such land issues and solve accordingly. Process of documentation and public inquiry added can be applied in such relevant cases.	Ward office, Municipality office, DLPIU Engineers	As soon as possible

Photos



Beneficiary name: Mr. Ram Kumar Syangtan, Ward no. 7, Ghoda Kudne Chaur, Devichaur, Godawari Municipality. 1 storey with attic load bearing SMM house have received upto 2nd tranche. Nearly 3 months was utilized to reconstruct this house and the owner has spent upto Rs 5 lakh amount for entire reconstruction. The house was considered complaint by the Joint M & E visit.



Beneficiary name: Mr. Sujan Thing, Ward no. 7, Ghoda Kudne Chaur, Devichaur, Godawari Municipality. 2 roomed, 1 storey with attic load bearing SMM house has 28 feet length and 15 feet breadth. The owner has received upto 2nd tranche. Nearly 3 months was utilized to reconstruct this house. The owner has taken Rs 2 lakh loan in 14% annual interest rate, from cooperative. The house was considered complaint by the Joint M & E visit.



Beneficiary name: Mr. Prem Bahadur Thing, Ward no. 7, Deurali, Devichaur, Godawari Municipality. 2 roomed 1 storey with attic load bearing SMM house has 30 feet length and 15 feet breadth. The owner has received upto 2nd tranche. The owner taken Rs 2 lakh loan in 14% annual interest rate, from cooperative. The house was considered complaint by the Joint M & E visit.



Beneficiary name: Mr. Indra Bahadur Syangtan, Ward no. 7, Deurali, Devichaur, Godawari Municipality. 2 roomed 1 storey with attic load bearing SMM house is under reconstruction phase from past 4 months. The owner has received 2nd tranche till now. Beneficiary cited the reason of wood shortage problem in reconstruction of the house. Currently, the beneficiary has accessed wood from the group cooperative. Further, beneficiary also revealed that water scarcity has also delayed in reconstruction the house. The owner currently resides in temporary shelter nearby.

Housing Typology Report



Beneficiary name: Tek Bahadur Ale Magar, Puwar Gaun, Ward no 10, Suryabinayak Municipality, BMC with 4 columns at back side- front view.



Beneficiary name: Parsi Shrestha, ward no 8, Gokarneshwor Municipality, the beneficiary has claimed to have retrofitted the house but adding RC frame to the load bearing brick in cement masonry.



Beneficiary name: Sunita Shrestha and Ganesh Bahadur Shrestha, Ward no. 8, Gokarneshwor Municipality. Beneficiary has added I-beam in the house only in the ground floor.



Beneficiary name: Santa Lama, ward no 8, Gokarneshwor Municipality. Retrofitting beneficiary, has done column jacketing of only the damaged pillar

Challenges and Way Forward

Challenge	Way Forward
Most of the structure constructed immediately after the earthquake and without the technical assistance are increasing the non-compliance cases.	Such houses must be suggested to apply the correction measures. For the houses which are not addressed by the correction measures, number of such houses must be collected, and NRA should make a policy to address such cases.
