

Monthly District Report

Kathmandu

22 October – 21 November 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Kathmandu	Field visit to Kathmandu Metropolitan City along with the Retrofitting task force and technical staffs, DLPIU building and HRRP was conducted to monitor the retrofitted houses.	11 Nov 2019	Kageshwori Manohara	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org	Field Visit Section
	Ward level General Coordination meeting.	11 Nov 2019	Ward no. 2, Kageshwori Manohara		Minute
	Follow up with the municipal and ward office regarding the NRA tranche deadlines, collection of the issue and gap reduction in the ongoing reconstruction work.	22 Oct – 21 Nov 2019			
	Update of the contact list, calendar, District activities in HRRP website, update of contact list	22 Oct – 21 Nov 2019			
	Update of the Palika Profile of all Municipalities/Metropolitan City of Kathmandu District.	22 Oct – 21 Nov 2019			
	Submission of Meal Data	5 Nov 2019			
	Update of 5W of Kathmandu district	22 Oct – 21 Nov 2019			

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Collection of the details of beneficiaries under the following categories - Non-enrolled beneficiaries - Beneficiaries who have not applied for the 2nd tranche within Kartik end - Vulnerable beneficiaries - Beneficiaries wanting to change from retrofitting to full construction and vice- versa.	Nov/Dec 2019	GMaLI- Kathmandu	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
Hiring of the Social mobilizer and Trained Masons in Kathmandu district.	Nov/Dec 2019		Meli Shah Focal person, DLPIU-Building, Kathmandu Contact no: 9841737073
Collection of the detail of heritage/culturally important areas, vulnerable areas, area under government development plan such as smart city.	Nov/Dec 2019	GMaLI- Kathmandu	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
Joint Monitoring visit to different Municipalities of Kathmandu district along with DLPIU- Building Kathmandu, retrofitting task force and HRRP to monitor the ongoing retrofitting works.	Nov/Dec 2019	DLPIU Building, Kathmandu and HRRP	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
District Facilitation meeting of the Kathmandu Valley	TBD (Mangshir 2076)	GMaLI- Kathmandu	
PA Collection and digitization of the beneficiaries of Kathmandu District	Sept/Oct 2019	GMaLI- Kathmandu	Anupa Basnet Finance Specialist DLPIU GMaLI Contact no: 9860468266
Updating of the Municipality profile every month.	Nov/Dec 2019	HRRP Kathmandu	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org

News & Updates


- With the given deadline of Kartik end (November 16, 2019) NRA has stopped the release of the second tranche for the reconstruction beneficiary. The deadline is not applicable for the beneficiaries under retrofitting.
- Retrofitting task force of Kathmandu District has been formed under the coordination of the District Support Engineer. The retrofitting task force consist of the engineers from DLPIU building and engineers deployed at each municipality of district. Currently, the verification of the beneficiaries under the retrofitting is being carried out in Kathmandu district.
- DLPIU-GMaLI has requested all the municipality to send the details of the beneficiaries who have not received 2nd tranche within the NRA deadline of Kartik end.
- DLPIU- GMaLI Kathmandu has coordinated with all the municipalities and metropolitan city to convey the NRA notice to ward offices and beneficiaries.
- DLPIU- Building/GMaLI Kathmandu has requested all the municipalities of Kathmandu district to send the details of the non-enrolled beneficiaries, list of vulnerable beneficiaries and the status of the beneficiaries who have not begun reconstruction even after getting the first tranche and the houses constructed before the deployment of the technical staff within Bhadra 2076. The list will be sent to NRA for further action.
- DLPIU-Building has finished collected the information of the houses constructed before the deployment of the technical staffs. Such houses need to be verified by the NRA technical staffs of respective municipalities and approved by the ward chief to be eligible for the reconstruction grant as per the NRA provision of such houses.
- Regarding the process of hiring of the social mobilizers and lead mason, DLPIU- Building has completed the interview process. The result will be announced soon.

Tranche Status (Kathmandu)


Tranche Status Table:

Name of Municipality	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Budhanilakantha Municipality	2740	2694	2084	2084	1120	950	15	1	1	0
Chandragiri Municipality	6414	5906	4837	4837	1778	1468	142	74	74	0
Dakshinkali Municipality	3542	4087	3900	3900	1736	1385	53	33	33	0
Gokarneshwor Municipality	2870	2939	2603	2603	1623	1418	24	8	8	0
Kageshwori Manohara Municipality	3741	3678	3283	3283	1881	1375	76	34	34	0
Kathmandu Metropolitan City	8738	7561	5994	5994	1615	1370	204	39	39	2
Kirtipur Municipality	3758	3231	2555	2555	1046	891	64	20	20	0
Nagarjun Municipality	4315	4447	4184	4184	1624	1412	94	5	5	0
Shankharapur Municipality	6032	6102	5574	5574	3156	2528	71	42	42	0
Tarakeshwor Municipality	6737	6174	5352	5352	2311	2064	111	36	36	1
Tokha Municipality	2237	1749	1561	1561	760	640	53	26	26	0

Graph of Tranche Status:

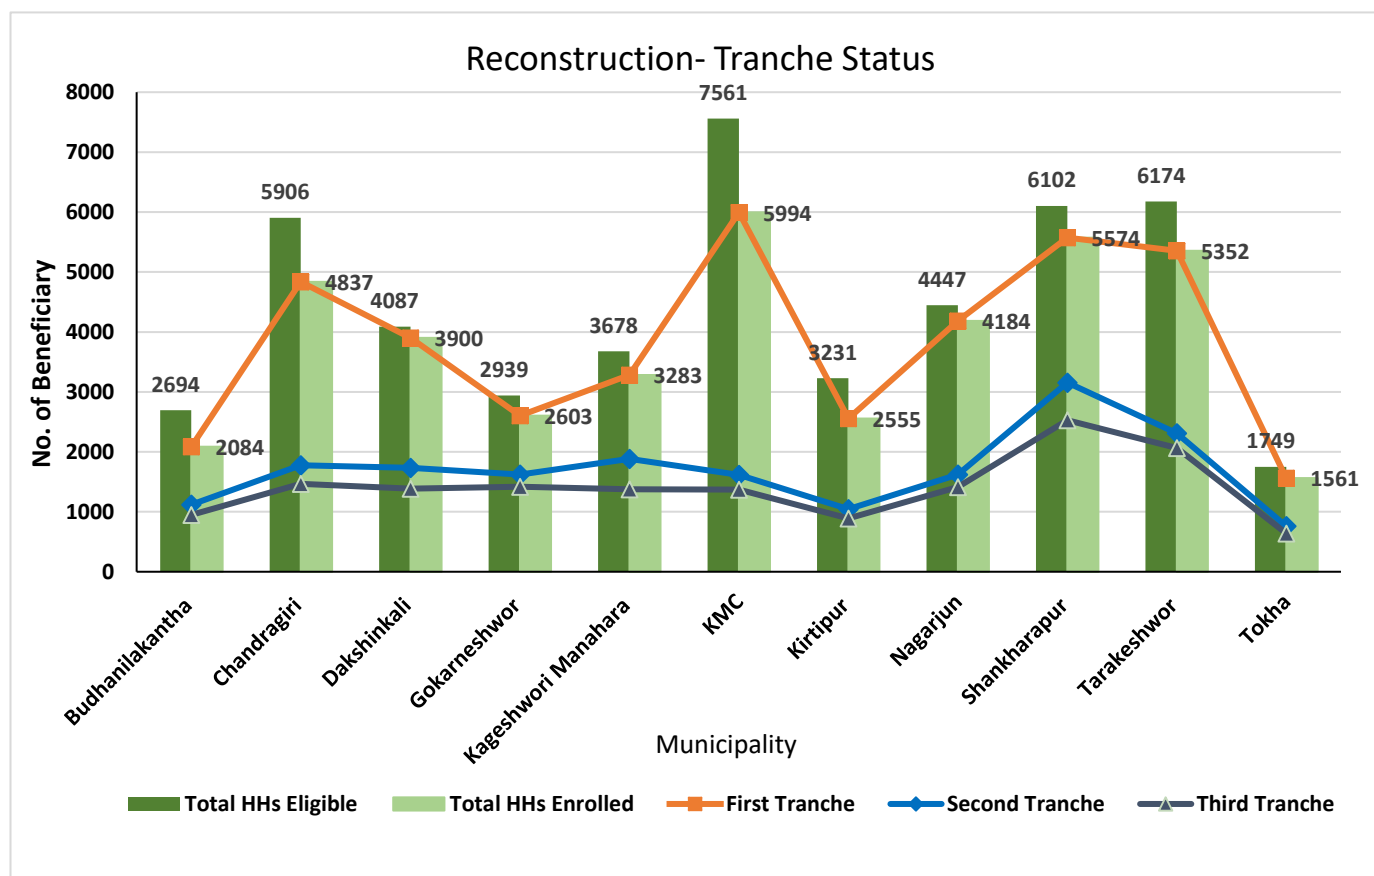

Graph for Retrofitting Status:

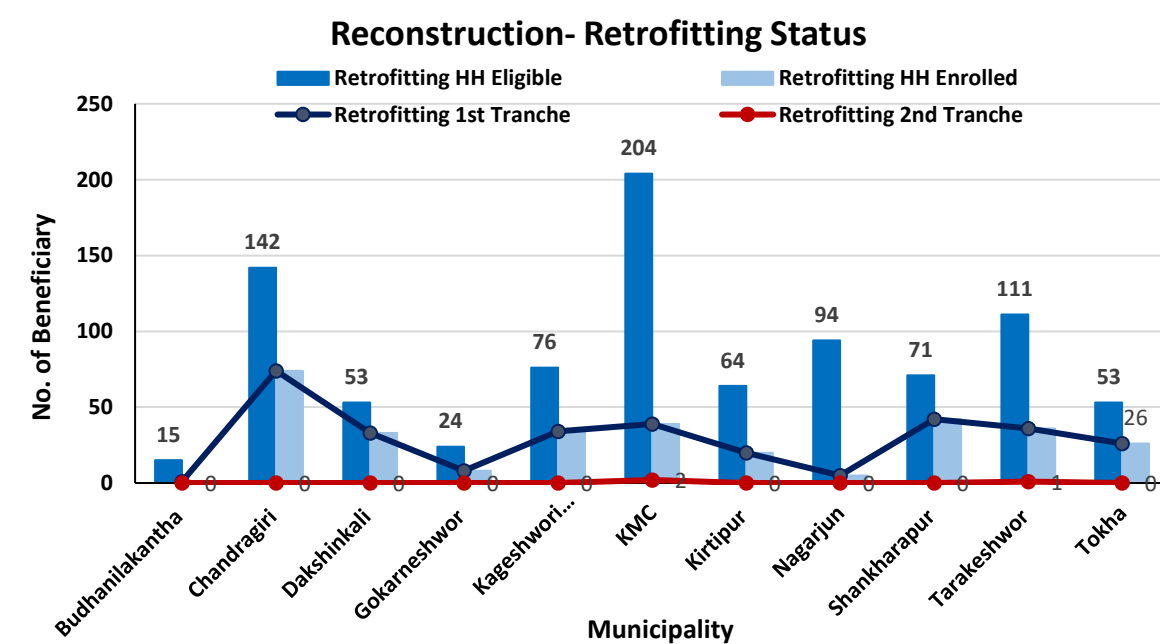

Field Visit Reports (Kathmandu)

Visit 1

Date	Location	Participants		
11 November 2019	Ward no 2 and 3, Kageshwori Manohara Municipality	• Bidhya Manandhar (DSE) • Shankhar Pokhrel (DSE) • Shiva Ram Basnet, ward secretary, Aalapot, ward no 2, Kageshwori Manohara Municipality • Sun Kumar Nagarkoti, ward secretary, Bhadrabas, ward no 3, Kageshwori Manohara Municipality • Sanam Lakhey, Ankita Shrestha (DLPIU-Kathmandu) • DLPIU Engineers- Kageshwori Manohara (Anil Paudel, Rupak Ghimire) • Sangib Shrestha (Baliyo Ghar, NSET) • Sweata Sijapati, HRRP, Kathmandu		
Objective(s)	• To observe the houses listed as non-compliance in ward no 2 and 3 and suggest the corrective measures to the beneficiaries. • To observe the retrofitted status in the area. • To interact with beneficiaries to understand the reconstruction/retrofitting issues and status.			
Why was the visit carried out in this location? Priority wise, Write any other reason				
The field visit was targeted to monitor the non-compliance and retrofitting cases in ward no 2 and 3 of Kageshwori Manohara Municipality. The area was selected as it being only site in Kathmandu district where PO (NSET) has been providing technical assistance and carrying details study of the houses listed under retrofitting.				
Summary				
Field Visit: A team of DSEs and Engineers (DLPIU Building), technical staffs of Kageshwori Manohara Municipality and Baliyo Ghar- NSET and HRRP Kathmandu visited ward no 2 and 3 of Kageshwori Manohara Municipality. The visit began with the brief meeting at ward office of ward no 2 for finding the challenges and issues prevalent in the ward as well as the municipality (Meeting Minute). The field visit was mainly focused on the observation of the non-compliance houses and houses listed under retrofitting. In total 22 houses were visited. The houses observed were mostly load bearing structures using bricks and alternative materials such as hollow blocks, cement blocks and CSEB. Most of the houses were found non-compliance due to missing bands, missing beam in RC slab roof, missing vertical reinforcements. DSEs suggested correction measure such as addition of splint and bandage, bands, vertical reinforcement for such non-complaint structures.				
Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)

Beneficiary had not signed the retrofitting agreement as they want to first save sufficient amount before beginning the retrofitting process.	The beneficiary was suggested to at least sign the agreement as the deadlines for completing the reconstruction and retrofitting.	The beneficiary agreed to sign the partnership agreement and consult the technical staff of NRA and NSET to find the economical feasible technology.	Beneficiary, Technical staffs, PO	
---	---	--	-----------------------------------	--

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)

Regarding the beneficiaries under retrofitting, among the total 11 beneficiaries of ward no 2 and 3 none has signed the tranche agreement. The beneficiaries are willing to retrofit their houses but due to the weak financial condition, none of the them are able to move on with the process. Hence, even though being listed under retrofitting they has not signed the agreement for the government grant as they are afraid that the tranche amount would be used for other purpose rather than retrofitting and if condition of returning the tranche amount arises, they would not be able to manage it. The beneficiary was suggested to sign the agreement if they really wish to retrofit the house and asked to consult with the NRA technical staffs and NSET technical staffs for cheaper and appropriate retrofitting technology for the house. National Society for Earthquake Technology – NSET Nepal has been providing technical assistance in the ward no 1 and 2 of Kageshwori Manohara Municipality.

Photos



The monitoring team suggesting correction measures to the beneficiary in ward no 2 of Kageshwori Manohara Municipality. The house was found to be non-compliance due to the missing of horizontal bands. To be eligible for the remaining grant beneficiary was suggest to add the band both either inside or outside of the house.



Mrs. Apsara Khadka along with her daughter in her newly constructed hybrid structure. The house had CGI covering in some section so the DSE suggested to change the CGI to wooden board and similar material to be eligible for the 2nd and 3rd tranche. The beneficiary has recently applied for the building permit at the municipality.

Housing Typology Report



Beneficiary name: Chandra Kumari Khadka, Aalapot ward no 2, Kageshwori Manohara Municipality. one storey CSEB structure. The beneficiary has constructed the house as per the government criteria and was found to be safe during the field visit. The file of the beneficiary has been forwarded for the 2nd and 3rd tranche.



Beneficiary name: Sadhu Ram Khadka, Aalapot ward no 2, Kageshwori Manohara Municipality. One storey BMC structure with RC slab. The house was found to be non-complaint due to missing bands and beam in the house. The beneficiary has requested for the 3rd tranche. DSE has suggested the beneficiary to add the band or provide splint and bandage to be eligible for the tranche but the beneficiary has no interest in doing so. Currently his file is on hold at the municipality.



Beneficiary name: Rajan Khadka, Aalapot ward no 2, Kageshwori Manohara Municipality. one storey BMC structure with RC slab. The house was found to be non-complaint due to missing bands and beam in the house. The beneficiary has requested for the 3rd tranche. DSE has suggested the beneficiary to add the bands to be eligible for the tranche .



Beneficiary name: Dil Bahadur Shrestha, Aalapot ward no 2, Kageshwori Manohara Municipality. one roomed BMC structure with CGI roofing. The beneficiary has constructed the house as per the government criteria and was found to be safe during the field visit. The file of the beneficiary has been forwarded for the 2nd and 3rd tranche.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
There are beneficiaries who are requesting for the second tranche even after the deadline of 2076 Kartik end set by NRA. What can be done in such case?	Engineers	Regarding such cases, NRA has closed the second tranche release process. All the ward offices and municipalities are requested to send the detail of the beneficiary who have not received the second tranche to GMaLI- Kathmandu as soon as possible. The official letter regarding this has been send to respective municipalities.(GMaLI- Project Manager)
There are beneficiaries who are willing to sign the partnership agreement for the reconstruction tranche even after the deadline of Asar 21, 2076 set by NRA. What can be done in such case?	Municipal Engineers Representatives/	Regarding such cases, NRA has opened the tranche agree for certain criteria such as vulnerable group, beneficiary residing in public or government land and so on. If there are such records, all the ward offices and municipality are requested to send the detail of the beneficiary along with the reason for the delay in signing the agreement to GMaLI- Kathmandu as soon as possible. (GMaLI- Project Manager).
My house was constructed before the mobilization of the technical team from the NRA. Will I be getting the government tranche?	Beneficiary	DLPIU- building has collected the data of the HHs that are constructed before the engineers were mobilized. The data has already been sent to NRA. If your name is in the list and is approved by NRA, then you will be receiving the full government reconstruction grant. (HRRP- Kathmandu)
My house is listed under retrofitting but due to lack of money I have not been able to begin the retrofitting work. Will I be able to get the tranche even after the Kartik end deadline?	Beneficiary	The Kartik end deadline is valid only for the reconstruction beneficiary who have received the first tranche. The deadline for the second tranche for retrofitting is still not set but NRA has set deadline of 2077 Asar end for the completion of both reconstruction and retrofitting. So, it would be better if you start the retrofitting work as soon as possible. (HRRP- Kathmandu)

Challenges and Way Forward

Challenge	Way Forward
As per the NRA deadline for the second tranche was 2076 Kartik end but there are beneficiaries who are still coming to apply for the second tranche.	Regarding this, the list of such beneficiaries needs to be collected along with the reason for the delay in the tranche request. Ward office should be responsible for collecting this detail and send the list to GMaLI- Kathmandu.

Challenges and Way Forward

Challenge	Way Forward
Majority of beneficiaries have not signed or started the retrofitting of the damaged houses. In Kathmandu only about 30% of the beneficiary has signed the retrofitting work.	DSE and the NRA technical staffs at municipality must seriously look after this issue. With the formation of the Retrofitting task force, the verification of the HHs under retrofitting must be done on individual level. Also, a community orientation program must be conducted at ward/municipal level for ensuring the beneficiaries that the retrofitting can increase the strength of the house and will be safer to live in.
The beneficiary who were under the Resurvey and Reverification are still waiting for the NRA's result. This is delaying the reconstruction/retrofitting process in Kathmandu District.	The result of the resurvey and reverification conducted with the lead of DLPIU-building are published in batch system after the decision made by the NRA executive committee. The process of publishing the result must be done faster as it might affect the approaching NRA deadline for the completion of the reconstruction/retrofitting within 2077 Asar end.

Case Study



Front view of the damaged house



Isometric side view of the damaged house

Mr. Prem Nagarkoti of Aalapot Ward no 1, Kageshwori Manohara Municipality has been listed under the retrofitting beneficiary after his house was partially damaged by the 2015 Gorkha earthquake. The house single woman headed with two children, one daughter and one son (listed under beneficiary). Two storey with attic load bearing Brick (Adobe) in mud mortar was constructed in 2059 B.S. Standard bricks were used in the front section whereas adobe with mud mortar was used in the remaining section of the walls. The house doesn't have any earthquake resistant elements and the cracks due to the earthquake were repaired with the mud plaster. The house owner is positive about retrofitting, but as a single woman headed household the family is not able to afford the materials costs and other expenses for retrofitting. Hence, even though being listed under retrofitting they has not signed the agreement for the government grant as they are afraid that the tranche amount would be used for other purpose rather than retrofitting and if condition of returning the tranche amount arises, they would not be able to manage it. The beneficiary was suggested to sign the agreement if they really wish to retrofit the house and asked to consult with the NRA technical staffs and NSET technical staffs for cheaper and appropriate retrofitting technology for the house. National Society for Earthquake Technology – NSET Nepal has been providing technical assistance in the ward no 1 and 2 of Kageshwori Manohara Municipality.
