

Monthly District Report

Kavrepalanchok

27 September – 21 October 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Kavrepalanchok	Support to GMALI on tranche cheque preparations	1-4 Oct	-	reshma@hrrpnepal.org	NA
	MEAL Reporting	2 Oct	-	reshma@hrrpnepal.org	GD
	Palika Profile Data Update	11 Oct	-	im.kavrepalanchok@hrrpnepal.org	GD
	Contact List Update	11 Oct	-	im.kavrepalanchok@hrrpnepal.org	GD
	Two weeks workplan preparation	16 Oct	-	reshma@hrrpnepal.org	GD
	Visit to SJASK's office (To verify and reconcile the data between SJASKs material distribution support and NRA MIS. As the details on PA number were missing, all the hard copies of the beneficiaries supported were assessed to address the 99 duplications in NRA MIS)	17 Oct	SJASK Office, Dhulikhel	reshma@hrrpnepal.org	NA
	Informal meeting with Building/DLPIU to discuss on plans of retrofit task force (Recruitment of social mobilizers and head mason is on process. Once they are recruited, every required detail regarding retrofit will be collected through them. Before the mobilization, proper orientation will be provided for which HRRP Kavre too will provide orientation and orientation material support. Currently the task force is dedicated to collection of beneficiaries' details who are interested to retrofit.)	18 Oct	Building/DLPIU, Dhulikhel	reshma@hrrpnepal.org	NA
	IM Support to national HRRP	16-18 Oct	NRA	im.kavrepalanchok@hrrpnepal.org	NA
	Coordination with Banepa Municipality and Building/DLPIU to participate in Urban Housing Reconstruction Session	16 Oct	-	reshma@hrrpnepal.org	NA
	Field visit to Mandandeupur Municipality (To collect urban issues, status of disaster management committee, progress of reconstruction and share infographics at municipality office To visit Teendhara at ChandeniMandan to observe CSEB block preparation for integrated settlement To observe the houses constructed through German Green Helmets support)	21 Oct	Mandandeupur Municipality Office Mahadevsthan, ChandeniMandan	reshma@hrrpnepal.org	Field visit section below

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
	Ward level meeting at ChandeniMandan, Mandandeupur-10	21 Oct	Ward Office	reshma@hrrpnepal.org	Meeting Minutes
	Follow-ups for Palika Profile Website Upload	1-21 Oct	NA	im.kavrepalanchok@hrrpnepal.org	Links
	Grievance Handling Support at GMALI	23 Aug-26 Sept	NA	reshma@hrrpnepal.org	NA

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Field visit to Model Retrofit house at Banepa	5 November, 10:00AM-2PM, Banepa	HRRP Kavre	reshma@hrrpnepal.org
Field visit to MahankalChaur, Bethanchok-5	6-7 November, 9:00AM-5:00PM, Bethanchok, Kavre	HRRP Kavre	reshma@hrrpnepal.org

Tranche Status (Kavrepalanchok)


Table of Tranche Status: As of 21st October 2019

Municipality	Reconstruction				Retrofit			Grievances	
	Eligible HHs	1st Tranche	2nd Tranche	3rd Tranche	Eligible HHs	1st Tranche	2nd Tranche	Registered	Addressed
Banepa NP	7,132	6,336	3,667	3,132	280	77	0	2226	2031
Bethanchowk GP	4,377	3,687	3,075	2,292	553	78	0	1202	1202
Bhumlu GP	6,210	5,850	5,259	4,619	79	17	0	1038	971
Chaurideurali GP	6,418	5,596	4,522	3,705	407	46	0	1578	1517
Dhulikhel NP	6,014	5,218	3,312	2,563	380	44	0	2151	1919
Khanikhola GP	2,864	2,565	2,358	1,410	232	43	0	683	681
Mahabharat GP	2,963	2,678	2,517	2,054	226	146	0	1075	1055
Mandandeupur NP	9,238	8,579	7,357	5,916	144	25	0	2300	1762
Namobuddha NP	7,659	6,386	3,909	2,905	700	20	0	2814	2296
Panauli NP	9,255	7,847	5,113	4,189	862	128	0	2874	2851
Panchkhal NP	9,960	9,010	6,892	5,260	339	111	0	3041	2932
Roshi GP	6,436	5,386	4,353	3,266	752	131	0	2257	2203
Temal GP	4,850	4,035	3,327	2,704	578	107	0	2101	2069

Graph of Tranche Status: As of 21st October 2019

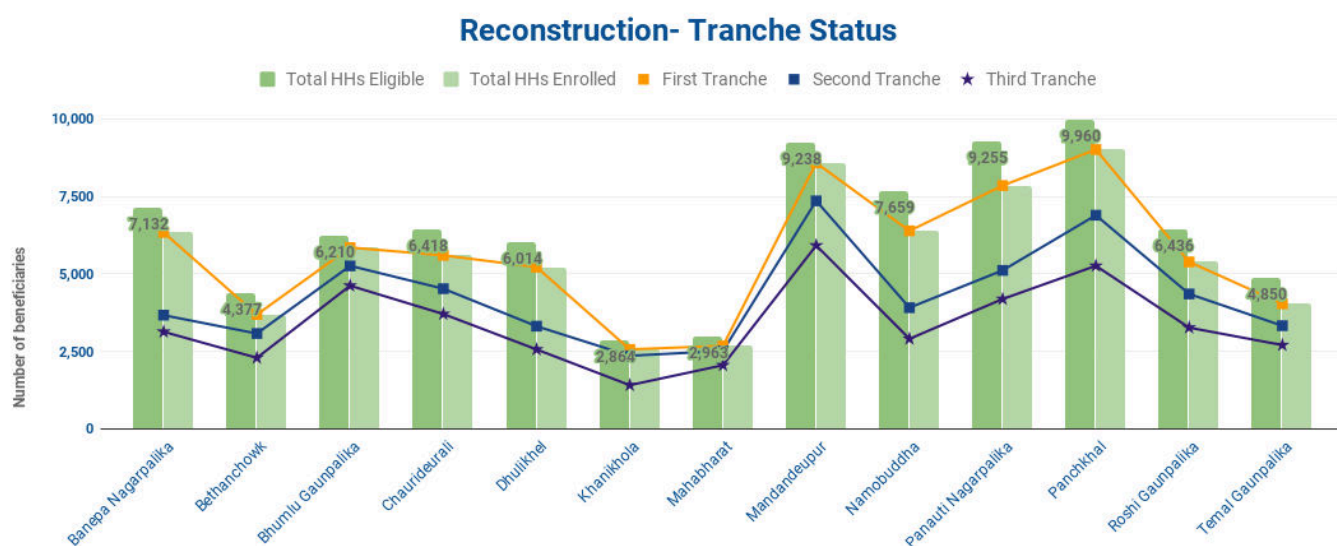

Graph for Retrofitting Status: As of 21st October 2019

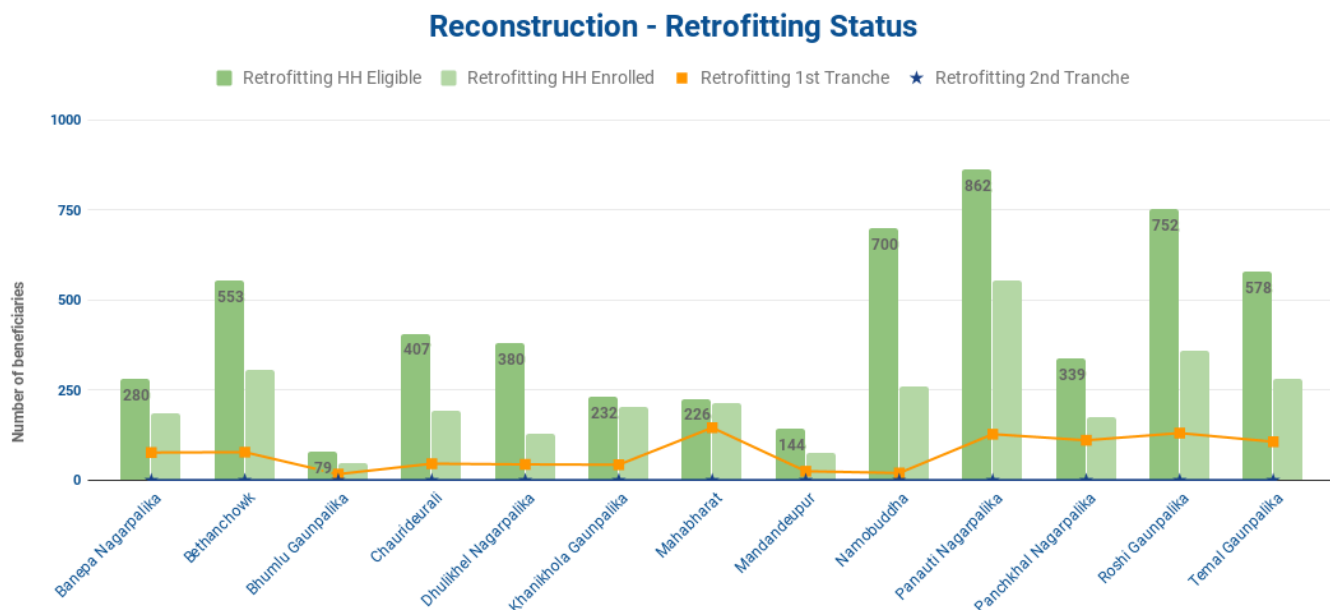

Field Visit Report (Kavrepalanchok)

Visit 1

Date	Location	Participants
21 October 2019	Mandandeupur Municipality Ward 7,8,9,10	Reshma Shrestha, HRRP Ishor Neupane, HRRP
Objective(s)	- To collect urban issues, status of disaster management committee, progress of reconstruction and share infographics at municipality office - To visit Teendhara at ChandeniMandan to observe CSEB block preparation for integrated settlement - To observe the houses constructed through German Green Helmets support - Conduct Ward level meetings - Share infographics - Collect housing typologies	
Why was the visit carried out in this location?		
This visit was conducted to collect details on housing reconstruction issues, building permit system, role of disaster management committees and to observe the activities of Pos in various wards.		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
NA		
Summary	During the meeting with the Chief Administrative Officer of the municipality, he highlighted the major reconstruction issue as retrofitting. Beneficiaries are reluctant to retrofit and most of them have applied for beneficiary change from retrofit to reconstruction but none of them have been changed till date. He also stressed on the need to abide by the current deadlines to complete reconstruction and not to extend the deadlines further whereas for the final grievances collected, they need to be addressed more carefully. The municipality was still unclear about the role of municipality in recommendation for House In Other Places and Landless cases. It is difficult and impossible for municipality and even for the wards to officially recommend those as they have no role in land purchase and sale. The need of strict rules to demolish the damaged pre-earthquake houses too was highlighted at the meeting. The building permit system at the municipality takes a minimum of 2 months and due to the lengthy process, building permits have not been made compulsory for the reconstruction cases though in the initial months of reconstruction, it was made compulsory. There is no any provision of revenue grants for reconstructed houses. A nine-member team of Disaster Management Committee has been formed at the municipality. In the meetings of the committee, all ward members and political leaders are invited without limiting it to the core members. 54 community-based DRM committees have been formed with support from Nepal Red Cross Society and they are more involved in preparedness and emergency response activities. Emergency stockpiling of relief materials have been done at all the wards. The municipality also has prepared DRM Plan and DRM Fund worth NPRs. 10 lakhs. Each ward has DRM Fund with NPRs. 1 lakh budget. Under Environment and DRR section for budget allocation, NPRs. 94 lakhs has been allocated for the current fiscal year. Hygiene promotion, sanitation and river bed mitigation works are being carried out with the budget. The Detailed Project Report for integrated settlement at Teendhara of ChandeniMandan has been prepared and submitted for approval by Habitat for Humanity. The settlement has been planned to include 29 houses, 1 community building and 1 gumba. The committee has acquired land worth 8 anna for each family and after the site development, each HH will possess 4 anna land. HfH has planned a four room CSEB block houses for the DPR and the DPR for CSEB block production has already been approved. 2,000 blocks are estimated for each house and HfH is providing the material and technical support for the block production. One member from each family are now involved in block production and they produce 500-600 blocks daily. German Green Helmets has supported the construction of 52 houses at Mahadevsthan, Mandandeupur-7 but with no approval from NRA. The support for the one storied brick in mud house was estimated around NPRs. 2 lakhs. Beneficiaries had to extend labor support through the perma system. As the support is less compared to the government tranche, the beneficiaries have requested the ward and municipality to coordinate for equal tranche support, the remaining to be covered from the government side.	

Field Visit:

- No. of HHs visited: 8
- No. of meetings with engineers: 0
- No. of meetings with local officials: 2

Meeting: [Meeting Minutes Mandandeupur-10](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Need for retrofit awareness and need to demolish the damaged pre-earthquake houses	Retrofit awareness programs to be carried immediately after Tihar by Building/DLPIU and the municipality to coordinate with wards and NRA to impose rules of demolishing damaged pre-earthquake houses	-	Ward Officials, Municipality, NRA, Building/DLPIU	NA

Photos



One family member from each of the 29 houses to be included in the integrated settlement are participating in the CSEB block preparation. All the HHs agreed to construct using CSEB blocks over bricks. Clay preparation, batching, mixing, moulding, compaction, drying and curing all are being done in parallel. 500-600 blocks are prepared each day and about 6,000 blocks have been prepared till date. All the materials are being supported by Habitat for Humanity and HfH has also submitted the DPR of the settlement for approval.

Photograph By: Reshma Shrestha



Participants moulding and compacting the blocks in the proportion Cement:Sand:Clay:Aggregate as 1:3:2:10. Two different types of block: half and full size are being prepared. In case any HH fails to volunteer for the block preparation, a compensation of NPRs. 1500 per day is issued.

Photograph By: Reshma Shrestha

Housing Typology Report



Address: Kavrepalanchok, Mandandeupur-9

Building Typology: BMC

Description: Dil Bahadur Tamang constructed his house at an approx. of NPRs. 16 lakhs. He relocated to this safer land a bit far from his pre-earthquake house (within the ward) where his land was at risk to landslides. He has received all three tranches of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Mandandeupur-9

Building Typology: BMC

Description: Bhim Bahadur Tamang has received all three tranches of housing reconstruction grant. This house was constructed immediately after earthquake, before the mobilization of NRA technical persons and had greater spans compared to the building standards. As suggested by the technical persons, extra walls were constructed to make the structure compliant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Mandandeupur-8

Building Typology: BMC

Description: Sita Tamang constructed her house with technical and material support from an organization, German Green Helmet. A total of 52 houses have been constructed in the ward by the organization. While the materials worth of NPRs. 1,80,000 was supported by the organization, the labor was contributed by all the HHs on labor exchange basis (Perma system). As the support is lesser compared to the government tranche, the HHs have requested the ward and municipality office to coordinate with NRA to provide equal tranche support.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Mandandeupur-10

Building Typology: Brick in Cement

Description: Tilak Bahadur Kunwar constructed his house in an approx. of NPRs. 23 lakhs and has received all three tranches of housing reconstruction grant.

Photographed By: Reshma Shrestha

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
How long does it take to convert the beneficiary name in case of deaths	Ward Chief, Beneficiary	The beneficiary conversion is done by central NRA and needs to be updated in the central MIS. The time duration is not exact and the variation is 1-3 months. This long duration for conversion has been raised multiple times and GMALI/DLPIU Chief too will be taking the issue to NRA.

Challenges and Way Forward

Challenge	Way Forward
Very low rate of retrofitting	Conduct community awareness programs.
