

Monthly District Report

Kavrepalanchok

12 July - 22 August 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Kavrepalanchok	GMALI/DLPIU Progress Review Meeting	12 July	Hotel Sarathi, Dhulikhel	nrakavre@gmail.com	NA
	Introductory Meeting with GMALI/DLPIU Chief (HRRP Kavre explained its working modality, POs work coverage and the general scenario of the district. The key contact details of the district and monthly report too were shared to GMALI/Chief)	18 July	GMALI/DLPIU Office, Dhulikhel	reshma@hrrpnepal.org	NA
	Introductory Meeting of GMALI/DLPIU with Caritas Nepal and ASF Nepal (The summary of overall project was briefed along with the key challenges faced during project implementation)	19 July	GMALI/DLPIU Office, Dhulikhel	reshma@hrrpnepal.org	NA
	Introductory Meeting of GMALI/DLPIU with UNOPS (The summary of overall project was briefed along with the key challenges faced during project implementation. Field visit to one of the model retrofit sites at Patlekhet was done.)	22 July	GMALI/DLPIU Office, Dhulikhel	reshma@hrrpnepal.org	NA
	Palika Profile Data Update	24 July	NA	im.kavrepalanchok@hrrpnepal.org	GD
	Contact List Update	25 July	NA	im.kavrepalanchok@hrrpnepal.org	GD
	5W Update	25 July	NA	im.kavrepalanchok@hrrpnepal.org	GD
	Meeting with Habitat for Humanity (HfH) and GMALI/DLPIU to	29 July	GMALI/DLPIU Office, Dhulikhel	reshma@hrrpnepal.org	NA

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
	discuss on possible areas and topics of reconstruction for HfH's project extension				
	Palika Level Coordination Meeting, Panchkhal NP	7 August	Panchkhal NP Meeting Hall	reshma@hrrpnepal.org	Meeting Minutes
	MEAL Reporting	8 August	NA	reshma@hrrpnepal.org	GD
	Palika Level Coordination Meeting, Roshi GP	9 August	Roshi GP, Meeting Hall	reshma@hrrpnepal.org	Meeting Minutes
	Palika Level Coordination Meeting, Namobuddha NP	13 August	Namobuddha NP, Meeting Hall	reshma@hrrpnepal.org	Meeting Minutes
	Field Visit to ChalaGanesthan and RyaleBhir for retrofit stories collection	14 August	ChalaGanesthan, Bethanchok-4 RyaleBhir, Panauti-1	reshma@hrrpnepal.org	Field Visit Section Below
	Housing Typology Survey	14 August	ChalaGanesthan, Bethanchok-4 RyaleBhir, Panauti-1	im.kavrepalanchok@hrrpnepal.org	Kobo Link
	Palika Level Coordination Meeting, Bethanchok GP	19 August	Bethanchok GP, Meeting Hall	reshma@hrrpnepal.org	Meeting Minutes
	Support to Urban Working Group	19 August	HRRP	reshma@hrrpnepal.org	NA
	Follow-ups for Palika Profile Website Upload	16-22 August	NA	im.kavrepalanchok@hrrpnepal.org	Links
	Follow up with wards for PA Form collection for the digitization	12 July-22 August	NA	reshma@hrrpnepal.org	NA
	Updating Annex for PA Form digitization	12 July-22 August	NA	reshma@hrrpnepal.org	NA
	Grievance Handling Support at GMALI	12 July-22 August	NA	reshma@hrrpnepal.org	NA

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
District Facilitation Meeting	26 August, 8:00AM-10:00AM, DCC Hall, Kavre	GMALI/DLPIU	nrakavre@gmail.com


Tranche Status (Kavrepalanchok)

Table of Tranche Status: As of 22nd August 2019


Municipality	Reconstruction				Retrofit			Grievances	
	Eligible HHs	1st Tranche	2nd Tranche	3rd Tranche	Eligible HHs	1st Tranche	2nd Tranche	Registered	Addressed
Banepa NP	6856	6,499	3,552	2,899	276	77	0	2226	2031
Bethanchowk GP	3824	3,970	3,005	2,042	553	78	0	1202	1202
Bhumlu GP	6120	5,890	5,184	4,466	89	17	0	1038	971
Chaurideurali GP	5975	5,735	4,465	3,529	442	46	0	1578	1517
Dhulikhel NP	5638	5,308	3,180	2,367	376	44	0	2151	1919
Khanikhola GP	2631	2,766	2,297	1,278	233	43	0	683	681
Mahabharat GP	2738	2,891	2,505	1,965	226	146	0	1075	1055
Mandandeupur NP	9080	8,618	7,208	5,572	157	25	0	2300	1762
Namobuddha NP	6959	6,641	3,822	2,666	700	20	0	2814	2296
Panauli NP	8392	9,137	6,745	4,824	404	111	0	2874	2851
Panchkhal NP	9571	8,303	4,960	3,838	862	128	0	3041	2932
Roshi GP	5669	5,727	4,279	3,023	764	131	0	2257	2203
Temal GP	4255	4306	3236	2449	598	107	0	2101	2069

Graph of Tranche Status: As of 22nd August 2019

Reconstruction- Tranche Status

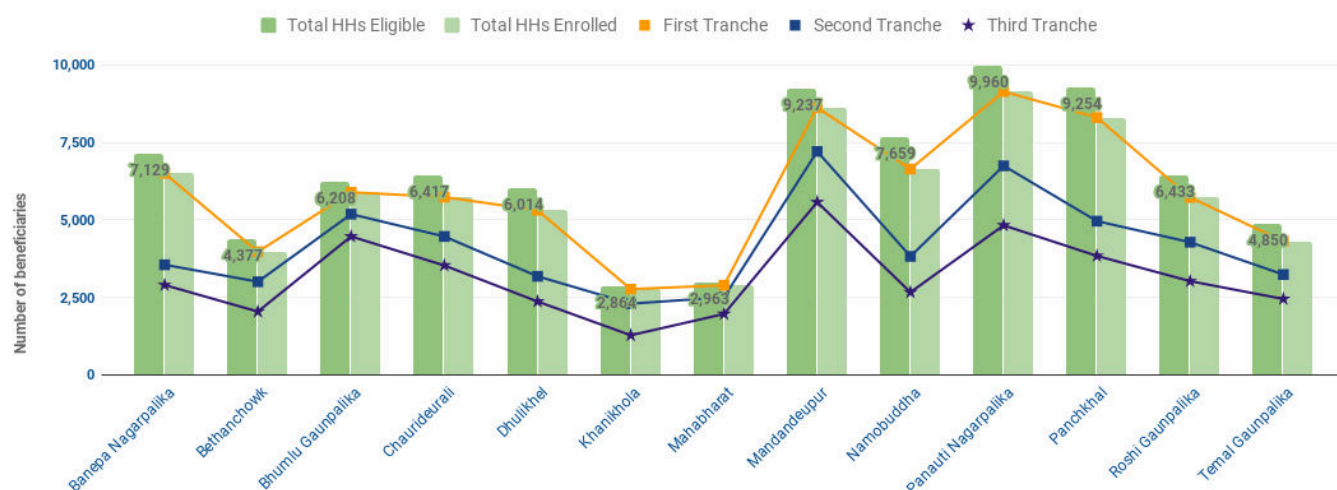

Graph for Retrofitting Status: As of 22nd August 2019

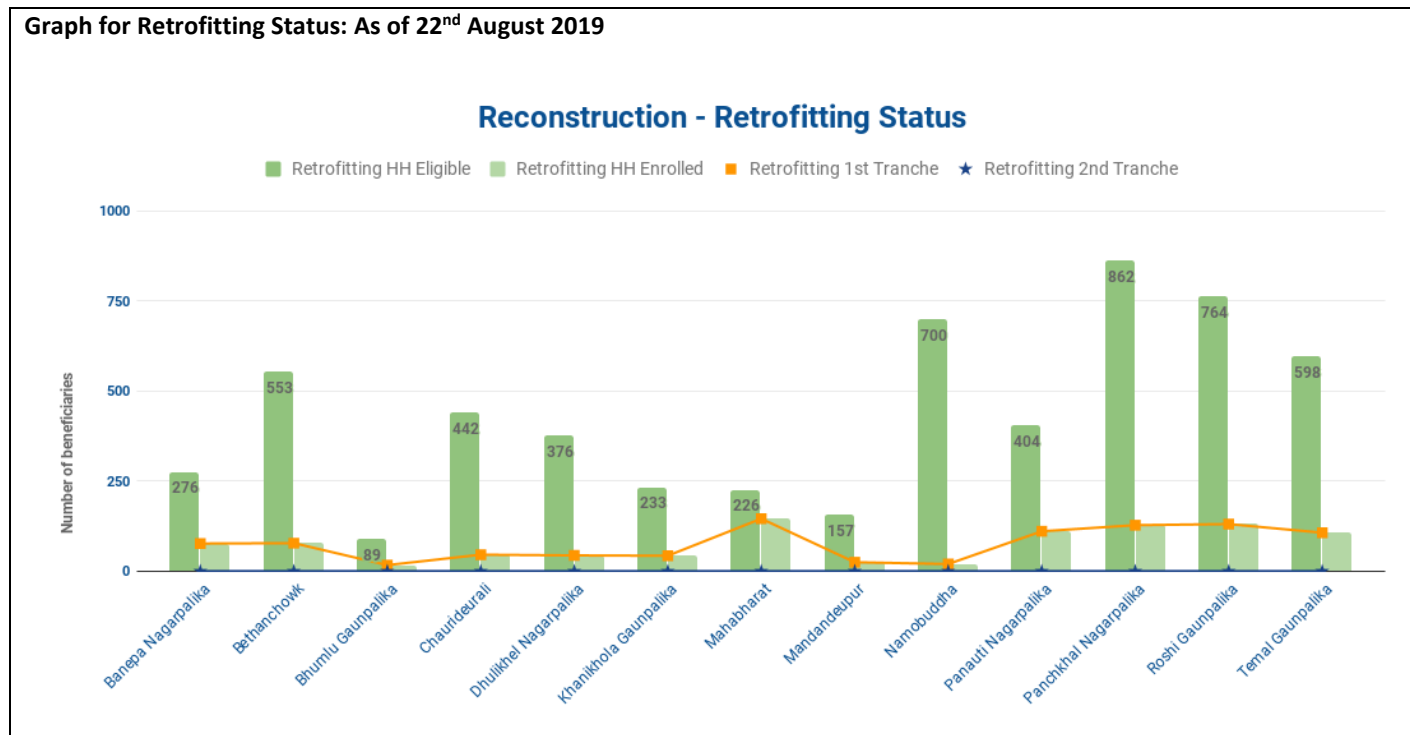

Field Visit Report (Kavrepalanchok)

Visit 1

Date	Location	Participants
14 August 2019	Chalal Ganesthan, Bethanchok GP RyaleBhir, Panauti NP	Reshma Shrestha, HRRP Ishor Neupane, HRRP
Objective(s)	- Meeting with Ward Chief on retrofit status - Visit to retrofit beneficiary reluctant to retrofit - Visit to model retrofit house - Housing typology collection	

Why was the visit carried out in this location?

To collect various stories on retrofitting, this visit was carried out.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

NA

Summary	During the visit, a brief interview with Ward Chief of ChalalGanesthan, Bethanchok-4, on the retrofit status, challenges and perception of local people towards retrofitting was conducted. Two retrofit beneficiaries at ChalalGanesthan who have received first tranche and have applied for beneficiary status change from retrofit to reconstruction too were visited. The model retrofit house at RyaleBhir, Panauti-1 too was visited to collect the experiences of the home owner towards retrofit.
----------------	--

Field Visit:

- No. of HHs visited: 8
- No. of meetings with engineers: 0
- No. of meetings with local officials: 1

Meeting: NA

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Long delay in switching beneficiary from RTB to RCB	Follow up with NRA and GMAI/DLPIU	-	Ward Officials	September 2019

Photos



Kailash Ram Tamang of ChalaGanesthan is a retrofit beneficiary. He has enrolled and received the first tranche of government grant and has also applied for the beneficiary change from retrofit to reconstruction. He is reluctant to retrofit due to the high cost. His house does not meet the retrofit standards of UNOPS/Build Change type designs as the house has large area and is L shaped.

Photograph By: Reshma Shrestha

Kunshang Lama Tamang of ChalaGanesthan is a retrofit beneficiary. He has enrolled as a retrofit beneficiary and received the first tranche of government grant. He still lives in his damaged pre earthquake house along with his three other family members. He applied for beneficiary change to RCB on Falgun 2075 but is still awaiting the change.

He has visited the retrofit demo house at Dhunkharka and also attended the retrofit awareness program organized by the ward in coordination with UNOPS. But he is still reluctant to retrofit as he has heard that retrofit is too expensive. He also thinks one lakh support for retrofit is too less. When he gets his beneficiary switched, he is planning to construct a two roomed house in a nearby plot and also keep the pre earthquake house intact.

Photograph By: Reshma Shrestha

Housing Typology Report



Address: Kavrepalanchok, Bethanchok-4

Building Typology: Brick in Cement

Description: Wang Dhoj Lama has received all three tranches of housing reconstruction grant. The house was constructed with an approx. NPRs. 8 lakhs.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Bethanchok-4

Building Typology: Stone in Mud

Description: Govinda Shrestha has received all three tranches of housing reconstruction grant. He along with his wife is staying in the pre earthquake house and will be moving to this reconstructed house after fixing the window panes.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Bethanchok-4

Building Typology: Brick in Cement

Description: This house was constructed in an approx. of NPRs. 15 lakhs. The owner has received all three tranches of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Bethanchok-4

Building Typology: Stone in Mud

Description: Santa Kumar Tamang constructed his house in an approx. of NPRs. 6 lakhs. He has received all three tranches of housing reconstruction grant.

Photographed By: Reshma Shrestha

Case Research

Perspective of Local Representative towards Retrofitting

Lal Bahadur Shrestha, Ward Chief, ChahalGanesthan, Bethanchok Gaupalika-4

A total of 73 beneficiaries at Bethanchok-4 have been listed as Retrofit Beneficiaries. Only 36 beneficiaries have enrolled and received the first tranche, amongst whom 28 have applied for beneficiary change from RTB to RCB, and the remaining too have expressed their interest towards beneficiary change. Though the notice of enrolment deadline was published and communicated months before the deadline, none of the remaining retrofit beneficiaries enrolled. For the beneficiary change, all complete documents of 26 beneficiaries have been forwarded to NRA while two are yet to be sent. None of the applications have been addressed till date.

Retrofitting has always remained the major challenge of reconstruction in the ward. The concept itself was new to the rural communities and for the major time period post the earthquake, the beneficiaries idealized that stone in mud houses are impossible to be retrofitted. In the later phase of reconstruction, retrofitting too has been prioritized. At the neighboring ward Dhunkharka, demo retrofit houses were constructed and masons were trained almost one and a half year ago by BuildChange. But still, the beneficiaries of ChahalGanesthan were reluctant towards retrofitting. The regular presence of the agency and its readiness to support the retrofit beneficiaries through technical and material assistance could not influence them as they were engraved with the perception that retrofitting is way too expensive and the retrofitting grant is too less compared to the actual cost.

Owing to the large number of retrofit beneficiaries and the nearing deadlines, the ward in coordination with UNOPS/BuildChange, gathered all the retrofit beneficiaries for the retrofit awareness program which too was a no success. Instead of garnering the best of knowledge of retrofit from the program, the beneficiaries had the accusations to the ward of denying them their right to switch their beneficiary identity to RCB. For this, the ward chief highlights the weak policies as the major reason. Had the policies been strict and demolition of pre-earthquake house been made compulsory for reconstruction beneficiary, retrofit beneficiaries would hesitate to apply for beneficiary change. The error in house survey also is a reason for retrofit reluctance. Two similar houses in the same neighborhood have been categorized differently as retrofit and reconstruction. So, the retrofit beneficiaries think they have been discriminated and want similar rights. They too are unaware of the impounding risk the damaged houses pose to their family as well as their community; instead they are in a lure of keeping their damaged house along with a smaller house with the reconstruction grant.

The Ward Chief is still putting his efforts to convince at least one of the beneficiaries to retrofit. Through one demo house and different support mechanisms of UNOPS, he still hopes the ward can progress in retrofitting.

Retrofit Demo House

Mithu Lama of RyaleBhir, Panauti NP-1 has retrofitted her house as a model retrofit house through the owner driven approach and with the complete technical assistance from UNOPS/BuildChange. The retrofit was started on 1st Asadh 2075 and was completed in three months. The total material cost was estimated around NPRs. 4 lakhs. She has received the first tranche of government grant and applied for the second tranche.

She expressed her interest to retrofit her house when UNOPS/BuildChange staffs were collecting interests of probable beneficiaries. She feels lucky to have been selected for the demo house and she got to keep her pre earthquake house intact but stronger than before. Soon after her house was selected for the retrofit, there were two different



groups of people; one who thought retrofit was a good idea and the next who asked to drop the idea of retrofit and instead reconstruct a new house. She stood by her initial decision of retrofitting and the ones who were against her decision appreciated her decision once the retrofit was complete. Hundreds of visitors have visited her house both during and after the retrofitting. She herself has felt the major difference after retrofitting. Previously, her damaged house shook even when she climbed the stairs while now even with the heavy vehicles moving, the house stands strong.

She is satisfied with the cost as well. With the 4 lakhs, she could have constructed only two roomed houses but with the same

Case Research

cost she got to strengthen her two storeys with an attic structure. Her model house has been a perfect example of model house. Many of her neighbors and visitors have expressed their interest to retrofit after visiting her house. One of her relatives at Patleket, Dhulikhel-11 too has retrofitted his house after observing her retrofitted house.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
How long does it take to convert the beneficiary status from retrofit to reconstruction?	Ward Chief, Beneficiary	The beneficiary conversion is done by central NRA and needs to be updated in the central MIS. The time duration is not exact and the variation is 1-3 months. This long duration for conversion has been raised multiple times and GMALI/DLPIU Chief too will be taking the issue to NRA.

Challenges and Way Forward

Challenge	Way Forward
Very low rate of retrofitting	Conduct community awareness programs through the model retrofits.
