

Monthly District Report

Kathmandu

27 September – 21 October 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Kathmandu	Field visit to Kathmandu Metropolitan City along with the Retrofitting task force and technical staffs, DLPIU building and HRRP was conducted to monitor the retrofitted houses.	17 October 2019	Kathmandu Metropolitan City	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org	Field Visit Section
	General meeting of DLPIU building and GMaLI along with the Focal person of each municipality of Kathmandu district.	21 October 2019	GMaLI Office, Babarmahal		Minute
	Update of the Palika Profile of all Municipalities/Metropolitan City of Kathmandu District.				Kageshwori Manohara Municipality (In Earthquake related section) Shankharapur Municipality Kathmandu Metropolitan City Municipality Tokha Municipality (In important links) Kirtipur Municipality Dakshinkali Municipality Budanilkhantha Municipality Nagarjun Municipality Tarakeshwor Municipality Chandragiri Municipality (In Profile section)
	Update of the contact list, calendar, District activities in HRRP website, update of contact list	27 Sept – 21 Oct 2019			
	Updating of the Urban status paper in	27 Sept – 21 Oct 2019			

Summary of events during this period

	coordination with the HRRP District and National team.				
	Follow up with the municipal and ward office regarding the NRA tranche deadlines, collection of the issue and gap reduction in the ongoing reconstruction work.	27 Sept – 21 Oct 2019			
	Update of 5W of Kathmandu district	27 Sept – 21 Oct 2019		Sachin Malego IM Officer Contact: 9842062006 sachin.malego@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Collection of the details of beneficiaries under the following categories - Non-enrolled beneficiaries - Vulnerable beneficiaries - Beneficiaries wanting to change from retrofitting to full construction and vice- versa.	Oct/Nov 2019	GMaLI- Kathmandu	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
Hiring of the Social mobilizer and Trained Masons in Kathmandu district.	Oct/Nov 2019		Melli Shah Focal engineer, DLPIU Building Contact: 9841737073
Collection of the detail of heritage/culturally important areas, vulnerable areas, area under government development plan such as smart city.	Oct/Nov 2019	GMaLI- Kathmandu	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
Joint Monitoring visit to different Municipalities of Kathmandu district along with DLPIU- Building Kathmandu, retrofitting task force and HRRP to monitor the ongoing retrofitting works.	Oct/Nov 2019	DLPIU Building, Kathmandu and HRRP	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org

Upcoming Events & Meetings

District Facilitation meeting of the Kathmandu Valley	TBD (Kartik 2076)	GMAI- Kathmandu	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
PA Collection and digitization of the beneficiaries of Kathmandu District	Sept/Oct 2019	GMAI- Kathmandu	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
Updating of the Municipality profile and the action plan every month and coordinate to upload the information in Municipalities websites	October 2019	HRRP Kathmandu	

News & Updates


- NRA has opened the partnership agreement and 1st tranche release in following categories:
 - Beneficiaries added through Grievance
 - Beneficiaries residing in Vulnerable and disaster-prone areas
 - Landless Beneficiaries
 - Those beneficiaries who are verified and allowed to reconstruct houses in public by the District reconstruction coordination committee.
 - Beneficiaries who have legally appealed to be eligible for the reconstruction grant.
 - Beneficiaries who have been changed from reconstruction grant to retrofitting and vice versa.
 - Beneficiaries under retrofitting grant.
- Retrofitting task force of Kathmandu District has been formed under the coordination of the District Support Engineer. The retrofitting task force consist of the engineers from DLPIU building and engineers deployed at each municipality of district.
- Action plan preparation of GMAI and Building for minimizing the gap in the tranche of Kathmandu district has been initiated. With the approaching deadline of Kartik end for the 2nd tranche, GMAI and Building has been requesting Municipalities and ward office for the timely information flow to the beneficiaries.
- DLPIU- GMAI Kathmandu has coordinated with all the municipalities and metropolitan city to convey the NRA notice to ward offices and beneficiaries.
- DLPIU- Building/GMAI Kathmandu has requested all the municipalities of Kathmandu district to send the details of the non-enrolled beneficiaries, list of vulnerable beneficiaries and the status of the beneficiaries who have not begun reconstruction even after getting the first tranche and the houses constructed before the deployment of the technical staff within Bhadra 2076. The list will be sent to NRA for further action.
- DLPIU building has been collecting the information of the houses constructed before the deployment of the technical staffs. Such houses need to be verified by the NRA technical staffs of respective municipalities and approved by the ward chief to be eligible for the reconstruction grant as per the NRA provision of such houses.

Tranche Status (Kathmandu)


Tranche Status Table:

Municipality	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Budhanilakantha Municipality	2740	2694	2087	2087	1086	914	15	1	1	1
Chandragiri Municipality	6414	5906	4894	4894	1615	1371	142	74	74	0
Dakshinkali Municipality	3542	4087	3808	3808	1720	1223	53	33	33	0
Gokarneshwor Municipality	2870	2939	2607	2607	1637	1418	24	8	8	0
Kageshwori Manahora Municipality	3741	3678	3378	3378	1904	1366	76	34	34	0
Kathmandu Metropolitan City	8738	7561	6050	6050	1614	1331	204	39	39	0
Kirtipur Municipality	3758	3231	2499	2499	992	816	64	20	20	0
Nagarjun Municipality	4315	4447	4110	4110	1565	1297	94	5	5	0
Shankharapur Municipality	6032	6102	5574	5574	3232	2434	71	42	42	0
Tarakeshwor Municipality	6737	6174	5271	5271	2377	1966	111	36	36	0
Tokha Municipality	2237	1749	1594	1594	723	600	53	26	26	0

Graph of Tranche Status:

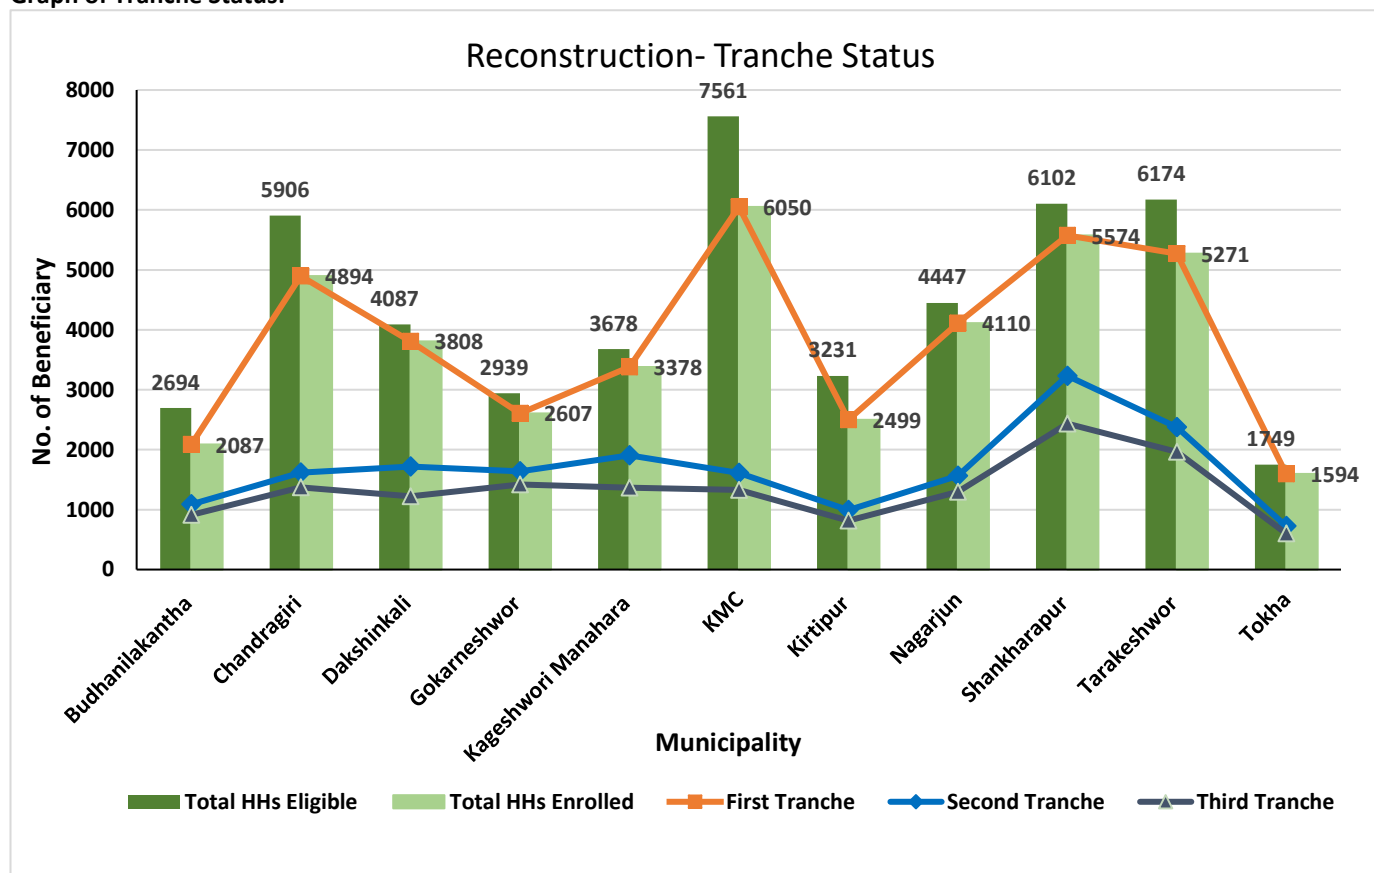

Graph for Retrofitting Status:

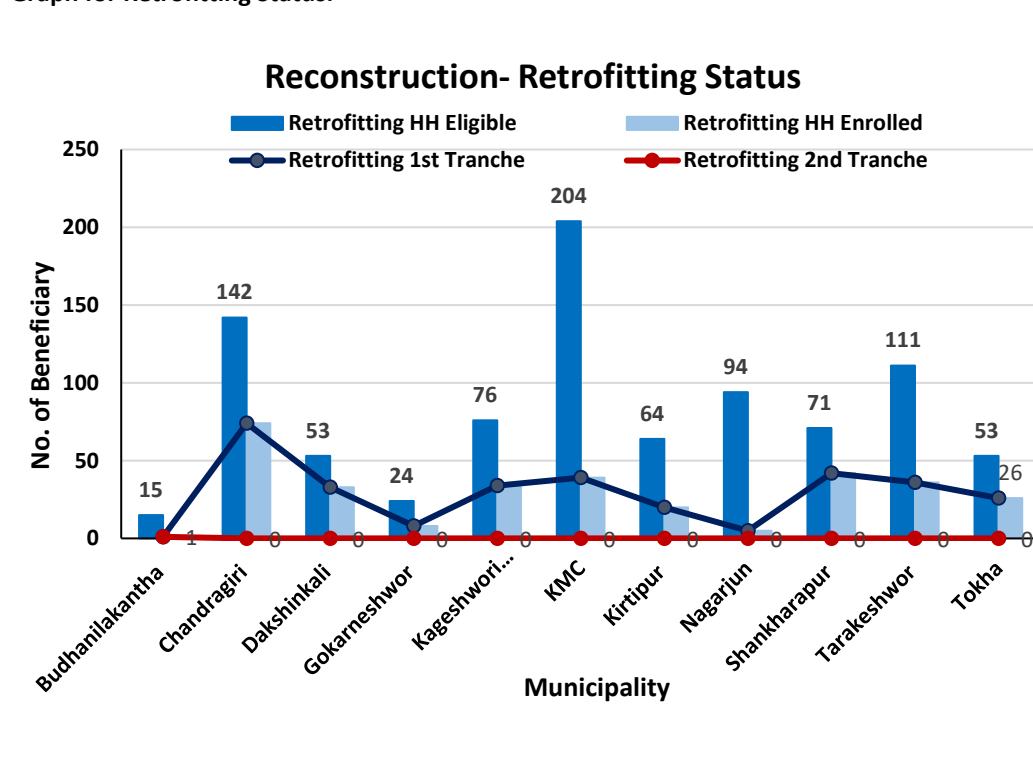

Field Visit Reports (Kathmandu)

Visit 1

Date	Location	Participants
17 October 2019	Ward no. 15, 26 and 29	- Bidhya Manandhar (DSE) - Shankhar Pokhrel (DSE), - Sanam Lakhey, Ankita Shrestha (DLPIU-Kathmandu) - DLPIU Engineers- Kathmandu Metropolitan City (Kreeti Gywali, Sanju Dawadi, Sashita K.C, Meena Sunar) - Sneha Malani, Volunteer, HRRP - Sweata Sijapati, HRRP, Kathmandu
Objective(s)	- To observe the retrofitted houses - To interact with beneficiaries to understand the reconstruction/retrofitting issues and status	

Why was the visit carried out in this location?

The field visit was targeted to monitor the ongoing retrofitting status/ retrofitted house of Kathmandu Metropolitan City as it has the highest number of beneficiaries i.e. 204 under retrofitting grant.

Summary

Field Visit:

HRRP Kathmandu along the newly formed Retrofitting task force comprising of DSEs and Engineers (DLPIU Building) and technical staffs of Kathmandu Metropolitan City, Kathmandu district. The field visit was mainly focused on the observation of the retrofitted houses. During the visit, the houses were found to be repaired rather than retrofitted. In total 4 houses were visited among which one two houses were cases of repair, one house has added I section in all the columns, and one house had jacketing of the column. One of the repaired houses was found to be vulnerable, so dismantling the damaged house and reconstruction new house was suggested during the visit.

All the beneficiary had signed the partnership agreement for the full construction so, they were suggested to apply for changing the category from full construction to retrofitting to be eligible for the grant.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Beneficiary had misconception of repair being considered as retrofit. The repaired house was found to be vulnerable.	The beneficiary was explained about the technical steps regarding retrofitting and how the structure would still be vulnerable with just few repairs.	The beneficiary agreed to dismantle the vulnerable structure and being the reconstruction process.	Beneficiary, Technical staffs	As soon as possible
Most of the retrofitted house were already complete and didn't had any photo during the retrofitting process.	The beneficiaries were asked to show a part where the I section was added.	Beneficiary showed the I section part by removing the cement at certain parts. DSE will be looking after the detail of the cases and will recommend further tranche process.	Beneficiary, DSE	As soon as possible

Photos



District Support Engineers suggesting the beneficiary what can be done for being eligible for the retrofitting grant.



Beneficiary removing section of the plaster and showing the proof of I section added to strengthen the damaged columns.

Housing Typology Report




Beneficiary name: Gyanendra Bir Malakar, ward no 29, Pabitra nagar, KMC. 3.5 storey RCC structure. The beneficiary has done jacketing of all the columns and is as per the retrofitting guideline. DSE suggested to submit the documents to change from reconstruction to retrofitting tranche and further result will be given after the structural analysis of the house.



Beneficiary name: Bindu Shahi, ward no 15, KMC. 5.5 storey RC frame structure of 9"X9" column. The beneficiary claimed to have retrofitted the house where only jacketing of 6 damaged column till 2 storey has been conducted. DSE have requested to submit the detail of the house for the structural analysis.



Beneficiary name: Babu Ram Shrestha, ward no 26, Kapurdhara, Kathmandu Metropolitan City. 2 storey BMM structure in the ground floor and BMC as super structure. The house was listed under reconstruction tranche, but the beneficiary has repaired the house and want to change to retrofitting. The structure is vulnerable with visible cracks and slight tilt. DSE suggested to dismantle the house and apply for the reconstruction tranche.

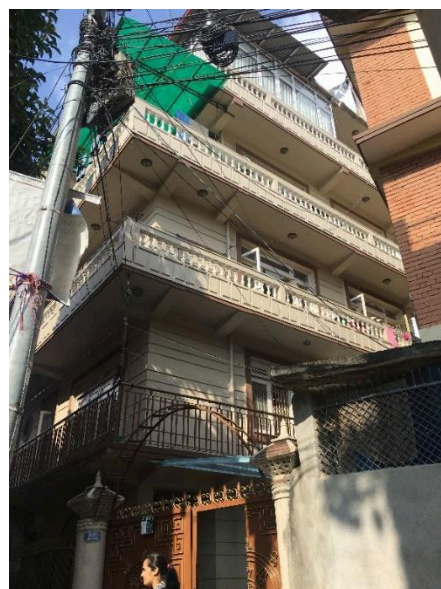

Beneficiary name: Kesangla Bhote, ward no 15, KMC. 4.5 storey RCC structure. The beneficiary had claimed to have added I section in the column. The beneficiary removed a part of the column to show the added I section. DSE have requested to submit the detail of the house for the structural analysis.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
There are beneficiaries who are willing to sign the partnership agreement for the reconstruction tranche even after the deadline of Asar 21, 2076 set by NRA. What can be done in such case?	Engineer	Regarding such cases, NRA has opened the tranche agree for certain criteria such as vulnerable group, beneficiary residing in public or government land and so on. The official documents regarding this will be send to all the concerned authority in later date. (GMAI- Project Manager)
What is the procedure for signing agreement in case of multiple ownership?	Engineer	NRA has provided full process of agreement process for the multiple ownership in the guideline. The guideline will be shared with all as soon as possible. (GMAI- Project Manager)
There are cases where the 1 st tranche amount is still in the bank. Due to lack of the information of engineers are not aware of who those beneficiaries are. Bank also doesn't provide the information of such beneficiary. What can be done in such case?	Engineer	GMAI Kathmandu will send the detail of such beneficiaries who have not withdrawn the 1 st tranche amount within Kartik 4, 2076. (GMAI- Project Manager)
What is the status of the soft loan provided by the bank?	Ward representatives	As of now the provision of the NRP 250,000 loan is not applicable but all banks in agreement with NRA has approved of NRP 300,000 loan to the beneficiaries. For this the constructed house will be the collateral itself. Regarding the interest of the bank, Nepal Government will pay 5% of the total interest and the remaining interest must be paid by the beneficiary. The choice of the bank also depends on the beneficiary.

Challenges and Way Forward

Challenge	Way Forward
NRA has made a decision to provide the full tranche for those houses constructed before the deployment of the technical staffs. There may be changes that beneficiaries with non-compliance structures may come forward to claim that the houses were constructed before the technical staffs were mobilized. The collection of such houses need to completed as soon as possible for avoiding fake cases.	Regarding this, the ward representatives as well as the technical staffs must seriously verify if the structure were constructed immediately after the earthquake.
Majority of beneficiaries have not yet started reconstructing their houses though they have received 1 st tranche from government.	Ward office should play constructive role in motivating beneficiaries to reconstruct houses. Ward-based engineers should be deployed so that beneficiaries can get technical assistance in rebuilding safe houses. The NRA deadline for the second tranche is end of Kartik 2076 so, the information must be delivered from municipality as well as ward office for its effective implementation. If beneficiaries not intending to reconstruct houses, then Ward office should lobby with them to return the 1 st tranche amount.
