

Monthly District Report

Kathmandu

14 June - 14 July 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Kathmandu	5 days training on Improved cooking stove under ESMP project to earthquake affected beneficiaries was conducted in Chandragiri Municipality. In total 8 participants (male -2, Female-6) from ward no 2 were trained during the event. A free toll kit for the construction of Improved cooking stove was provided to the participants.	11 – 15 June 2019	Chandragiri Municipality	Moti prasad Lamichanne, Social Specialist, DLPIU- GMAII Contact: 9857631119	
	5 days training on Improved cooking stove under ESMP project to earthquake affected beneficiaries was conducted in Gokarneshwor Municipality. In total 10 participants (all male) from ward no 1 and 3 were trained during the event. A free toll kit for the construction of Improved cooking stove was provided to the participants.	12 – 16 June 2019	Gokarneshwor Municipality	Moti prasad Lamichanne, Social Specialist, DLPIU- GMAII Contact: 9857631119	
	Interaction Program for The Reconstruction of Gumba Of Kathmandu District	18 June 2019	DCC hall, Babarmahal, Kathmandu	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	http://www.hrrp.nepal.org/uploads/media/Gumbameetin_gmintues_2019062_1151505.pdf
	Joint M & E Visit of HRRP Kathmandu and DLPIU- building Kathmandu.	20 June 2019	Chandragiri Municipality , Kathmandu	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	Field visit section
	A general ward level coordination meeting	20 June 2019	Chandragiri Municipality	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	http://www.hrrp.nepal.org/recent-minutes/551

Summary of events during this period

2 days training Solid waste Management under ESMP project to earthquake affected beneficiaries was conducted in Tokha Municipality. In total 17 participants (all Female) from ward no 1, 2 and 4 were trained during the event	20 – 21 June 2019	Tokha Municipality	Moti prasad Lamichanne, Social Specialist, DLPIU- GMaLI Contact: 9857631119	
2 days training Solid waste Management under ESMP project to earthquake affected beneficiaries was conducted in Tarakeshwor Municipality. In total 23 participants (all Female) from ward no 7 and 10 were trained during the event	20 – 21 June 2019	Tokha Municipality	Moti prasad Lamichanne, Social Specialist, DLPIU- GMaLI Contact: 9857631119	
A general coordination meeting with the representative from Himalaya Dan Foundation.	4 July 2019	GMaLI office, Babarmahal	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	
Partner Satisfaction Survey Round 5 of HRRP, Kathmandu District	2- 19 July 2019		Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	
Update of the housing typology in GD and Flickr	14 June – 11 July 2019		Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	
Update of the contact list, calendar, District activities in HRRP website, update of contact list	14 June – 11 July 2019		Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	
Updating of the Urban status paper in coordination with the HRRP District and National team.	14 June – 11 July 2019		Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	
Follow up with the municipal and ward office regarding the NRA tranche deadlines, collection of the issue and gap reduction in	14 June – 11 July 2019		Sweata Sijapati District Technical Coordinator, Kathmandu	

Summary of events during this period

	the ongoing reconstruction work.			sweata.sijapati@hrrp.nepal.org	
	Update of 5W of Kathmandu district	14 June – 11 July 2019		Sachin Malego IM Officer Contact: 9842062006 sachin.malego@hrrp.nepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Joint Monitoring visit to different Municipalities of Kathmandu district along with DLPIU- Building Kathmandu, M&E consultant, District Support engineers and DLPIU technical staffs deployed at Municipality and ward level.	TBD	DLPIU Building, Kathmandu and HRRP	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
District Facilitation meeting of the Kathmandu Valley	TBD (1 st week of Shrawan 2076)	GMaLI- Kathmandu	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
Municipality level meeting to address the issues of the non-enrolled beneficiaries, vulnerable beneficiaries.	12 July – 12 August	GMaLI- Kathmandu, HRRP	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
Updating of the Municipality profile and the action plan every month and coordinate to upload the information in Municipalities websites	12 July – 12 August	HRRP Kathmandu	Sachin Malego IM Officer Contact: 9842062006 sachin.malego@hrrpnepal.org

News & Updates

- The NRA has set the deadline for the reconstruction tranche as follows:

राष्ट्रिय पुनर्निर्माण प्राधिकरण सिंहदरवार, काठमाण्डौ अत्यन्त जरुरी सूचना

राष्ट्रिय पुनर्निर्माण प्राधिकरणको मिति २०७६ जेष्ठ ३१ गतेको निर्णयअनुसार निजी आवास पुनर्निर्माणका सम्बन्धमा मिष्ठानानुसारको व्यवस्था गरेकाले सबैलाई यस अनुसार गर्नुहुन जानकारी गराइन्छ ।

सि. नं.	कार्य	समय सिमा
१	२०७६ जेष्ठ मसान्त सम्म लाभग्राही सूचीमा समावेश भएकाले अनुदान संझौता गर्ने	२०७६ असार २१
२	अनुदान संझौता गरेकाले पहिलो किस्ता लिने	२०७६ असार मसान्त
३	२०७५ असार मसान्त सम्म पहिलो किस्ता लिएकाले दोस्रो किस्ता लिने	२०७६ कात्तिक मसान्त
४	२०७५ असार सम्म दोस्रो किस्ता लिएकाले तेस्रो किस्ता लिने	२०७६ माघ मसान्त
५	प्राविधिक पुग्नु अगाडी बनेका घरहरुको विवरण उपलब्ध गराउने	२०७६ असार १५
६	जोखिम वर्गमा परेका लाभग्राहीहरुको अदर्यावधिक विवरण उपलब्ध गराउने	२०७६ भाद्र मसान्त
७	छुट सर्वेक्षणका लागि गुनासो दर्ता गरी सिफारिश लिई सक्ने	२०७६ जेष्ठ मसान्त
८	छुट सर्वेक्षणको लगत संकलन सम्पन्न गर्ने	२०७६ असार १५



राष्ट्रिय पुनर्निर्माण प्राधिकरण

सिंहदरवार, काठमाण्डौ

टोल फ्री नं १६६०-०१- ७२०००, ९८०१५७२१११

www.nra.gov.np


- GMaLI has coordinated with all the municipalities and metropolitan city to convey the NRA notice to ward offices and beneficiaries.
- In lead of DLPIU-Building the resurvey and reverification of the Grievance is being collected in Kathmandu District has been completed.

Tranche Status (Kathmandu)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Budhanilakantha Municipality	2740	2694	2078	2078	1061	878	11	1	1	1
Chandragiri Municipality	6414	5906	4876	4769	1529	1285	128	46	46	0
Dakshinkali Municipality	3542	4087	3806	3805	1595	1074	52	32	32	0
Gokarneshwor Municipality	2870	2939	2564	2564	1538	1233	20	8	8	0
Kageshwori Manahora Municipality	3741	3678	3304	3304	1776	1173	75	25	25	0
Kathmandu Metropolitan City	8738	7561	6009	6009	1486	1212	173	34	34	0
Kirtipur Municipality	3758	3231	2495	2495	966	793	44	20	20	0
Nagarjun Municipality	4315	4447	4110	4110	1543	1259	38	5	5	0
Shankharapur Municipality	6032	6102	5567	5567	2940	1911	110	42	42	0
Tarakeshwor Municipality	6737	6174	5252	5252	2155	1837	107	33	33	0
Tokha Municipality	2237	1749	1594	1594	700	573	48	26	26	0

Graph of Tranche Status:

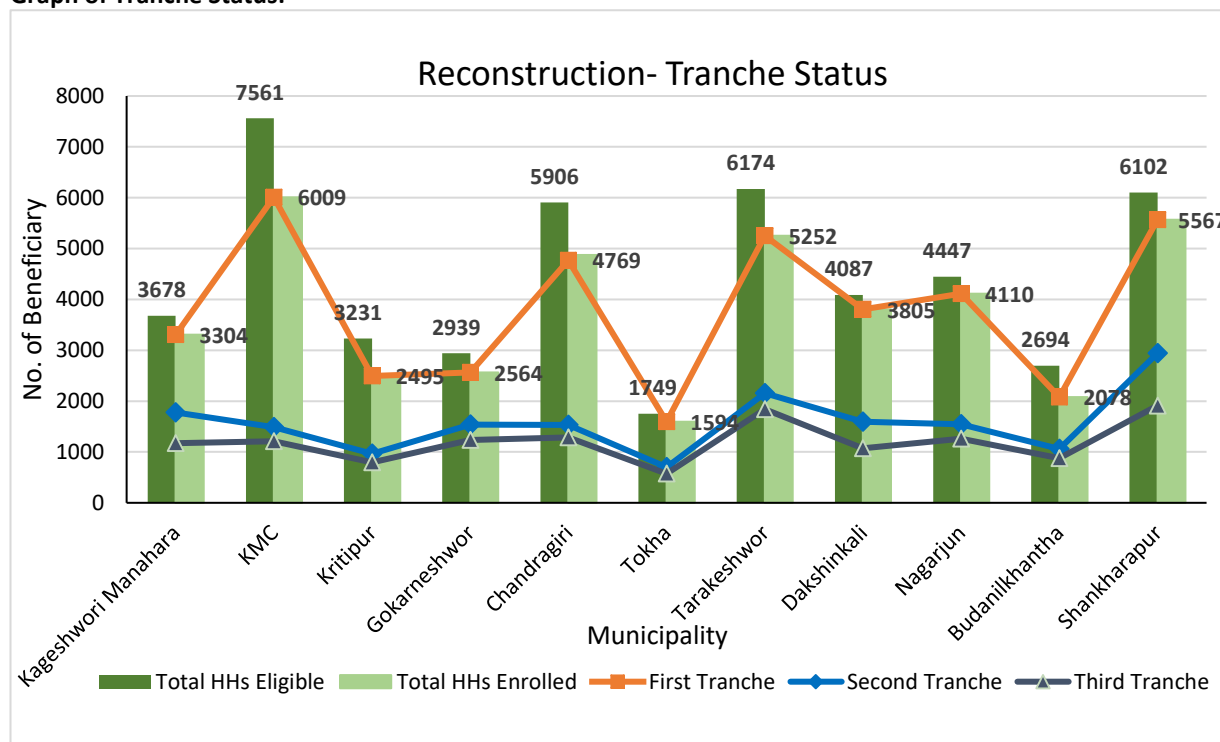

Graph for Retrofitting Status:

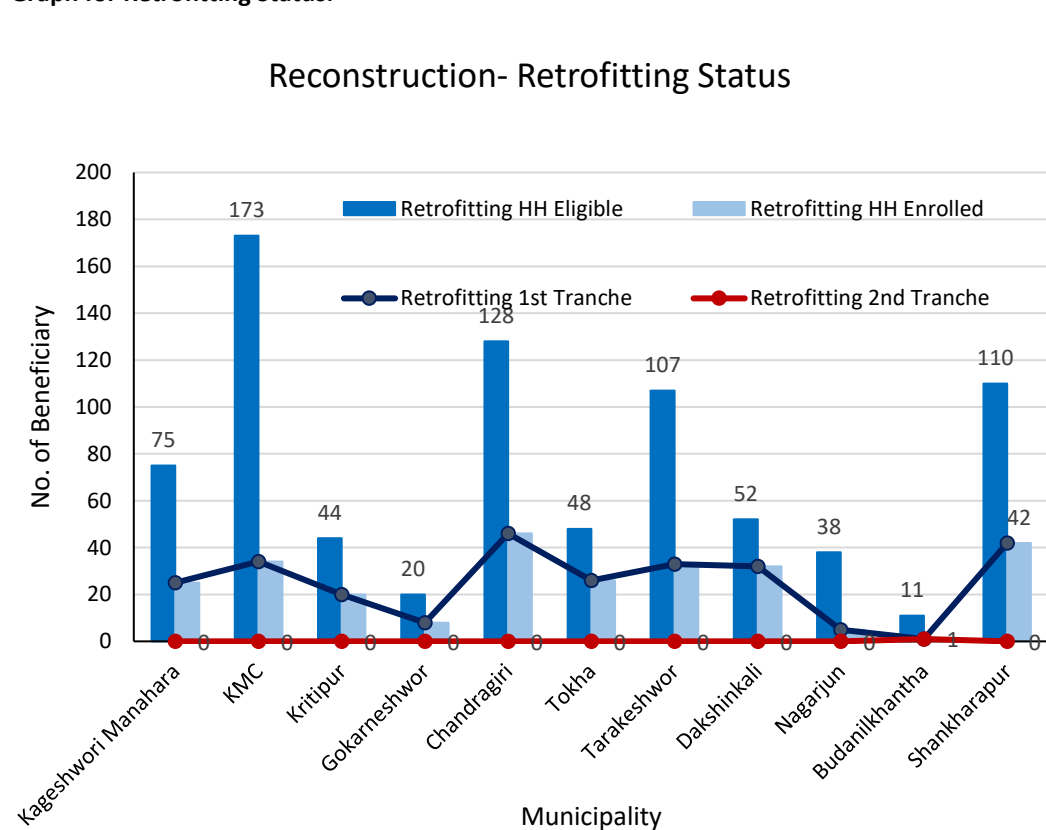

Field Visit Reports (Kathmandu)

Visit 1

Date	Location	Participants
20 June 2019	Ward no. 1, 10 and 12, Chandragiri Municipality	- Bidhya Manandhar (DSE) - Prajwal Karki (DSE), - Melli Shah (DLPIU- Kathmandu – Focal Person) - Sanam Lakhey (DLPIU- Kathmandu) - Rosha Thaku (DLPIU- Kathmandu) - DLPIU Engineers- Chandragiri Municipality (Sharada Pandey, Juhi Joshi, Cherina Awale, Deep Jwala Chhetri, Samjhana Budathoki) - Sweata Sijapati, HRRP, Kathmandu
Objective(s)	- To observe the non-compliant houses and to provide way forward regarding the technical assistance. - To interact with beneficiaries to understand the reconstruction issues and status - To collect housing typology	

Why was the visit carried out in this location?

The field visit was targeted to this site due to high number of non-compliance cases especially in 9"X12" column size and structurally unsafe, load bearing structure missing the earthquake resistant elements Hybrid construction using two or more material in a single-story structure. As the beneficiaries were not convinced by the correction measures suggested by the technical staff, the visit was accompanied by the district support engineers.

Summary

Field Visit:

HRRP Kathmandu along DSE and technical staffs from DLPIU Building conducted joint field monitoring at Ward no 1, 10 and 12 of Chandragiri Municipality, Kathmandu district. The field visit was mainly focused on the observation of the Non-compliance cases and beneficiaries claiming for the 2nd and 3rd tranches in the area. During the visit DSEs suggested the possible correction measures and way forward to the beneficiaries for being eligible for the tranche. In total 11 houses were visited among which majority of the houses were hybrid structure. Similarly, the other non -compliance case was 9"X12" column, load bearing structure missing the earthquake resistant elements and so on. During the visit the monitoring of the resurvey and reverification of the grievance was also conducted. The field visit began with a ward level meeting at ward no. 10 in presence of the ward chief. Along with the ward chief a site visit to a multiple beneficiary was conducted were not able to construct the house due to small land parcel after the property division. DSE suggested to construct a single structure but with different entrance and staircase and as per the government technical guideline to be eligible for the reconstruction grant In total 9 HHs were visited among which 2 beneficiaries had completed their structure but were not verified as beneficiaries during the previous grievance collection. They were listed for the resurvey and reverification and their grievance collection was done during the site visit. Some of the beneficiaries interacted during the visit had still not signed the PA agreement due to lack of landownership issues. Before beginning the field visit a brief meeting with the technical staffs deployed in the municipality was conducted to identify the measure issues and the selection of the household to be visited.

During the meeting the measures issues highlighted by the technical staffs were

- Due to landownership documents and road extension program some beneficiaries are not able to sign the grant agreement.
- Non-compliance houses constructed before the NRA guidelines
- Missing of earthquake resistant elements, and 9"X12" column size.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
The houses constructed were found to be constructed without the earthquake resistant elements such as vertical reinforcements and so on.	The beneficiary was suggested to add the band for the exterior of the wall and the vertical reinforcement in the corners	The beneficiary agreed to apply the correction measures as per suggested by the DSE.	Beneficiary, Technical staffs	As soon as possible

Some of the beneficiaries still had not signed the PA agreement due to ROW and no landownership documents.	The beneficiaries were suggested to visit the GMaLI office for the possible solution in this regard.	GMaLI office will provide the details on the required documentation for the beneficiary to be eligible to sign the agreement.	Beneficiary, Municipality, GMaLI	As soon as possible
--	--	---	----------------------------------	---------------------

Photos



Ward level coordination meeting of joint monitoring team of DLPIU Building and HRRP at ward no 10, Chandragiri Municipality, Kathmandu.



Joint monitoring team along with the ward chairperson visiting the site during the joint monitoring visit



The technical staffs conducting the grievance collection in ward no. 10 of Chandragiri Municipality as part of the final resurvey and reverification of the beneficiaries affected due to 2015 Gorkha earthquake.



The house of Mr. Krishna Gopal Nakarmi, under the grievance was listed as Damage grade 4 during the resurvey and reverification collection in ward no 12, Chandragiri Municipality.

Housing Typology Report



Beneficiary name: Shyam Krishna Maharjan, Balambu, ward no 12, Chandragiri Municipality. Load bearing brick in cement mortar structure. The structure is non-compliance as the corner stitch, bands and vertical reinforcement are missing. The correction measures were suggested during the visit.



Beneficiary name: Rup Kumar Shrestha, Balambu, ward no 12, Chandragiri Municipality. The beneficiary has received all the tranches.



Beneficiary name: Pradip karki, ward no 1, Chandragiri Municipality. One storey load Bearing brick and cement Mortar Masonry. The house was found to be compliance and the technical inspection was conducted during the visit.



Beneficiary name: Rup Kumar Shrestha, ward no 12, Chandragiri Municipality. Two storey load Bearing brick and cement Mortar Masonry. The structure is listed as non-compliance due to larger opening. The beneficiary is planning to keep rolling shutter in the ground floor.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
The reconstruction of the damaged house is restricted due to the road extension project. Due to this the Partnership agreement has also not	Engineer	Regarding such cases, identify the name of such beneficiaries and forward the case to GMAI Kathmandu for further action to be taken to address this issue (HRRP)

Questions Collected

been signed. What can be done in such case?		
The land belongs to 5 family members but due to small land parcel after the division of the land, 5 beneficiaries are not being able to start the reconstruction process. What can be possible solution for such cases?	Ward Chief	In such case the beneficiaries can construct a single technically compliance structure but with different entrance and staircase to be eligible for the reconstruction grant.

Challenges and Way Forward

Challenge	Way Forward
Majority of beneficiaries have not yet started reconstructing their houses though they have received 1 st tranche from government.	Ward office should play constructive role in motivating beneficiaries to reconstruct houses. Ward-based engineers should be deployed so that beneficiaries can get technical assistance in rebuilding safe houses. If beneficiaries not intending to reconstruct houses, then Ward office should lobby with them to return the 1 st tranche amount.
Most of the structure constructed immediately after the earthquake and without the technical assistance are increasing the non-compliance cases.	Such houses must be suggested to apply the correction measures. For the houses which are not addressed by the correction measures, number of such houses must be collected, and NRA should make a policy to address such cases.

Case Study

Success story of the Landslide preventive measure



The landslide area of Lapsiphedi, ward no 4, Shankharapur Municipality.



The landslide area of Lapsiphedi, ward no 4, Shankharapur Municipality after the completion of the landslide mitigation measure.

During the rainy season of 2018 the continuous rainfall caused a loosened the soil in the slope which resulted in the landslide in Dhungana Tole (27.745N, 85.47861111E), Lapsiphedi ward no 4, Shankharapur Municipality. The landslide swept away the part of the hills nearby exposing the houses to the edge of the hill. As per the site selection for the implementation of the sub project of Environment and Social Management plan under the Environment and Social Management Framework for the earthquake affected beneficiaries, the application of the landslide protection measure was listed as the top priority from the municipality. The site verification of the landslide protection measure was carried out on 9-10 January 2019 (25-26/09/2075) along with technical team, Environment and Social development specialist and NRA Geo-technical survey team on 26 March 2019 (21/12/2075). As of the site verification by DL-PIU KTM and NRA Geo-technical survey team at Lapsiphedi, the settlement lies in Category II of the disaster-prone area. The total of 40 people in 10 households, all earthquake beneficiaries and already received all the 3 tranches of housing reconstruction but are at potential risk due to the landslide. The plan includes Gabion Toe wall, Drainage works, and Bioengineering works.

The landslide preventive work started from 29 May 2019 in presence of the technical team, DLPIU- GMaLI and HRRP and was completed in 2 July 2019. As per the plan the Gabion Toe wall of 108 cu. m was constructed, for drainage management and seepage control HDPE pipe wrapped with Geomembrane was used and finally as part of the Bioengineering work plantation of 150 *Amliso Rhysome* and 60 small shrubs were done. The budget for the project was provided by DLPIU GMaLI- Kathmandu (85%) and the user committee (15%). The project has benefitted total 10 households of Dhungana Tole, Lapsiphedi-4, Shankharapur.
