

# HRRP District Coordination Meeting Minutes

|                          |                                                     |          |          |
|--------------------------|-----------------------------------------------------|----------|----------|
| Meeting Purpose:         | HRRP General Coordination Meeting                   |          |          |
| Meeting Date:            | 24/07/2018 (24 <sup>th</sup> July 2018)             |          |          |
| Meeting Time:            | 11am – 2pm                                          |          |          |
| Meeting Location:        | Devkota Chowk, Manthali DTO Meeting Hall, Ramechhap |          |          |
| Meeting Facilitator:     | Prakash Bishwakarma                                 |          |          |
| Minutes Taken By:        | Tulasi Ram Lamichhane/ Jawed Mohammad               |          |          |
| Summary of participants: | Total: 25                                           | Female:2 | Male: 23 |

## Discussion: (Items/Knowledge Shared)

- Before starting discussion HRRP Mr. Prakash Bishwakarma District coordinator welcome all the participants and shared all the agendas for discussion. Similarly, District Coordinator of HRRP also make reviews of discussion and agendas of previous meeting. In last meeting all partner's organization updated their activities except Red cross and KAM for SUD. In the last meeting the discussion was made all partner's organization should support to the local level in the respective working area of partner's organization to collect the status of vulnerable beneficiaries.
- Addenda's for General Coordination meeting:
  - **Welcome/Introduction**
  - **Review of the previous month's meeting**
  - **POs update – please share your update packs so that can be shared in the meeting minute and bi-weekly bulletin. Please prepared short PPT for meeting and Gmai purpose with hard-copy its mandatory**
  - **POs' further plans and programs to support reconstruction: private housing, WASH, Livelihood, Health, Local Governance, Reconstruction Planning, Education, Community Infrastructure etc.**
  - **4W to 5W transfer orientation for POs**
  - **AoB**
- **Welcome/Introduction**  
On 24<sup>th</sup> July 2018 NRA/ HRRP Ramechhap have successfully completed General Coordination Meeting in Ramechhap, Manthali at DTO office, meeting Hall. NRA/HRRP Ramechhap General Coordination Meeting was chaired by Mr. Krishna Lal Piya- DTO/Chief – Grant Management and local infrastructure/ NRA-Ramechhap. A total of 25 participants were participated in the coordination meeting from different government and non-government organization. The meeting was facilitated by Mr. Prakash Bishwakarma –District General Coordinator and supported by Mr. Tulsi Ram Lamichhane-District/ Javeed Mohamad Technical Coordinator/ Information management officer. Mr. Prakash Bishwakarma – District General Coordinator – HRRP welcomed all the participants attended in the coordination meeting and had a round of introduction with each other. He also shared the objective and agendas of the coordination meeting.
- **HRRP updates:**  
Mr. Prakash Bishwakarma- District coordinator present and shared current reconstruction status of the District to the meeting participants that Sunapati and Doramba Rural Municipality is little bit behind regarding to the remaining Rural Municipality. He also shared upcoming event of HRRP that is 5W orientation and joint field monitoring visit to Sunapati and Dorumba

# HRRP District Coordination Meeting Minutes

## Discussion: (Items/Knowledge Shared)

Rural Municipality. Likewise, he also shared some of the common issues and challenges found in the joint monitoring Visit.

### ○ District Support Engineer (DSE/ DLPIU)

- Mr. Keshab raj Pandey present the non-complains issue in the district. A total of 1170 non-complains had been registered in the district till date. Among them 942 noncompliance had been made correction from the District Support Engineer (DSE).
- A total of 70-80 noncompliance beneficiaries have been already received government tranche after DSE correction.
- After inspection from DSE of non- complains houses of beneficiaries, respective Engineer from the ward and partner's organization engineer should monitor time to time for the right correction.

### ○ Partners Update

In Ramechhap District there are 6 partner's organization are actively working in the district based on the reporting to NRA/HRRP.



|                                                 |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <p>Nepal Red Cross Society (NRCS) Ramechhap</p> | <ul style="list-style-type: none"> <li>○ Nepal Red Cross Society is working in Manthali Municipality 1&amp;2 and Ramchhap Municipality ward-5Rampur of Ramechhap District.</li> <li>○ Nepal Red Cross Society is Working in four major area i.e Shelter, Livelihood, Wash and Health.</li> <li>○ A total of 1079 households is supporting by NRCS in Ramechhap district i.e Manthali Ward-1&amp;2 and Ramechhap ward no-5.</li> <li>○ <b>Reconstruction/shelter update is as below:</b> <ul style="list-style-type: none"> <li>- 241 beneficiaries were trained as a meson on Earthquake resistant building.</li> <li>- A total of 917 houses were completed DPC level.</li> <li>- A total of 793 houses were completed sill band.</li> <li>- A total of 764 houses were completed lintel band.</li> <li>- A total of 712 houses were completed roof covering.</li> </ul> </li> <li>○ <b>WASH</b> <ul style="list-style-type: none"> <li>- A total of 567 toilets were constructed in Ward-5, Rampur of Ramechhap municipality of Ramechhap District.</li> <li>- 16 WSS identified and prioritized in Ramechhap municipality ard-5 Rampur. Among them 5 WSS were constructed. 3 WSS is in Rampur and 2 is in Manthali Municipality.</li> <li>- A total of 11 Junior Engineer were trained in Technical WASH training.</li> <li>- 33 hand washing facilitators were trained in respective working area of NRCS.</li> </ul> </li> <li>○ <b>Health</b> <ul style="list-style-type: none"> <li>- Full Immunization in Manthali Municipality.</li> <li>- 600 LLIN distributed to the pregnant women in respective working area of NRCS.</li> </ul> </li> </ul> |
|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|

## HRRP District Coordination Meeting Minutes

| Discussion: (Items/Knowledge Shared) |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |
|--------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                      | <ul style="list-style-type: none"> <li>- 388 students were trained on HIV prevention.</li> <li>- 24 volunteers were trained on community health.</li> <li>- 20 waka waka (touch) are distribution to FCHVs of respective working area of NRCS.</li> <li>- 24 Volunteers, social mobilizers and JEs were trained on First Aid.</li> <li>o <b>Livelihood:</b> <ul style="list-style-type: none"> <li>- 2 Small irrigation channel restored in the respective working area of NRCS.</li> <li>- A total of 270 personnel were trained on commercial goat farming.</li> <li>- 433 personnel were oriented on safe animal shed.</li> <li>- 105 sample of soil test is completed for agriculture.</li> <li>- 4808 livestock were insurance in Rampur village of Ramechhap municipality.</li> <li>- 365 goat shed constructed in Manthali Municipality of Ramechhap district.</li> </ul> </li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |
| HELVATAS/SCOOT WILSON                | <ul style="list-style-type: none"> <li>- HELVETAS is working in the district for the duration from Jan 2018 to June 2020 to support reconstruction.</li> <li>- The major two components of the project are i) Technical Supports to homeowner and ii) Skills training for earthquake house reconstruction and future safe construction</li> <li>- <b>Helvetas/ EFSR II</b> covers 5 local levels in Ramechhap district namely Doramba, Khadadevi, Likhu Tamakoshi (4 wards- 1,5,6,7 only), Sunapati and Manthali Municipality (Except Ward No 10 and Red Cross Working area of ward no 1). Scott Wilson Nepal is collaborating partner to provide technical assistance in Manthali municipality and Sunapati rural municipality in Ramechhap.</li> <li>- <b>Management Arrangements:</b> Office Setup in Gaunpalika- Likhu Tamakoshi, Doramba and Khadadevi and Regular Administrative activities</li> <li>- <b>Door to door Technical Supports to Homeowner and Facilitation:</b> EFSR continued door to door technical supports and facilitation to the houses under construction in all the 5 rural/municipalities. Based on EPMS database of the project, EFSR has provided technical supports to 3,694 HHs. Facilitation and procedural supports linking to the tranche are other important social supports provided to the house owners.</li> </ul> <p>Out of 25,890 total existing beneficiaries, the following is the status of grant received in EFSR Working area.</p> |

# HRRP District Coordination Meeting Minutes

## Discussion: (Items/Knowledge Shared)

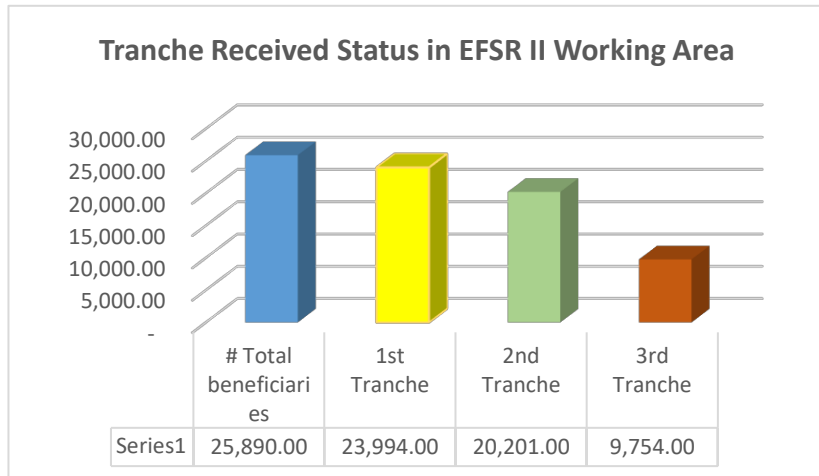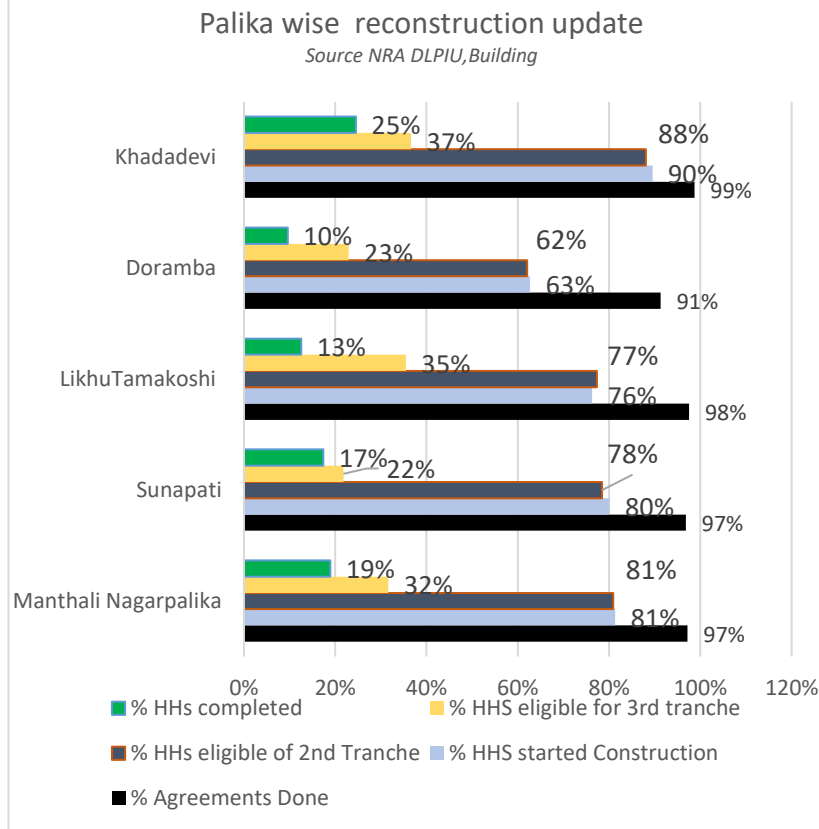

- EFSR has strategize to coordinate closely with DLPIU, ward engineer and mobilize Sub Engineer level staffs to support non complaint households.
- **Coordination Meetings with stakeholders:** Regular coordination and update sharing meeting with palika, wards and NRA ward engineers has been conducted on a regular basis, once a month in all over the EFSR working areas.

# HRRP District Coordination Meeting Minutes

| Discussion: (Items/Knowledge Shared) |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |                        |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
|--------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------|---------------------|------------------------|--------------|------|--------------------|---------------------|------|-----|-------------------------------------|------|-----|--------------------------------------|------|-----|-------------------------------------|------|-----|--------------------------------------|-----|-----|-------------------------------------|-----|-----|-----------------------|-----|-----|------------------------|-----|-----|--|
|                                      | <ul style="list-style-type: none"> <li>- Annual programme and budget of EFSR has been endorse by rural/municipal council in all the ESFR working palikas.</li> <li>- <b>Capacity Building Activities:</b> The following two capacity building activities have been organized during this period</li> <li>- Safety and security training to CRPs- 48 field level staffs</li> <li>- Mentoring to CRPs on facilitation and social mobilization skills</li> <li>- <b>Key Issues and Challenges:</b> Transportation of materials, rainy season, Beneficiaries not needy/willing to reconstruct, Vulnerable population- further financial and facilitation supports needed, Imitation of prior con-compliant works by house owner and persistence for grant eligibility, Week internet facility at wards and Internal database system of EFSR, however is in process of upgrading</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             |                        |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| MEDIAR                               | <ul style="list-style-type: none"> <li>- Agreement for working in Likhu Tamakoshi Rural Municipality in Ward 3&amp;6 Bejiulikot.</li> <li>- Agreement for 1296 household of Bejiulikot (3-4)</li> <li>- MEDIAR is working with its partner organization Community Development Society.</li> <li>- MEDIAR is working to support Technical Assistant and as well supporting financial support to a total of 310 households in ward 3 and 4 Bejiulikot.</li> </ul> <p>Summary of Reconstruction of Bijulikot (3&amp;6) Ward of LikhuTamakhosi rural municipality, Technical assistant provided by: MEDIAR/CDS</p> <table> <tr> <th>Description</th><th>Target and achieved</th><th>Remarks and Percentage</th></tr> <tr> <td>Total target</td><td>1296</td><td>33 from grievances</td></tr> <tr> <td>Total House Started</td><td>1229</td><td>97%</td></tr> <tr> <td>1<sup>st</sup> instalment received</td><td>1272</td><td>98%</td></tr> <tr> <td>2<sup>nd</sup> instalment Forwarded</td><td>1216</td><td>96%</td></tr> <tr> <td>2<sup>nd</sup> instalment received</td><td>1192</td><td>94%</td></tr> <tr> <td>3<sup>rd</sup> instalment Forwarded</td><td>899</td><td>71%</td></tr> <tr> <td>3<sup>rd</sup> instalment received</td><td>804</td><td>63%</td></tr> <tr> <td>Total House completed</td><td>979</td><td>77%</td></tr> <tr> <td>Total House Demolition</td><td>439</td><td>35%</td></tr> </table> <ul style="list-style-type: none"> <li>- Major achievement on this month:               <ul style="list-style-type: none"> <li>• Total house completed at Bijulikot by this month:- 979 nos</li> </ul> </li> </ul> | Description            | Target and achieved | Remarks and Percentage | Total target | 1296 | 33 from grievances | Total House Started | 1229 | 97% | 1 <sup>st</sup> instalment received | 1272 | 98% | 2 <sup>nd</sup> instalment Forwarded | 1216 | 96% | 2 <sup>nd</sup> instalment received | 1192 | 94% | 3 <sup>rd</sup> instalment Forwarded | 899 | 71% | 3 <sup>rd</sup> instalment received | 804 | 63% | Total House completed | 979 | 77% | Total House Demolition | 439 | 35% |  |
| Description                          | Target and achieved                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | Remarks and Percentage |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| Total target                         | 1296                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | 33 from grievances     |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| Total House Started                  | 1229                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | 97%                    |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| 1 <sup>st</sup> instalment received  | 1272                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | 98%                    |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| 2 <sup>nd</sup> instalment Forwarded | 1216                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | 96%                    |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| 2 <sup>nd</sup> instalment received  | 1192                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | 94%                    |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| 3 <sup>rd</sup> instalment Forwarded | 899                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | 71%                    |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| 3 <sup>rd</sup> instalment received  | 804                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | 63%                    |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| Total House completed                | 979                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | 77%                    |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |
| Total House Demolition               | 439                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | 35%                    |                     |                        |              |      |                    |                     |      |     |                                     |      |     |                                      |      |     |                                     |      |     |                                      |     |     |                                     |     |     |                       |     |     |                        |     |     |  |

# HRRP District Coordination Meeting Minutes

| Discussion: (Items/Knowledge Shared) |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |
|--------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                      | <ul style="list-style-type: none"> <li>• Training on Improved Cooking stove (ICS) provided to 18 individuals of Bijulikot VDC</li> <li>• Provide Tarps to Ongoing Construction Houses-36 Nos</li> <li>• 41 Nos of ICS has been constructed</li> <li>• Evaluation Visit from SWC has been done.</li> <li>• NRA visit from KTM- for extension of the project</li> <li>- Upcoming plan:               <ul style="list-style-type: none"> <li>• Provide more tarps to support ongoing construction in this rainy month</li> <li>• Ongoing Construction Supervision and Monitoring</li> <li>• Refresher Mason training</li> <li>• Staffs training and Capacity building</li> <li>• Start Staffs Phase out process (downsize)</li> <li>• ICS construction- Ongoing</li> <li>• Handover of first project (after completing remaining houses)</li> <li>• Global Medair CEO – Visit at Nepal (September Month)</li> </ul> </li> <li>- <b>Challenges:</b> <ul style="list-style-type: none"> <li>• Grievances again added.</li> <li>• 35 beneficiaries for retrofitting + 9 previous =44Nos</li> <li>• Retrofitting beneficiaries wants to be on Regular beneficiaries (3 Lakh amount)</li> <li>• Follow up has been done from ward office</li> <li>• Gouvernemental Timeline -?</li> <li>• Rainy season, most of the local mason and beneficiaries engaged in Agricultural works</li> <li>• Transportation of materials-Scarcity at District (Hope it Will be resolved now)</li> </ul> </li> </ul> |
| KA M for SuD                         | <p>Kam For Sud Nepal is working in Ramechhap through it project Post-earthquake reconstruction from January 2016 to December 2018. The following below are the highlights of the Kam for sud program achievement till date:</p> <ul style="list-style-type: none"> <li>- In collaboration with a CTEVT-accredited training institution, 68 masons and 20 carpenters have been trained for 50 days on earthquake-resistant building techniques, based on stone masonry with mud mortar and wooden reinforcements. Among them, 10 carpenters have received additional training on bamboo treatment and 10 masons have been trained in stone masonry</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              |

## HRRP District Coordination Meeting Minutes

### Discussion: (Items/Knowledge Shared)

- with cement mortar and reinforced cement concrete (RCC) technology that is used for the health post and the schools.
- A technical support and monitoring of the building sites has been initially provided to 200 households and is on-going for another 400 households plus, until the end of 2018. This consists of training social mobilizers in each ward and providing technical follow up at the building sites through skilled instructors. Altogether about 600 houses have been reconstructed and are under building process, so far
  - Two schools and one health post with maternity ward are under construction in Saipu. The construction has been delayed compared to the initial plan, due to the lack of manpower (priority has been given to the private houses). Nevertheless, Kam For Sud Nepal expects to complete the three projects as fast as possible. However, projects period will be extended. The full construction cost is financed by Kam For Sud Nepal.

### Challenges

- Unavailability of manpower for a long time is the most challenging issue for the projects to get completed on time
- Limited means of transportation is delayed the process of construction
- Deteriorating & Fragile road condition
- Frequent increase in price of construction material and transportation fare
- Recently monsoon has been disturbing smooth working condition.
- Due to above mentioned and other various reasons, projects are not completing within project's completion time frame affecting the cost. Thus, extension of project period is required.

### Decisions:

#### **PARKING LOT:** *[Describe any items that may have been deferred for a later discussion]*

- *Focal Person Confirmation for Reconstruction*  
The meeting has entered the topic but cannot conclude it this time.

# HRRP District Coordination Meeting Minutes

## Discussion: (Items/Knowledge Shared)

N/A

## Miscellaneous Items / AOB:

N/A

## Decisions Made: (What, Why, Impacts)

- The progress and challenges faced by the NGOs/INGOs working in the district in the private housing reconstruction was discussion and works hard to find the target with in the time period.

## Next Steps/action points:

## Person(s) Responsible

## Due Date

[Insert next step]

[Insert next step]

| SN | Attendees                | Gender | Organization          | Designation                  | Phone No.  | Email                         |
|----|--------------------------|--------|-----------------------|------------------------------|------------|-------------------------------|
| 1  | Krishna Lal Piya         | M      | NRA/Gmali             | Office chief                 | 9854043491 | Klpiya057@gmail.com           |
| 2  | Raju Thapa Magar         | M      | DTO                   | Engineer                     | 9849137571 | Livilraju77@gmail.com         |
| 3  | Damodar Prashad Ghimirie | M      | NRA                   | Na.Su.                       | 9744007807 |                               |
| 4  | Sandesh Chaulagain       | M      | Manthali Municipality | IM officer                   | 9846448426 |                               |
| 5  | Kumar Dahal              | M      | CDS                   | WO                           | 9849089447 | kumardahal@gmail.com          |
| 6  | Roshan Kumar Yadav       | M      | NRA/Gmali             | Engineer                     | 9863820884 | Roshanyadav42@gmail.com       |
| 7  | Nikesh Maharajan         | M      | DLPIU                 | DSE                          | 9849197244 | Nikesh.mijn@gmail.com         |
| 8  | Nanu Bogati              | F      | DLPIU/ Building       | Sub-Emgineer                 | 9861145959 | Bogatinanu143@gmail.com       |
| 9  | Keshab raj Pandey        | M      | DLPIU                 | DSE                          | 9851129012 | Keshabrajpandey2000@gmail.com |
| 10 | Nabinda Thapa            | F      | HELVETAS/EPS RII      | Cluster Coordinator          | 9856040887 | Nabinda.thapa@helvetas.org    |
| 11 | Balram Shrestha          | M      | Embassy/SDC           | GDO                          | 9741165086 | Shresthabalram.sdc@gmail.com  |
| 12 | Hom Prashad Ghimire      | M      | Gmali                 | Computer operator            | 9843112098 | ghimireah@gmail.com           |
| 13 | Santosh sijalee Magar    | M      | CDS                   | Program Coordinator          | 9849551874 | cdsmagar@gmail.com            |
| 14 | Rajan Shrestha           | M      | KFSN                  | Project Coordinator          | 9841352510 | rajankfsn@csrnepal.org        |
| 15 | Jeevesh karna            | M      | SW Nepal/EFSR II      | Field Coordinator            | 9851017906 | jeeveshkarna@gmail.com        |
| 16 | Ajaya Mahara             | M      | MEDAIR                | Sr. PSO                      | 9849427447 | Pso-npl@medial.org            |
| 17 | Dev raj Gautam           | M      | MEDAIR                | Program Maanger              | 9851225844 | Shelterpm-npl@medair.org      |
| 18 | Deepak Thaguna           | M      | DLPIU/ Building       | Engineer                     | 9843311148 |                               |
| 19 | Thir Bdr. Thapa          | M      | Sabal Nepal           | DRR                          | 9854040255 | Thir.thapa@care.org           |
| 20 | Dhan Raj Manadal         | M      | PAF                   | Consultant                   | 9844251018 | Er.dhanrajmandal@gmail.com    |
| 21 | Jagdish chanda           | M      | DLPIU/Building        | Engineer/ FP                 | 9861928905 | Sirischand037@gmail.com       |
| 22 | Jaya ram Basnet          | M      | NRCS                  | District Program coordinator | 9841653249 | Jaya.basnet@gmail.com         |

## HRRP District Coordination Meeting Minutes

|    |                      |   |      |     |            |                                  |
|----|----------------------|---|------|-----|------------|----------------------------------|
| 23 | Prakash Bishwakarma  | M | HRRP | DC  | 9841720436 | dc.ramechhap@hrrpnepal.org       |
| 24 | Tulsi ram Lamichhane | M | HRRP | DTC | 9851213610 | Techcord.ramechhap@hrrpnepal.org |
| 25 | Md. Jawed            | M | HRRP | IMO | 9862298704 | Im.ramechhap@hrrpnepal.org       |

Photos:



Partners Organization member from HELVETAS presenting their organization Update to the meeting participants.



Gmali /NRA Chief Mr. Krishna Lal Piya putting his motivational remarks to the coordination meeting participants.



Participants are providing their views and concentration regarding the presentation by Partners organization



HRRP District Coordination updating and review the decision and discussion to the participants of previous coordination meeting.
