

# Fortnightly District Report

## Gorkha

18 – 31 January 2019

### Summary of events during this period

| Name of activity/event                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                            | Event date                    | Participants summary |        | Contact Person                                                                                                                                                                                                     | Reference Document      |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------|----------------------|--------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |                               | Male                 | Female |                                                                                                                                                                                                                    |                         |
| HRRP team in coordination with of ODRC/UNDP participated in the rural municipality level meeting in Gandaki rural municipality. The meeting was chaired by Gandaki rural municipality chairperson, Mr. Hom Bahadur Rana Magar and with chief guest Er. Ram Sharan Acharya, GMALI chief, Gorkha. Some key points and highlights of the meeting have been detailed in the field visit section below.                                                                                                                                                                                                                | 21 <sup>th</sup> January 2018 | 30                   | 11     | <a href="mailto:techcord.gorkha@hrrpnepal.org">techcord.gorkha@hrrpnepal.org</a> ; <a href="mailto:im.gorkha@hrrpnepal.org">im.gorkha@hrrpnepal.org</a>                                                            | See field visit section |
| HRRP district technical coordinator, Mr. Atit Shrestha, participated in the launch of People 2 People (P2P) program of IOM and Gorkha urban municipality in Gorkha. Under the P2P program, IOM will support in construction of 1 evacuation center in Gorkha urban municipality and with coordination support of Gorkha urban municipality have proposed Chhepatar, Gorkha urban municipality ward no 10 as the construction site. The Mayor of Gorkha urban municipality, Mr. Rajan Raj Panta inaugurated the P2P program and asked for the support of everyone for the successful implementation of the program | 25 <sup>th</sup> January 2018 |                      |        | <a href="mailto:techcord.gorkha@hrrpnepal.org">techcord.gorkha@hrrpnepal.org</a>                                                                                                                                   |                         |
| HRRP team in coordination with ODRC/UNDP organized and participated in the rural municipality level meeting in Siranchowk rural municipality. The meeting was chaired by Siranchowk rural municipality chairperson, Mr. Raju Gurung and with chief guest Er. Ram Sharan Acharya, GMALI chief, Gorkha. Some key points and highlights of the meeting have been detailed in the field visit section below.                                                                                                                                                                                                          | 25 <sup>th</sup> January 2018 | 41                   | 4      | <a href="mailto:techcord.gorkha@hrrpnepal.org">techcord.gorkha@hrrpnepal.org</a>                                                                                                                                   | See field visit section |
| HRRP team in coordination with ODRC/UNDP jointly organized and participated in the rural municipality level meeting at Shahid Laxan rural municipality. The meeting was chaired by Shahid Laxan rural municipality chairperson, Mr. Ramesh Babu Thapa Magar and with chief guest Er. Ram Sharan Acharya, GMALI chief, Gorkha. Some key points and highlights in the meeting have been detailed in field visit section.                                                                                                                                                                                            | 28 <sup>th</sup> January 2019 | 32                   | 4      | <a href="mailto:dc.gorkha@hrrpnepal.org">dc.gorkha@hrrpnepal.org</a>                                                                                                                                               | Field Visit section     |
| HRRP/GMALI organized monthly coordination meeting in the district. The meeting was chaired by the GMALI representative Mr. Shivaji Prasad Dhungana and participated by the active POs in the district. Some of the key points discussed in the meeting are:                                                                                                                                                                                                                                                                                                                                                       | 29 <sup>th</sup> January 2019 | 20                   | 5      | <a href="mailto:dc.gorkha@hrrpnepal.org">dc.gorkha@hrrpnepal.org</a> , <a href="mailto:techcoord@hrrpnepal.org">techcoord@hrrpnepal.org</a> , <a href="mailto:im.gorkha@hrrpnepal.org">im.gorkha@hrrpnepal.org</a> | Meeting minute          |

## Summary of events during this period

|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |  |  |  |  |  |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|--|--|--|--|
| <ul style="list-style-type: none"> <li>Follow up and action points for the previous month's meeting parking lot agenda – reconstruction completion certificate – and for this POs in coordination with respective rural and urban municipalities will distribute reconstruction certificate and further similarity in certificate quality will be ensured in all palikas.</li> <li>Landless issues were broadly discussed, and further issues were also noted, for instance, PA agreement of landless beneficiaries that there were six landless beneficiaries who can't have made PA agreement so far, and with the regular initiation of by PIN/CSRC in the district and so far, there are 47 issue were solved.</li> <li>The meeting also had discussion regarding one room houses status and possibility of its assessment to figure out the exact number of such houses in the district.</li> </ul> |  |  |  |  |  |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|--|--|--|--|

## Upcoming Events & Meetings

| Name of activity/event                         | Date, Time, and Location                                                      | Organizer                                    | Contact Person                                                                                                                                                                                                                       |
|------------------------------------------------|-------------------------------------------------------------------------------|----------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Joint Monitoring with M&E CLPIU and DLPIU team | 7 <sup>th</sup> February 2019, 10 am, Vaachek, Mucchowk, Ajirkot Municipality | HRRP/GMALI                                   | <a href="mailto:dc.gorkha@hrrpnepal.org">dc.gorkha@hrrpnepal.org</a> ;<br><a href="mailto:techcord.gorkha@hrrpnepal.org">techcord.gorkha@hrrpnepal.org</a> ;<br><a href="mailto:im.gorkha@hrrpnepal.org">im.gorkha@hrrpnepal.org</a> |
| Palika level coordination meeting              | 13 <sup>th</sup> February 2019, 10 am, Vaachek, Ajirkot Municipality          | Ajirkot Rural Municipality, HRRP/GMALI, ODRC | <a href="mailto:dc.gorkha@hrrpnepal.org">dc.gorkha@hrrpnepal.org</a> ;<br><a href="mailto:techcord.gorkha@hrrpnepal.org">techcord.gorkha@hrrpnepal.org</a> ;<br><a href="mailto:im.gorkha@hrrpnepal.org">im.gorkha@hrrpnepal.org</a> |

- Lapraki questions for delay in construction of integrated settlement
- A separate guideline of reconstruction endorsed by local level
- A Mobile Revolving Fund in Gorkha for EQ beneficiaries

[illegible]

- Materials Revolving Funding started into Gandaki Rural Municipality  
<https://www.onlinekhabar.com/2019/01/738305#.XFGcK437qkA.facebook>


## गोरखामा भूकम्पपीडितका लागि सामान घुम्तीकोष




## Tranche Status

| Rural /Municipality       | Aarughat                                                                                                                | Ajirkot | Bhimsen | Chum Nubri | Dharche | Gandaki | Gorkha | Palungtar | Sahid Lakhani | Siranchok | Sulikot |
|---------------------------|-------------------------------------------------------------------------------------------------------------------------|---------|---------|------------|---------|---------|--------|-----------|---------------|-----------|---------|
| Total HHs Surveyed        | 6919                                                                                                                    | 4169    | 6616    | 2132       | 3905    | 5790    | 13413  | 11362     | 7494          | 6951      | 7160    |
| Total HHs Eligible        | 6911                                                                                                                    | 4123    | 6834    | 2275       | 4169    | 5603    | 10094  | 9700      | 7059          | 6819      | 7181    |
| Total HHs Enrolled        | 6659                                                                                                                    | 3955    | 6635    | 1812       | 3731    | 4815    | 9133   | 8309      | 6082          | 5922      | 6856    |
| First Tranche             | 6659                                                                                                                    | 3955    | 6635    | 1812       | 3731    | 4815    | 9133   | 8309      | 6082          | 5922      | 6856    |
| Second Tranche            | 5948                                                                                                                    | 3682    | 5980    | 1480       | 2916    | 3711    | 7727   | 6498      | 4985          | 5224      | 6382    |
| Third Tranche             | 4795                                                                                                                    | 3194    | 4746    | 1114       | 2550    | 2557    | 6849   | 4929      | 4188          | 4255      | 5721    |
| Total HH Constructed      | 4795                                                                                                                    | 3194    | 4746    | 1114       | 2550    | 2557    | 6849   | 4929      | 4188          | 4255      | 5721    |
| Grievance Registered      | 16622 (Total in district)                                                                                               |         |         |            |         |         |        |           |               |           |         |
| Grievance Addressed       | 967                                                                                                                     | 452     | 941     | 279        | 1121    | 1390    | 2496   | 3770      | 2282          | 2023      | 901     |
| RF HH Eligible            | 171                                                                                                                     | 63      | 168     | 49         | 280     | 441     | 1079   | 1038      | 836           | 904       | 177     |
| RF HH Enrolled            | 171                                                                                                                     | 63      | 168     | 49         | 280     | 441     | 1079   | 1038      | 836           | 904       | 177     |
| RF 1st Tranche            | 30                                                                                                                      | 3       | 32      |            | 29      | 29      | 513    | 169       | 27            | 20        |         |
| RF 2nd Tranche            |                                                                                                                         |         |         |            |         |         | 6      |           |               | 1         |         |
| Non-Compliance Registered | 2413 (Total in district)                                                                                                |         |         |            |         |         |        |           |               |           |         |
| Non-Compliance Addressed  | 58-Failed for tranche<br>2298- Recommended for 2 <sup>nd</sup> Tranche<br>2139- Recommended for 3 <sup>rd</sup> Tranche |         |         |            |         |         |        |           |               |           |         |


Graph of Tranche Status:

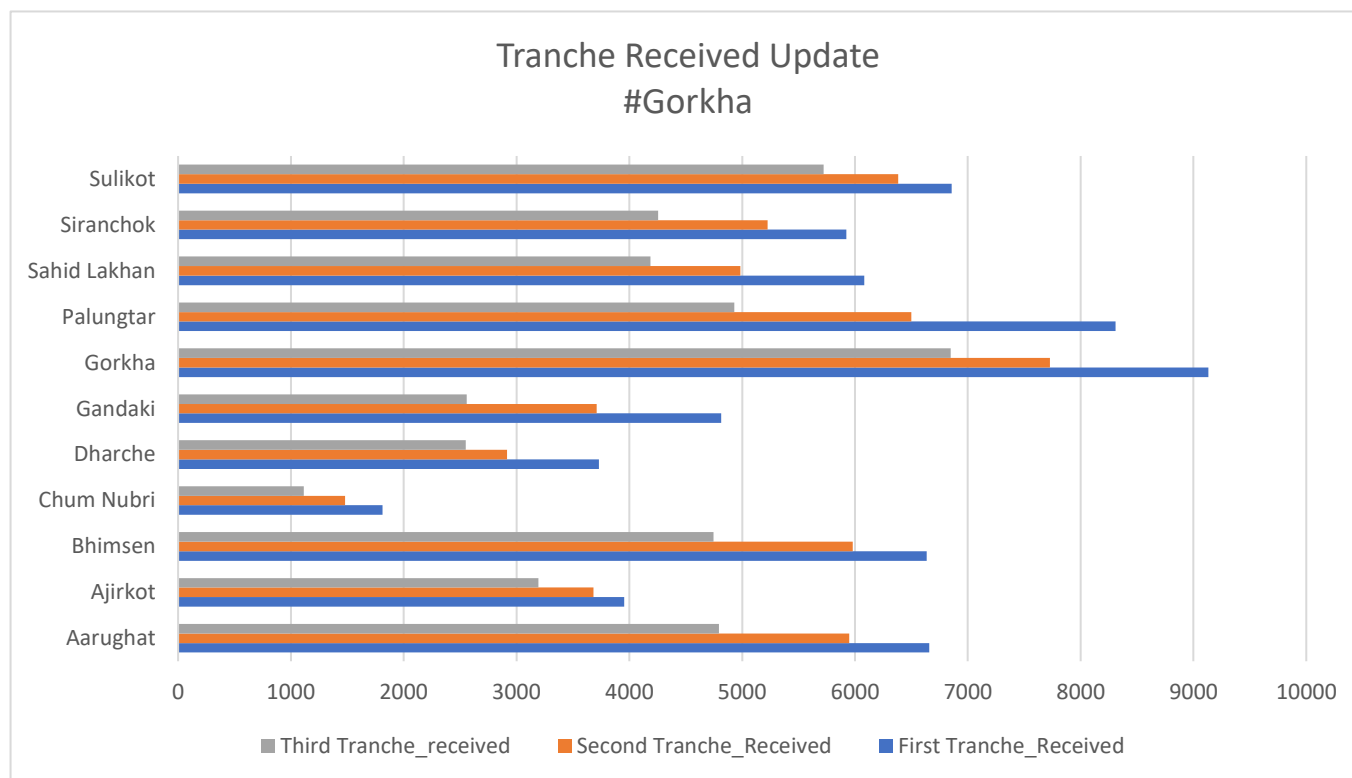

Graph for Retrofitting Status:

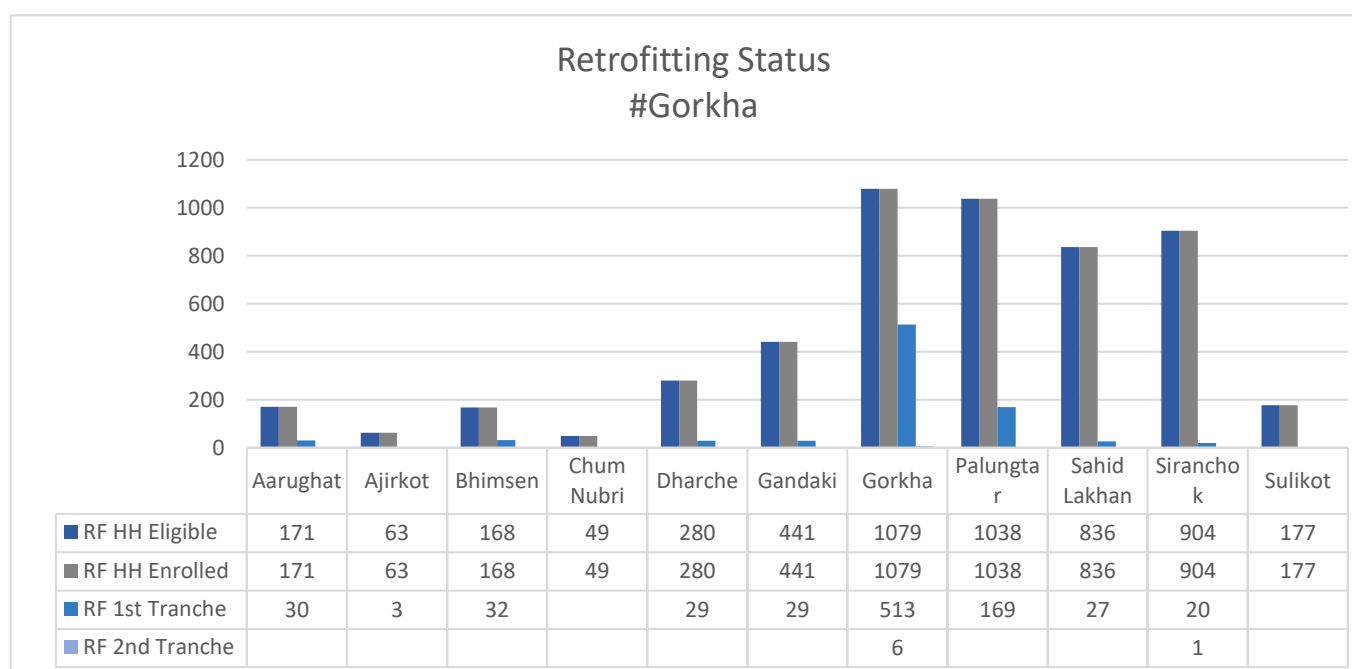

Graph for Grievance Status:

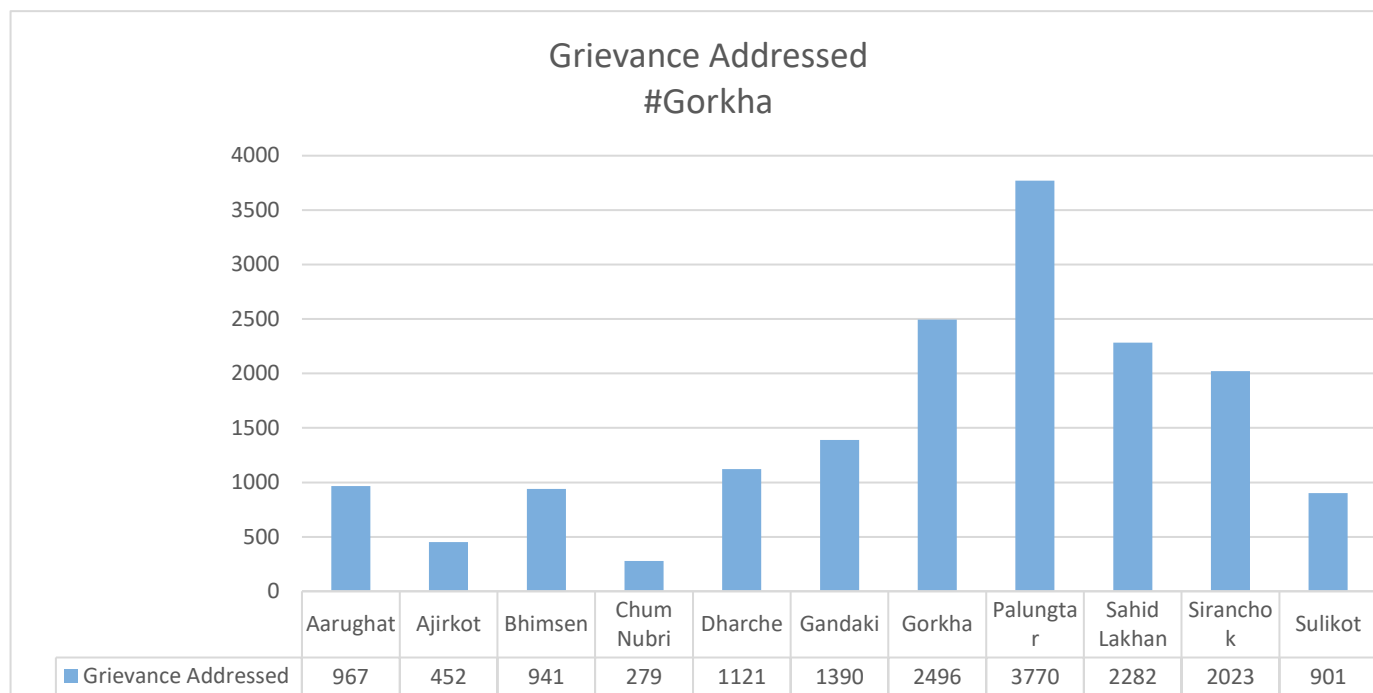

## Field Visit /Joint Field Monitoring Visit Reports

### Visit 1

| Date       | Location                                           | Participants from HRRP and stakeholders                                                                                                                                                                                                                                                                                    |
|------------|----------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 21/01/2019 | Gandaki rural municipality, ward no 6. Bhumlichowk | <ul style="list-style-type: none"> <li>Mr. Ram Sharan Acharya (Chief GMALI) and GMALI team</li> <li>Mr. Atit Shrestha (DTC, HRRP)</li> <li>Mr. Birodh Kattel (DIMO, HRRP)</li> <li>Mr. Ram Sapkota (DC, ODRC)</li> <li>Mr. Ghanshyam Khatiwada (Social Expert, ODRC)</li> <li>Mr. Sitaram Shrestha (ED, SSICDC)</li> </ul> |

### Objective(s)

- Gandaki rural municipality level meeting with POs and Palika stakeholders regarding reconstruction
- Observation of reconstruction activities of POs at field level

### Summary

HRRP team with ODRC/UNDP team travelled to Bhumlichowk, Gandaki rural municipality. The main agenda of the field visit was palika level meeting and observation of reconstruction activities of ODRC at field level of Gandaki rural municipality. HRRP along with ODRC/UNDP participated in the rural municipality level meeting in Gandaki rural municipality. The meeting was chaired by Gandaki rural municipality chairperson, Mr. Hom Bahadur Rana Magar and with chief guest Er. Ram Sharan Acharya, GMALI chief, Gorkha. Some key points and highlights from the meeting:

- ODRC/UNDP presented the reconstruction status of their supported wards and HRRP presented the reconstruction status of other wards of Gandaki rural municipality.
- During the interaction session GMALI chief responded to the queries from municipal authorities regarding beneficiary's duplication, removal of people from the reconstruction beneficiaries list, delay in payment of tranche and holdup of tranche of beneficiaries in banks. GMALI chief responded by sharing the current working of GMALI at district level and assured of full support and policy procedure for removal of beneficiaries.
- Mr. Hom Bahadur Rana Magar, chairperson of Gandaki rural municipality shared his dissatisfaction about the present reconstruction progress of Gandaki rural municipality and asked for more follow up with beneficiaries from ward chairpersons and member for pushing the progress. He also shared that rural municipality will again organize palika level meeting for sharing the progress within 2 months and closed the meeting.

After the meeting, the team of HRRP and district team of ODRC interacted with the field team of ODRC regarding progress of reconstruction in ODRC supported wards of Gandaki rural municipalities. ODRC is supporting 3 wards (ward no. 2, 1 and 6 i.e previous Tanglichowk vdc, Makaising vdc. and Bhumlichowk vdc) of Gandaki rural municipalities with socio technical facilitation. The progress of housing reconstruction in those 3 wards is good (nearly 75%) as compared to other wards, as shared by cluster coordinator of ODRC. There are issues of beneficiaries who are not willing to reconstruct their houses. The name of those beneficiaries has been submitted to the ward offices and follow up with those beneficiaries will be done by both ward offices and ODRC team for either start construction of their houses or return the first tranche amount. Similarly, beneficiary's duplication with Janta Aawas Project and process has been started to cut the name of those beneficiaries from earthquake beneficiaries list.

After that the team headed back to Gorkha bazaar.

| Challenges / Issues Identified                                                                              | Action Required                                                                                                                                                                                       | Responsible                                  | Time Frame          |
|-------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------|---------------------|
| Cut of name of beneficiaries not willing to reconstruct their houses from reconstruction beneficiaries list | Need to follow up with the beneficiaries who are not willing to do reconstruction of their houses and advise them to return the first tranche amount to GMALI Gorkha as per the procedure set by NRA. | Ward offices, rural municipalities and GMALI | As soon as possible |



## Photos



Caption: Er. Ram Sharan Acharya, Chief, GMALI Gorkha, responding to queries from everyone present in the palika level meeting



Caption: Mr. Birodh Kattel, DIMO HRRP presenting the reconstruction status of overall Gandaki rural municipality.

## Field Visit /Joint Field Monitoring Visit Reports

### Visit 2

| Date       | Location                                           | Participants from HRRP and stakeholders                                                                                                                                                                                                                                                                               |
|------------|----------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 25/01/2019 | Siranchowk rural municipality, ward no 5, Chhoprak | <ul style="list-style-type: none"> <li>Mr. Ram Sharan Acharya (Chief GMALI) and GMALI team</li> <li>Mr. Yubak Shrestha (DLPIU Building Focal Person)</li> <li>Mr. Bikendra Khaytu (Engineer, DLPIU Building)</li> <li>Mr. Atit Shrestha (DTC, HRRP)</li> <li>Mr. Ghanshyam Khatiwada (Social Expert, ODRC)</li> </ul> |

### Objective(s)

- Siranchowk rural municipality level meeting with POs and Palika stakeholders regarding reconstruction
- Observation of reconstruction activities of POs at field level

### Summary

HRRP team in coordination with ODRC/UNDP team travelled to Chhoprak, Siranchowk rural municipality. The main agenda of the field visit was palika level meeting and observation of reconstruction activities of ODRC at field level of Siranchowk rural municipality. HRRP along with ODRC/UNDP participated in the rural municipality level meeting in Siranchowk rural municipality. The meeting was chaired by Siranchowk rural municipality chairperson, Mr. Raju Gurung and with chief guest Er. Ram Sharan Acharya, GMALI chief, Gorkha and Er. Yubak Shrestha, Focal Person DLPIU Building as guest. Some key points and highlights from the meeting:

- GMALI chief Er. Ram Sharan Acharya presented the progress status and key issues and working procedure in Gorkha district (progress specific of Siranchowk rural municipality)
- ODRC/UNDP presented the reconstruction status of their supported wards of Siranchowk rural municipality.
- During the open interaction session GMALI chief responded to the queries from municipal authorities regarding beneficiary's duplication, removal of people from the reconstruction beneficiaries list, beneficiaries listed in house in another place, resurvey and reverification. GMALI chief responded by sharing the current working of GMALI at district level and assured of full support. He also shared about provision in



policy for house in another place and shared that unless changes in policy, the people listed there cannot be changed.

- Mr. Raju Gurung, chairperson of Siranchowk rural municipality shared his dissatisfaction about the present procedure for punarabedhan (reapply for inclusion in reconstruction beneficiaries list) and issue of house in another place. Mr. Raju Gurung also asked GMALI chief of Gorkha to coordinate with central NRA for changes in policy regarding this.
- He also closed the meeting after his comments

After the meeting, the team of HRRP and district team of ODRC interacted with the field team of ODRC regarding progress of reconstruction in ODRC supported wards of Siranchowk rural municipalities. ODRC is supporting 5 wards (ward no. 2, 3, 4, 5 and 6 i.e previous Thalajung vdc, Harmi vdc, Chhoprak and Gaankhu vdc) of Siranchowk rural municipalities with socio technical facilitation. The progress of housing reconstruction in Siranchowk rural municipality is good (71.85% progress as 3 wards are covered by EHRP JICA and 5 wards by ODRC/UNDP). There are issues of beneficiaries who are not willing to reconstruct their houses. The name of those beneficiaries has been submitted to the ward offices and follow up with those beneficiaries will be done by both ward offices and ODRC team for either start construction of their houses or return the first tranche amount. After that the team headed back to Gorkha bazaar.

| Challenges / Issues Identified                                                                                                                                                                                | Action Required                                                                                                                                                                                                         | Responsible                                  | Time Frame          |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------|---------------------|
| Beneficiaries who are listed under house in another place (HOAP) in grievance result but don't have house in another place. How can these beneficiaries be included in earthquake housing beneficiaries list? | Ward offices and rural municipality office need to verify that the beneficiaries don't have house in another place and forward the documents to GMALI office, for further coordination with NRA for further processing. | Ward offices, rural municipalities and GMALI | As soon as possible |

#### Photos



Caption: Er. Ram Sharan Acharya, Chief, GMALI Gorkha, responding to queries from everyone present in the palika level meeting



Caption: Mr. Raju Gurung, chairperson, Siranchowk rural municipality sharing his views to everyone present in the palika level meeting

## Field Visit /Joint Field Monitoring Visit Reports

### Visit 3

| Date       | Location                                               | Participants from HRRP and stakeholders                                                                 |
|------------|--------------------------------------------------------|---------------------------------------------------------------------------------------------------------|
| 28/01/2019 | Shahid Lakhani rural municipality, ward no 6, Ghairung | <ul style="list-style-type: none"> <li>• Mr. Ram Sharan Acharya (Chief GMALI) and GMALI team</li> </ul> |

|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              |                                                                                                                                                                                                                                    |                                                                                                                                                                                               |                     |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              |                                                                                                                                                                                                                                    | <ul style="list-style-type: none"><li>• Mr. Yubak Shrestha (DLPIU Building Focal Person)</li><li>• Mr. Chandra Gurung, HRRP</li><li>• Mr. Ghanshyam Khatiwada (Social Expert, ODRC)</li></ul> |                     |
| Objective(s)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 |                                                                                                                                                                                                                                    |                                                                                                                                                                                               |                     |
| <ul style="list-style-type: none"><li>• Shahid Lakhan rural municipality level meeting with POs and Palika stakeholders regarding reconstruction</li><li>• Also, field monitoring of reconstruction activities of POs at field level</li></ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |                                                                                                                                                                                                                                    |                                                                                                                                                                                               |                     |
| Summary                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |                                                                                                                                                                                                                                    |                                                                                                                                                                                               |                     |
| <p>HRRP team with ODRC/UNDP team travelled to Shahid Lakhan rural municipality. The main agenda of the field visit was palika level meeting and monitoring of reconstruction activities at field level of Gandaki rural municipality. HRRP along with ODRC/UNDP participated in the rural municipality level meeting at Shahid Lakhan rural municipality. The meeting was chaired by Shahid Lakhan rural municipality chairperson, Mr. Ramesh Thapa Magar and with chief guest Er. Ram Sharan Acharya, GMALI chief, Gorkha and Er. Yubak Shrestha, Focal Person DLPIU Building as guest. Some key points and highlights from the meeting:</p> <ul style="list-style-type: none"><li>• ODRC/UNDP presented the reconstruction status of their supported wards and progress of private housing reconstruction status with their socio-technical support</li><li>• HRRP presented the reconstruction status of rural municipality level reconstruction status and urged to initiate local level reconstruction action plan, palika profiles and palika level profiles updates in the respective website.</li><li>• In the interaction session GMALI chief responded to the queries from municipal authorities regarding beneficiary’s duplication, removal of people from the reconstruction beneficiaries list, delay in payment of tranche and holdup of tranche of beneficiaries in banks. GMALI chief responded by sharing the current working of GMALI at district level and assured of full support and policy procedure for removal of beneficiaries.</li><li>• Mr. Ramesh Babu Thapa Magar, chairperson of Shahid Lakhan rural municipality shared his efforts palika is undertaking to expediate the reconstruction. He strongly added to conclude the process of housing reconstruction by clearly identifying the ones who are not willing to build their houses even if they have already taken the first tranche and certain special cases can be considered for the vulnerable beneficiaries.</li><li>• He also shared that rural municipality set a provision of mobile fund to provide lend to the beneficiaries to construct their houses up to one hundred thousand in each nine wards.</li></ul> <p>the team of HRRP/GMALI team including ODRC interacted with the field team of ODRC regarding progress of reconstruction in ODRC supported wards of rural municipalities. There are issues of beneficiaries who are not willing to reconstruct their houses. The name of those beneficiaries has been submitted to the ward offices and follow up with those beneficiaries will be done by both ward offices either they should start construction of their houses or return the first tranche amount.</p> |                                                                                                                                                                                                                                    |                                                                                                                                                                                               |                     |
| Challenges / Issues Identified                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | Action Required                                                                                                                                                                                                                    | Responsible                                                                                                                                                                                   | Time Frame          |
| Beneficiaries who are still not starting to construct their houses                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | Need to identify if those beneficiaries really want to build the houses or not. If they are vulnerable – socio-economically, they ward or rural municipality will consider such issues, otherwise, rural municipality take action. | Ward offices, rural municipalities and GMALI                                                                                                                                                  | As soon as possible |
| Photos                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |                                                                                                                                                                                                                                    |                                                                                                                                                                                               |                     |






Caption: Er. Ram Sharan Acharya, Chief, GMALI Gorkha, responding to queries from everyone present in the meeting



Caption: Mr. Ramesh Babu Thapa Magar, chairperson, Shahid Lakhan rural municipality sharing his views in the meeting

## Housing Typology Report

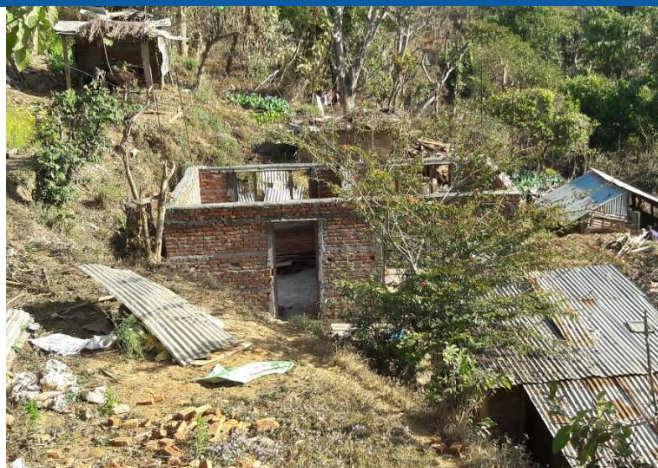

Caption: Nirmala Kattel's brick masonry cement mortar house in Gorkha urban municipality ward no. 8, Katteldanda. The house owner has received second tranche.

Photo Courtesy: Birodh Kattel, HRRP



Caption: Sudarshan Kattel's RCC house in Gorkha urban municipality ward no. 8, Katteldanda. The house owner has not received second or third tranche.


Photo Courtesy: Birodh Kattel, HRRP





Caption: Under construction house at plinth level in integrated settlement of Milan Basti in Bhimsen Thapa rural municipality, ward no. 5, Baguwa. Name of the house owner and tranche status unknown. This house will be constructed with CSEB blocks with RCC band (superstructure)

Photo Courtesy: Atit Shrestha, HRRP

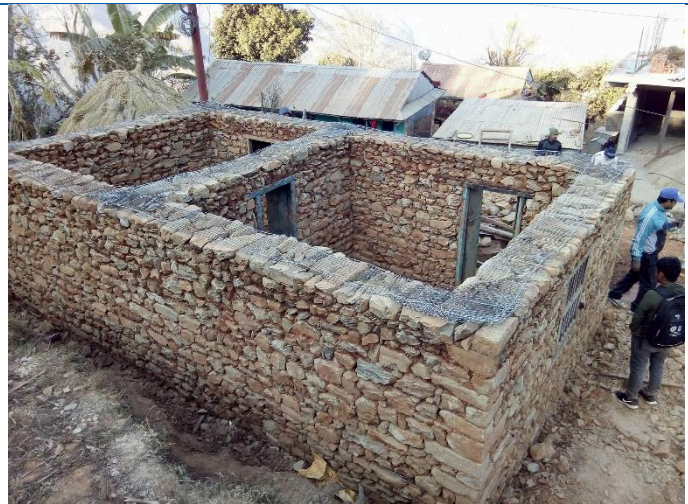

Caption: Dil kumari Gurung's stone masonry mud mortar house with guided wire mesh band in Gandaki rural municipality ward no. 2, Tanglichowk. The house is constructed with guided wire mesh in bands. This house has been constructed with the technical support of ODRC/UNDP

Photo Courtesy: ODRC/UNDP team

## Questions Collected

| Question                                                                                                                               | Who Asked the Question? | Response Provided (By Whom)                                                                                                                                                          |
|----------------------------------------------------------------------------------------------------------------------------------------|-------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| How can beneficiaries willing to return tranche money get information regarding procedure about the returning of first tranche amount? | Beneficiaries           | Beneficiaries can get the information from the GMALI office in the district or contact the NRA hotline number for the information regarding how to return the tranche money. (GMALI) |
| Should beneficiaries follow the right of way rule or not during house reconstruction?                                                  | Beneficiaries           | NRA does not have any role in this. Beneficiaries should coordinate with local bodies and act accordingly for reconstruction of houses. (GMALI)                                      |

## Challenges and Way Forward

| Challenge                                                                                | Way Forward                                                                                                                                                                                              |
|------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Masons with skills for carrying out retrofitting work                                    | Organize skill training/OJT for masons to transfer the knowledge of different retrofitting techniques to masons.                                                                                         |
| Issuing construction completion certificate to household who have completed construction | Carrying out final inspection of house by DLPIU engineers and issuing construction completion certificate in coordination with ward offices, rural/urban municipality offices, DLPIU building and GMALI. |

## Case Story

### Technical Support to beneficiaries

50 years old Bishnu Maya Devkota has long term health problem. She has 6 family members in her family. Her husband also has long term health problem. Her house was collapsed on Earthquake. After April Earthquake, they were living on CGI made temporary shelter. She doesn't have any technical ideas and economic capacity to build new house. During the tole reconstruction committee meeting supported by Nepal Housing Reconstruction Project (ODRC/UNDP); she was presented as a vulnerable beneficiary with problem to reconstruct her house.

After that, ward office also declared her name in vulnerable list. Ward office and Nepal Housing Reconstruction Project decided to help Devkota family during construction process. As they spend first tranche in medical treatment, they do not have money to pay mason. As their economic condition is very bad, local masons refuse to work on their construction. They had arranged some construction materials but not enough to start construction.

NHRP team helped her in arranging the required materials and supported her in construction through their trained mason. After three working days of construction through the ANS (trained masons) and technical team; Devkota family's house is built up to DPC level and eligible for 2<sup>nd</sup> tranche recommendation.

ANS Sita Devi helps them for second tranche process by linking up with DLPIU Engineer. She is regularly visiting Devkota family's house during critical stages of construction.



House owner Bishnu Maya Devkota during construction.
