

Monthly District Report

Kathmandu

9 May - 13 June 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Kathmandu	Joint M & E Visit of HRRP Kathmandu and DLPIU- building Kathmandu.	13 May 2019	Nagarjun Municipality , Kathmandu	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	Field visit section
	Interaction program with the focal person of 1 Metropolitan City and 10 Municipalities of Kathmandu district	20 May 2019	DCC hall, Babarmahal, Kathmandu	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	Minutes
	Meeting with Sheetal Shakya from SOUP/ Shapla Neer for timely update of 5W and PO's participation in meetings.	24 May 2019		Sachin Malego IM Officer Contact: 9842062006 sachin.malego@hrrp.nepal.org	Remarks: SOUP/Shapla Neer has now started a timely 5W update from this month's 5W.
	A general municipal coordination meeting	29 May 2019	Shankharapur Municipality	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	Minutes
	A general municipal coordination meeting	29 May 2019	Gokarneshwor Municipality	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	Minutes
	A general ward level coordination meeting	29 May 2019	Baluwa, Ward no 3, Gokarneshwor Municipality	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	Minutes

Summary of events during this period

	District Facilitation and Coordination Meeting of the Kathmandu district	2 June 2019	Dining Park, New Baneswor	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	Report
	Update of the housing typology in GD and Flickr	11 May –13 June 2019		Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	
	Update of the calendar, District activities in HRRP website, update of contact list	11 May –13 June 2019		Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrp.nepal.org	
	Update of 5W and Palika profile of Kathmandu district	11 May –13 June 2019		Sachin Malego IM Officer Contact: 9842062006 sachin.malego@hrrp.nepal.org	
	Debugging of dead links in HRRP's website	11 May –13 June 2019		Sachin Malego Saujan Shrestha	
	Preparation of list of PO's whose data needs to be verified in 5W and follow up with POs	11 May –13 June 2019		Sachin Malego IM Officer Contact: 9842062006 sachin.malego@hrrp.nepal.org	
	5W data segregation and dissemination of all PO's working and phased out.	11 May –13 June 2019		Sachin Malego IM Officer Contact: 9842062006 sachin.malego@hrrp.nepal.org	Segregated data

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Joint Monitoring visit to different Municipalities of Kathmandu district along with DLPIU- Building Kathmandu, M&E consultant, District Support	TBD, Kathmandu Metropolitan City Municipality	DLPIU Building, Kathmandu and HRRP	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org

Upcoming Events & Meetings

engineers and DLPIU technical staffs deployed at Municipality and ward level.			
Municipality level meeting to address the issues of the non-enrolled beneficiaries, vulnerable beneficiaries.	13 June – 13 July	GMaLI- Kathmandu, HRRP	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org
Updating of the Municipality profile and the action plan every month and coordinate to upload the information in Municipalities websites	13 June – 13 July	HRRP Kathmandu	Sachin Malego IM Officer Contact: 9842062006 sachin.malego@hrrpnepal.org

News & Updates


- Er. Hari Prasad Sharma has been appointed as Chief of DLPIU NRA GMaLI Kathmandu.
- GMaLI has send the list of non-enrolled beneficiaries of all Municipalities in Kathmandu district and has requested the Municipality authority to coordinate with the ward representative to address the issues by either encouraging them to sign the reconstruction grant agreement as soon as possible or remove their name from the beneficiary list.
- In lead of DLPIU-Building the resurvey and reverification of the Grievance is being collected in Kathmandu District.

Tranche Status (Kathmandu)


Tranche Status Table:

Name of Municipality	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Budhanilakantha Municipality	2740	2694	2078	2078	1061	855	11	1	1	1
Chandragiri Municipality	6414	5906	4876	4769	1447	1245	128	46	46	0
Dakshinkali Municipality	3542	4087	3805	3805	1586	1037	52	32	32	0
Gokarneshwor Municipality	2870	2939	2564	2564	1538	1233	20	8	8	0
Kageshwori Manahora Municipality	3741	3678	3295	3295	1776	1168	75	25	25	0
Kathmandu Metropolitan City	8738	7561	6002	6002	1445	1184	173	34	34	0
Kirtipur Municipality	3758	3231	2495	2489	952	782	44	20	20	0
Nagarjun Municipality	4315	4447	4109	4109	1526	1222	38	5	5	0
Shankharapur Municipality	6032	6102	5564	5564	2891	1856	110	42	42	0
Tarakeshwor Municipality	6737	6174	5245	5245	2143	1753	107	33	33	0
Tokha Municipality	2237	1749	1592	1592	700	573	48	26	26	0

Graph of Tranche Status:

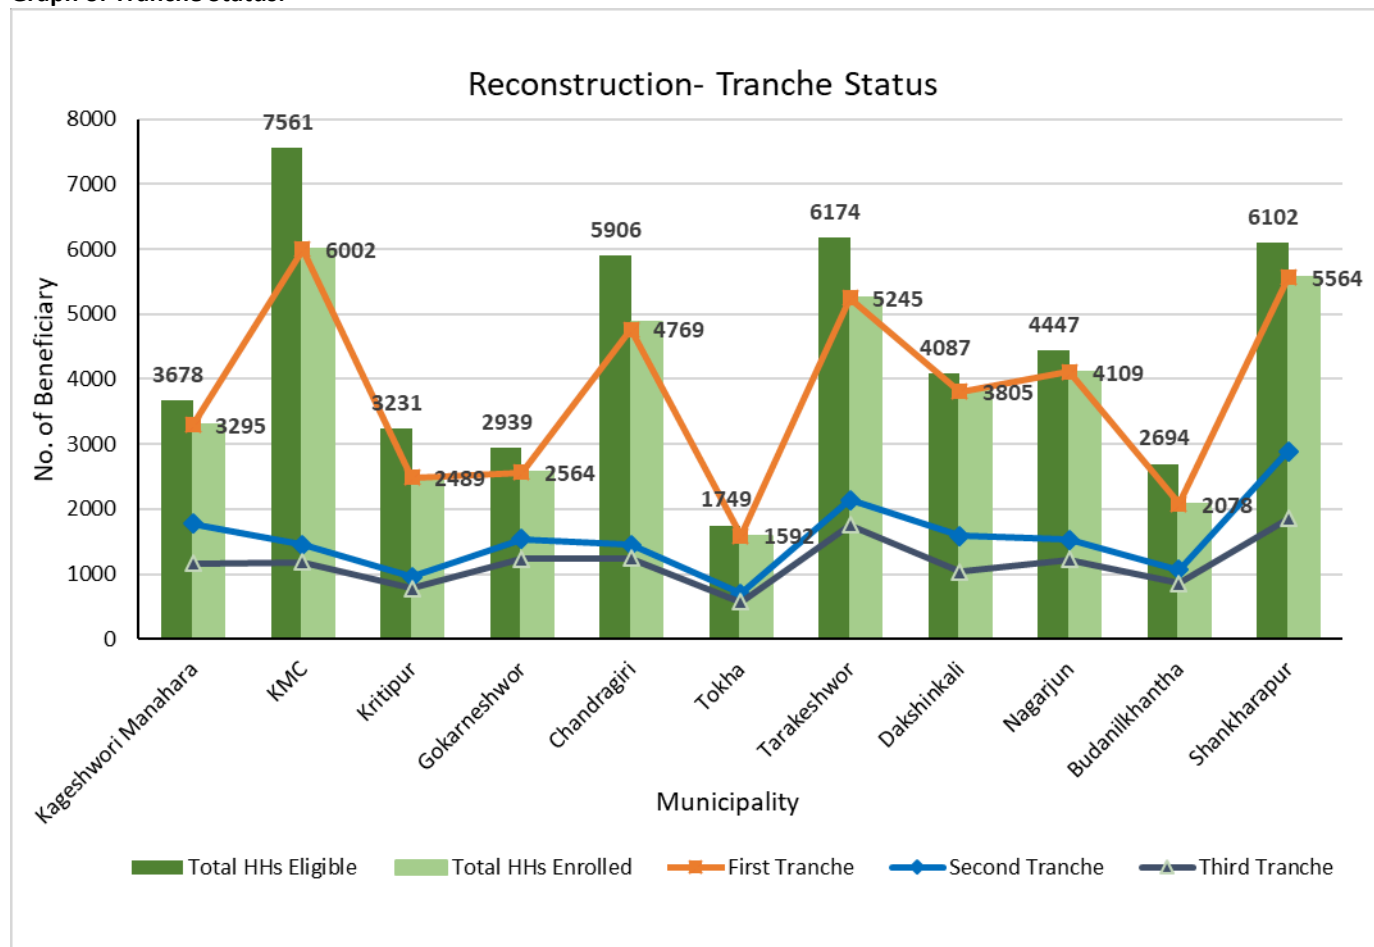

Graph for Retrofitting Status:

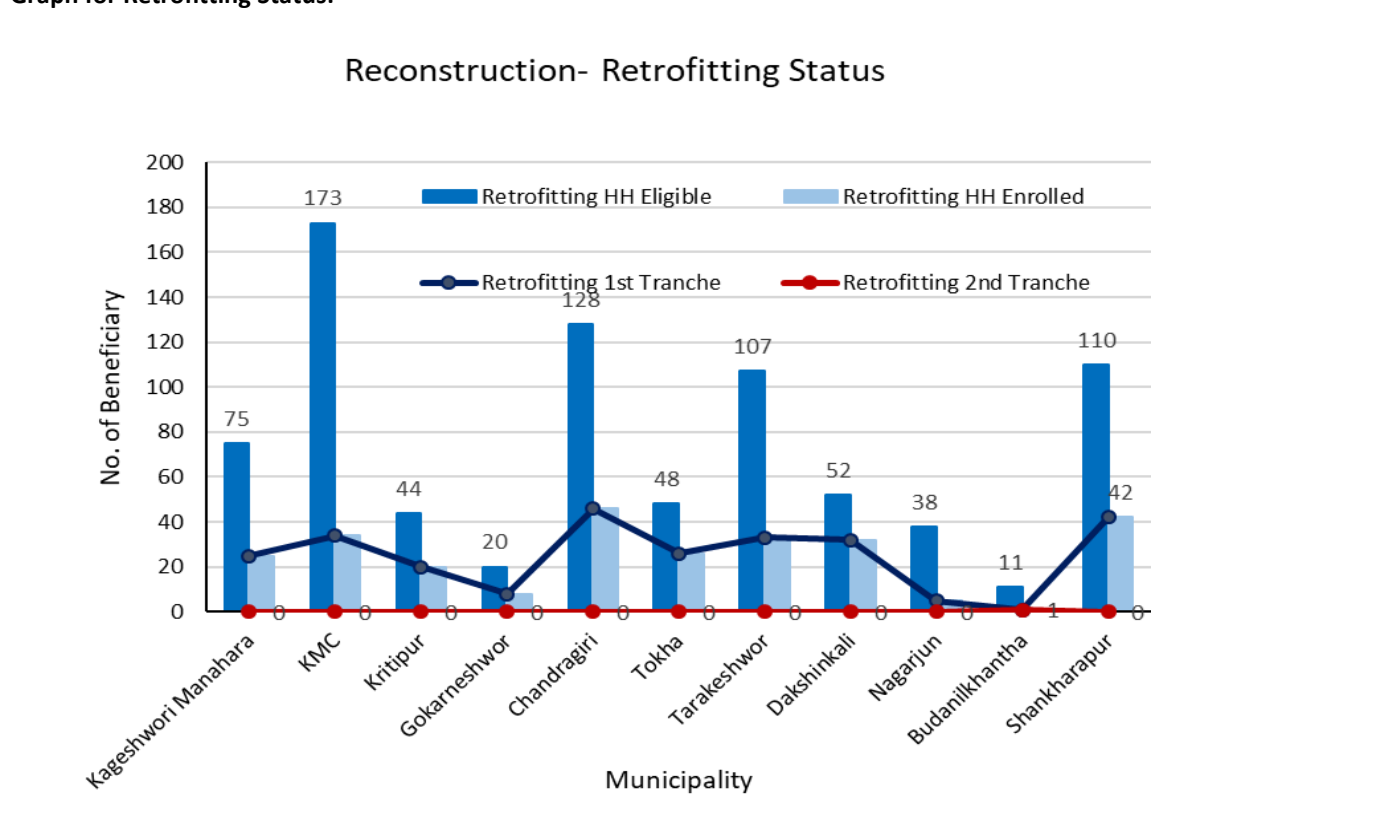

Field Visit Reports (Kathmandu)

Visit 1

Date	Location	Participants
13 May 2019	Ward no. 3, 5, 6, Nagarjun Municipality	- Bidhya Manandhar (DSE) - Prajwal Karki (DSE), - Sanam Lakhey (DLPIU- Kathmandu) - DLPIU Engineers- Nagarjun Municipality (Poonam Pandey, Roshani Shrestha, Dip Kumar Giri, Yogendra Kunwar) - Sweata Sijapati, HRRP, Kathmandu
Objective(s)	- To observe the non-compliant houses and to provide way forward regarding the technical assistance. - To interact with beneficiaries to understand the reconstruction issues and status - To collect housing typology	

Why was the visit carried out in this location?

The field visit was targeted to this site due to high number of non-compliance cases especially in Hybrid construction using two or more material in a single-story structure. As the beneficiaries were not convinced by the correction measures suggested by the technical staff, the visit was accompanied by the district support engineers.

Summary

Field Visit:

HRRP Kathmandu along DSE and technical staffs from DLPIU Building conducted joint field monitoring at Ward no 3 , 5 and 6 of Nagarjun Municipality, Kathmandu district. The field visit was mainly focused on the observation of the Non-compliance cases and beneficiaries claiming for the 2nd and 3rd tranches in the area. During the visit DSEs suggested the possible correction measures and way forward to the beneficiaries for being eligible for the tranche. In total 11 houses were visited among which majority of the houses were hybrid structure. Similarly, the other non -compliance case was 9"X12" column in more than 2 storey structure and houses missing the earthquake resistant elements and so on.

In total 11 HHs were visited among which 2 beneficiaries has still not signed the PA agreement due to lack of landownership issues. Before beginning the field visit a brief meeting with the technical staffs deployed in the municipality was conducted to identify the measure issues and the selection of the household to be visited.

During the meeting the measures issues highlighted by the technical staffs were

- Construction of hybrid structure using multiple materials in a single storey
- Non-compliance houses constructed before the NRA guidelines
- Missing of earthquake resistant elements especially roof bands

Previous meeting conducted in the Municipality : https://drive.google.com/open?id=1K2YDAgBTviYD1Gg-p7_3a4ibYtdQisNP

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
The houses constructed were found to be constructed without the earthquake resistant elements such as vertical reinforcements and so on.	The beneficiary was suggested to add the band for the exterior of the wall and the vertical reinforcement in the corners	The beneficiary agreed to apply the correction measures as per suggested by the DSE.	Beneficiary, Technical staffs	As soon as possible
Some of the beneficiaries still had not signed the PA agreement due to temporary landownership paper.	The beneficiaries were suggested to visit the GMaLI office for the possible solution in this regard.	GMaLI office will provide the details on the required documentation for the beneficiary to be eligible to sign the agreement.	Beneficiary, Municipality, GMaLI	As soon as possible

Photos				
				
Team of DLPIU-Building and HRRP along with the beneficiary during the joint monitoring visit		District Support Engineers suggesting the correction measure for the non-complaint structure		

Housing Typology Report



Beneficiary name: Shiva kumar Khanal, ward no 4, Nagarjun Municipality. Hybrid structure where vertical member missing, the connection of the steel post and the roof is not proper.



Beneficiary name: Ram Bahadur Sarki, ward no 4, Nagarjun Municipality. One roomed BMC structure. The house is listed as non-Compliance (Missing bands and vertical reinforcement). The correction measure was suggested to the beneficiary.



Beneficiary name: Biku Maya Khadgi, ward no 6, Nagarjun Municipality. 1 and half storey Prefab structure. The house was considered unsafe due to the RC slab in the first storey



Beneficiary name: Thakuwa Pakwar, ward no 3, Nagarjun Municipality. 2 storey Reinforced Cement Concrete Framed Building (RCC). The house was found to be complaint during the visit.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Can we sign the partnership agreement with the temporary landownership documents?	Beneficiary	Yes, with the letter from the ward office and approval from the Municipality the agreement can be conducted. For more detail please visit the DLPIU- GMaLi office, Kathmandu. (HRRP)
To make my house stronger I constructed RC slab in the prefab structure but why can't I get the 2 nd and 3 rd tranche?	Beneficiary	If the structure has been made as per the technical guideline everyone will get the tranche. In this case, there will be no problem in receiving the 2 nd tranche but for the 3 rd tranche the rigid roof in light material is making the structure vulnerable so as for now the file cannot be forwarded. (DSE)

Challenges and Way Forward

Challenge	Way Forward
Majority of beneficiaries have not signed the partner agreement though being listed as beneficiary.	GMaLi in coordination with the municipality and ward office has requested to publish notice to call such beneficiaries to either sign an agreement or remove their name from the beneficiary list.
Many beneficiaries have started modifying their houses after receiving all the tranche money.	Ward office and municipality should conduct an awareness program and discourage such practice. Municipality should strictly check such houses before distributing the completion certificate.
Most of the structure constructed immediately after the earthquake and without the technical assistance are increasing the non-compliance cases.	Such houses must be suggested to apply the correction measures. For the houses which are not addressed by the correction measures, number of such houses must be collected, and NRA should make a policy to address such cases.

Case Study

Demolition of the Damaged House – An initiation to Support Vulnerable Beneficiaries



Damaged Structure of Mr. Kuma Maharjan due to 2015 Gorkha Earthquake



Temporary shelter of Mr. Kuma Maharjan made up of CGI sheets.

Mr. Kuma Maharjan residence of Thalkhu, ward no 6, Dakshinkali Municipality is listed as one of the beneficiaries under the government housing reconstruction grant program. Mr. Maharjan falls under the vulnerable group for being a senior citizen. Currently he is residing in a temporary shelter along with his brother who is also a senior citizen and physically weak and daughter who is also their caretaker. Due to poor economical and physical condition he has still not been able to demolish his damaged house and begin the reconstruction.

An orientation and consultation program was conducted in Dakshinkali Municipality by DLPIU, Grant Management and Local Infrastructure Kathmandu under the Environment and Social Management plan under the Environment and Social Management Framework. To address the issue raised during the program held on 31 December 2018 (2075/08/16) the municipality has selected debris management of Thalkhu and as their sub-project.

The site verification was carried out on 17-19/ 10/16 along with Municipality engineer and Environment and Social development specialist. As per the approved sub- project of ESMP major mitigation measures dismantling of the damaged house, management of the debris about 300m away (site recommended by the ward office). The budget of the Demolition and debris management is estimated to be approximately NRP 71,174. Mr. Maharjan has received the 1st tranche of the housing reconstruction grant. Regarding the reconstruction of the house, the ward office has taken the full responsibility of constructing two roomed load bearing brick in cement mortar masonry structure within NRP. 300,000 grant money.
