

District Report

Rasuwa

3-16 August 2018

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
As per the request from Oxfam (Mr. Bibek Ghimire) HRRP district team shared vulnerable HHs list of Uttargaya and Naukunda rural municipality. Total number of vulnerable HHs is: Uttargaya RM total HHs list=64 Naukunda RM total HHs list= 89	6-Aug,2018	1	0	BGhimire@oxfam.org.uk Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org	Click the LINK
Meal data for month of July was updated at national level. Updated events and field visits: 1)An orientation of NRA 5W event. 2)Field visit at Gosaikunda ward no.5 and kalika ward no 1.	8-Aug,2018	1	0	Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org meal@hrrpnepal.org	For Meal Data Click the LINK
On the request from Rasuwa chief district officer Mr. Krishna Poudel HRRP produce Dhunche to Gosaikunda trek map both in Nepali and English and handover at DAO office.	11-Aug,2018	3	0	im.manager@hrrpnepal.org resham@hrrpnepal.org im.rasuwa@hrrpnepal.org techcord.rasuwa@hrrpnepal.org	For Map (CLICK HERE)
As per the request from Building -DLPIU chief of Rasuwa. HRRP prepared the presentation slide and hand over to him.	12-Aug,2018	1	0	phaderadhira@gmail.com im.rasuwa@hrrpnepal.org techcord.rasuwa@hrrpnepal.org	For presentation file (CLICK HERE)
HRRP district team conducted field visit at kailka RM ward number 2 and 3. In the joint monitoring visit Mr. Bikash Acharya from TI Nepal, Hemnath Khatiwada president of Nepal press union, ward member Gita Neupanea together with HRRP team.	03-Aug to -04-Aug,2018	4	1	hemnathkhatiwada@gmail.com bikash@tinepal.org im.rasuwa@hrrpnepal.org techcord.rasuwa@hrrpnepal.org	Detail report is on field visit report section

Summary of events during this period

HRRP district team uploaded training database of more than 90 events in EHRP IMS system. As per the request from central GMALI HRRP is working in EHRP MIS for training database.	6-Aug to 15 -Aug ,2018	1	0	comms1@hrrpnepal.org im.rasuwa@hrrpnepal.org techcord.rasuwa@hrrpnepal.org	
As per the request of GMALI chief Mr. Krishna kant Upadhyaya HRRP DTC was involved in the joint field monitoring of construction material quality checking with, Mr. Sitaram Thapa (assistant CDO), Mr. Roshan Jha (DLPIU engineer) and Thaneshwor Bhushal (Planning Officer, District Coordination Committee)	16-Aug 2018	4	0	techcord.rasuwa@hrrpnepal.org im.rasuwa@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
District Coordination Meeting		GMALI/HRRP Rasuwa	Im.rasuwa@hrrpnepal.org Techcord.rasuwa@hrrpnepal.org

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date:	Location:	Participants from HRRP and stakeholders
2018-08-03 to 2018-08-04	Kailika RM ward Number 2 and 3	- Rijan Gajurel - Biren Shah - Bikash Acharya - Hemnath Khatiwada - Gita Neupane
Objective(s)	- To interact with local representative, engineers along with beneficiaries to know the reconstruction progress and challenges. - To find urban reconstruction progress and challenges.	
Summary	During the Joint monitoring visit, we have visited Kalika RM office and ward number 3,4 of the RM and discussed the reconstruction process and challenges faced by RM with vice chairperson Mr. Bhavani Parsad Neupane.	

Photos



The house belongs to Mr. Sarada Devi Acharya. She has received the third tranche of GoN housing grant. The house is a two rooms BMC structure (red colour) with truss above and light flexible CGI sheet roof. This house and the side house is of two beneficiaries, but after receiving the third tranche they laid a single truss and CGI sheet roof respectively making the house a single structure. The attached house with no colour belongs to Mr. Dunanath Acharya. This house is a one room BMC structure. The ground floor was constructed separately but while laying the top floor truss it was laid monolithically making the structure single house.




The house belongs to Mr. Aitaram Damai. The housing tranche, technical support and documentation support is done by Lumanti support group for Shelter. The house is a two room RCC structure. According to the house owner the total cost of construction was Nrs 11 lakhs and the grant was not sufficient for the construction so a loan of Rs 5 lakhs was taken by the house owner from Sahakari bikash.

Housing Typology Report



The house belongs to Mr. Ram Prasad Dhakal. The housing tranche, technical support and documentation support is done by Lumanti support group for Shelter. The construction of the house is completed. The house is a one-storey, two rooms RCC structure. An additional support of Rs 15 thousand for toilet construction and one day mason wage of 4 masons i.e. Rs 4000 was given as an additional support to the house owners.

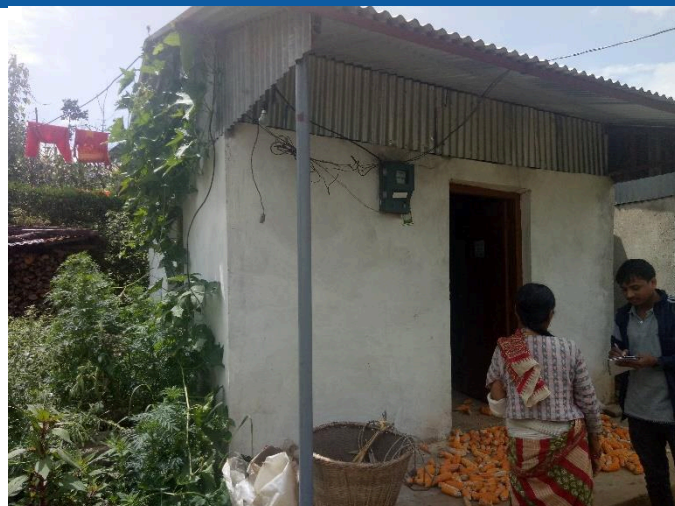

The house belongs to Mr. Ram Krishna Dhakal. He has received the third tranche of GoN housing grant. The construction of the house is completed. The house is a One room BMC structure with flexible CGI roof.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
When the certificate is distribute for construction completion certificate for construction completed HHs? Who is lead agency for this process RM, GMaLI, Building -DLPIU?	Vice chair person of Kalika RM Mr.Bhavni Parsad Neupane	Till date no any certificate was distribute for construction completed HHs from GoN side. We will rise the issue at GMaLI, Building -DLPIU on this regards. Rijan Gajurel HRRP district coordinator.

Challenges and Way Forward

Challenge	Way Forward
Lack of technical assistance in the field. NRA engineers are not in regular monitoring to the house. When they visited for the inspection, they only commented for non-compliance.	RM and Building-DLPIU should monitor the engineer and instruction for regular visit.
When will retrofit start? People don't have trained manpower for the retrofit, they are waiting the response from NRA side.	Training and other technical issue with proper communication to the common people should be done before monsoon starts.
