



Housing Recovery and Reconstruction Platform

Preparation for WB Stakeholder Consultation on Lessons Learned and Way Forward for the Housing Reconstruction Programme

19 JULY 2018

HRRP OFFICE, JWAGAL

Agenda



- **2-2:10 PM: Introduction**
- **2:10-2:40 PM: Groupwork**
- **2:40-2:55 PM: HRRP presentation**
- **2:55-4 PM: Discussion and preparation of key points**

Groupwork



- What are the opportunities in the housing reconstruction? (Anu)
- What are the challenges in the housing reconstruction? (Rupa)
- What has worked well in the housing reconstruction so far? (Minar)
- What has not worked well in the reconstruction so far? (Kuber)

HRRP Presentation



Kashmir EQ 2005



Strategic Recovery Objective 1




Restore and improve disaster resilient housing, government buildings and cultural heritage, in rural areas and cities


Owners will be provided financial assistance in tranches, supported by timely provision of technical assistance, training and facilitation, so that people can rebuild as soon as possible. It is critical that there is a uniform approach to support and implementation for universal coverage in the 31 earthquake affected districts, including the 14 most-affected districts, irrespective of funding sources.


Meeting SRO1?



- More than 150 million USD already spent on TA but coverage is low
- Why?
- What are the options to scale up coverage?

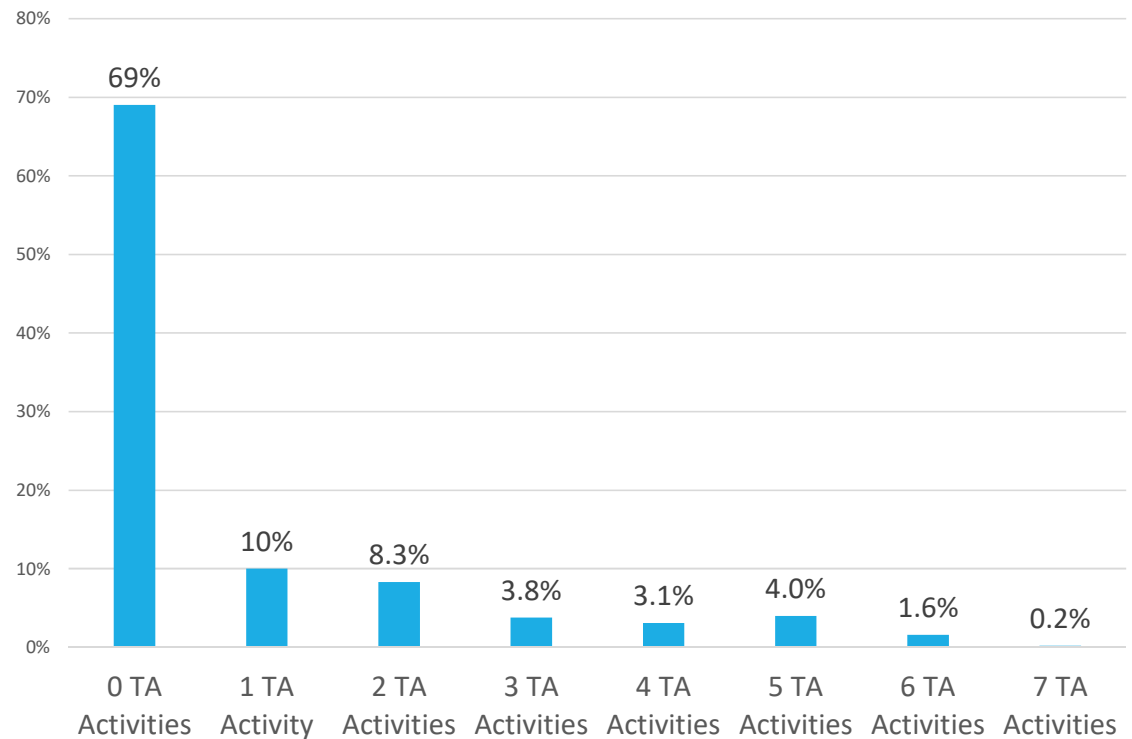

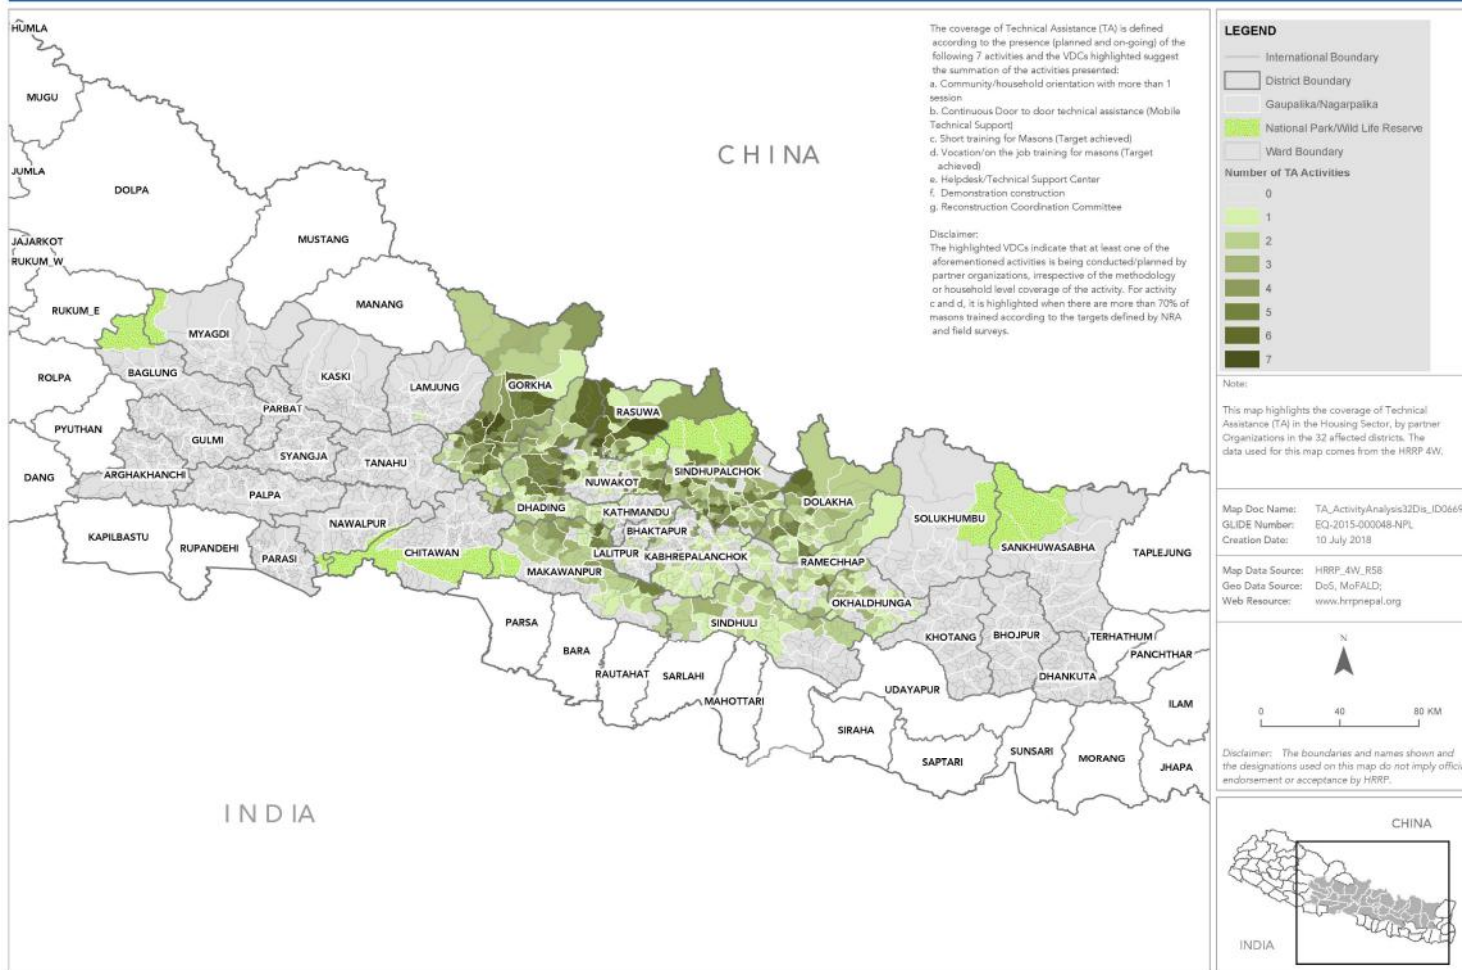

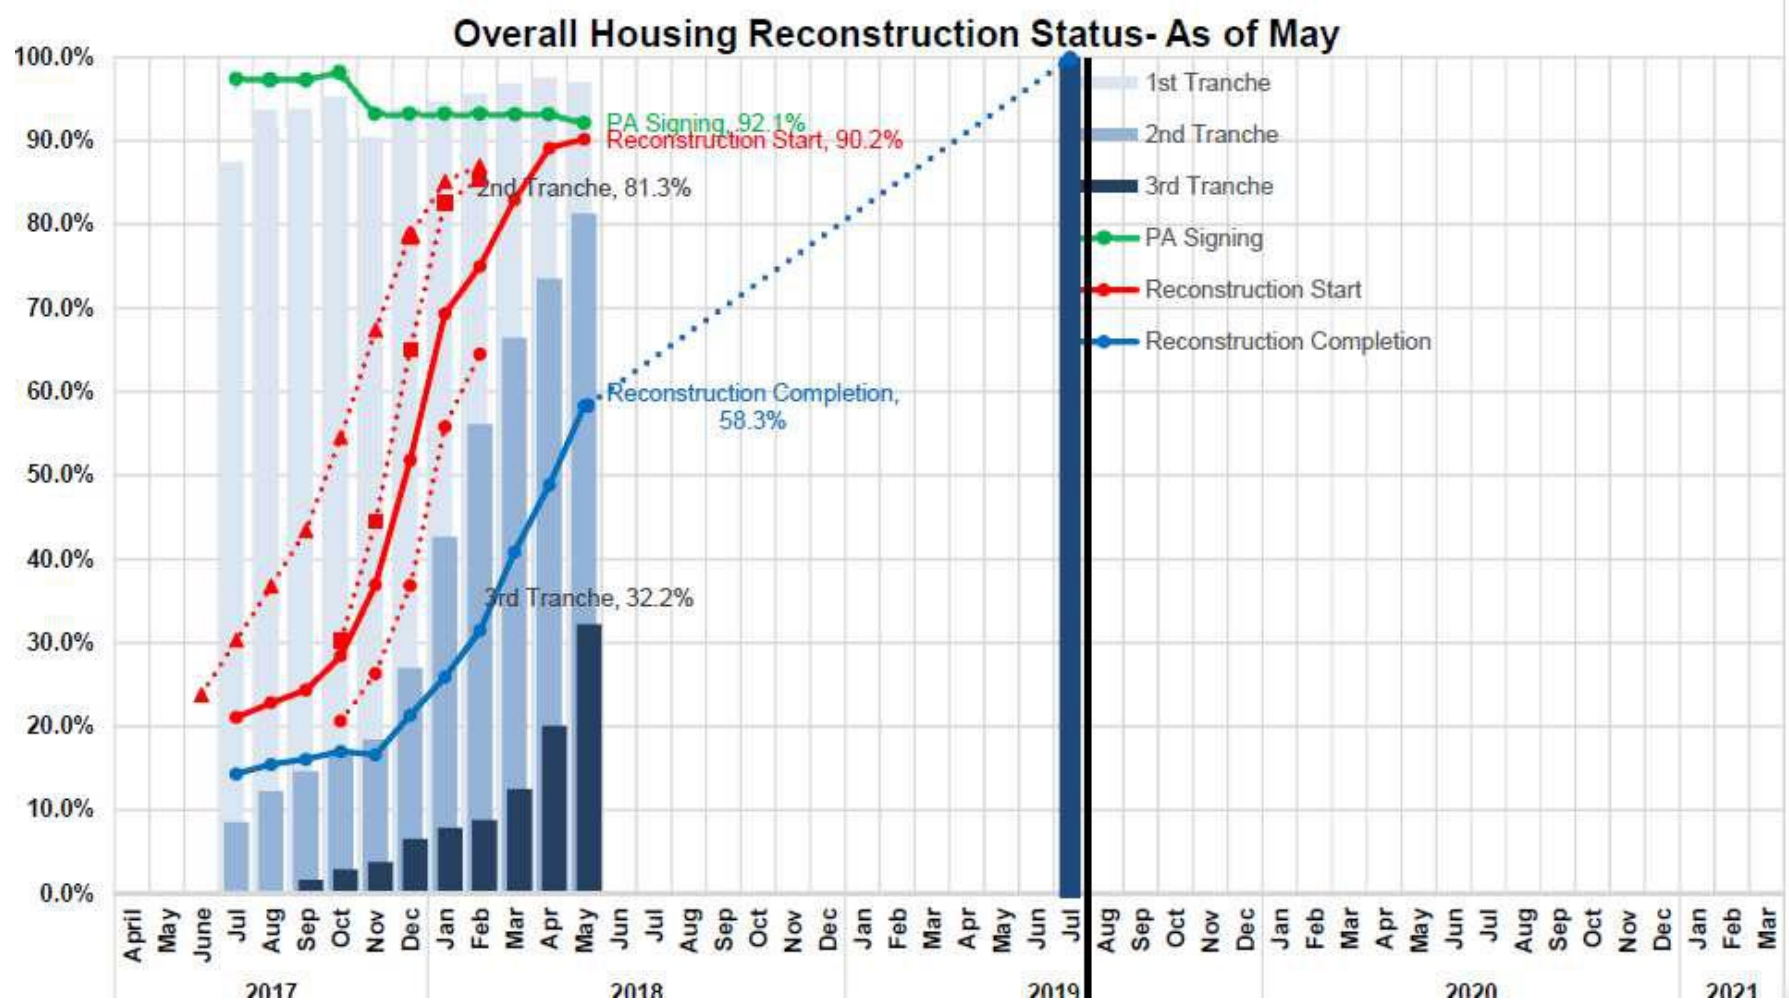


Achieving Req'd. / Expected Outcomes?



“The quality of the housing reconstruction will determine how the overall reconstruction is viewed, if the housing reconstruction is well managed and effective then the reconstruction programme will be considered a success.”

General Nadeem

Retired Director of the Pakistan ERRA
Speaking with Shelter Cluster partners on 8
October 2015

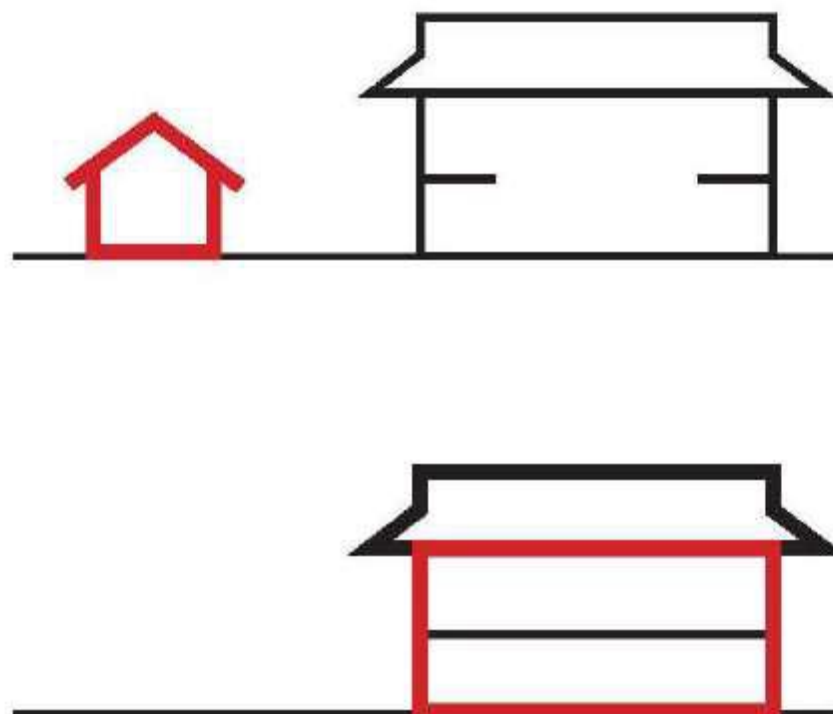

District and Municipal View



- NRA, Building DLPIU engineers are only using and recommending the design catalog models
- NRA, Building DLPIU engineers are not given basic TOTs such as mason TOT prior to their deployment. In some cases, they lack communication skills, and are not polite and professional with the poor beneficiaries.
- Reconstruction policies are wrongly interpreted due to miscommunication at the grass root level.
- Many households are interested to carry out retrofitting instead of reconstruction but the engineers do not have information on how to manage this, confusion about retrofitting grant process
- Reconstruction at the urban areas takes long time and many earthquake affected households in urban areas are renting temporary accommodation
- Construction of single room houses just to get the tranches is the most common challenge
- Challenges with logistics – road access, transport, electricity, phone network, internet, etc.

District and Municipal View Contd.



- Relocation and resettlement process
- Deadlines – 1/2 room houses being constructed just to get grant, do not meet living requirements, often called ‘bhukhumpa ghar’ (EQ houses)
- Debt, high interest rates
- Supply chain management / support, availability and cost of construction materials
- Non-compliances
- Differences between municipal policies / by-laws and reconstruction policy
- Grievance process – people that should be eligible for grant not on list, grievance process taking long time, people not aware of how to follow up

District and Municipal Recommendations



- Place staff in bank to support tranche disbursement – example from Dolakha
- Engineer deployed in municipality to prepare building drawings free of charge – example from Kathmandu
- Deployment of social mobilisers to support households to access information and guidance – example from multiple districts
- Training for technical people and home owners on retrofitting – suggestion from Makwanpur


NRA, Building DLPIU Engineers




- Currently conducting survey
- 74% engineers, 23% sub-engineers, 3% assistant sub-engineers
- 59.4% hired in 2016, 21.7% in 2017, 18.9% in 2018
- 45% did not receive any training before deployment, 25% have not received training since deployment
- Conducting visits to an average of 49 houses per month, average time per visit just under an hour
- Walking is primary mode of transport for 96%
- 56.5% prepare plan for visits with municipality, 91% based on requests from HHs
- 51% have faced pressure from home owners to pass the house, and 36% have faced pressure from ward / municipal officials

- How often do you receive updates from DLPIU? 29% once a month, 37% once a week, 16% once every two weeks, 18% other


How do you access information on reconstruction standards and policies, and any updates to these?

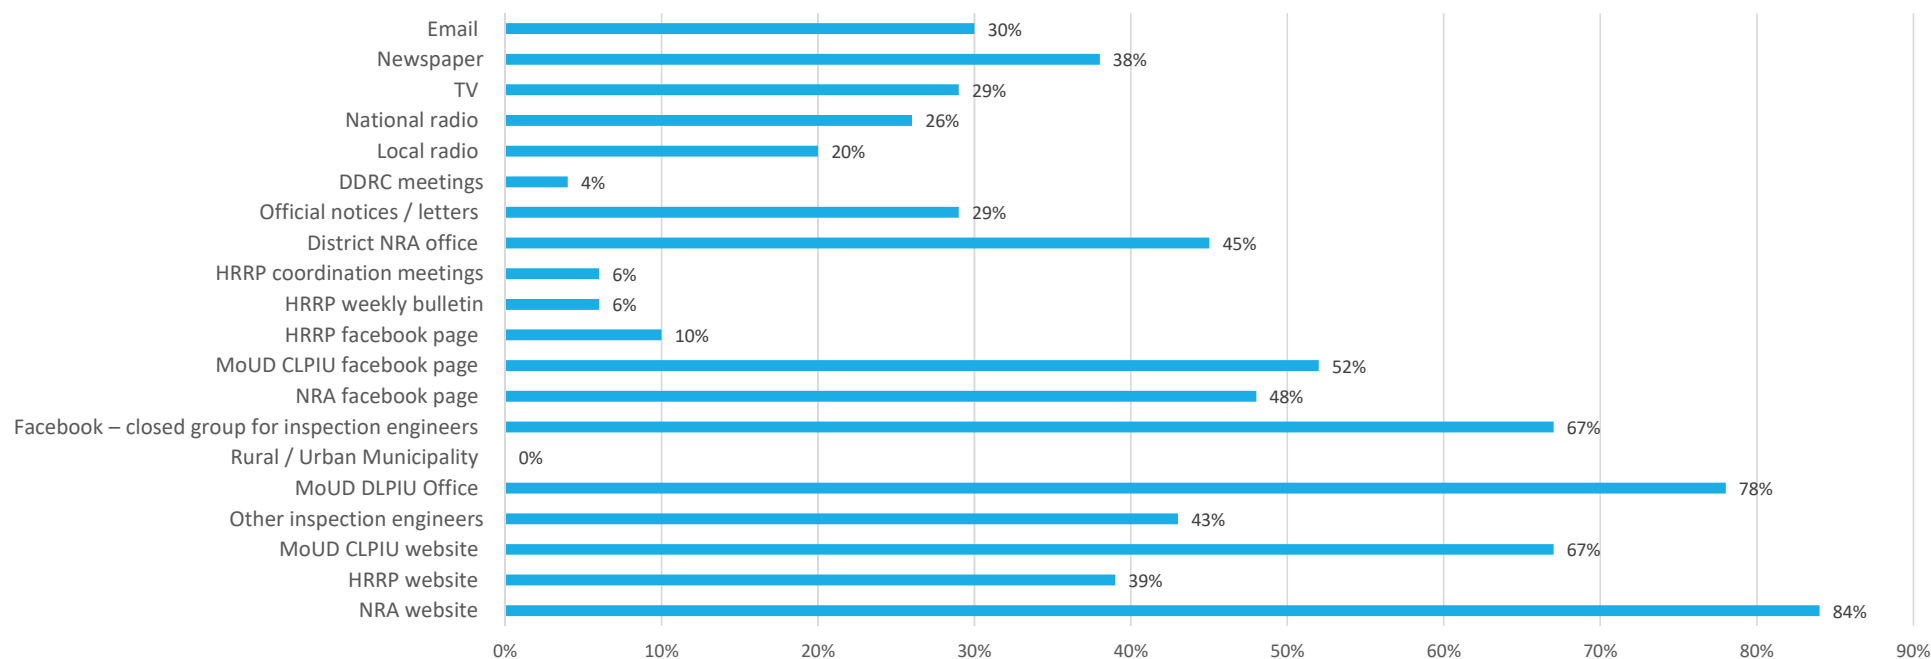

What are the challenges you face in sharing information with households?

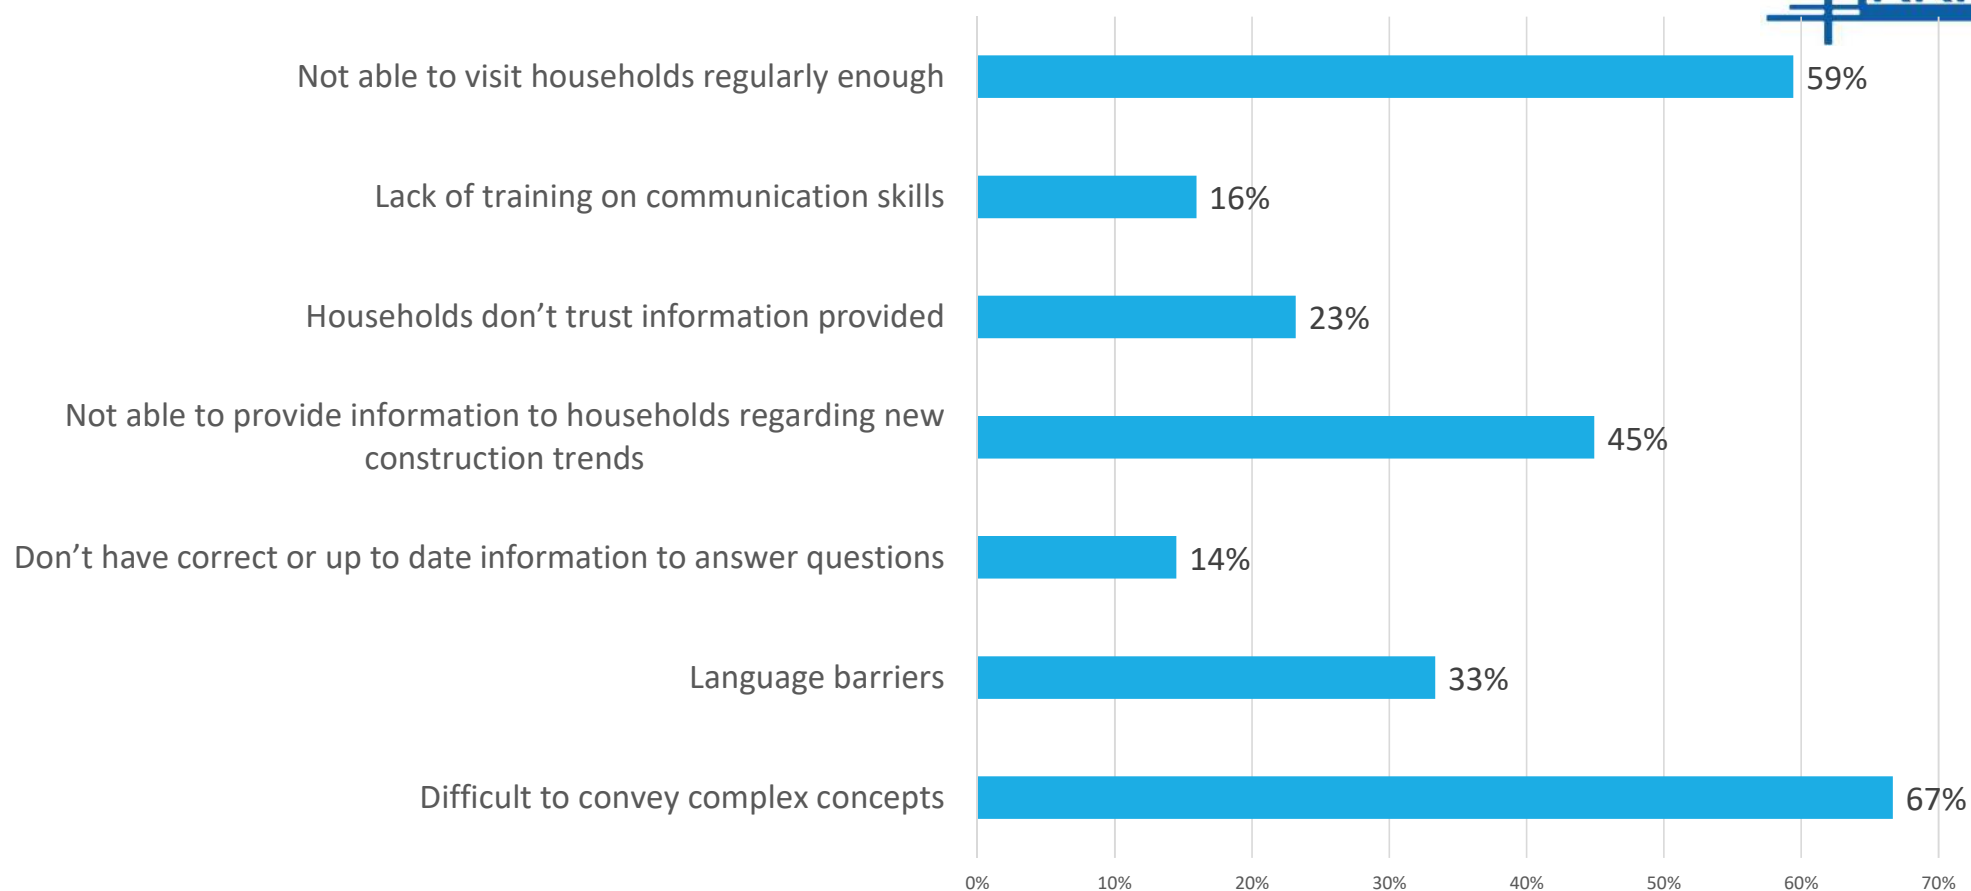

What have you found to be the best ways to share information with households?

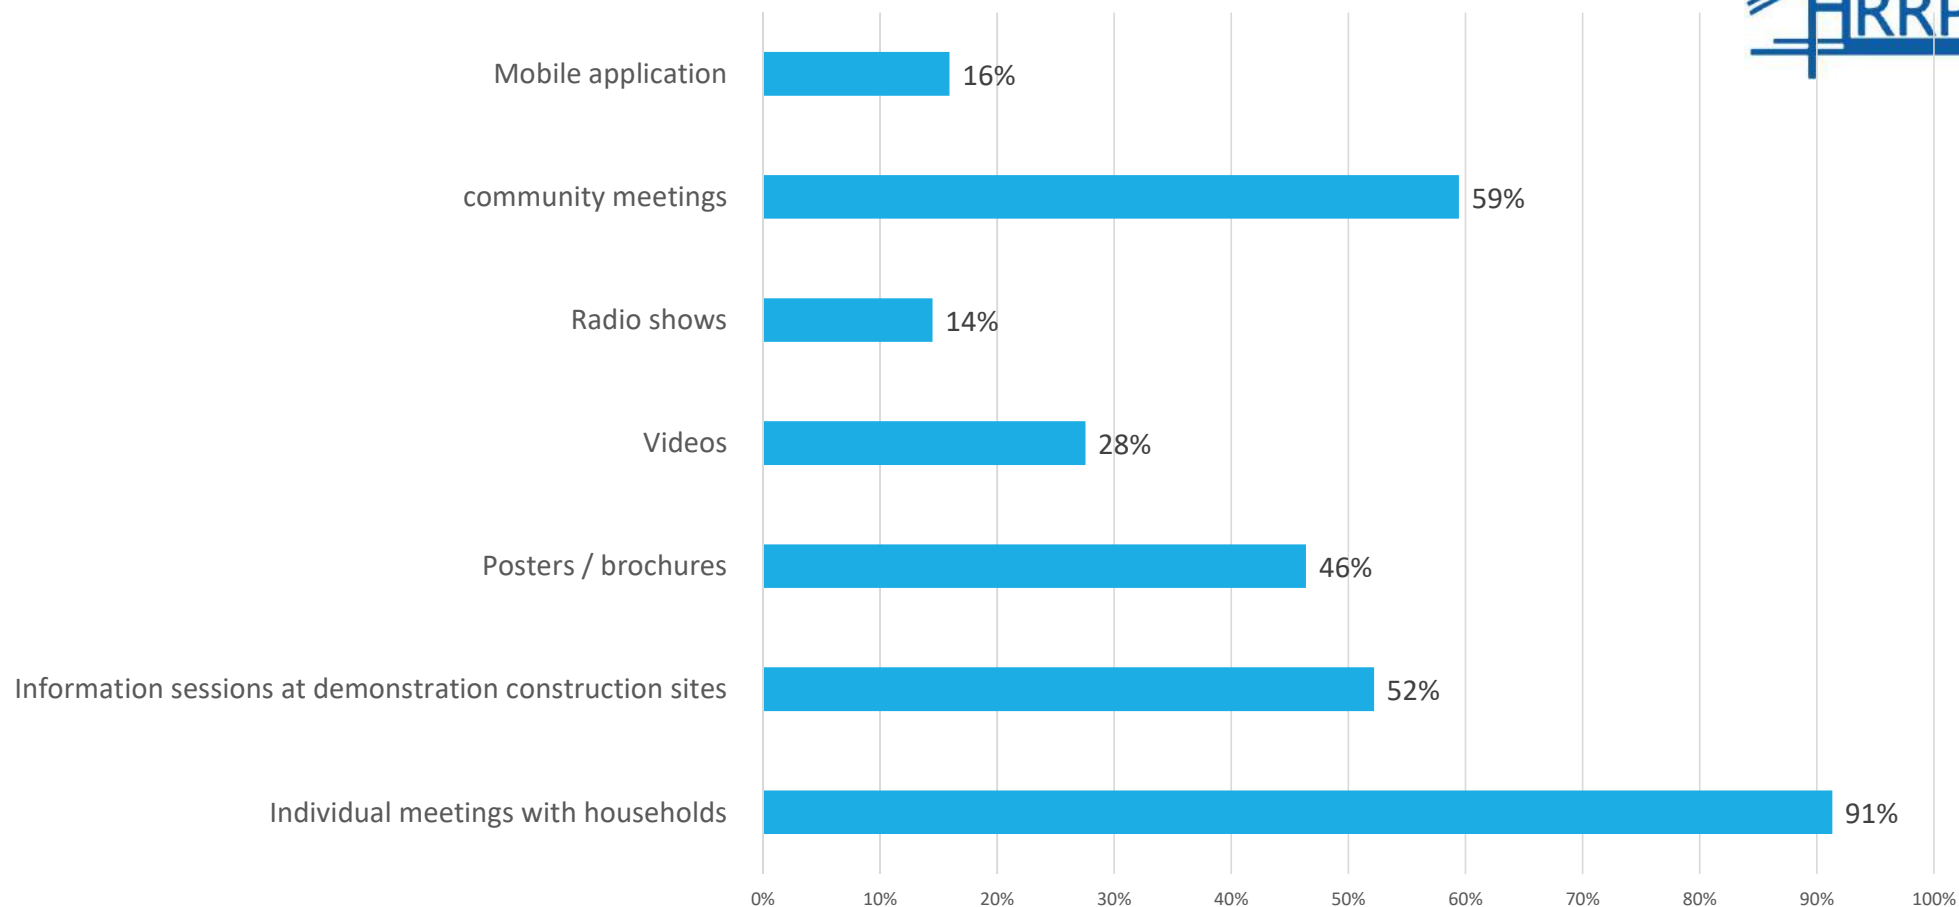

NRA, Building DLPIU Engineers



- What support is required?
 - Better access to information and information sharing processes
 - Improved coordination
 - Support to address technical issues, e.g. non-compliances
 - Partner with local community members / social mobilisers to facilitate work
 - Transport, office space

Capacity Building for Municipal and Ward Officials




- High level of investment and many actors involved but issues with coverage and quality / standardisation of approach
- Examples of activities:
 - Development of Local Disaster Risk Management Planning (LDRMP) – some municipalities, supported by DFID, CARE, and Christian Aid
 - Orientation to municipal officials on the reconstruction policy, procedures, and guidelines – mix of actors, generally just one session (not continuous), poor coverage in 18 districts
 - Municipality website and IM staff – all municipalities, UNDP
 - Good governance – across almost all municipalities, multiple organisations
 - Municipal Reconstruction Focal person
 - Municipal revolving fund


18 Districts



- GMALI-DLPIU established in all 18 districts and likely to be operational after 15 July 2018
- Apart from four districts (Sankhuwasabha, Dhankuta, Parbat and Bhojpur), Building DLPIU MIS system is in place
- Huge gaps in coverage of socio-technical assistance
- Government technical staffs have not been trained or oriented on process, system and technical guidelines and manuals
- District Support Engineers have not been deployed in most of the districts
- Many non-compliances
- Diverse housing construction typologies and new construction trends e.g. hollow concrete blocks, steel frame etc.
- Misinformation and confusion are present at all levels – field, local, and district
- Deadlines are causing stress and concern for people

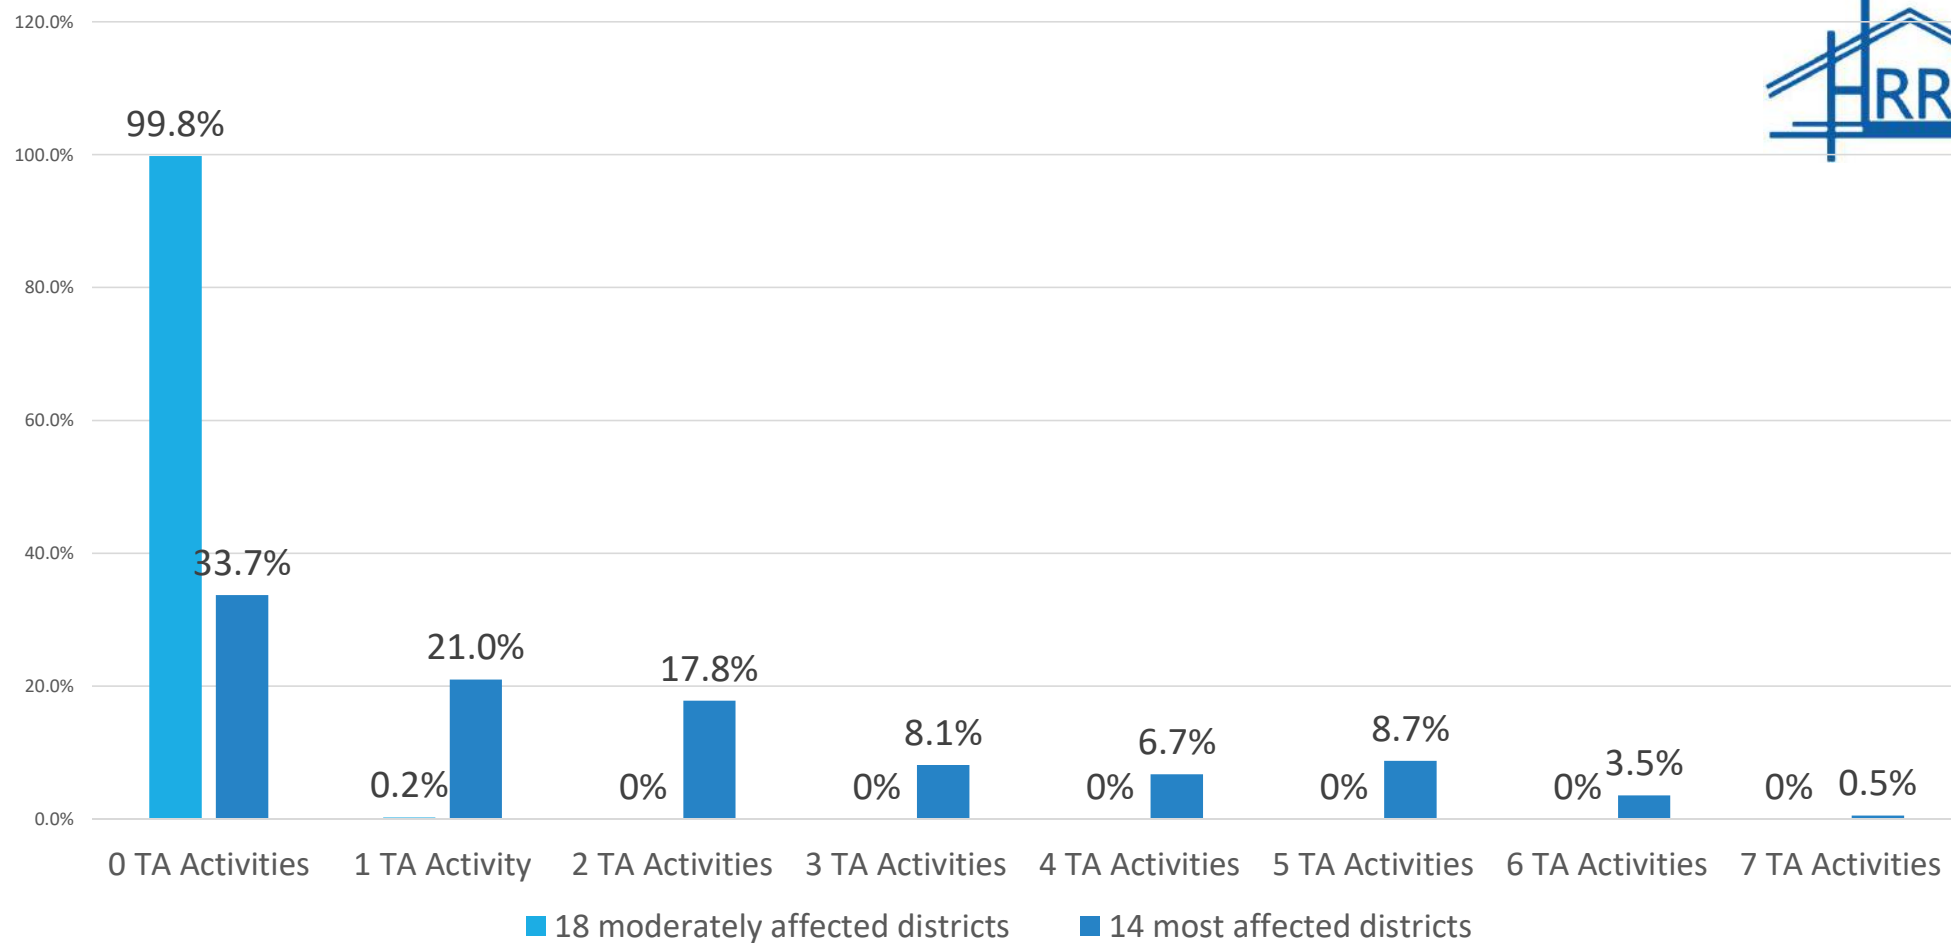



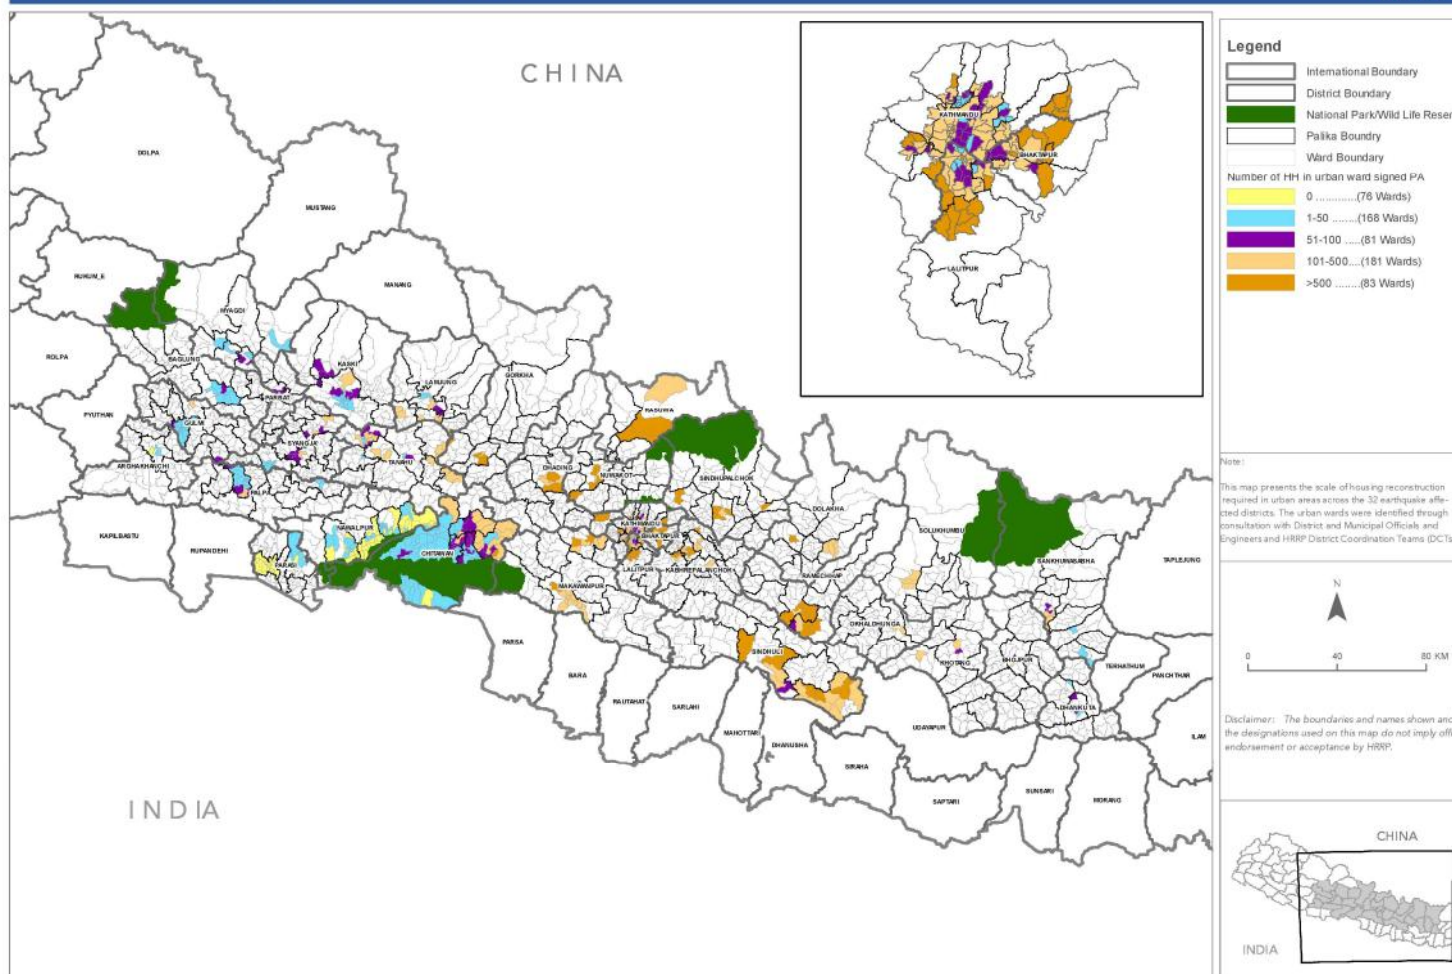

Urban Reconstruction



Pakistan urban lessons learned

90% of temporary shelters still used 13 years after earthquake.

Rental and interim costs have slowed housing reconstruction.

Joint family property ownership makes decision making complex and takes time.

Funding larger building reconstruction takes time.

Urban land values, new buildings are bigger.

No strengthening of municipal regulatory capacity

Urban housing reconstruction is underway in 2018 with no technical guidance

Sound familiar?

Urban Reconstruction Contd.



- There is still time – lots of time!
- Sector globally is still trying to work out how to address urban recovery – huge potential for Nepal to contribute
- What are the policies / policy changes needed for urban? E.g. in Gujarat reconstruction grant in urban areas was almost double the grant for rural areas
- Different requirements for traditional / heritage settlements, high-rise buildings
- Technical assistance in urban areas requires different approach
- Role of building permit process, municipalities – build on previous work in this area

PDRF – Rural Housing Sector Plan



TABLE: FINANCIAL REQUIREMENTS FOR RURAL HOUSING PROGRAMME

Year	2016	2017	2018	2019	2020	Total	On-budget sources	Off-budget sources	Unknown
Budget in Million NPR	73,340	77,460	68,430	39,245	27,585	286,060	134,000	1,600	149,652
Program									
Rural housing reconstruction program - housing subsidy	35,000	40,000	35,000	10,000	5,000	125,000	125,000		0
Rural housing reconstruction program - technical assistance	4,000	3,000	3,000	3,000	1,000	14,000	4,000		10,000
Rural housing reconstruction program - vulnerable top-up subsidy	6,000	2,000	1,000	500	500	10,000			10,000
Rural housing repair and retrofitting subsidy	4,000	1,400				5,400			5,400
Designated area subsidy	1,500	1,500	1,500	500		5,000			5,000
Rural housing services promotion, eg: rainwater mgt, sanitation, energy	300	300	300	300	240	1,440			1,440
Shelter, monsoon, seasonal support, temporary and community shelter	2,500	500				3,000	500		2,500
Housing supply chain and distribution	840	840	500	400	300	2,880			2,880
Financing housing credit	8,000	10,000	10,000	10,000	10,000	48,000			48,000
VDC planning, community planning, mobilisation, technical assistance, advice,	300	300	300	300	240	1,440			1,440
Trail and trail bridge rehabilitation, local access	2,000	2,000	760	500	500	5,760	300	99	5,361
Community livelihood rehabilitation and enterprise, inc small business, markets, animal sheds, food storage, cash for work	1,500	1,500	1,000	1,000	760	5,760		1,509	4,251
Technical support for land and risk issues	250.0	250.0	250.0	125.0	125.0	1,000.0			1,000.0
Community infrastructure rehabilitation, inc local water supply, block grants / community contracts / direct contracts	4,000	8,000	10,000	8,000	6,000	36,000			36,000
Technical support for land and risk issues	250	250	250	125	125	1,000			1,000
Geodetic survey and risk assessment	1,000	500	500			2,000			2,000
Displaced households support for acquiring sites through subsidy	1,000	3,000	1,000	1,000		6,000			6,000
Community relocation, site and infrastructure development	500	1,500	1,500	2,000	1,500	7,000	5,000		2,000
Settlement mitigation works	400	620	820	620	420	2,880			2,880
Integrated settlement and settlement development	250	250	1,000	1,000	1,000	3,500			3,500



PDRF – Urban Housing Sector Plan



TABLE: FINANCIAL REQUIREMENTS FOR PRIORITY RECOVERY PROGRAMME

Year	2016	2017	2018	2019	2020	Total	On-budget sources	Off-budget sources	Unknown
Budget in Million NPR	19,814	19,475	17,694	17,569	15,507	90,059	20,000		70,059
Program									
Regeneration of 63 (52 in Kathmandu valley) heritage settlements	4,000	4,000	4,000	4,000	4,000	20,000			20,000
Housing Reconstruction	4,000	4,000	4,000	4,000	4,000	20,000	20,000		
Funding support for financing housing credit	4,159	4,159	4,159	4,159	4,157	20,793			
Vulnerable top up subsidy	600	600	600	600	600	3,000			
Repair and retrofit subsidy	1,000	1,000	500	500		3,000			
Material supply, enterprise, livelihood	2,000	1,500	300	500	500	5,000			
Sustainable housing services	200	200	200	200	200	1,000			
Emergency shelter and camps	500	200	100	100	100	1,000			
Community grants for local infrastructure	1,500	1,500	1,500	1,500	300	6,300			
Safe demolition	75	25				100			
Communication campaigns	250	250	250	125	125	1,000			
Risk sensitive land use plan preparation and implementation for 31 settlements with adequate provision for open spaces	310	310	310	310	310	1,550			1,550
Rental housing for urban poor	50	50	50	50	50	250			250
Integrated recustering of urban settlements		250	250	250	250	1,000			
Preparation of Guidelines, planning norms, standards, bye-laws for safer housing and settlement reconstruction	60	25				85			85
Construction of 1 model houses in each of the 30 urban settlements	30	15				45			45
Institutional development and capacity enhancement for building back better	250	250	250	250	200	1,200			1,200
Review national plans, strategies and building codes	10	6				16			16
Preparation of housing technology and design options	10	10				20			20
Implementation of national plan of action for safer building construction	10	25	25	25	15	100			100
Setting up resource and training centers	100	100				200			200
Technical assistance for revitalization of traditional settlements of Kathmandu valley	500	500	500	500	200	2,200			2,200
Revitalization of 44 informal settlements of Kathmandu valley	200	500	500	500	500	2,200			2,200







Housing Reconstruction Programme “Reboot”



- Rebrand as a **Government led Housing Rehabilitation and Reconstruction Programme and move away from collection of Government approved PO Projects**
- Remove deadlines, or extend for at least the next two building seasons
- Scale up coverage of socio-technical assistance with common standards and approach
- Urban reconstruction
- 18 Districts
- Mass communications to address misinformation and rumours
- Increased support for NRA, Building DLPIU engineers, sub-engineers, and assistant sub-engineers, and District Support Engineers
- Develop common approach for continuous capacity building support to municipal and ward officials on reconstruction

“If we aim to ensure people are supported to take informed action, whether through building codes or other measures, we should anticipate an iterative process that is continuously learning, responding to opportunities and challenges.”

RECONSTRUCTION AS TRANSFORMATION
SOUTHASIADISASTERS.NET, ISSUE NO. 171

Discussion
