

HRRP District Coordination Meeting Minutes

Meeting Purpose:	General Meeting		
Meeting Date:	28/03/2019		
Meeting Time:	11 AM – 01:00 PM		
Meeting Location:	GMALI OFFICE, BIDUR, NUWAKOT		
Meeting Facilitator:	Badri Pyakurel, Bicky Lakkha (Acting GMALI Chief,		
Minutes Taken By:	Badri Pyakurel		
Summary of participants:	Total: 16	Female: 1	Male: 15

Discussion: (Items/Knowledge Shared)

Agendas:

1. Welcome and Introduction
2. HRRP updates on reconstruction Status
3. Partner Organization presentation/update
4. Discussion based on issue and challenges.
5. AOB

Decisions:

1. Welcome and Introduction

The coordination meeting was chaired by Acting GMALI Chief Bicky Lakha. The program was facilitated by district coordinator of Nuwakot HRRP Mr. Badri Pyakurel and was started by welcoming the participants and they all introduce each other. Then he presented the agendas of meeting and discussed based on this.

2. HRRP updates on reconstruction Status

HRRP DC, Badri Pyakurel has distributed print copy of tranche recent update based on palikas of GMALI data and the details of Nuwakot district are also listed below as reference.


Rural /Municipality	Belkot gadhi NP	Bidur NP	Dupcheshwor RM	Kakani RM	Kispa ng RM	Liku RM	Meghang RM	Panchkanya RM	Shivapuri RM	Suryagadhi RM	Tadi RM	Tarkeshwaor RM
Total HHs Surveyed	9409	11203	5448	6157	1816	4003	4052	3692	5616	4197	4231	3760
Total HHs Eligible	11037	12893	5873	6916	4788	5109	4510	4460	6514	5019	4590	4707
Total HHs Enrolled	10348	11960	5661	6395	4510	4726	4263	4239	6108	4879	4468	4318
First Tranche	10348	11960	5661	6395	4274	4726	4263	4239	6108	4879	4468	4318
Second Tranche	8923	10578	5346	5598	3872	3817	3992	3687	5249	4151	4096	3874
Third Tranche	3022	7093	4051	3466	2693	2631	3522	2509	3592	2599	3095	3082

Source: Gmali Nuwakot, as of March 28, 2019

HRRP District Coordination Meeting Minutes

Discussion: (Items/Knowledge Shared)

Grand distribution by Partner Organizations

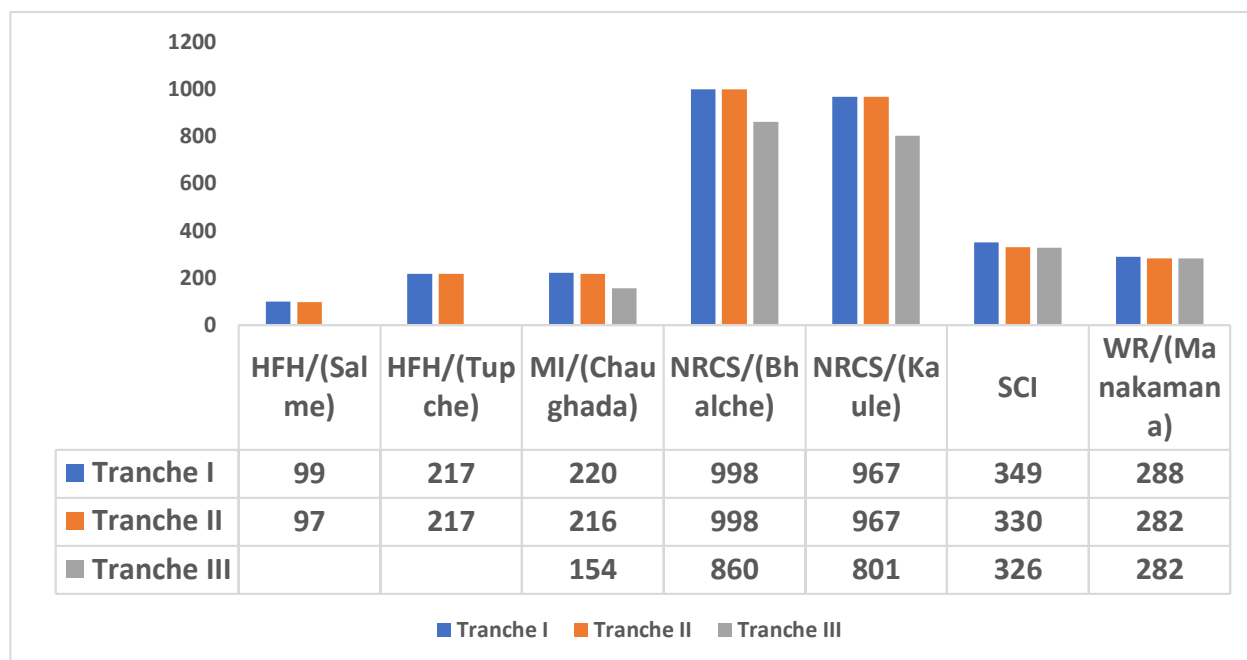

3. Partner Organization presentation/update

CDC, Nuwakot: It is working in Shivapuri Rm as implementing partner of UK Aid Purnima. It has 14 water supply and sanitation project is Continued 13 are in selection Process and 9 are rehabilitation project.

FNCCI: FNCCI is working for construction related business support program with partnership of Purnima. It has 10 target of facilitation to entrepreneurs and completed for 25. It has support for Loan to the female lead business, such support are from microfinance institutions. It has conducted training on business plan development for 4 days.

CSRC Durable Solution: It has program to support as a facilitator for the geo-hazard vulnerable housing in Nuwakot. 381 family from Nuwakot has listed as geo-hazard. These family have recommended for relocation from their original place. Among them 207hh were purchased safe land for their dwelling. 60hh had already constructed their houses in safe and 82 have safe land and 6 constructed house in others' land. There is issue on such construction. 77hh are listed as landless from Nuwakot district. There is plan to 44 hh, for integrated settlement from Bidur municipality. There is issue to develop DPR for the settlement. It has discussed and recommend for DLPIU, building for DPR.

HRRP District Coordination Meeting Minutes

Discussion: (Items/Knowledge Shared)

Land less beneficiaries' status as follows:

SN	R/Municipality	Applied no Landless for land	Approval from NRA
1	Kakani RM	31	0
2	Suryagadhi RM	12	8
3	Shivapuri RM	3	0
4	Kispang RM	11	10
5	Panchakanya RM	6	1
6	Tadi RM	28	0
7	Likhu RM	32	9
8	Tarakeshwar RM	3	0
9	Bidur Municipality	89	42
10	Belkotgadhi RM	15	7
	Total	230	77

NSET (Baliyo Ghar): Nset, Baliyo Ghar is working for technical support program in Shivapuri VDCs. It has mainly 7 technical assistance to Shivapuri, thanapati, Likhu, Talahu and Chhap VDC. It has completed 1399 Community orientation, 7271 mobile clinic support and 49 Mason OJT. It has planning for retrofitting technical and other support for 18 hh of Shivapuri. Two retrofitting training has started and others are in process to identify the hhs.

PURNIMA Project: It has program in Shivapuri, Dupcheswar and Tadi Rural Municipality in different four working areas. 1. Technical Assistance to Palika: Revenue generation meeting/orientation has conducted in all three palikas. 2. Support to Recostruction: water supply and sanitation Project has conducted to all three Palika through local partners. School construction is in planning phase. 3. Private sector support: Nuwakot FNCCI has selected as partner, It was started to support to entrepreneur for different legal procedure and bank loan process. 4. Leave no Behind: The support has continue through challenge fund. It's partner is in survey phase. The Program is conducting in 5 vulnerable criteria.

Oxfam is working for the relocated families from Bhalche, Lachyang, Urleni and Rasuwa. It has completed its support to 50 hh from Urleni, Bhalche and Lachyang. . Likewise Meghang-4, Kimtang and Kispang, Santi bazaar has started construction. Oxfam has support on irrigation cannel construction, water supply project construction in Dupcheswor, Tadi, Suryagadhi and Japhati Bidur.

CARDSN: It is working as implementing partner of Oxfam. Now it has progress on Kharanitar. 34 hh are completed, 14 are on completion of plinth level 30 are started and remaining are started and plan to complete within Jun 2019. It has 8 water supply project on progress. Some are completed and some are on completion phase. It has a water supply project on tadi for Budune relocation site along with host community kharanitar as well. CARDSN has started to work in Ramati settlement from Ghyangphedi. It has started for land pooling activities.

HRRP District Coordination Meeting Minutes

Discussion: (Items/Knowledge Shared)

Sahayata Samajik Sanstha: It is working as implementing partner of Oxfam working in Bidur-9, Japhati for the relocating family from Kispang-1, Bhalche. SSS is working for 18 hh are final phase and 36 are just started in Shantibazzar. Among them 21 are on to roof level and remaining are on preparation for DPC. It has plan to conclude with in March 2019 but remaining activities will be concluded with in June last 2019. It has program of Livelihood support to the project site for the end of March only.

KCDC: KCDC, Implementing partner of OXAM, is working for relocated hh from Lachyang VDC. 14hh are relocated from Lachyang. The 14 are going to conclude within coming month and started to work for 18 hh in Kimtang.

UNOPS/GOI: Government of India Support to Housing Reconstruction in Nuwakot district has started to work from March 2018. It has plan to support to 23088hh as STFC service and others. 174 GOI beneficiaries have received banking support. 91 have received support to obtain building permits and 844 have received drawings. Total no visited TSC are 7625 and 5301 beneficiaries have visited TSCs.

M&E Specialist; Satyanarayan Chaudhari has suggested to work with good coordination among the stakeholders which may help to reduce gaps and problem sharing.

GMALI; Thanks note has been given by Bickey Lakha, GMALI Nuwakot Acting Chief for the presence in the meeting. He focused for better coordination in planning and implementing phase for the qualitative activities. He has requested to all participants for the regular reporting to the channel.

PARKING LOT: *[Describe any items that may have been deferred for a later discussion]*

Miscellaneous Items / AOB:

1. *Discussed in different issues facing Field in individual level.*

CSRC has request to support in Bidur Municipality to facilitate for land less people who are willing to stay the same place where they are staying since 20 years.

Decisions Made: (What, Why, Impacts)

Next Steps/action points:

[Insert next step]

[Insert next step]

Person(s) Responsible

Due Date

HRRP District Coordination Meeting Minutes

Attendees	Gender	Organization	Designation	Phone No.	Email
Bicky Lakha	M	GMALI	Acting Chief	9849179333	bickeylakha@gmail.com
Badri Pyakurel	M	HRRP	District Coordinator	9851154201	dc.nuwakot@hrrpnepal.org
Satya Narayan Chaudhari	M	GMALI	M&E Specialist	984130949	satya.isha95@gmail.com
Pravuram Pokharel	M	DLPIU-Building	M&E Expert	9851224243	prabhupidge@gmail.com
Chandra aale	M	Purnima	District coordinator	9845580764	Cmagar621@gmail.com
Ghanendra Pd. Rijal	M	NCCI	PC	9852681494	ghanendrarijal@gmail.com
Kabita Bhnadari	F	KCDC	Meal Officer	9843013200	bhandarikabita7@gmail.com
Kiran Sharestha	M	UNOPS/STFC Project	AFP	9849123995	kirans@unops.org
Niraj Raut	M	UNOPS/STFC Project	Associate D. Engineer	9842378322	nirajr@unops.org
Sujit Dhakal	M	UNOPS/STFC Project	DPM	9841781309	sujitdhkl@gmail.com
Sailesh Acharya	M	CDC Nepal	PM	9851191411	cdcnepal.pm@gmail.com
Prakash Shrestha	M	NSET/Baliyo Ghar	DC/ER	9851230841	prakashshrestha@nset.org.np
Bishal Gautam	M	Sahayata Samajik Sanatha	PC	9851187139	bishalgautam@gmail.com
Sushil Timsina	M	Room To Read	FPM	9851214203	sushil.timsina@roomtoread.org
Bishwash nepali	M	CSRC	DAC	9851241866	biswash@csrcnepal.org
Binod Adhikari	M	GMALI	MIS Specialist	9846142007	adhikaribnod@gmail.com

HRRP District Coordination Meeting Minutes

