

Monthly District Report

Lalitpur, Bhaktapur

12 July- 22 August 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Lalitpur	The general ward-level coordination meeting was conducted at Ward offices of Ward no. 3, 11 and 16 of Lalitpur Metropolitan City. Ward Chief in presence of Ward Members representatives from DLPIU Building Lalitpur (M & E Consultant, District Support Engineer, Palika Reconstruction Engineers) and HRRP attended the meeting. The purpose of the meeting was to track the reasons behind delaying in reconstruction of houses by beneficiaries that have already taken 1 st tranche.	26 th July 2019	Respective Ward offices of Ward no. 3, 11 and 16, Lalitpur Metropolitan City	Er. Roshan Raj Giri M & E Consultant DLPIU Building Lalitpur roshanrgiri@gmail.com Contact: 9841335744	Meeting minute
	Interactive discussion on landless earthquake beneficiaries in three urban municipalities of Lalitpur district was conducted by DLPIU GMALI Lalitpur with support from Durable Solutions/CSRC. The various regulations and guidelines regarding landless beneficiaries was presented among the elected mayors, deputy mayors and ward officials during the discussion, which also emphasized on finding the common solutions to solve the landlessness issues. Dr. Chandra Bahadur Shrestha, Executive Member of NRA clarified the queries and issues on landlessness.	30 th -31 th July and 1 st August	Respective offices of Mahalaxmi Municipality, Lalitpur Metropolitan City Office and Godawari Municipality	Mr. Yamnath Giri M & E Specialist DLPIU NRA GMALI Lalitpur Yamnathgiri2014@gmail.com Contact: 9851239785	
	Joint M & E visit was organised by GMALI and Building Lalitpur and HRRP Lalitpur Team at Ward no 6 of Godawari Municipality. The purpose of the visit was to observe the houses made by Satya Sai Kendra.	8 August 2019	Shikharpa, Ward no 6, Godawari Municipality	Mr. Yamnath Giri M & E Specialist DLPIU NRA GMALI Lalitpur Yamnathgiri2014@gmail.com Contact: 9851239785	Field visit section
	General ward coordination meeting was conducted at Ward no 21, Khokana, Lalitpur Metropolitan City. Representatives from GMALI Lalitpur and HRRP Lalitpur Team attended the coordination meeting. The purpose of the visit was to discuss on housing reconstruction issues perpetuated in Ward no 21.	9 August 2019	Khokana, Ward no. 21, Lalitpur Metropolitan City	Mr. Yamnath Giri M & E Specialist DLPIU NRA GMALI Lalitpur Yamnathgiri2014@gmail.com Contact: 9851239785	Meeting minute
	General ward coordination meeting was conducted at Ward no 2, Sanepa, Lalitpur Metropolitan City. Representatives from DLPIUs Lalitpur (GMALI and Building) and HRRP	12 August 2019	Sanepa, Ward no. 2, Lalitpur Metropolitan City	Mr. Yamnath Giri M & E Specialist DLPIU NRA GMALI Lalitpur Yamnathgiri2014@gmail.com Contact: 9851239785	Meeting minute

Summary of events during this period

	Lalitpur Team attended the coordination meeting. The purpose of the visit was to discuss on housing reconstruction issues perpetuated in Ward no 2 and suggest way forwards.				
	Follow up with upload of Palika Profile in websites of Palikas	12 July-22 August 2019	Respective palikas of Lalitpur district	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster ambika.amatya@hrrpnepal.org Contact: 9841356409	Check websites of respective palikas for the upload of palika profile
	Tranche status of Lalitpur updated to GD sheet in Palika Profile	1 August 2019		Sachin Malego IM Officer, HRRP	Google drive
	Support to National HRRP for design and publication of Experiences booklet	Ongoing		Sachin Malego, IM Officer, HRRP	
	Contact list update and 5 W data update	Ongoing		Sachin Malego IM Officer, HRRP and Ambika Amatya, District Coordinator HRRP	Google drive
	Visit to Lamjung and Tanahun for MIS support for Data Update and Data Cleaning	12-16 August 2019		Sachin Malego IM Officer, HRRP Yubaraj Bhandari NIMO, HRRP	Lamjung Tanahun (Note: Since pilot data cleaning of these district is running this link is not to be shared in public).
	Development of VBA Application for Beneficiary Status	Ongoing		Sachin Malego IM Officer, HRRP	
Bhaktapur	Joint M & E visit was organised by DLPIU Building Bhaktapur and HRRP Bhaktapur Team at Ward no 8 of Changunarayan Municipality. The purpose of the visit was to observe the non compliance housing reconstruction cases	6 th August 2019	Ward no 8, Changunarayan Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357	Field visit section
	Joint M & E visit was organised by DLPIU Building Bhaktapur and HRRP Bhaktapur Team at Ward no 9 of Suryabinayak Municipality. The purpose of the visit was to conduct sampling of 3 rd inspection of houses.	7 th August 2019	Ward no 9, Suryabinayak Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357	Field visit section
	Tranche status of Lalitpur updated to GD sheet in Palika Profile	15 August 2019		Sachin Malego IM Officer, HRRP	Palika Profile
	Coordination with DLPIUs (Building and GMALI) office and Changunarayan Municipality office for purpose of conducting External Evaluation of HRRP 3	20 August 2019	Respective offices of DLPIUs (GMALI and Building) and Palika Office	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster ambika.amatya@hrrpnepal.org Contact: 9841356409	Schedule of HRRP 3 External Evaluation
	HRRP 3 External Evaluation: Focus Group Discussion (FGD) with district reconstruction stakeholders and palikas of Bhaktapur	22 August 2019	Respective offices of DLPIUs (GMALI and Building) and Palika Office	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster ambika.amatya@hrrpnepal.org Contact: 9841356409	TOR of HRRP 3 External Evaluation
	Follow up with upload of Palika Profile in websites of Palikas	12 July-22 August 2019	Respective palikas of Bhaktapur district	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster ambika.amatya@hrrpnepal.org Contact: 9841356409	Check websites of respective palikas for the upload of palika profile
	Tranche status of Bhaktapur updated to GD sheet in Palika Profile	19 August 2019		Sachin Malego IM Officer, HRRP	Google drive
	Update of Contact list and 5 W update	Ongoing		Sachin Malego	Google drive

Summary of events during this period

				IM Officer, HRRP and Ambika Amatya, District Coordinator HRRP	
--	--	--	--	---	--

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Joint M & E visit to observe reconstruction efforts of beneficiaries in Bhaktapur and Lalitpur districts	23 rd August- September 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster ambika.amatya@hrrpnepal.org Contact: 9841356409
General Palika level and Ward level meeting and consultation with elected ward officials over the reconstruction progress and status of the visited wards of Bhaktapur and Lalitpur district	23 rd August- September 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster ambika.amatya@hrrpnepal.org Contact: 9841356409

News & Updates


- The National Reconstruction Authority (NRA) has removed names of those who have not signed grant agreement for private housing reconstruction before July 06, 2019 from the private housing reconstruction beneficiary list.
- Likewise, those who have signed the agreement but have not taken their first tranche by July 16, 2019 have also been removed from the beneficiary list.
- According to the NRA, 57,309 did not sign grant agreement although they were in the beneficiary list. Altogether, 769,624 beneficiaries out of total 826,933 beneficiaries have signed the grant agreement as of today.
- Likewise, 5,540 beneficiaries did not take the first tranche even after signing the grant agreement.

Tranche Status (Lalitpur)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	3361	3370	3133	3122	2623	2126	252	203	185	0
Godawari Nagarpalika	10950	9598	8052	7985	2807	2365	323	130	126	0
Konjyosom Gaunpalika	2580	2154	2086	2081	1829	1447	372	323	313	0
Lalitpur Mahanagarpalika	6594	7373	6354	6336	1339	887	275	123	118	0
Mahalaxmi Nagarpalika	4409	3669	3104	3101	944	814	83	33	31	0
Mahankal Gaunpalika	2451	2271	2240	2238	1828	1259	61	50	47	0

Graph of Tranche Status:

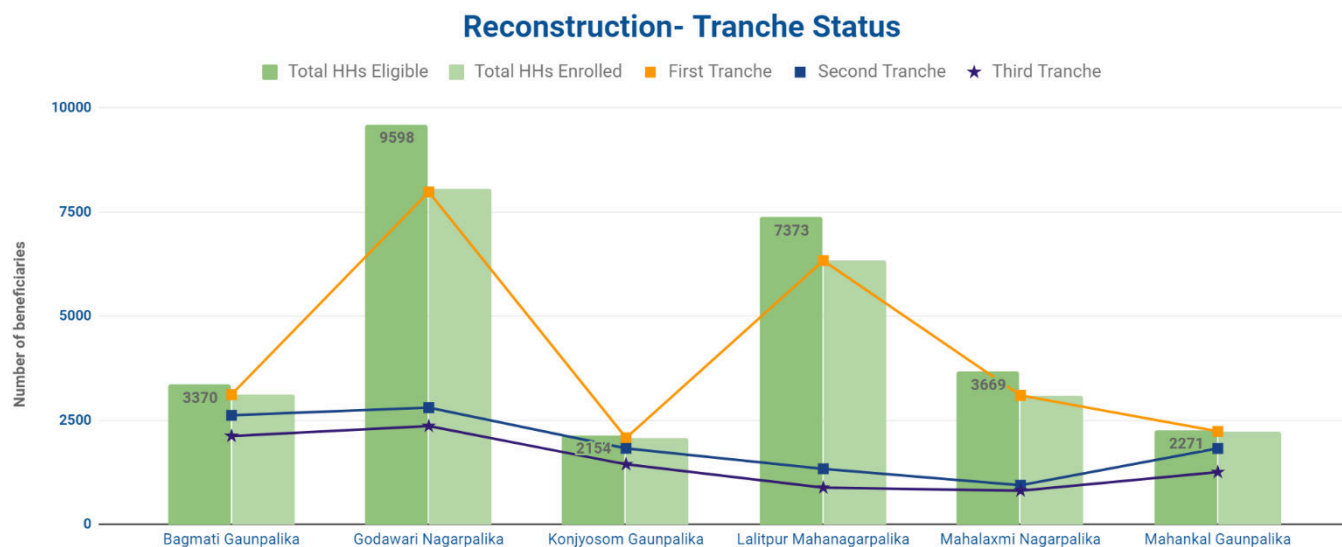

Graph for Retrofitting Status:

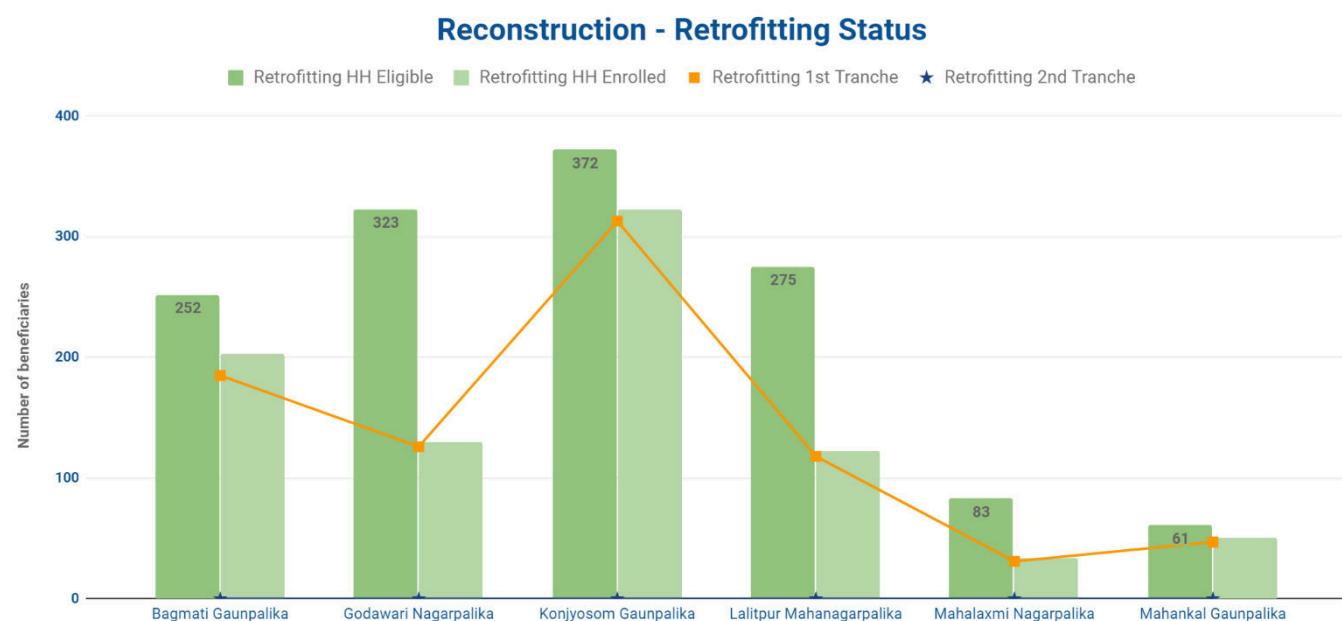


Tranche Status (Bhaktapur)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bhaktapur Nagarpalika	8175	7656	5637	5637	1756	1552	161	43	43	0
Changunarayan Nagarpalika	11059	11000	9826	9826	3523	3367	212	109	109	0
Madhyapur Thimi Nagarpalika	3015	2333	2080	2080	701	678	95	61	61	0
Suryabinayak Nagarpalika	7948	7425	6998	6998	2779	2575	234	105	105	0

Graph of Tranche Status:

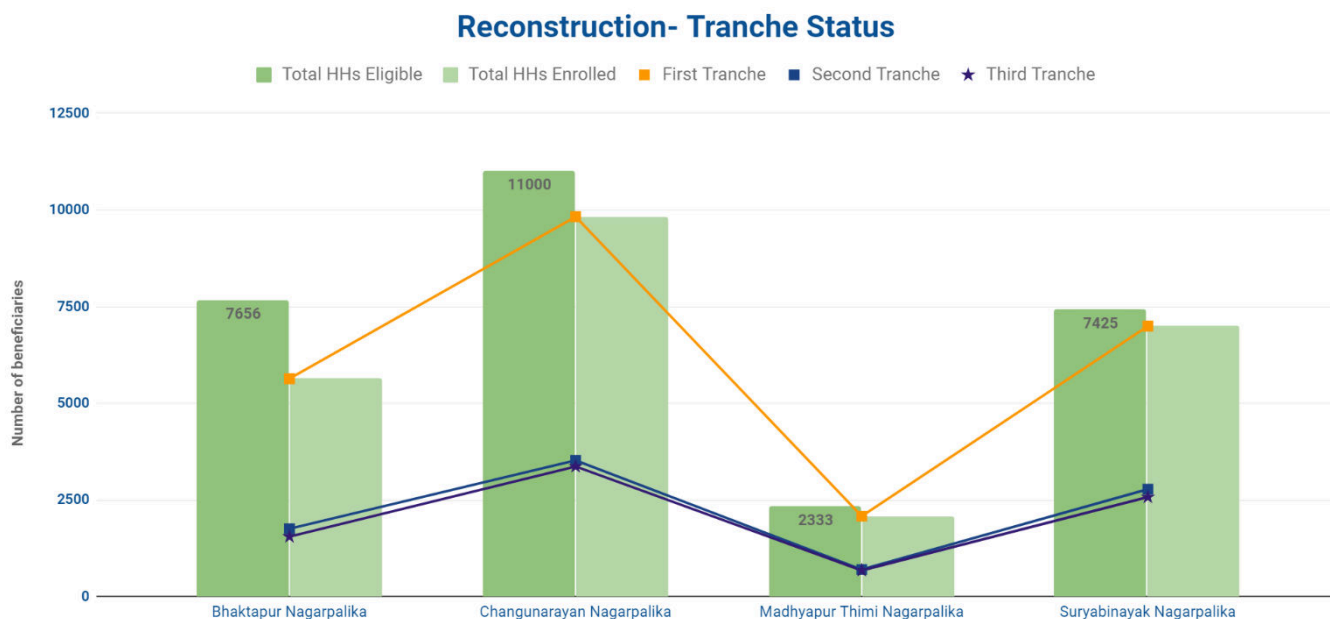

Graph for Retrofitting Status:

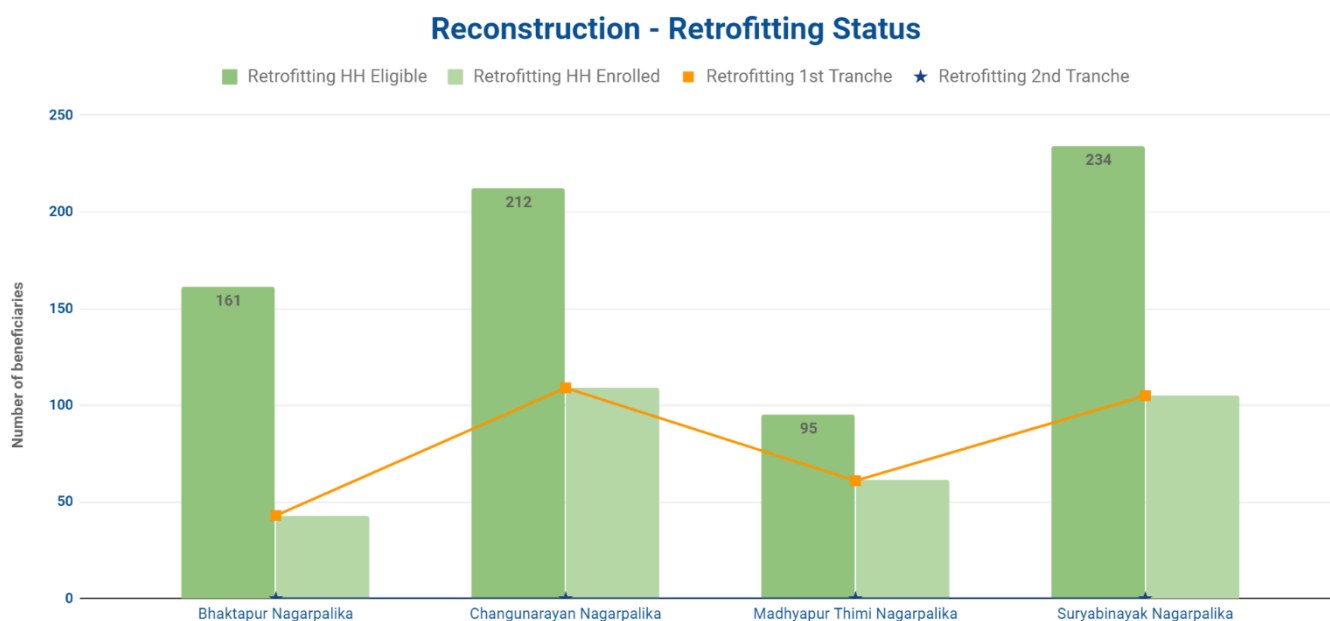

Field Visit Reports (Lalitpur)

Visit 1

Date	Location	Participants
6 August 2019	Ward no. 8, Sudal, Changunarayan Municipality, Bhaktapur district	- Ambika Amatya, District Coordinator, HRRP Lalitpur Cluster - Roshan Keshari, M & E Consultant, DLPIU Building Bhaktapur - Prabesh Adhikari, DSE, DLPIU Building Bhaktapur - Shiva Prasad Bhandari, DSE, DLPIU Building Bhaktapur - Bibha Sainju, Engineer, DLPIU Building Bhaktapur

		Manju Sukhupayo, Archana Prajapati (Engineers Changunarayan Municipality)
--	--	---

Objective(s)	- To observe the reconstruction status of the houses and provide relevant suggestions further. - To collect housing typology in KoBo App
---------------------	---

Why was the visit carried out in this location?

Changunarayan Municipality is in P1 priority as according to HRRP's municipal targeting in shelter reconstruction. Therefore, this Joint Monitoring Visit was organised to observe some of the non-compliance cases and to provide way forward for the beneficiaries whose housing grant application cases were in pending stage in DLPIU Building Bhaktapur.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

<https://drive.google.com/open?id=15Zk2be0hk0rIKjuOJdhOJ3i9YMZFgeHw>
<https://drive.google.com/open?id=1EkLxJjeto6UKq7JspkPYI7G3Zdidd9lq>
<https://drive.google.com/open?id=1Vo7EEB8RtR41q2BFS1Qku1aBbrS8lqW9>

Summary

HRRP Lalitpur District Coordination Team coordinated with DLPIU Building Bhaktapur to conduct Joint M & E Visit in Ward no 8, Sudal Changunarayan Municipality. There were plenty of non compliance cases in row in various parts of Ward no. 8 Sudal. The joint M & E visit team observed nearly 13 houses, out of which majority were wall system brick masonry in cement mortar and stone masonry in mud mortar, have taken 1st tranche only and were non complaint. The reasons of tagging non complaint to the observed houses were due to missing of major bands (sil, lintel, roof) with 9 inch wall on ground floor and attic height increased. The houses that have missed major bands with 9 inch wall on ground floor were suggested to apply correction methods by using chicken wire mess and plastering on it. Toilets were also found missing in majority of 2 rooms plus attic SMM and BMC house. Currently the beneficiaries were using the rebuilt house as storage of fodder, fuelwood and partly as shed house for their cattle. It was revealed from beneficiaries that they have rebuild the house in order to access government grants which they further clarify that if government is providing the grants to the citizens then why not access it.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Beneficiaries are so much concerned and attentive about accessing government grants only rather than rebuilding a compliant and liveable houses	Application of correction methods using chicken wire mess and wall jacketing was suggested to beneficiaries.	Concerned beneficiaries will do their best to apply correction methods to their rebuild houses.	Beneficiaries	As soon as possible

Photos



Beneficiary name: Deepak Phnuyal, Ward no. 8, Sudal, Changunarayan Municipality, 1 storey plus attic wall system BMC house has 2 rooms. Owner has used salvaged material and has received 1 st tranche only. In order to make the house complaint, the owner was suggested to keep a long band right down the roof band and right above the windows in center. The rebuild house is being used as storage of fodder and as shed for cattle.	Beneficiary name: Kanchhi Dangal, Ward no. 8, Sudal, Changunarayan Municipality, 1 storey plus attic wall system BMC house has 2 rooms. Attic height increased and salvaged material has been used. Ground floor has 9 inch wall, corner stitch and bands has claimed to be kept by the owner who has received 1 st tranche and applied 2 nd and 3 rd tranche together. Currently the rebuild house is being used as storage of fodder and as shed for cattle.
--	---

Field Visit Reports (Bhaktapur)

Visit 2		
Date	Location	Participants
7 August 2019	Ward no. 9, Nangkhel, Suryabinayak Municipality, Bhaktapur district	- Ambika Amatya, District Coordinator, HRRP Lalitpur Cluster - Roshan Keshari, M & E Consultant, DLPIU Building Bhaktapur - Prabesh Adhikari, DSE, DLPIU Building Bhaktapur

		- Shiva Prasad Bhandari, DSE, DLPIU Building Bhaktapur - Suraj Shrestha, Engineer, DLPIU Building Bhaktapur - Jeena Suwal, Saru Chansi Shrestha (Engineers Suryabinayak Municipality)
Objective(s)	- To observe the reconstruction status of the houses and provide relevant suggestions further. - To conduct sampling of rebuild houses for 3rd inspection - To collect housing typology in KoBo App	
Why was the visit carried out in this location?		
To conduct sampling of houses for 3 rd inspection.		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
Summary		
HRRP Lalitpur District Coordination Team coordinated with DLPIU Building Bhaktapur to conduct Joint M & E Visit in Ward no 9, Nagkhel, Suryabinayak Municipality. HRRP Lalitpur and Bhaktapur Coordination Team along with M & E Consultant (DLPIU Building Bhaktapur), District Support Engineer and engineers of DLPIU Building Bhaktapur and of Suryabinayak Municipality conducted field visit Ward no 9. The field visit team observed nearly 6 houses in total. The visit was specifically targeted to cover the sampling of 3rd inspection. Meeting with Mr. Dhruba Gaida, Chief, DLPIU GMALI Bhaktapur district The Joint M & E visit team member including of Er, Mahalaxmi Joshi, Chief of Building Bhaktapur, M & E Consultant, DSE, engineers, interacted with Dhruba Gaida, Chief of GMALI Bhaktapur. The agendas of the interaction was – to deploy engineers in ward office, to request palikas to submit list of houses that were soon rebuild ater earthquake and before deployment of engineers, to conduct palika level meeting wit elected officials and chief administration and planning engineers in order to bring synergy in building bylaws and minimum requirement of building code. Meeting with reconstruction engineers of Suryabinayak Municipality Engineers were informed that their contract will be renewed given the timeline of 3 months in which the further renewal will be based on their performances. They were also informed that in order to bring effectiveness in providing technical assistance to houses in rebuilding phases, their presence is utmost required in Ward offices.		
Challenges / Issues Identified	Solutions Provided	Decision Taken
Technical support provided to beneficiaries were not significant as noncompliance cases continued to rise.	Technical personnel deployed in concerned municipalities should assist beneficiaries in rebuilding an earthquake resistant safer houses so that hassles in grant access would be reduced.	To mobilise concerned technical personnel at Ward level by coordinating with Palikas and Ward office.
Photos		
		
Beneficiary name: Ashkumar Kasula, Ward no. 9, Nagkhel, Suryabinayak Municipality, 5 rooms 2 storey RCC house is complaint and has received all 3 tranche from government.	Beneficiary name: Chaityaram Byanju and Shankar Das Byanju (<i>multiple beneficiaries</i>), Ward no. 9, Nagkhel, Suryabinayak Municipality, 2 rooms in each house 1 storey RCC house is complaint and has received all 3 tranche from government. The two rooms each belongs to multiple beneficiary which is separated by two door each.	

Field Visit Reports (Lalitpur)

Visit 3

Date	Location	Participants
8 th August 2019	Ward no 6, Shikharpa, Godawari Municipality, Lalitpur district	- Krishna Lal Piya, Project Chief, GMALI Lalitpur - Jeewan Kumar Ghimire, Section Officer, GMALI Lalitpur - Roshan Raj Giri, M & E Consultant, DLPIU Building Lalitpur - Yamnath Giri, M & E Specialist, EHRP/GMALI Lalitpur - Prajwol Karki, DSE, DLPIU Building Lalitpur - Ambika Amatya, District Coordinator, HRRP Lalitpur - Technical personnel from Godawari Municipality
Objective(s)	- To observe the reconstruction status of the houses taken by Satya Sai Kendra. To collect technical details of the - To take building typology on KoBo Collect App.	

Why was the visit carried out in this location?

Some POs has supported the housing reconstruction of beneficiaries in various parts of Godawari Municipality. Some of these POs have supported rebuilding process without informing GMALI Lalitpur because of which issues of double payments were seen in the MIS systems. In order to track the POs and beneficiaries that have taken double payments, the visit was organised to take details of the houses from technical point of view.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

<https://drive.google.com/open?id=1dws4MdCLIGNqZOO9GGyp2idijNh1tH7z>

Summary

HRRP Lalitpur Coordination Team along with GMALI Lalitpur and M & E Consultant (DLPIU Building Lalitpur), District Support Engineer and engineers conducted field visit Ward no 6, Godawari Municipality. The field visit team observed nearly 6 houses in total. The observed houses reconstructed by Satya Sai Kendra at Shikharpa, Ward no. 6 has 3 rooms with bamboo infill as wall and plastering are done. Steel post are used as frames and CGI sheets as roofing material. A total of 33 houses have been rebuild by Satya Sai Kendra and construction have completed 2 years back.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Double payments issues particularly of beneficiaries who were supported by POs is still taking time to be solved	Beneficiaries will be informed to consult with respective POs and GMALI offices in taking inputs about returning the payments received knowing and unknowing in context of their shelter reconstructed by support from POs.	To inform ward office and municipalities to help in this process of reducing the double payments issues	DLPIUs (Building, GMALI) Engineers, POs, Beneficiaries	As early as possible.

Photos



Image: A typical house made from support of Satya Sai Kendra at Ward no. 6, Shikharpa, Godawari Municipality. 3 rooms with bamboo infill as wall and plastering are done but no toilet. Steel post are used as frames and CGI sheets as roofing material.



Beneficiary name: Sanumaiya Nagarkoti, Ward no. 6, Shikharpa, Godawari Municipality, 3 rooms with bamboo infill as wall and plastering are done but no toilet. Steel post are used as frames and CGI sheets as roofing material.

Housing Typology Report (Max 4 Photos, Select best photos from each district)



Beneficiary name: Ward no. 5, Changunarayan Municipality, 1 storey load bearing BMC. Non-compliance structure (missing beam, bands). The house was constructed immediately after earthquake.



Beneficiary name: Jiban Poudel, Ward no. 2, Changunarayan Municipality, Bhaktapur, RC frame structure, non-compliance (9"X12" column- unsafe during analysis), constructed immediately after earthquake



Beneficiary Name: Hubbaraj Sapkota, Ward no. 4, Kaleshwor, Mahankal Rural Municipality. Load bearing 1 storey SMC house plus attic has requested for 3rd tranche during inspection. Date: 180915



Beneficiary Name: Bhakta Bahadur Waiba, Ward no. 4, Kaleshwor, Mahankal Rural municipality. Load bearing 1 storey BMC house plus attic has requested for 3rd tranche during inspection. Date: 180915

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
How to access subsidized loans by those who are financially poor, yet willing to reconstruct their houses?	Ward Member	The beneficiaries who have not been able to reconstruct their private houses even after taking the first tranche of Rs. 50,000 can now take a loan of up to Rs. 300,000. Such facility is provided under the Integrated Guideline on Interest Exemption for Subsidized Loan approved by the government last year. Representative from DLPIUs (Building and GMALI)

Questions Collected

What are the criteria for forwarding files of houses having multiple beneficiaries living in single house?	Beneficiary	Regarding multiple beneficiaries, if they have two entrance doors and two staircases to reach two different houses in same plot of land, and have Building permit and joint land certificates, then tranche application of such houses can be forwarded. (M & E Consultant, DLPIU Building)
--	-------------	---

Challenges and Way Forward

Challenge	Way Forward
Beneficiaries are more concerned in taking government grants rather than increasing their resilience towards future disaster shocks	Responsible agencies should properly inform beneficiaries in rebuilding a proper and liveable shelter by using government's grant. Further, current reconstruction practices and processes should leave meaningful impact in communities with a concept of build back better and increasing resilience of communities towards shocks of future earthquake and other types of disasters.
Thousands of beneficiary despite of taking 1 st tranche from NRA have not started reconstructing their houses damaged from earthquake	Concerned DLPIUs (Building & GMALI office) are aware of this fact. Discussions have been raised so that concrete steps can be taken to curtail the names of beneficiaries that have taken 1 st tranche and not have reconstructed their houses yet. Further, there is need of conducting periodic visit to Ward office, clarify the queries and information of grant access process, about housing designs, about building code, minimum requirements etc. to Ward office, as particularly elected Ward Chiefs are the first port of call to address relevant queries in their Ward areas.
