

# District Report

## Nuwakot

21 Dec 2018 – 3 Jan 2019

| Summary of events during this period                                                                                                                                                                                                                                                                                                                                                                                                                                                            |              |                      |        |                                                                                                                                                    |                                                                       |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------|----------------------|--------|----------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------|
| Name of activity/event                                                                                                                                                                                                                                                                                                                                                                                                                                                                          | Event date   | Participants summary |        | Contact Person                                                                                                                                     | Reference Document                                                    |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 |              | Male                 | Female |                                                                                                                                                    |                                                                       |
| Participate in Stakeholder discussion organized by Transparency International Nepal. TI Nepal is working for good governance on reconstruction activities. HRRP Dc has presented the reconstruction activities, its issues and challenges as the part of GMALI Nuwakot.                                                                                                                                                                                                                         | 26 Dec, 2018 |                      |        | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a>                                                                             |                                                                       |
| District Coordination Meeting:<br><b>Oxfam</b> has program to support to the 240 relocated beneficiaries from different parts of Nuwakot District. But now most of the activities are halted due to the tranche issues. That means most of the beneficiaries have taken the second and third tranche for the construction of vulnerable place. Oxfam has requested the appropriate solution. The next issue is that Japhati, Shanti Bazaar and Darne has link road issue to the purchased land. | 26 Dec, 2018 | 10                   | 3      | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a><br><a href="mailto:/im.nuwakot@hrrpnepal.org">/im.nuwakot@hrrpnepal.org</a> | <a href="#">Meeting Minutes</a>                                       |
| <b>District Level Palika orientation:</b> 11 Palika representatives were presented in the orientation. Chandra Bahadur Shrestha, Executive Member of NRA and Other representatives from different organization were presented. GMALI, DLPIUs (Building, Education) has presented the progress.                                                                                                                                                                                                  | 30 Dec, 2018 |                      |        | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a><br><a href="mailto:/im.nuwakot@hrrpnepal.org">/im.nuwakot@hrrpnepal.org</a> | <a href="#">Photos</a>                                                |
| District Level Reconstruction Committee Meeting and MoU signing program: Mr Narayan Khatiwada Member of Legislation has represented as the chair of the meeting. Most of the member of Sangh and Pradesh have presented in the meeting. 12 Different Decision has made during the Meeting.                                                                                                                                                                                                      | 31 Dec, 2018 |                      |        | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a><br><a href="mailto:/im.nuwakot@hrrpnepal.org">/im.nuwakot@hrrpnepal.org</a> | <a href="#">Meeting Minutes</a><br><br><a href="#">MoU Panchkanya</a> |

### Summary of events during this period

|                                                                                                                                                                                                                                                                                                                  |             |  |  |                                                                                                                                                    |  |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--|--|----------------------------------------------------------------------------------------------------------------------------------------------------|--|
| MoU: MoU Between palika and Gmali has signed, Bidur and Belkotgadhi Municipality, Kakani, Dupcheswar, Tadi Tarakeswar, Meghang, Kispang Likhu, Panchkakanya were presented. Two RM Suryagadhi and Shivapuri were not presented in the meeting. DCC will coordinate to sign the MoU for the Rural Municipalities. |             |  |  |                                                                                                                                                    |  |
| Coordinate with NGOs coordinate for 5w data and training database update.                                                                                                                                                                                                                                        |             |  |  | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a><br><a href="mailto:/im.nuwakot@hrrpnepal.org">/im.nuwakot@hrrpnepal.org</a> |  |
| Communicating and working with POS for 5W and training database update (room to read, MI, UNOPS, ACF and NSET                                                                                                                                                                                                    |             |  |  | <a href="mailto:im.nuwakot@hrrpnepal.org">im.nuwakot@hrrpnepal.org</a>                                                                             |  |
| Data updated in Google sheet and action plan update                                                                                                                                                                                                                                                              |             |  |  | <a href="mailto:im.nuwakot@hrrpnepal.org">im.nuwakot@hrrpnepal.org</a>                                                                             |  |
| Participated in the DPACK meeting of HFH/ASF, Review session of reconstruction on salme <b>(First tranche 99, second 97)</b>                                                                                                                                                                                     | 28 Dec 2018 |  |  | <a href="mailto:im.nuwakot@hrrpnepal.org">im.nuwakot@hrrpnepal.org</a>                                                                             |  |
| 5W uploaded in the drive                                                                                                                                                                                                                                                                                         | 26 Dec 2018 |  |  | <a href="mailto:Im.nuwakot@hrrpnepal.org">Im.nuwakot@hrrpnepal.org</a>                                                                             |  |
| Field visit to Chaughada, 01 Panchakanya along with team DLPU GMALI, DUDBC, Ward chair, Gaupalika President, Journalist for monitoring field. Details are written below                                                                                                                                          | 03 Jan 2019 |  |  | <a href="mailto:Im.nuwakot@hrrpnepal.org">Im.nuwakot@hrrpnepal.org</a>                                                                             |  |

### Upcoming Events & Meetings

| Name of activity/event            | Date, Time, and Location | Organizer    | Contact Person                                                                                                                                     |
|-----------------------------------|--------------------------|--------------|----------------------------------------------------------------------------------------------------------------------------------------------------|
| Palika Level Coordination Meeting |                          | HRRP Nuwakot | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a><br><a href="mailto:/im.nuwakot@hrrpnepal.org">/im.nuwakot@hrrpnepal.org</a> |


## Tranche Status

| Rural /Municipality        | Belkotgadhi NP | Bidur NP | Dupcheshwor RM | Kakani RM | Kispang RM | Likhu RM | Meghang RM | Panchkanya RM | Shivapuri RM | Suryagadhi RM | Tadi RM | Tarkeshwaor Rm |
|----------------------------|----------------|----------|----------------|-----------|------------|----------|------------|---------------|--------------|---------------|---------|----------------|
| Total HHs Surveyed         | 9409           | 11203    | 5448           | 6157      | 1816       | 4003     | 4052       | 3692          | 5616         | 4197          | 4231    | 3760           |
| Total HHs Eligible         | 11036          | 12667    | 5873           | 6916      | 2369       | 5107     | 4500       | 4226          | 6513         | 5019          | 4604    | 4353           |
| Total HHs Enrolled         | 11278          | 12544    | 5911           | 6918      | 2375       | 5164     | 4471       | 4178          | 6604         | 5186          | 4646    | 4156           |
| First Tranche              | 9651           | 11316    | 5486           | 6159      | 4164       | 4060     | 4023       | 3843          | 5707         | 4364          | 4413    | 3772           |
| Second Tranche             | 8560           | 10329    | 5206           | 5397      | 3900       | 3652     | 3844       | 3622          | 4988         | 4008          | 4136    | 3531           |
| Third Tranche              | 300            | 4250     | 3069           | 2733      | 2362       | 1987     | 2847       | 1930          | 2725         | 1754          | 2249    | 2359           |
| Grievance Registered       | 2271           | 1693     | 425            | 1389      | 809        | 1329     | 511        | 910           | 995          | 923           | 701     | 672            |
| Grievance Addressed        | 1627           | 1464     | 425            | 759       | 553        | 1104     | 448        | 534           | 897          | 822           | 373     | 593            |
| RF HH Eligible             | 256            | 236      | 35             | 160       | 25         | 154      | 141        | 88            | 63           | 16            | 23      | 247            |
| RF HH Enrolled             |                | 18       | 1              | 44        |            | 9        |            | 18            | 1            | 44            |         | 9              |
| RF 1 <sup>st</sup> Tranche |                | 18       | 1              | 44        |            | 9        |            | 18            | 1            | 44            |         | 9              |
| RF 2 <sup>nd</sup> Tranche |                |          |                |           |            |          |            |               |              |               |         |                |


as of 1<sup>st</sup> Dec 2018.

Source : GMALI Nuwakot

### Palika wise representation - Tranche Status

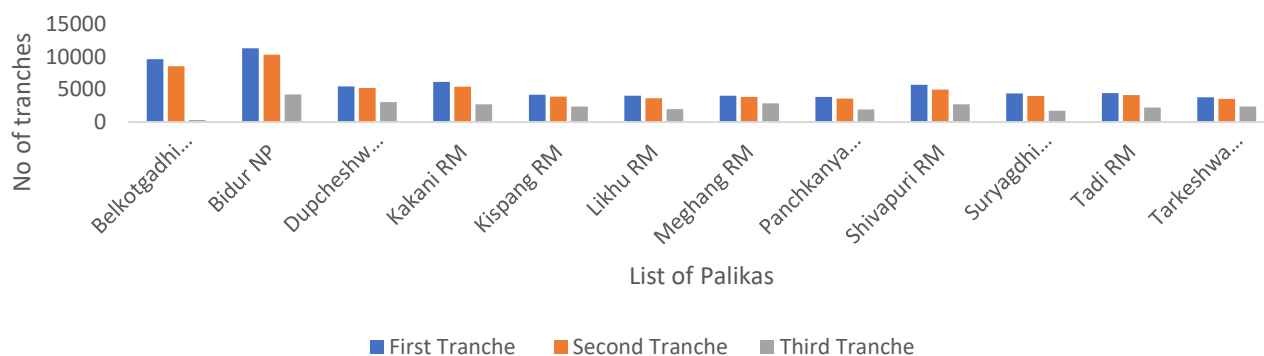

### Grievance Registered Vs Grievance Addressed

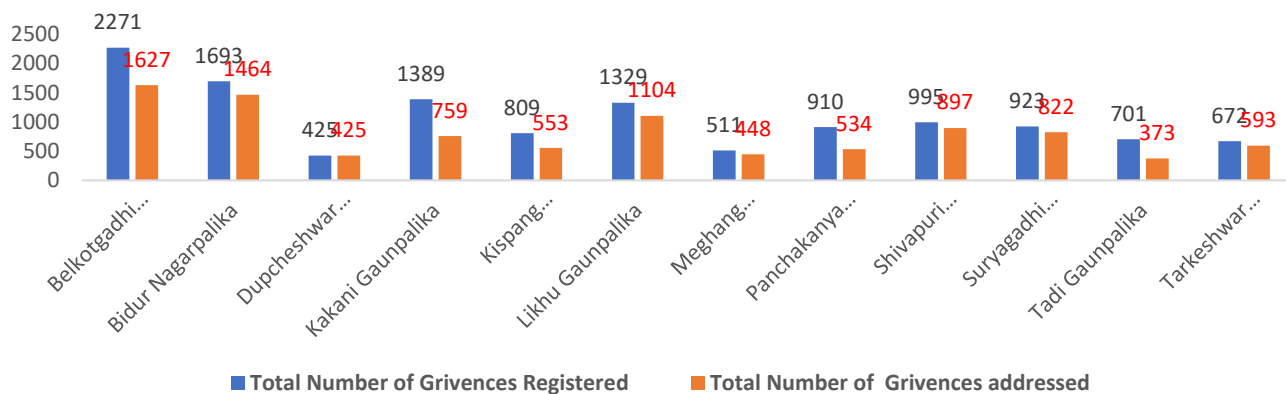

## Field Visit /Joint Field Monitoring Visit Reports

### Visit 1

| Date        | Location                   | Participants from HRRP and stakeholders                                                                                                                                           |
|-------------|----------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 3 Jan, 2019 | Panchakanya-1, AApatchaura | <ul style="list-style-type: none"> <li>Buddhasing Thakuri, IM Officer HRRP</li> <li>Satyanarayan Chaudhari, M&amp;E NRA</li> <li>Binod Adhikari, MIS Specialist, GMALI</li> </ul> |

### Objective(s)

- Objective 1: Joint Monitoring to assist on technical problem identification and Solution
- Objective 2: To know the reconstruction trend and highlighting the issues related to grant
- Objective 3: To understand the field challenges and best practice

### Summary

Panchakanya Gaupalika Ward 01, Former Chaghada – 04, They initially planned for 255 beneficiaries, but NRA identified only 220 beneficiaries and they provide first tranche to 218, second tranche to 218 and third tranche to 153 households. The partner MI/RSDC, DLPIU GMALI, DUDBC, HRRP, Ward chair, Palika President and TV journalist combinedly monitored the field. The best thing is that almost all the houses are built for the living purpose so that there are only 3-5 numbers of one room house which is the needy one. The local masons are used for the reconstruction. At the same time, they have been supporting for building **health post, WASH and planning for livelihood**. Since start of the project, they are supporting to all the beneficiaries for technical assistance and community orientation which results compliance on the field.

| Challenges / Issues Identified                              | Action Required                            | Responsible             | Timeframe |
|-------------------------------------------------------------|--------------------------------------------|-------------------------|-----------|
| Transportation of reconstruction Materials                  | promote to use locally available materials | POs, Ward offices       | Regular   |
| Quality of reconstruction materials                         | Quality assurance to local supplier        | DCC, Rural Municipality | Regular   |
| Social Issues                                               |                                            |                         |           |
| Technical Issues on retrofitting, Vulnerable groups support |                                            |                         |           |

### Photos



House Owner: Kanchi Rai  
Location: Chaughada, 01-Panchakanya Gaupalika.

House Owner: **Ward 1 - Health Post**  
Location: Chaughada, 01-Panchakanya Gaupalika



Tranche Status: Third Tranche taken  
Supported by Malteser international (RSDC) for providing third tranche and technical assistance  
*Photo: Buddha Singh Thakuri*

MI/RSDC supported to build 4 room health post for ward.  
Timeline (Within April). Local trained masons used


*Photo: Buddha Singh thakuri*

## Housing Typology Report



House Owner: Guman Sing Rai (83 Years Old)  
Location: Chaughada, Panchakanya 01  
Tranche Status: RSDC supported to build one room house for House owner because he is still living in cracked house thus, they decided to build by using CSEB blocks.  
*Photo: Buddha Singh Thakuri*

House Owner: Fulmaya Rai  
Location: Chaughada, 01 Panchakanya  
She has already taken second tranche but waiting for third tranche.  
*Photo: Buddha Singh Thakuri*

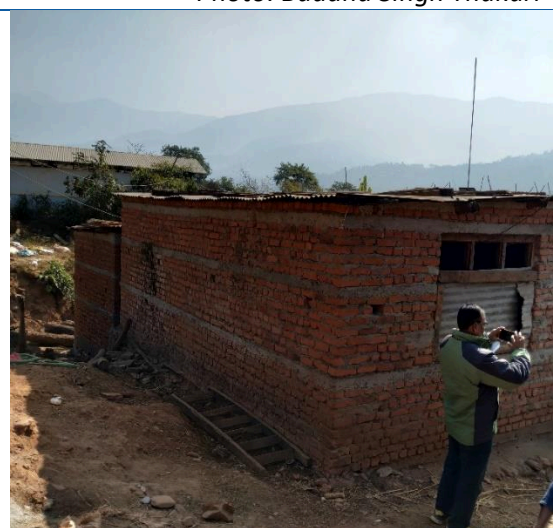

House Owner: Man Bahadur Rai  
Location: Chaughada 01, Panchakanya  
3<sup>rd</sup> tranche taken  
*Photo: Buddha Singh Thakuri*

House Owner: Madhusudhan Phuyal  
Location: Chaughada 01, Panchakanya  
Tranche Status: 3<sup>rd</sup> tranche taken  
*Photo: Buddha Singh Thakuri*

|                                                                                                                                       |                                                                                                                                      |
|---------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------|
|                                                       |                                                    |
| <p><b>Program Preparation Meeting:</b> In 29 December Evening, has conducted a meeting as preparation for the Palika Orientation.</p> | <p><b>Meeting Of District Coordination Committee:</b> Chaired by Mr. Narayan Khatiwada Legislative member from Nuwakot District.</p> |
|                                                      |                                                   |
| <p><b>Progress:</b> Presentation From Gmali and DLPIU (building &amp; Education) have presented the presentation in orientation.</p>  | <p><b>Smiling after MoU Signing:</b> MoU signed and exchanged between GMALI and Myaghang RM.</p>                                     |

## Challenges and Way Forward

| Challenge                                                                                                                                                                                                           | Way Forward                                                                                                                    |
|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------|
| <p><b>Lack of technical assistance in the hard to reach field area.</b> NRA engineers are not in regular monitoring to the house. When they visited for the inspection, they only commented for non-compliance.</p> | <p>MOUD-DLPIU should monitor the engineer and instruction for regular visit.</p>                                               |
| <p><b>Delayed and partial addressing of grievance.</b> Real victim from the earthquake has not addressed as beneficiaries. They have applied for grievance many times but not addressed.</p>                        | <p>NRAs should address as soon as possible by the help of local elected persons, Like ward chair and other members.</p>        |
| <p><b>When will retrofit start?</b> People don't have trained manpower for the retrofit, they are waiting the response from NRA side.</p>                                                                           | <p>Training and other technical issue with proper communication to the common people should be done before monsoon starts.</p> |
