

District Report

Nuwakot

15 February - 14 March 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Attend District Coordinator's Meeting in HRRP Head Office.	February 15 , 2019			dc.nuwakot@hrrpnepal.org	
Discussion with Transparency International: working agencies on reconstruction, progress VS expense	February 20, 2018			dc.nuwakot@hrrpnepal.org	
Update planning follow up to Palika. 7 Palika has update the planning in their website.	February 20, 2018			dc.nuwakot@hrrpnepal.org	<i>Emails</i>
Field Visit to Suryagadhi-4, Haldekalika. Oxfam has supported to build 14 hh from lachyang VDC. 10 hh are completed and Oxfam and its implementing partner has planning to complete it all with in March 2019.	February 25, 2018			dc.nuwakot@hrrpnepal.org	<i>See Detail in field visit Section</i>
District Coordination Meeting: Most of the private housing has completed. Some issues are remained, landless, zeohazzard relocation, grievance address. 77 landless application has addressed. 307 relocation have purchased land in secure place. Retrofitting has not started yet. POs should concentrate to support for vulnerable people.	February 27 , 2019	15	3	dc.nuwakot@hrrpnepal.org	<i>meeting minute</i>
Phone and Email follow up to Palikas for the reconstruction planning. 11 Palika has send signed palika level reconstruction Planing, update on respective website.	March 5-12, 2019			dc.nuwakot@hrrpnepal.org	
Participate in district level Reconstruction Facilitation Committee. –The Meeting was chaired by SantaMan Tamang, DCC Nuwakot, Uddaba Bdr. Thapa CDO Nuwakot and all representatives are presented. Major three decision has made:	March 13, 2019			dc.nuwakot@hrrpnepal.org	

Summary of events during this period

1. Meeting with bank representative has called in 19 Mach to sort out the long hold beneficiaries' amount by some banks. 2. To release the tranche to the relocated beneficiaries, decision will take after field visit report. 3. Recommendation issue of Suryagadhi will be finalized after the field visit report of GMALI.					

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
District Level Coordination Meeting		HRRP Nuwakot	dc.nuwakot@hrrpnepal.org /im.nuwakot@hrrpnepal.org

Tranche Status												
Rural /Municipality	Belkotgadhi NP	Bidur NP	Dupcheshwor RM	Kakani RM	Kispang RM	Likhu RM	Meghang RM	Panchkanya RM	Shivapuri RM	Suryagadhi RM	Tadi RM	Tarkeshwaor Rm
Total HHs Surveyed	9409	11203	5448	6157	1816	4003	4052	3692	5616	4197	4231	3760
Total HHs Eligible	11037	12893	5873	6916	4788	5109	4510	4460	6514	5019	4590	4707
Total HHs Enrolled	10348	11960	5661	6395	4510	4726	4263	4239	6108	4879	4468	4318
First Tranche	10348	11960	5661	6395	4274	4726	4263	4239	6108	4879	4468	4318
Second Tranche	8923	10578	5346	5598	3872	3817	3992	3687	5249	4151	4096	3874
Third Tranche	3022	7093	4051	3466	2693	2631	3522	2509	3592	2599	3095	3082
Total HH Constructed												
Grievance Registered	2271	1693	425	1389	809	1329	511	910	995	923	701	672
Grievance Addressed	1627	1464	425	759	553	1104	448	534	897	822	373	593
RF HH Eligible	256	236	35	160	25	154	141	88	63	16	23	247
RF HH Enrolled		18	1	44		9		18	1	44		9
RF 1 st Tranche		18	1	44		9		18	1	44		9

as of March 13, 2019.


Source : GMALI Nuwakot

Graph of Tranche Status:

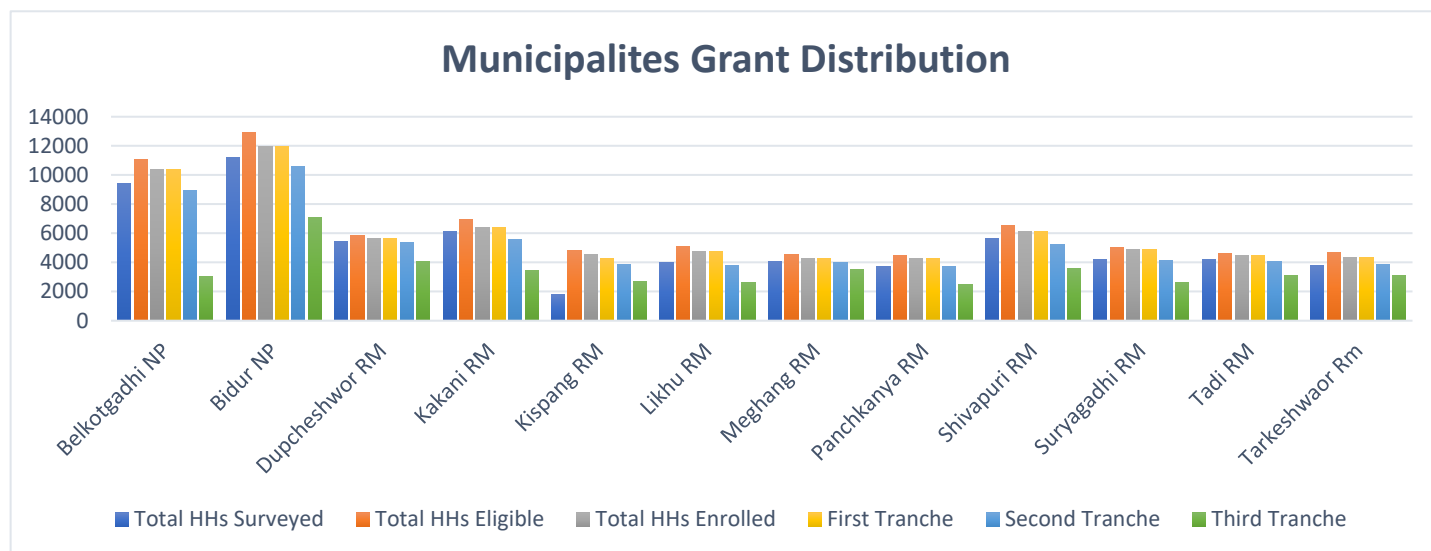

Graph for Retrofitting Status: NA

Graph for Grievance Status:

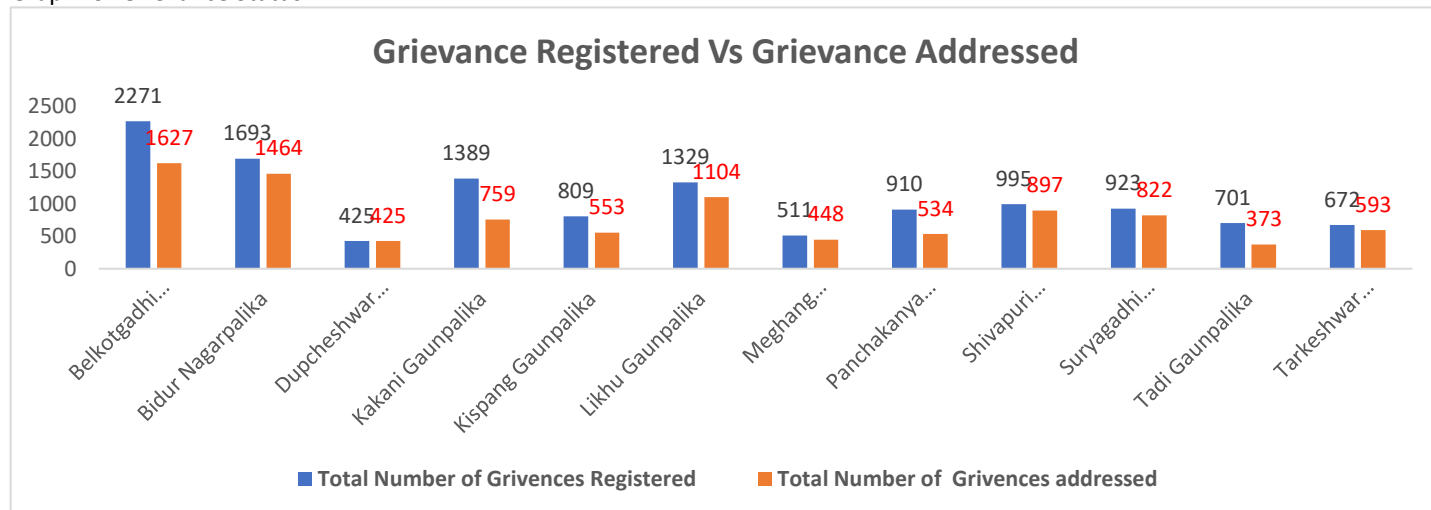

Field Visit /Joint Field Monitoring Visit Reports

Visit 1		
Date	Location	Participants from HRRP and stakeholders
Feb 25, 2019	Suryagadhi Rural Municipality ward no-4, Haldekalika	- Badri Pyakurel, DC HRRP - Bickey Lakha, Act GMALI Chief, Nuwakot
Objective(s)		

- Objective 1: Monitoring the activities performed by KCDC IP of Oxfam
- Objective 2: To know the reconstruction trend and highlighting the issues related to grant
- Objective 3: To understand the field challenges and best practice

Summary			
KCDC, Implementing partner of OXAM, is working for relocated hh from Lachyang VDC. 14hh are relocated from Lachyang. The relocation place is nearby area of former Lachyang VDC. Oxfam has support for the private housing through the skill transfer, training to the local for CSEB construction. National Reconstruction Authority (NRA) has support to them for land purchase and all construction activities are being conducted with support from OXFAM. Among the 14, 10hh are in final stage of roofing and 1 in on foundation construction and 3 has plan to start. KCDC has informed to the team, the program has plan to complete with in March 2019. The Program has support on wash, irrigation canal for host community as well. It has program of water supply project to the hh and host community. Host community has involved for livelihood support program through skill development.			
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Lack of House owner's Participation in Construction.	Support organization should involve in Social Mobilization Process	Support Organizations.	Regular
Transportation of reconstruction Materials	promote to use locally available materials	POs, Ward offices	Regular
Lack of trained mason	training to local mason for retrofitting	POs and NRA	Regular
Lack of Information regarding the technical on retrofitting and correction.	Training/orientation engineers deployed in local level.	POS, NRA	As soon as possible.

Photos



Display board in Project site. We can see the project cost, benefitted family, project duration and project activities are detailed in the board. The board has installed in project site.

Relocation area from Lachyang-9. 14 hh are relocated. NRA has support to buy the land and Oxfam has support to build the houses and livelihood support through skill development in different field of agricultural production.

Housing Typology Report



House Owner: Sukradev Lama
Location: Suryagadhi-4, Haldekalika
Typology: BMC (Cost; approx. 6 lakh)
Tranche Status: non listed beneficiaries. Waiting for grievance list.

Photo: Badri Pyakurel



House Owner: Sukalal Lama
Location: Suryagadhi-4, Haldekalika
Typology: Stone mud mortar with cement plaster (the owner has plan for next storey)
Tranche Status: has received 3rd tranche.

Photo: Badri Pyakurel



House Owner: Sanu Tamang
Location: Suryagadhi-4, Haldekalika
Typology: Stone mud mortar (SMM)
Tranche status: has received 3rd tranche.

Photo: Badri Pyakurel



House Owner: Relocated 14 HH from Lachyang
Location: Suryagadhi-4, Haldekalika
Typology: CSEB Block with truss roof.
Tranche status: Oxfam has support for the construction.

Photo: Badri Pyakurel



Oxfam's Implementing Partner, Sahayata Samajik Sanstha (SSS) has support to adolescent girl's friendly toilet in Kundala Basic School, Suryagadhi-4, Haldekalika.

Chair Person of SSS, Shivaram Rijal has handed over the construction to Palika Chair Santa Bahadur Tamang, Suryagadhi RM.
