

Fortnightly District Report

Dhading

18 - 31 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Joint monitoring visit at Palika offices with CLPIU/Building- M&E, DLPIU/Building and GMaLI regarding: - Palika action plan orientation, compilation and collection through palika offices. - Discussion on palika profile with Gajuri, Benighat-Rorang, Galchi, Thakre and Dhunibesi palikas of the district.	21-25 Jan. 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	Detail at field visit section 1
Central NRA meeting with DLPIU-Building, GMaLI, DCC, DAO and DLPIU-Education at District Coordination Committee office.	25 Jan. 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	Detail at New and update.
Informal discussion with GMaLI on joint monitoring visit of government authorities and partner organizations.	19 th Jan 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	
Joint monitoring field visit at Palika offices (Tripurasundari RM, Gangajamuna - Ree VDC, Khaniyabas RM) with CLPIU/Building- M&E, DLPIU/Building and GMaLI regarding: 1) Palika and ward level meeting and discussion on status of reconstruction. 2) Housing typology observation and collection. 3) Preparation of Palika's Action Plan. 4) Interaction with ward beneficiaries on housing reconstruction issues and collection of success stories. 5) Non-Compliance issues at these rural municipalities. 6) Discussion on palika action plan at all palikas.	28 Jan. – 1 Feb. 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	Detail at field visit section 2


Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Support GMaLI on PA collection from Bank offices.	6 th – 8 th Feb. 2019.	GMaLI	dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org
DFID partners meeting	6 th Feb 2019	DFID	Ishwar Pudasaini
District Coordination Meeting	13 th Feb 2019	HRRP	dc.dhading@hrrpnepal.org

Tranche Status

Rural /Municipality	Beni Ghat Rorang RM	Dhuni Besi M	Galchi RM	Gan gajamun a RM	Gajuri RM	Jwala mukh i RM	Khaniy a bas RM	Netra wati RM	Nil khanta M	Ruby Valle y RM	Siddha lekh RM	Thak r RM	Trip ura Sund ari Rm
Total HHs Surveyed	5501	7499	6724	6732	5625	6014	3632	4016	13471	3270	5975	6722	6474
Total HHs Eligible	4910	7158	5997	6447	5105	5390	3469	3866	12183	2850	5359	6384	5697
Total HHs Enrolled	4349	6582	5657	6339	4655	4910	3392	3694	11601	2734	5034	6024	5561
First Tranche	4349	6582	5657	6339	4655	4910	3392	3694	11601	2734	5034	6024	5561
Second Tranche	3682	4328	4978	5637	4100	3760	2948	3274	9514	2282	4358	4753	4878
Third Tranche	2393	2901	2300	3958	2602	2664	1837	2708	7134	1537	3045	2751	3343
Total HH Constructed	2507	3177	2545	4252	2731	2848	1874	2782	7826	1615	3395	3419	3499
Grievance Registered	1690	1067	1273	720	1427	2424	658	641	2394	650	1521	1310	1002
Grievance Addressed	599	356	728	285	530	700	164	153	1374	420	640	341	785
RF HH Eligible	618	98	314	42	432	675	12	43	559	187	463	255	215
RF HH Enrolled	618	98	314	42	432	675	12	43	559	187	463	255	215
RF 1 st Tranche	0	9	36	2	45	35	0	1	53	43	0	10	10
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	22	252	130	31	268	87	7	27	281	0	291	275	144
Non-Compliance Addressed	20	174	91	27	207	73	7	22	210	0	219	160	126

Palika wise Trache Status :-

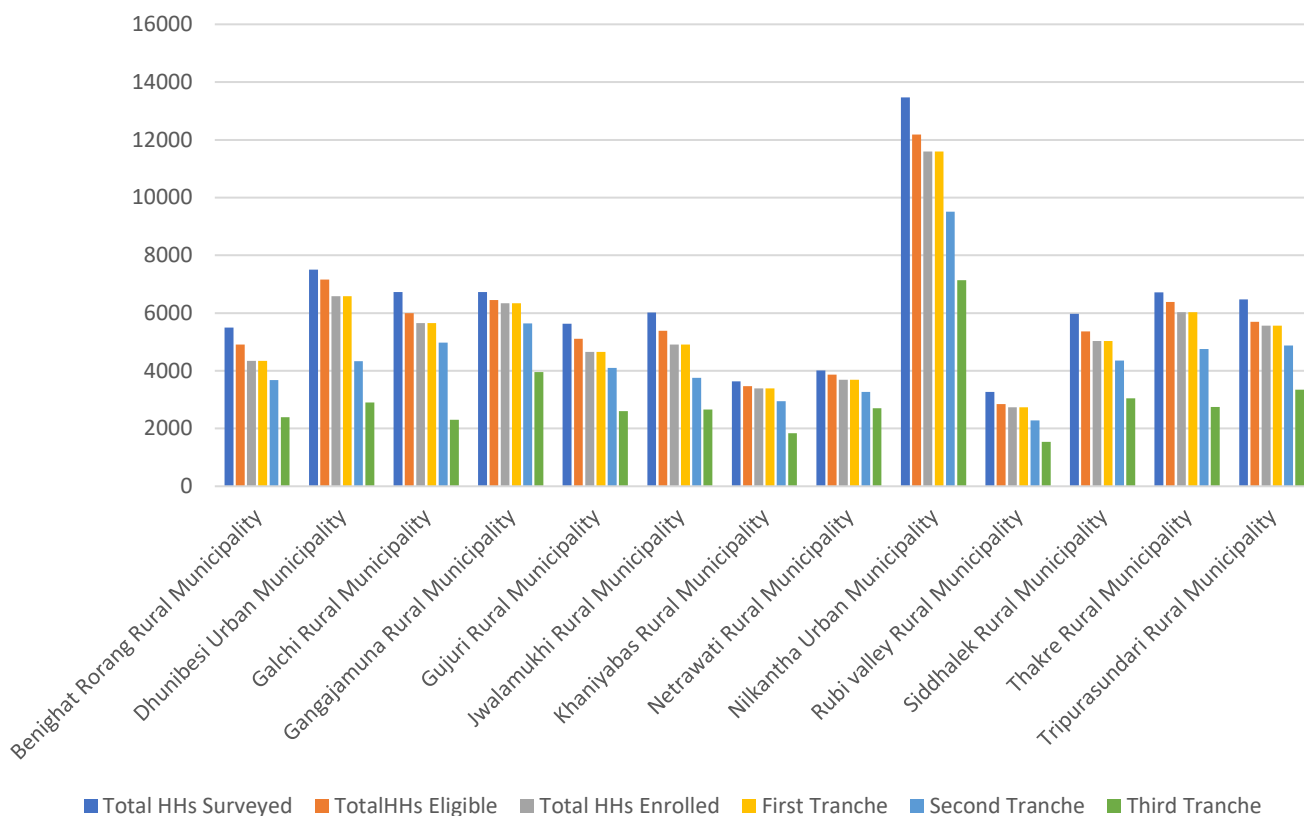

News & Updates

- 1) **NRA CEO Susil Gyawali visited Dhading district offices and conducted a close coordination meeting with DLPIU-Building, GMaLI, DCC, DAO and DLPIU-Education on 25th January 2019 at District Coordination Committee hall.**

A sudden visit was carried out by NRA CEO Susil Gyawali at Dhading district on Friday 25 January 2019. Immediately, all major government stakeholders were called for close coordinated interaction regarding ongoing reconstruction progress, challenges and way forwards. The program was conducted by DLPIU/Building. The discussion was focused on only one agenda:



a) Partner Agreement (PA) digitalization.

As per World Bank requirement, beneficiary agreement cards need to be digitalized for reimbursement of grant amount.



NRA CEO highly emphasized to work on the regard from DLPIU/Building and GMaLI. He suggested that those PA which have not been collected yet from Palika/ward offices must be collected from banks.

While the bank may or may not have all beneficiary agreement cards, in such cases the field level NRA engineers need to collect them using tablets. There has been a huge gap in PA digitalization of Dhading, around 10-11 thousand PAs needed to be immediately collected, digitalized and uploaded in the system.

As per CEO, all these tasks can be prioritized in either manner i.e. collect it from beneficiary at field or from bank offices. Majority of the NRA engineers raised questions on unavailability of tablets with them and the software used to upload detail and photos have bugs that need corrections from MIS developer.

Joint Monitoring Field Visit Report

Visit 1

Date	Location	Participants from HRRP and stakeholders
21 – 25 January 2019	Gajuri RM, Benighat-Rorang RM, Galchi RM, Thakre RM and Dhunibesi municipality offices	- Prabin Gautam (HRRP-DC) - Sachin Sapkota (HRRP-DTC) - Khagendra Awasti (CLPIU-M&E) - Rajesh Shrestha (NRA/DSE) - Ananda Raj Pandey (GMAI)

Objective(s)

- Field visit at Palika offices.
- Conduct orientation on development of palika action plans.
- Housing typology observation and collection.

Summary

- 1) A joint field visit was conducted at palika offices regarding orientation on Palika Action Plans and palika profile.

At Thakre RM, the palika mayor mentioned that there are about 49 households (HHs) who have been living at other's property since five generations. These HHs are unable to sign agreement with NRA for government grant support due to lack of land certificate. As per NRA, they are eligible to receive two lakhs land grant for buying new land but those HHs don't want to leave the place of origin. Due to this, those earthquake victims have not started constructing their houses yet.

The palika mayor said that, "As they have been living at that place for more than 5 generations, they should not be displaced from their place of origin even while the land belongs to owner".



Photo: - Jointly Observing Load Bearing Masonry Structure

It is a one storey load bearing masonry structure with CGI sheet as roofing. In ground floor beneficiary uses block and brick as masonry along with horizontal sill bands. Some of the portion of masonry are done by brick while most of the part are block masonry. The Beneficiary has received second tranche.

- 2) HRRP conducted Palika level meeting at Benighat Rorang Rural Municipality in presence of Palika chief and Chief Administrative officer on 22nd Jan 2019. The meeting was focused on Reconstruction Burning issues and challenges.

In Benighat Rorang(BR) Rural Municipality The beneficiaries were having trouble through grievance resolving delay. People had claimed the registration for listing as beneficiaries through NRA grievance process. Most of them have not constructed their houses because of delay of grievance result and waiting for government grant support. The availability of NRA engineers was satisfactory within the Rural Municipality. Benighat-Rorang RM Chief have less understandings about reconstruction and don't have good coordination with Technical group (NRA engineers). We try to explain about the process and guidelines, but he did not respond positively and leave the floor. Engineer are facing a bit problem in BR Rural Municipality due to the negative attitude of Palika chief with the Technical Group.



Photo: - Palika Level Meeting at Benighat Rorang Rural Municipality

- 3) We had Informal meeting with Technical group of Benighat Rorang Rural Municipality i.e. Engineer, Sub-Engineer & Assistant Sub Engineer on 22nd Jan 2019 regarding Non-Compliance Issues of the ward.



As per close discussion with them, some of the Non-compliance's issues in RCC Structure and Load Bearing

Structure are as follows: -

1) Non-Complaint Issues in RCC Structure

- Plan and Elevation Irregularities
- Less Reinforcement in Column Beam i.e. Less than 8 nos.
- Room area greater than 13.5 Sqm.
- One bay Building.
- Column size less than (12 x 12) inch.
- Insufficient foundation size.
- Aspect Ratio.
- Missing Grid Column.
- Insufficient Lap.
- Insufficient Anchorage bonding.
- Haphazard lapping in beam and column

2) Non-Complaint Issues in Load Bearing Structure

- Structural span more than 4.5 mts.
- Missing band i.e. horizontal band, Vertical band, sill band, Lintel band, Plinth band, roof band etc.
- Insufficient foundation size.
- Lack of through stone.
- Inappropriate Position and Size of Opening

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Benighat-Rorang RM officers have less understandings about reconstruction with NRA engineers and did not respond positively with the team.		Palika officer.	
Palika focused on providing all grant supports to those beneficiaries who have not followed NRA guidelines and built non-compliance houses.		Palika, GMaLI and NRA-engineers.	
Issue on delay of grievance resolving from NRA. Beneficiaries claim that they have registered grievance more than two times but, yet no result/solutions have come out.		GMaLI and Ward	

Housing Typology Report



Name: - Rajan Paudel

Location: - Thakre Rural Municipality, Dhading

It is one storey special moment resisting frame structure (RCC) with material used M20 Grade of concrete in pillar, beam, band and 9" infilled wall with brick in cement mortar (1:4). Its floor area is less than 1000 sqft whose Column size is (9" x 12") with 6-12mmØ. The beneficiary has received 2nd tranche of government grants.



Name: - Timba Prasad Nepal

Location: - Thakre Rural Municipality, Dhading

It is two storey special moment resisting frame structure (RCC) with material used M20 Grade of concrete in pillar, beam, band and 9" infilled wall with brick in cement mortar (1:4). Its floor area is more than 1000 sqft whose beam size is (9" x 13") with 4-16mm Ø and Column size (12" x 12") with 4-16mm, 4-12mmØ. The beneficiary has received All Tranche of government grants.



Name: - Aatma Ram Tamang

Location: - Ramche – 07, Thakre Rural Municipality, Dhading

It is one storey load bearing structure with material used burned brick with cement mortar. Its floor area is less than 1000 sqft. He has use vertical pipes in place of vertical rod deu to which engineer has send this file to DSE for analysis. The beneficiary has received 1st tranche of government grants.



Name: - ChandraKant Duwadi

Location: - Nalang, Siddhalekh Rural Municipality, Dhading

It is a one storey plus attic stone mound mortar load bearing structure. Its floor area is less than 1000 sqft. The height of building is more than mention in the MRT. The beneficiary has received 2nd tranche of government grants.

Joint Monitoring Field Visit Report

Visit 1

Date	Location	Participants from HRRP and stakeholders
28 th Jan – 1 st Feb 2019	Tripurasundari Rural Municipality Gangajamuna Rural Municipality Khaniyabas Rural Municipality	- Prabin Gautam (HRRP-DC) - Sachin Sapkota (HRRP-DTC) - Khagendra Awasti (CLPIU-M&E) - Rajesh Shrestha (NRA/DSE) - Ananda Raj Pandey (GMAII)

Objective(s)

- Palika level meeting and discussion on status of reconstruction.
- Housing typology observation and collection.
- Preparation of Palika's Action Plan.
- Interaction with ward beneficiaries on housing reconstruction issues and collection of success stories.
- High number of fake beneficiaries registered.
- Non-Compliance issues at these rural municipalities.
- Discussion on palika action plan at all palikas.

Summary

- 1) A joint field visit was conducted at different palikas of Dhading regarding orientation on Palika Action Plans, Palika profile and Burning issues regarding reconstructions.
- a) The joint monitoring field visit was conducted at Tripurasundari Rural Municipality, an interaction program was organized with beneficiaries, ward chief and field visit team. Salyantar has plain land area in comparison to other neighboring VDCs. As it is well connected with road access, it has been the major center area for settlement. Most of beneficiaries of Salyantar VDC are focused for construction of RCC designed buildings. This field visit gave an opportunity of observing current reconstruction of Salyantar.

The visit provided chances to find enquiries and verify them as per our information. Open conversation was made between local people and interactive talks were carried out regarding reconstruction and related issues. People were unaware of when in future should they receive further tranches.



- b) HRRP conducted Palika level meeting at Tripurasundari Rural Municipality in presence of Palika chief, Co-Chief, Chief Administrative officer, Technical Group and Beneficiaries on 29th Jan 2019. The meeting was focused on Reconstruction Burning issues and challenges.

In Tripurasundari Rural Municipality As per the report from “Third Party Monitoring Agent” some of the households at the ward were not identified (i.e. houses were not built) while the tranche amounts had been already received. some of the households were minutely monitored and was found that beneficiaries had received government grant support even their houses were not built, or the houses were not under compliance. This might have been due pressure from beneficiaries to political leaders for receiving tranches on time as the deadlines from NRA was made. Palika Chief is positive towards reconstruction and have good coordination with the technical group.



Photo: - Palika level Meeting at Tripurasundari RM

- 2) The joint monitoring field visit was conducted at Gangajamuna Rural Municipality, as majority of the community are Tamang, language barrier is one of the challenges for POs and NRA engineers. The housing progress is achieved in enough numbers, due to remoteness of the location, absence of NRA engineers is often. Less number of women are involved in reconstruction activity.



Photo: - Uniformly constructed structure at Aalu Pokhara, Gangajamuna Rural Municipality, Dhading.

Most of the houses in these VDC were damaged in earthquake 2072, After Reconstruction Grant from Nepal Government VDC constructed similar type of structure to make it uniform using locally available materials i.e. Stone, Wood, CGI Sheet etc. Most of the structure built in these areas are Earthquake resistant.



- 3) HRRP conducted Palika level meeting at Khaniyabas Rural Municipality on 31st Jan 2019. The meeting was focused on Reconstruction Burning issues and challenges.



The meeting was mainly focused on reconstruction issues and palika challenges. The participants of the palika meeting were CAO Dipesh Bidari, Khagendra Awasti (MoUD/CLPIU-M&E), HRRP-team, Rajesh Shrestha (DSE) & Ananda Raj Pandey (GMAI). As per Administrative Office Dipesh Bidari Due to remoteness of the location, absence of NRA engineers is often.

- Some of individuals are still not registered through grievance process and this delay of result publication from NRA has caused misunderstandings among community and palika/ward office.
- There are many lands less issues in Gangajamuna RM, Ward representatives don't have information regarding land less, they have confusion on the process. We shared our experience along with the process of getting 2 lakhs from Nepal government. Finally, we suggested them to contact in GMAI (CSRC) who works for land less issue.
- Still there are many people who haven't listed as beneficiaries. The beneficiaries were having trouble through grievance resolving delay within the ward. People had claimed the registration for listing as beneficiaries through NRA grievance process. Most of them have not constructed their houses because

- of delay of grievance result and waiting for government grant support.
- Some of the individuals who were categorized under retrofit beneficiary were willing to revert to full damage grade beneficiary, thus ward offices have conducted required inspection process involving NRA field engineers, ward chief and palika officers to address those issues. The finalized files were forwarded to district NRA office for further processing.
- HRRP informed that beneficiaries who do not want to construct house and are willing to return the government grant amount can return to Nepal Reconstruction Authority office at “Rastriya Banijya Bank”.
- A discussion was made regarding distribution of completion certificates to those ward beneficiaries where reconstruction is high.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Unknown of the process on how to claim for registration under beneficiary list from non-beneficiary.	HRRP suggests step-by-step process on how they can claim it.	Ward office.	
Issue on delay of grievance resolving from NRA. Beneficiaries claim that they have registered grievance more than two times but, yet no result/solutions have come out.	Grievance resolved list must be provided at ward office.	GMaLI-Dhading and ward office.	

Housing Typology Report



Name: - Bharat Sharma
Location: - Salyantar, Tripurasundari Rural Municipality
It is one storey load bearing structure with material used burned brick with cement mortar, its floor area is less than 1000 sqft. The beneficiary has received 2nd tranche of government grants.



Name: - Laxman Shrestha
Location: - Salyantar, Tripurasundari Rural Municipality
It is two storey Hybridstructure with material used burned brick with cement mortar in ground floor and CGI sheet in second floor, its floor area is less than 1000 sqft. The beneficiary has received all tranche of government grants.



Name: - Bir Bahadur Gurung
Location: - Sadhan ward no- 05, Gangajamuna Rural Municipality, Dhading
It is one storey plus Attic load bearing structure with material used Stone with cement mortar. The beneficiary has received 2nd tranche of government grants.



Name: - Dai Bahadur Tamang
Location: - Latap Ree Vdc, Gangajamuna Rural Municipality, Dhading
It is a Two storey Hybrid structure with material used burned brick with cement mortar in ground floor and CGI sheet in second floor. The beneficiary has received all tranches of government grants.

Case Story

Name : Saili Gurung
Age : 32

years

A 32 years old widow woman, Saili Gurung, is resident of Netrawati Rural Municipality ward no 5, Banachaur tole. She has 1 son and 1 daughter her husband is dead. Her sole source of income is farming and social security allowance. She is a most vulnerable woman. Ever since she has been struggling to sustain her life. She is one of the beneficiaries of Pourakhi Nepal/Repair and Reconstruction project.

She was selected most vulnerable list, but she was not ready to construct new house because they don't have necessary money for new house construction though they are staying in old damage house. She has been motivated serial of meeting and communicating by project team to Saili Gurung was convinced to start new house. After receiving the vulnerable grant, she expressed happy for they live in new earthquake resistant house. The project has brought a transformation in her shelter condition.

She suggests that, "Pourakhi Nepal organization should be more active, in the upcoming days, in promoting income-generating social service and grant support programs so that people can get motivated, especially in living in their life".



Supported by: Paurakhi Nepal, Dhading.
