

Monthly District Report

Kathmandu

12 July - 22 August 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Kathmandu	Technical Meeting with the Technical staffs of Tokha Municipality of Kathmandu district to discuss on the non-compliance cases and its way forward.	1 August 2019	Tokha Municipality Office	Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org	Meeting Details
	Joint M & E Visit of HRRP Kathmandu and DLPIU-building Kathmandu.	1 August 2019	Tokha Municipality Office		Field visit section
	General orientation and discussion program focusing on the private housing reconstruction of Kageshwori Manohara Municipality Kathmandu district	5 August 2019	Kageshwori Manohara Municipality Office		Meeting Details
	General orientation and discussion program focusing on the private housing reconstruction of Tokha Municipality, Kathmandu district	5 August 2019	Tokha Municipality Office		Meeting Details
	District Facilitation Meeting of Kathmandu District	7 August 2019	DCC Office, Babarmahal		Meeting details
	General orientation and discussion program focusing on the private housing reconstruction of Chandragiri Municipality, Kathmandu district	7 August 2019	Chandragiri Municipality Office		Meeting Details
	General orientation and discussion program focusing on the private housing reconstruction of Dakshinkali Municipality, Kathmandu district	8 August 2019	Dakshinkali Municipality Office		Meeting Details
	General orientation and discussion program focusing on the private	8 August 2019	Kirtipur Municipality Office		Meeting Details

Summary of events during this period

housing reconstruction of Kirtipur Municipality, Kathmandu district					
General orientation and discussion program focusing on the private housing reconstruction of Shankharapur Municipality, Kathmandu district	12 August 2019	Shankharapur Municipality Office			Meeting Details
General orientation and discussion program focusing on the private housing reconstruction of Budanilkhantha Municipality, Kathmandu district	18 August 2019	Budanilkhantha Municipality Office			Meeting Details
General orientation and discussion program focusing on the private housing reconstruction of Tarakeshwor Municipality, Kathmandu district	19 August 2019	Tarakeshwor Municipality Office			Meeting Details
General orientation and discussion program focusing on the private housing reconstruction of Gokarneshwor Municipality, Kathmandu district	20 August 2019	Gokarneshwor Municipality Office			Meeting Details
General Meeting with the Municipality representatives of Kathmandu Metropolitan City Kathmandu district	21 August 2019	DCC Hall, Babbarmahal			Meeting Details
Palika Profile of all Municipalities/Metropolitan City of Kathmandu District has been uploaded in the website of respective municipality.			Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org		1. Kageshwori Manohara Municipality (In Earthquake related section) 2. Shankharapur Municipality 3. Kathmandu Metropolitan City 4. Municipality 5. Tokha Municipality (In important links) 6. Kirtipur Municipality 7. Dakshinkali Municipality 8. Budanilkhantha Municipality

Summary of events during this period

					9. Nagarjun Municipality 10. Tarakeshwor Municipality 11. Chandragiri Municipality (In Profile section)
	Update of the housing typology	12 July – 22 Aug 2019			
	Update of the contact list, calendar, District activities in HRRP website, update of contact list	12 July – 22 Aug 2019		Sweata Sijapati District Technical Coordinator Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org	
	Updating of the Urban status paper in coordination with the HRRP District and National team.	12 July – 20 Aug 2019			
	Follow up with the municipal and ward office regarding the NRA tranche deadlines, collection of the issue and gap reduction in the ongoing reconstruction work.	12 July – 22 Aug 2019			
	Update of 5W of Kathmandu district	12 July – 22 Aug 2019		Sachin Malego IM Officer Contact: 9842062006 sachin.malego@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
General Meeting with the Municipality representatives of Nagarjun Municipality Kathmandu district	25 August 2019, Nagarjun Municipality Office, Sitapaila	GMaLI- Kathmandu	
Collection of the details of beneficiaries under the following categories - Non-enrolled beneficiaries - Vulnerable beneficiaries - Beneficiaries wanting to change from retrofitting	Within Bhadra 2076	GMaLI- Kathmandu	Sweata Sijapati District Technical Coordinator, Kathmandu Contact: 9861796464 sweata.sijapati@hrrpnepal.org

Upcoming Events & Meetings

to full construction and vice- versa.			
Collection of the detail of heritage/culturally important areas, vulnerable areas, area under government development plan such as smart city.	Within Bhadra 2076	GMaLI- Kathmandu	
Joint Monitoring visit to different Municipalities of Kathmandu district along with DLPIU- Building Kathmandu, M&E consultant, District Support engineers and DLPIU technical staffs deployed at Municipality and ward level.	September 2019	DLPIU Building, Kathmandu and HRRP	
District Facilitation meeting of the Kathmandu Valley	TBD (Bhadra 2076)	GMaLI- Kathmandu	
Municipality level meeting to address the issues of the non-enrolled beneficiaries, vulnerable beneficiaries.	September 2019	GMaLI- Kathmandu, HRRP	
PA Collection and digitization of the beneficiaries of Kathmandu District	September 2019	GMaLI- Kathmandu	
Updating of the Municipality profile and the action plan every month and coordinate to upload the information in Municipalities websites	September 2019	HRRP Kathmandu	

News & Updates

- DLPIU- GMAI Kathmandu has coordinated with all the municipalities and metropolitan city to convey the NRA notice to ward offices and beneficiaries.
- DLPIU- GMAI Kathmandu has requested all the municipalities of Kathmandu district to send the details of the non-enrolled beneficiaries, list of vulnerable beneficiaries and the status of the beneficiaries who have not begun reconstruction even after getting the first tranche with 1 September 2019 (Bhadra 15, 2076).
- In lead of DLPIU-Building the resurvey and reverification of the Grievance is being collected in Kathmandu District has been completed.
- NRA has made the policy for allowing the reconstructed in all the previously restricted land such as government, forest area, public land, trust land and so on. The policy for the reconstruction in such land are provided below: ([NRA-Reference Document](#))

१०. (ग) लाभग्राहीको सूचीमा परेका भूमिहिन भूकम्पपीडितहरूले घरबासको लागि उपर्युक्त बमोजिम स्थानान्तरण हुन नचाहेको हकमा निजहरूले परम्परादेखि भोग गर्दै आएको साविकको घडेरी जग्गामा नै निजी आवास पुनर्निर्माण गर्न चाहेको अवस्थामा निजहरूले भोग गरेको जग्गामा घरबासको क्रममा जडान भएका धारा, विद्युत, टेलिफोन आदिको प्रमाण सहित सार्वजनिक मुचुल्काको आधारमा स्थानीय तहबाट सिफारिश भै राष्ट्रिय पुनर्निर्माण प्राधिकरणको काम कारवाहीमा समन्वय गर्न गठित जिल्ला समन्वय समितिको निर्णयको आधारमा सोही स्थानमा निजी आवास पुनर्निर्माण गर्न अनुदान रकम उपलब्ध गराउने । यस्तो जग्गामा पुनर्निर्माण गर्ने निजी आवासको हकमा घरको लम्बाई, चौडाई, उचाई, साइट प्लान, सडकको अधिकार क्षेत्रभित्रबाट दूरी लगायत विवरणहरू पेश गरी घर निर्माण स्वीकृतिका लागि दिएको निवेदन स्थानीय तहले अभिलेखीकरण गरी निर्माण स्वीकृति दिनेछ । तर यस्तो स्वीकृतिलाई जग्गा दर्ताको प्रमाणको रूपमा लिइने छैन ।


१२. सार्वजनिक जग्गा, सरकारी र वन क्षेत्रको जग्गा बाहेक विभिन्न किसिमका गुठी, विर्ता र गुठी अधिनस्थ जग्गा, मोही लागेको जग्गा, स्ववासी, बेनिस्सा, गाउँ ब्लक, कोदाली, आँकडा, विटौरी, उखडा समेतका जग्गामा बसोबास भई घर क्षति भएका लाभग्राहीका हकमा निज बसोबासीसंग घरबास भएको जग्गाको भोग सम्बन्धी कुनै निस्सा, रसिदवा पूर्जा भए सो निस्सा रसिद वा पूर्जाको आधारमा स्थानीय तहले गरिदिएको सिफारिश र त्यस्तो निस्सा रसिद वा पूर्जा नभएको अवस्थामा सोही व्यहोराको सिफारिस एवं क्षतिग्रस्त घरबास भएको जग्गाको कम्तिमा दुई जना संधियारहरूले घरबास भएको जग्गाको, भोग चलन गरेको हो भनी गरिदिएको सर्जमिन मुचुल्काका आधारमा त्यस्ता घरघनी लाभग्राहीसंग घरपनर्माण अनुदान सम्झौता गर्न सकिनेछ । तर यस्तो सम्झौतालाई जग्गा दर्ताको प्रमाणको रूपमालिइने छैन । *भूकम्प प्रभावित जिल्लाका स्थानीय तहहरूमा भूकम्प प्रभावित लाभग्राहीले निर्माण गर्ने निजी आवासको हकमा घरहरूको लम्बाई, चौडाई, उचाई, साइट प्लान, सडकको अधिकार क्षेत्रभित्र (*Right of way*) बाट दूरी लगायत विवरणहरू पेश गरी घरनिर्माण स्वीकृतिका लागि दिइएको निवेदन *स्थानीय तहले अभिलेखीकरण गरी निर्माण गर्न स्वीकृति दिनेछ । यस सम्बन्धित अन्य व्यवस्था अनुसूची-६ बमोजिम हुनेछ ।

Tranche Status (Kathmandu)


Tranche Status Table:

Municipality	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Budhanilakantha Municipality	2740	2694	2078	2078	1061	878	11	1	1	1
Chandragiri Municipality	6414	5906	4876	4769	1529	1285	128	46	46	0
Dakshinkali Municipality	3542	4087	3806	3805	1595	1074	52	32	32	0
Gokarneshwor Municipality	2870	2939	2564	2564	1538	1233	20	8	8	0
Kageshwori Manahora Municipality	3741	3678	3304	3304	1776	1173	75	25	25	0
Kathmandu Metropolitan City	8738	7561	6009	6009	1486	1212	173	34	34	0
Kirtipur Municipality	3758	3231	2495	2495	966	793	44	20	20	0
Nagarjun Municipality	4315	4447	4110	4110	1543	1259	38	5	5	0
Shankharapur Municipality	6032	6102	5567	5567	2940	1911	110	42	42	0
Tarakeshwor Municipality	6737	6174	5252	5252	2155	1837	107	33	33	0
Tokha Municipality	2237	1749	1594	1594	700	573	48	26	26	0

Graph of Tranche Status:

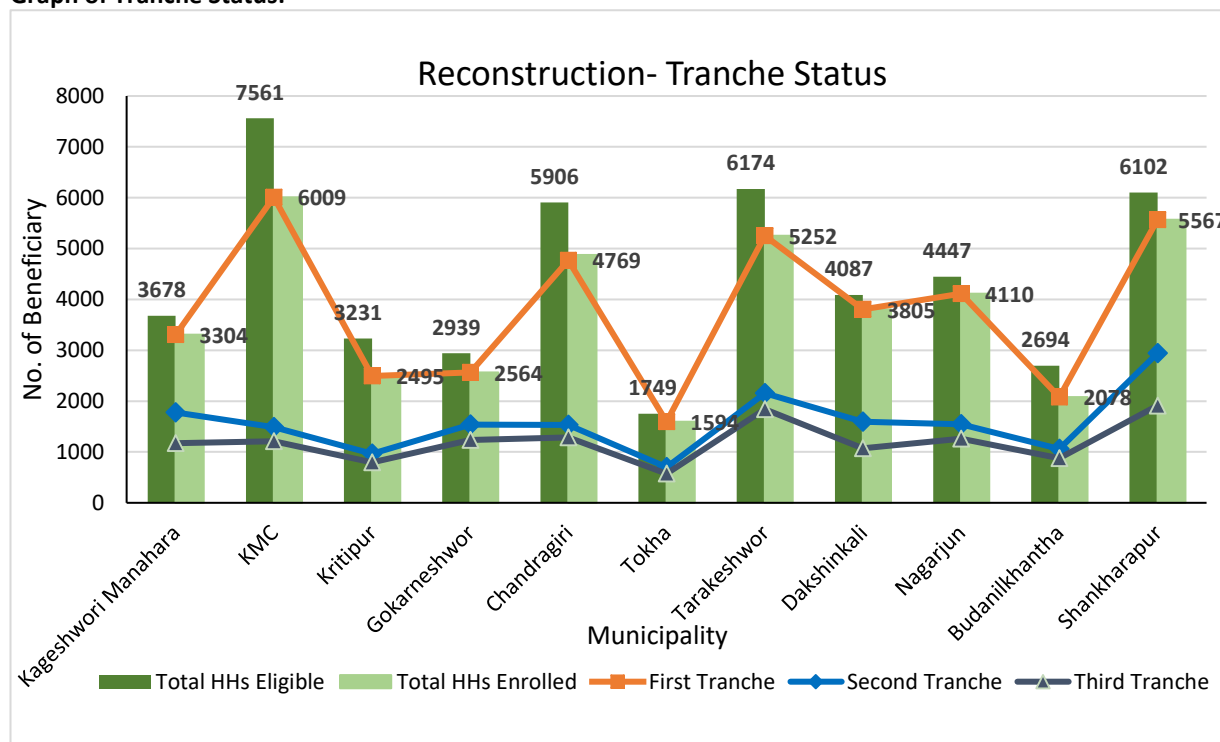

Graph for Retrofitting Status:

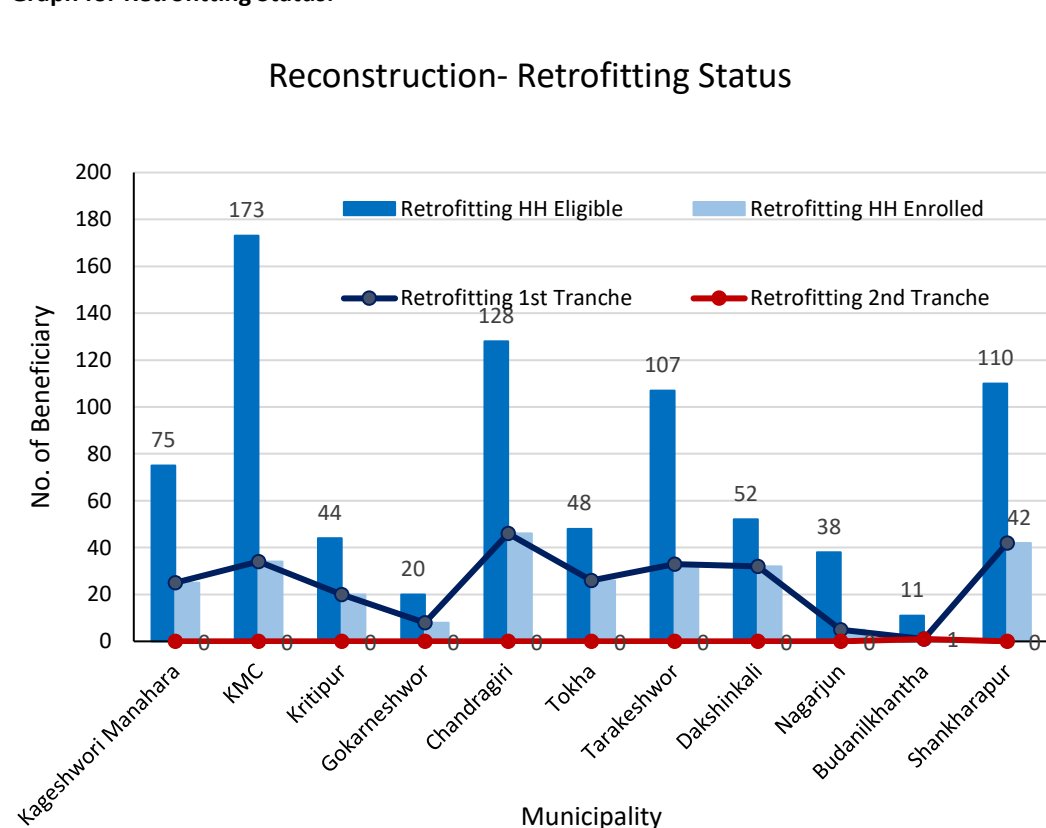

Field Visit Reports (Kathmandu)

Visit 1

Date	Location	Participants
1 August 2019	Ward no. 1, 10 and 12, Tokha Municipality	- Bidhya Manandhar (DSE) - Prajwal Karki (DSE), - Sanam Lakhey (DLPIU- Building Kathmandu) - Rajani Shrestha (DLPIU-Building Kathmandu) - DLPIU Engineers- Tokha Municipality (Pratikshya Tripathi, Sita Baral, Sujana Thapaliya, Ashish Ranabhat) - Sweata Sijapati, HRRP, Kathmandu
Objective(s)	- To observe the non-compliant houses and to provide way forward regarding the technical assistance. - To interact with beneficiaries to understand the reconstruction issues and status - To collect housing typology	

Why was the visit carried out in this location?

The field visit was targeted to this site due to high number of non-compliance cases especially in 9"X12" column size and structurally unsafe, 9" wall in two storey load bearing structure and missing the earthquake resistant elements. As the beneficiaries were not convinced by the correction measures suggested by the technical staff, the visit was accompanied by the District Support Engineers (DSE).

Summary

Field Visit:

HRRP Kathmandu along DSE and technical staffs from DLPIU Building conducted joint field monitoring at Ward no 1, 6 and 10 of Tokha Municipality, Kathmandu district. The field visit was mainly focused on the observation of the Non-compliance cases and beneficiaries claiming for the 2nd and 3rd tranches in the area. During the visit DSEs suggested the possible correction measures and way forward to the beneficiaries for being eligible for the tranche. In total 8 houses were visited among which majority of the houses were recommended to add DPC bands. Similarly, the other non-compliance case was large opening size, load bearing structure missing the earthquake resistant elements and so on.

Some of the beneficiaries interacted during the visit had still not signed the PA agreement due to lack of landownership issues. Before beginning the field visit a brief meeting with the technical staffs deployed in the municipality was conducted to identify the measure issues and the selection of the household to be visited.

During the meeting the measures issues highlighted by the technical staffs were

- Due to landownership documents and road extension program some beneficiaries are not able to sign the grant agreement.
- Non-compliance houses constructed before the NRA technical staffs were deployed.
- Missing of earthquake resistant elements, and 9"X12" column size.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
The houses constructed were found to be constructed without the earthquake resistant elements such as vertical reinforcements and so on.	The beneficiary was suggested to add the band for the exterior of the wall and the vertical reinforcement in the corners	The beneficiary agreed to apply the correction measures as per suggested by the DSE.	Beneficiary, Technical staffs	As soon as possible

Some of the beneficiaries still had not signed the PA agreement due to ROW and no landownership documents.	The beneficiaries were suggested to visit the GMaLI office for the possible solution in this regard.	GMaLI office will provide the details on the required documentation for the beneficiary to be eligible to sign the agreement.	Beneficiary, Municipality, GMaLI	As soon as possible
--	--	---	----------------------------------	---------------------

Photos



DSE interacting with the beneficiary during the field visit



Technical staffs suggesting the correction measures to the beneficiary during the field visit.



The hybrid structure visited during the field visit at Jhor was considered non-compliance.



The RC frame structure of Ms. Asha Maru Dongol, ward no 6, Tokha has received all the government tranche.

Housing Typology Report



Beneficiary name: Jagat Lal Shrestha, Gongabu ward no 10, Tokha Municipality. 3 storey steel structure was listed as non-compliance due to large opening areas making it vulnerable. DSE suggested for the structural analysis of the structure.



Beneficiary name: Santosh Adhikari, ward no 1, Tokha Municipality. One storey load bearing brick masonry in cement mortar Structure was considered non-compliance due to larger opening area as well as larger room size. DSE suggested addition of DPC band in between the room to increase the strength of the walls.



Beneficiary name: Gita Ghimire, Jhor, Ward no 1, Tokha Municipality. 2 storey load bearing brick masonry in cement mortar Structure was considered non-compliance due to 9" wall structure. As the beneficiary has used, I beam of 6-inch, the DSE suggested the house to be treated as steel frame structure.



Beneficiary name: Purna Man Dongol, ward no 6, Tokha Municipality. One and half storey brick masonry in cement mortar Structure was considered non-compliance due to fixed roof in both storey which makes the structure technically vulnerable.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
The reconstruction of the damaged house is restricted due to the road extension project. Due to this the Partnership agreement has also not been signed. What can be done in such case?	Engineer	Regarding such cases, identify the name of such beneficiaries and forward the case to GMAI Kathmandu for further action to be taken to address this issue (HRRP)
What is the procedure of the land purchase?	Ward representatives	NRA has provision of providing NRP 200,000 for those beneficiaries who don't have land, residing in government, public or vulnerable land. The ward and municipality have to verify that the beneficiary doesn't have land all over country. The beneficiary must find the land by themselves. (GMAI- Project Manager)
What is the status of the soft loan provided by the bank?	Ward representatives	As of now the provision of the NRP 250,000 loan is not applicable but all banks in agreement with NRA has approved of NRP 300,000 loan to the beneficiaries. For this the constructed house will be the collateral itself. Regarding the interest of the bank, Nepal Government will pay 5% of the total interest and the remaining interest must be paid by the beneficiary. The choice of the bank also depends on the beneficiary.
The non-enrolled beneficiaries are coming to ward offices for the partnership agreement of the housing grant even after the NRA deadline of Asar 2076. What can be done for such beneficiaries?	Ward representatives	As for now the agreement system has been temporarily shutdown by the NRA. All the ward representatives are requested to send the name of such beneficiaries along with the reason of the delay in the signing the agreement. The details of such beneficiaries with the genuine reason will be sent to NRA for further decision.

Challenges and Way Forward

Challenge	Way Forward
NRA has made a decision to provide the full tranche for those houses constructed before the deployment of the technical staffs. There may be changes that beneficiaries with non-compliance structures may come	Regarding this, the ward representatives as well as the technical staffs must seriously verify if the structure were constructed immediately after the earthquake.

Challenges and Way Forward

Challenge	Way Forward
forward to claim that the houses were constructed before the technical staffs were mobilized.	
Majority of beneficiaries have not yet started reconstructing their houses though they have received 1 st tranche from government.	Ward office should play constructive role in motivating beneficiaries to reconstruct houses. Ward-based engineers should be deployed so that beneficiaries can get technical assistance in rebuilding safe houses. The NRA deadline for the second tranche is end of Kartik 2076 so, the information must be delivered from municipality as well as ward office for its effective implementation. If beneficiaries not intending to reconstruct houses, then Ward office should lobby with them to return the 1 st tranche amount.
