

Fortnightly District Report

Ramechhap

18 – 31 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Ramechhap team has successfully completed the Joint Field monitoring visit to Sunapati Rural municipality Ward-4, Bethan starting from 21-23 rd January 2019. During the field visit ward level meeting was conducted at Bethan ward-4 ward office with the presence of ward chairperson, DLPIU technical persons and ward representative. Similarly, team has observed the typology of private housing construction in the area. M&E consultant, District support engineer, Field coordinator from Scott Wilson Nepal and HRRP District coordinator and Technical Coordinator participated in the joint field monitoring visit.	21-23 rd January 2019	5		Mr. Prakash Bishwakarma	Click here for field visit report
Ramechhap HRRP team has successfully completed the General coordination meeting on 29 th January 2019 at Gmali office meeting hall. The meeting was chaired by Gmali chief Mr. Krishna Lal piya. A total of 25 participants are participated in the meeting program from government office and partner organization. All the partner's organization present their progress and update of their project. MIS specialist from Gmali has present the reconstruction status of the district. The program was closed with the remarks from the Gmali chief.	29 th January 2019	22	3	Mr. Prakash Bishwakarma	Click here for Minutes
Fortnightly Housing typology of Ramechhap has been updated.	30 th January 2019			Tulasi ram lamichhane	Click here for Housing Typology Report
Housing Typologies has been updated in flickr	30 th January 2019			Tulasi ram lamichhane	
5 W update of Ramechhap round 7	29 th January 2019			Mohamad Javeed	Click Here

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Joint monitoring Field Visit	4-5 Feb 2019, Chisapani, Manthali municipality	HRRP	Prakash Bishwakarma

News & Updates

N/A

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
21-23 rd January 2019	Sunapati Rural Municipality ward-4, Bethan	✓ Janak Raj Joshi, CLPIU, M&E consultant ✓ Keshav Raj Pandey District Support Engineer, DLPIU Ramechhap ✓ Jeevesh Karna, Field Coordinator, Scoot Wilson Nepal ✓ Prakash Bishwakarma, District General Coordinator-HRRP ✓ Tulasi Ram Lamichhane, District Technical Coordinator-HRRP

Objective(s)

- To observe the reconstruction status of the beneficiaries
- To provide inputs to the beneficiaries in regards of housing reconstruction and non-compliances issues.
- Meeting with the local representatives to discussion on reconstruction challenges and issues.

Summary

Description of field visit (maximum 300 words)

Previously Bethan is a village development committee in Ramechhap in the Janakpur Zone of north-Easter Nepal. Recently Bethan is located at Sunapati Municipality ward-4 in new local governance structure. Regarding the reconstruction data a total of 1109 beneficiaries are identified as an earthquake beneficiary. Among them a total of 1082 beneficiaries had been done agreement with the government for reconstruction grant. The reconstruction status of the ward-4 Bethan listed below:

Total Beneficiaries	Total Agreement	1 st Tranche	2 nd Tranche	3 rd Tranche	Retrofitting beneficiaries	Non-Compliances
966 + 143 (Grievance)	1082	1082	898	541	230	9

Key point of the visit at Ward-4, Bethan Sunapati Rural Municipality

- A total of 2 technical person engineer and sub-engineer from DLPIU and 2 technical people from Scoot Winson Nepal have been deployed at Bethan Ward-4 the mobilization and coordination of the technical person with beneficiaries found satisfaction says by the chairperson of ward-4, Bethan.
- The mobilization of the technical person deployed at Bethan was good because the reconstruction rate was satisfaction and the interaction between technical person and reconstruction beneficiaries were frequently reported by chairperson.
- A total of 12 beneficiaries had not received government tranche even after they have done agreement with the government.
- The chairperson has reported that the third tranche has been delayed due to low construction because of scarcity of water in all over the ward and earthquake caused the dried of water sources.
- A total of 230 beneficiaries are identified as a retrofitting beneficiary but chairperson says the retrofitting beneficiaries are in real full earthquake beneficiaries because most of the beneficiaries had been already construction new house and sifted.
- About 45% of houses are RCC houses in Bethan regarding to another rural municipality.
- Some of the beneficiaries came to ward office to know about the procedure for returning back the tranche. They want to return the tranche because some have their houses in Kathmandu and some beneficiaries doesn't want to build house in village.
- A total of 150 beneficiaries have been given the application to the ward office for re-survey regarding reconstruction. The re-survey is going to organize at Ramechhap very soon after completing all necessary works.
- Technical person reported the delayed bank process has been identified at Bethan-4 of Sunapati Rural Municipality.
- Chairperson of ward-4, Bethan reported that all retrofitting beneficiaries had given application to the ward office to transformation in reconstruction complete beneficiaries.
- A total of 30-40 beneficiaries are still remaining DPC construction in ward-4 Bethan reported by technical person at meeting.
- DLPIU district support engineer and M&E consultant has requested technical person to make last inspection activities for to distribution reconstruction completion certificate.
- Scoot Wilson Nepal has working in Bethan ward-4 providing technical support as a partner organization.

Some photo of Activities during the period



Ward level meeting with local representative and technical person at Bethan-4, Sunapati RM




DLPIU District Support Engineer and M&E Consultant inspecting house at Ward-4, Bethan Sunapati RM

Tranche Status


Rural/Municipality	Doramba	Gokulganga	KhadaDevi	Likhu	Manthali	Ramechhap	Sunapati	Umakunda
Total HHs Surveyed & GR	5,085	6,343	5,210	5,685	11,103	6,581	3,669	4,984
Total HHs Eligible	5,085	6,343	5,210	5,685	11,103	6,581	3,669	4,984
Total HHs Enrolled	4,674	5,804	5,081	5,498	10,574	6,344	3,473	4,459
First Tranche	4,667	5,785	5,077	5,497	10,562	6,338	3,470	4,458
Second Tranche	3,549	4,923	4,477	4,709	9,151	5,398	3,055	3,863
Third Tranche	2,379	3,818	3,631	3,799	7,070	4,377	1,823	2,413
Total HH Constructed	2200	3890	3590	3790	7060	4390	2150	2350
Grievance Registered	2448	1031	2007	1562	2815	1841	1392	843
Grievance Addressed	2448	1031	2007	1562	2815	1841	1392	843
RF HH Eligible	344	58	620	235	258	154	350	130
RF HH Enrolled								
RF 1st Tranche								
RF 2nd Tranche								
Non-Compliance Registered	31	57	7	69	78	26	7	2
Non-Compliance Addressed	31	57	7	69	78	26	7	2

Source: DLPIU-Building, GMALI

Graph of Tranche Status:

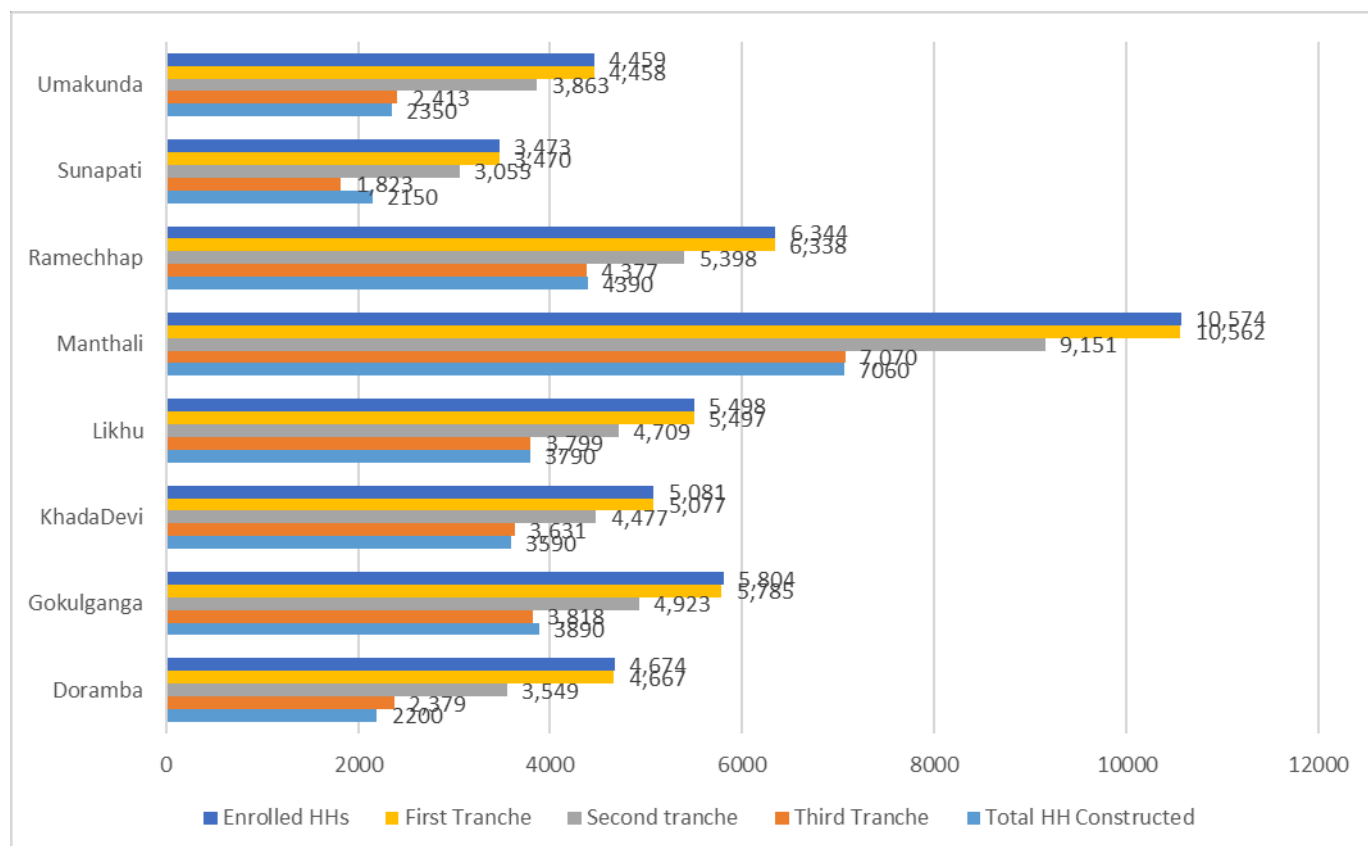

Graph for Non - Compliance Status:

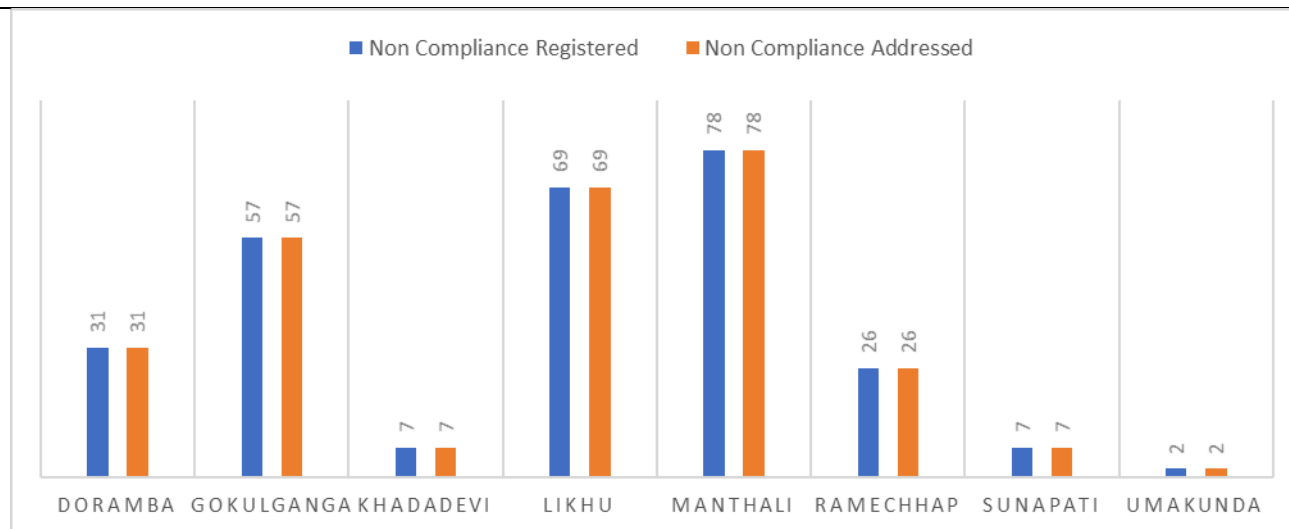

Housing Typology Report



The house of Ashok Lama constructed in Bethan, Sunapati Gaupalika-4. The house is constructed using interlocking bricks. The house owner has received second tranche of reconstruction grant and has been forwarded for third tranche.



The house of Dirgha Lama constructed in Bethan, Sunapati Gaupalika-4. The house is RC Frame structure with all 12"x12" column and brick masonry has been used for the walls. The house owner is in the retrofitting beneficiary list and has not done agreement with NRA for the grant process however he has demolished the previous vulnerable house and constructed the new earthquake resilient house. He has launched the file for the beneficiary conversion procedure.



The house of Thulnani Tamang (PA 21-3-6-0-75) constructed in Bethan, Sunapati Gaupalika-4. The house has been constructed before the arrival of engineers in the ward ie on 2015 May. He has done agreement with NRA and received the first tranche of reconstruction grant. He was willing to reconstruct new house but the decision from PM has halted the new house construction process. His house does not comply with NBC. His house has been forwarded in the list of houses constructed before arrival of technical persons.



The house of Arjun Khadka constructed in Bethan, Sunapati Gaupalika-4. The house is a RC frame structure with 12"x12" column and brick masonry for wall construction. The house is constructed as per the type design provided by NRA. The house owner has received all three tranches of reconstruction tranche.



The house of Narayan Khadka constructed in Bethan, Sunapati Gaupalika-4. The house is constructed using interlocking bricks. The house owner has received second tranche of reconstruction grant and has been forwarded for third tranche.



The house of Raju Pandey constructed in Bethan, Sunapati Gaupalika-4. The house is constructed using stone in mud mortar. RC bands have been provided in the house with flexible roof. The house owner has received all three tranches of reconstruction grant.



The house of Prem Raj Pandey constructed in Bethan, Sunapati Gaupalika-4. The house is constructed using stone in mud mortar. RC bands have been provided in the house with flexible roof. The house owner has received all three tranches of reconstruction grant.



The house of Hari Krishna Pandey constructed in Bethan, Sunapati Gaupalika-4. The house is constructed using stone in mud mortar. RC bands have been provided in the house with flexible roof. The house owner has received all three tranches of reconstruction grant.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)

Challenges and Way Forward

Challenge	Way Forward
What is the process of returning the tranche if the house owner is not willing to construct house and return tranche?	The beneficiary must contact GMALI Office if interested to return the tranche and deposit the tranche in the account provided by GMALI.
What is the process of beneficiary conversion RT to RCB	The report from engineer showing that the damage grade of the house is above 3 major and above and send to GMALI for the necessary process after filling the forms available. GMALI will send to NRA for the further process.
No trained masons	Mason trainings should be conducted as soon as possible.

Case Story *(Please submit at least one case story per report.)*

N/A
