

Monthly District Report

Nuwakot, Rasuwa

27 September - 21 October 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Nuwakot	Field Visit to Dupcheswar-6, Ramati. -74 hh are constructing for vulnerable integrated settlement from Ghyangphedi, Dupcheswar-1. -34 are in roofing stage. -Consumer group members are in process to get infrastructure support from NRA.	16 Oct 2019		Badri Pyakurel District Coordinator badri.pyakurel@hrrpnepal.oeg	
	Meeting/Interaction with District Level Retrofitting Task Force - 2 Meeting has organized, decided to make a reporting format and collect the palika level progress On Retrofitting -Plaika Level task force has formulated and conducted a meeting to each. -Planned to conduct an orientation in first week of November	17 Oct 2019	DLPIU Building, Nuwakot	Badri Pyakurel District Coordinator badri.pyakurel@hrrpnepal.oeg Rajendra Chilwal, Coordinator District Level Task Force rajchi75@gmail.com	
	Contact List update	18 Oct, 2019		Badri Pyakurel District Coordinator badri.pyakurel@hrrpnepal.oeg	
	Palika Profile data update	18 Oct, 2019		Badri Pyakurel District Coordinator badri.pyakurel@hrrpnepal.oeg	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Nuwakot District Facilitation Meeting	23 December, 2019	GMALI Nuwakot	Satya Narayan Chudhari, M&E Gmaili Nuwakot, satya.isha95@gmail.com


Tranche Status (Nuwakot)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Belkotgadhi Nagarpalika	10719	11037	10523	10523	9627	10523	256	7	7	0
Bidur Nagarpalika	15204	13097	12202	12202	11366	12202	240	90	90	0
Dupcheshwar Gaunpalika	5827	5884	5715	5715	5520	5715	35	1	1	0
Kakani Gaunpalika	6905	6954	6507	6507	5979	6507	175	49	49	0
Kispang Gaunpalika	4637	4788	4635	4635	4257	4635	51	1	1	0
Likhu Gaunpalika	4973	5110	4769	4769	4392	4769	155	15	15	0
Meghang Gaunpalika	4739	4520	4289	4289	4183	4289	152	1	1	0
Panchakanya Gaunpalika	4243	4566	4357	4357	4000	4357	96	6	6	0
Shivapuri Gaunpalika	6292	6524	6264	6264	5600	6264	65	0	0	0
Suryagadhi Gaunpalika	4560	5024	4913	4913	4587	4913	17	1	1	0
Tadi Gaunpalika	4476	4592	4480	4480	4299	4480	23	3	3	0
Tarkeshwar Gaunpalika	4573	4713	4397	4397	4145	4397	254	3	3	0


Graph of Tranche Status:

Reconstruction- Tranche Status

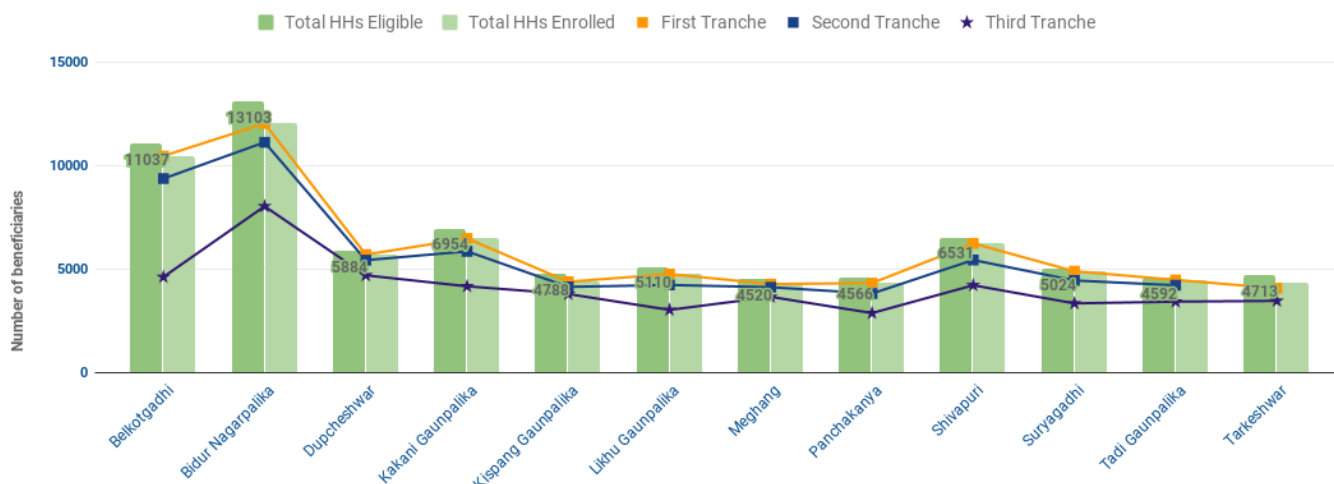

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

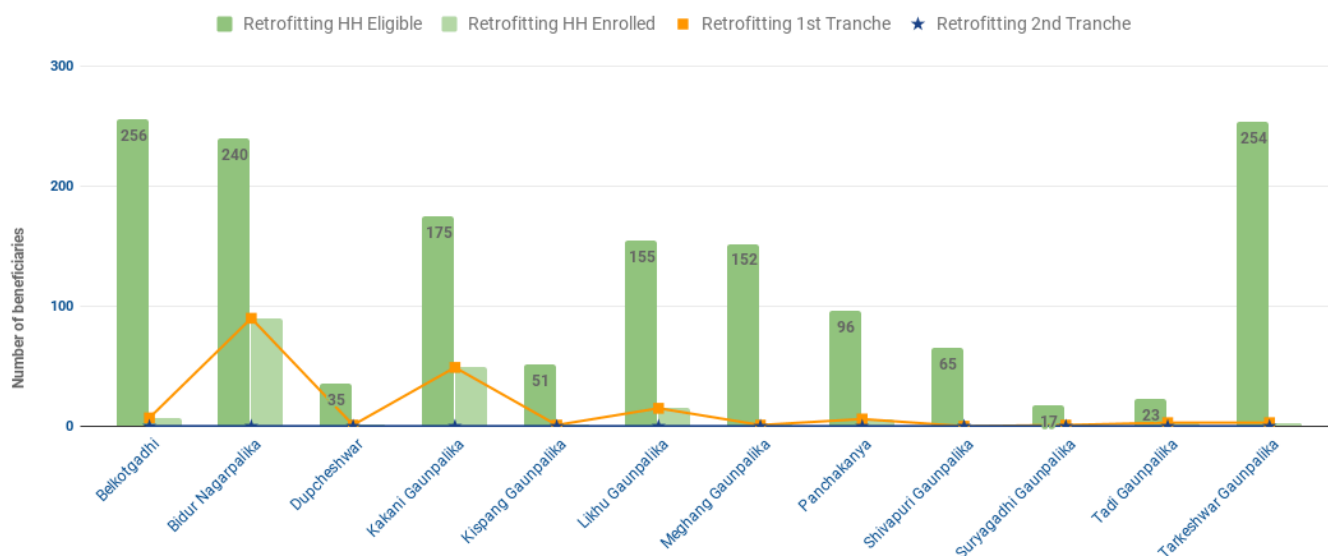


Tranche Status (Rasuwa)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Gosaikunda Gaunpalika	2224	1979	1873	1855	1776	1519	84	68	67	0
Kalika Gaunpalika	2530	2591	2498	2498	2443	2360	35	13	13	0
Naukunda Gaunpalika	3298	3349	3311	3311	3223	3140	18	13	13	0
Parbati Kunda Gaunpalika	1981	1964	1823	1823	1727	1517	59	34	34	0
Uttargaya Gaunpalika	2611	2631	2307	2307	2075	1966	26	11	11	0

Graph of Tranche Status:

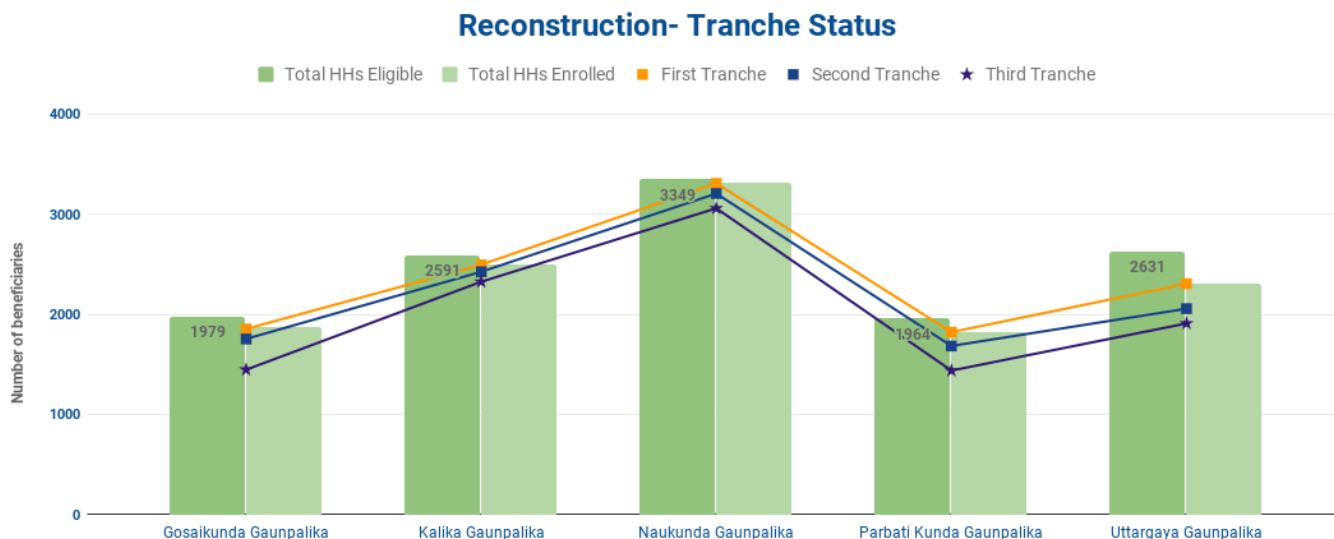

Graph for Retrofitting Status:

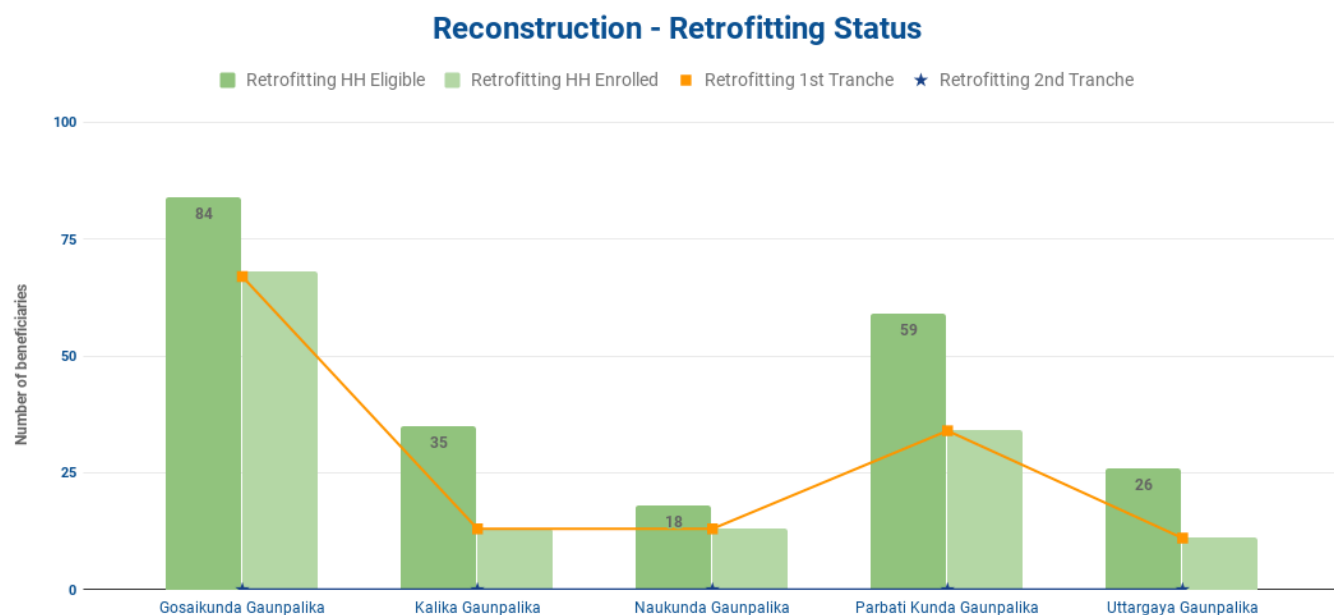

Field Visit Reports (Nuwakot)

Visit 1

Date		Location	Participants
16 October, 2019		Ward no. 6, Dupcheswar RM-6, Ramati	• Badri Pyakurel, District Coordinator, HRRP-Nuwakot •
Objective(s)	• To understand the factors of Integrated Settlement • To interact with the Relocated beneficiaries to understand their status • To discuss with Consumer group and implementing agencies for the progress.		
Why was the visit carried out in this location?			

The integrated settlement has started to construct recently. To know its progress detail, Problem facing and to know the challenges facing during the implementation.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

Ramati Relocation area has 74 beneficiaries from Dupcheswar-1, Ghyangphedi. The selection of the relocation site had been selected in December 2017. NRA has completed the land purchased for the long time ago though the settlement has started since May-June 2019. Oxfam is supporting to all the beneficiaries to build house through its implementing partner. Oxfam has already completed 6 integrated settlement in Kharanitar, Suryagadhi, Meghang, Kispang and Bidur.

In Ramati 34hh are in roof level, some are started and not started as well. The site has started to construct from the beginning of monsoon season and we can see monsoon has affected badly in transportation of construction materials. Then the construction has halted due to the great Nepalese festival Dashain,

A brief update and sharing discussion of reconstruction status made with User group chairperson Mr. Karma Tamang along with his team for the prompt response after the monsoon and festival. He shows his suspect to manage all the construction to the specific area procured. The main challenge of the construction is to manage the slope land and connect road to transport the construction materials. They are in process to receive the structure support from NRA. As per the representatives of implementing partner of Oxfam, they have plan to complete the site till Dec 2019.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Manson, Festival and lack of technical manpower in local level has delayed the construction.	Proper planning is needed to complete the construction in time.		Implementing partner and Palika	

Photos



Ramati Relocation Area, Dupcheswar, Nuwakot

Photos



Ramati Relocation Area, Dupcheswar, Nuwakot

Housing Typology Report (Max 4 Photos, Select best photos from each district)



Beneficiary name: Ram Sharan Pyakurel, Ward no 11, Bidur Municipality. 1 storey, 2 roomed Brick Cement structure with rigid roof. The beneficiary has already received all tranches.



Integrated Settlement in Tadi RM-2, Budune, Nuwakot. The settlement consisting 71hh from Tadi-1, Urleni. The Construction has supported by Oxfam.
