

HRRP BULLETIN

24 December 2018



A woman weaving in Chumnuhari Rural Municipality. Photo credit: Ajit Tiwari. Ajit has shared his experience working as an NRA, Building DLPIU inspection engineer in this remote part of Northern Gorkha in this edition of the bulletin.

Highlights


- Request for review of [draft Hollow Concrete Block \(HCB\) manual](#)
- [NRA, DLPIU Technical Staff Report from Chumnuhari Rural Municipality, Northern Gorkha](#)
- Data on first tranche return and case studies highlighting concerns and issues with this process
- Comparison of tranche disbursement progress in urban wards vs. rural wards, and urban wards in the Kathmandu Valley vs. urban wards outside the Kathmandu Valley
- Update on District Level Reconstruction Orientation and Review Workshops – now completed in 15 districts
- [Community Perception Survey, Reconstruction, Food Security & Livelihood, and Protection, Common Feedback Project, November 2018](#)

UPDATES & REQUESTS


National

[NRA, CLPIU GMALI and Building, Grant Disbursement Data, as of 24 December:](#)


Reconstruction Grant	26 November	10 December	24 December
Total No. Eligible HHs	822,706	822,719	823,385
HHs Enrolled	731,639	738,523	740,907
HHs Received 1 st Tranche	727,123	731,441	734,392
HHs Applied for 2 nd Tranche	531,573	557,034	594,354
HHs Received 2 nd Tranche	519,428	521,431	523,889
Non-compliant at 2 nd Tranche			4,823
HHs Applied for 3 rd Tranche	346,973	369,135	415,664
HHs Received 3 rd Tranche	324,304	331,543	336,263
Non-compliant at 3 rd Tranche			2,355
Houses Completed			367,334
HHs with Completion Certificate			4,750
Retrofit Grant	26 November	10 December	24 December
Total No. Eligible HHs	60,952	60,984	61,591
HHs Enrolled	12,507	12,698	13,591
HHs Received 1 st Tranche	10,819	11,011	11,974
HHs Received 2 nd Tranche	3	4	4

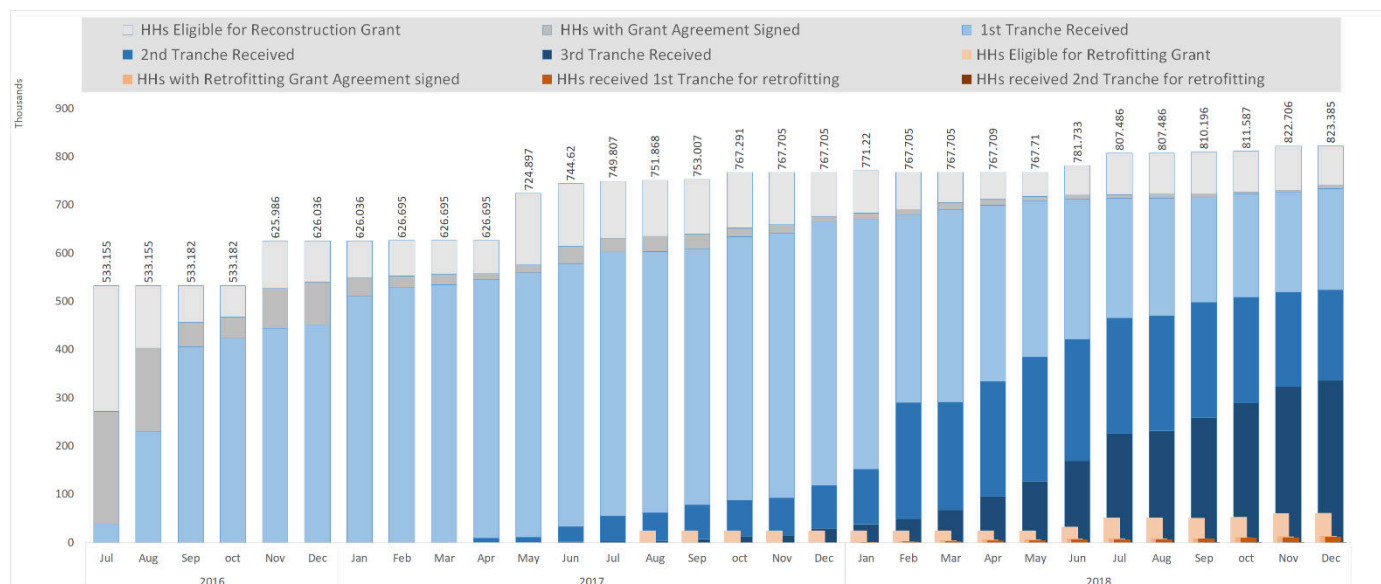

Progress with the disbursement of the GoN housing reconstruction and retrofit grants based on NRA, GMALI CLPIU, and Building CLPIU data from July 2016 to 24 December 2018.

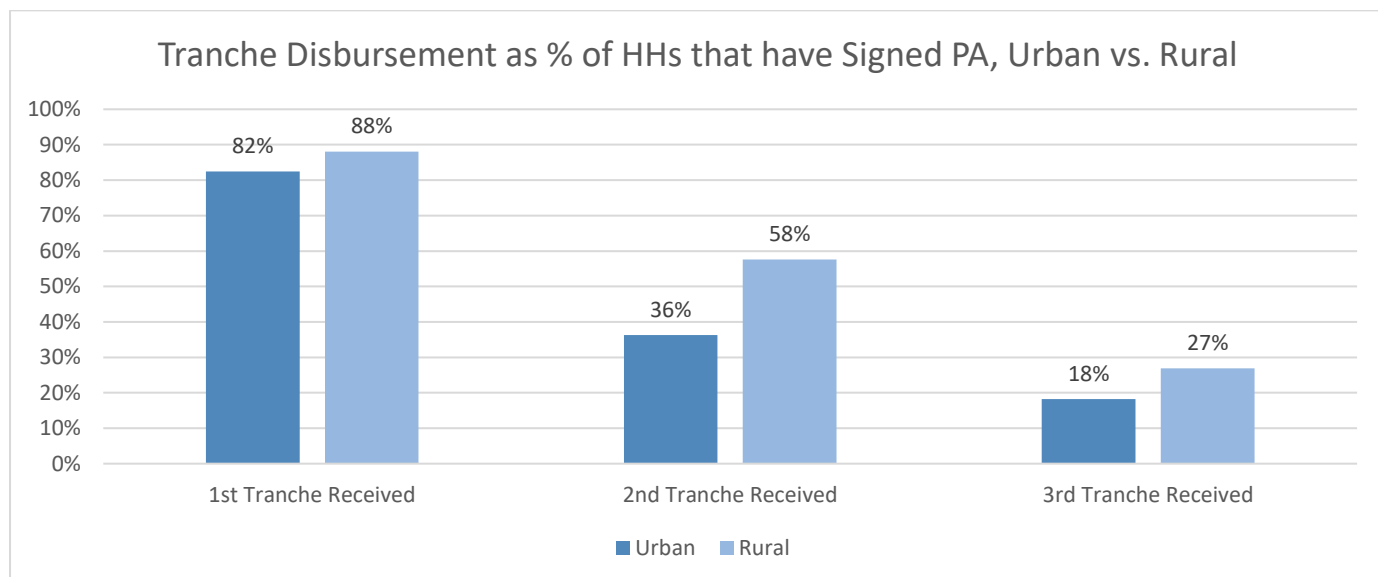


Based on GMALI-CLPIU inspection data, as of 5 December. Maps of % by ward are available [here](#). The urban wards were identified through consultation with District and Municipal Officials, Engineers and HRRP District Coordination Teams (DCTs).

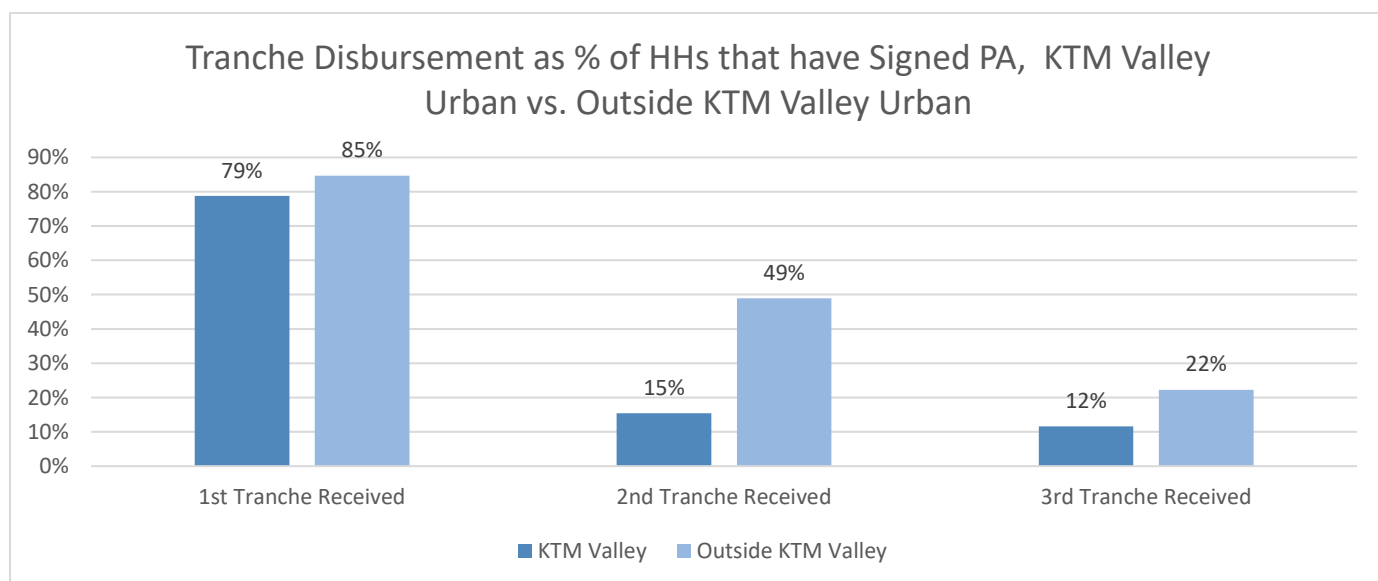

Based on GMALI-CLPIU inspection data, as of 5 December. Maps of % by ward are available [here](#). The urban wards were identified through consultation with District and Municipal Officials, Engineers and HRRP District Coordination Teams (DCTs).

Tracking Return of First Tranche: numbers are based on data collected by HRRP District Coordination Teams (DCTs) through the GMALI DLPIU offices.

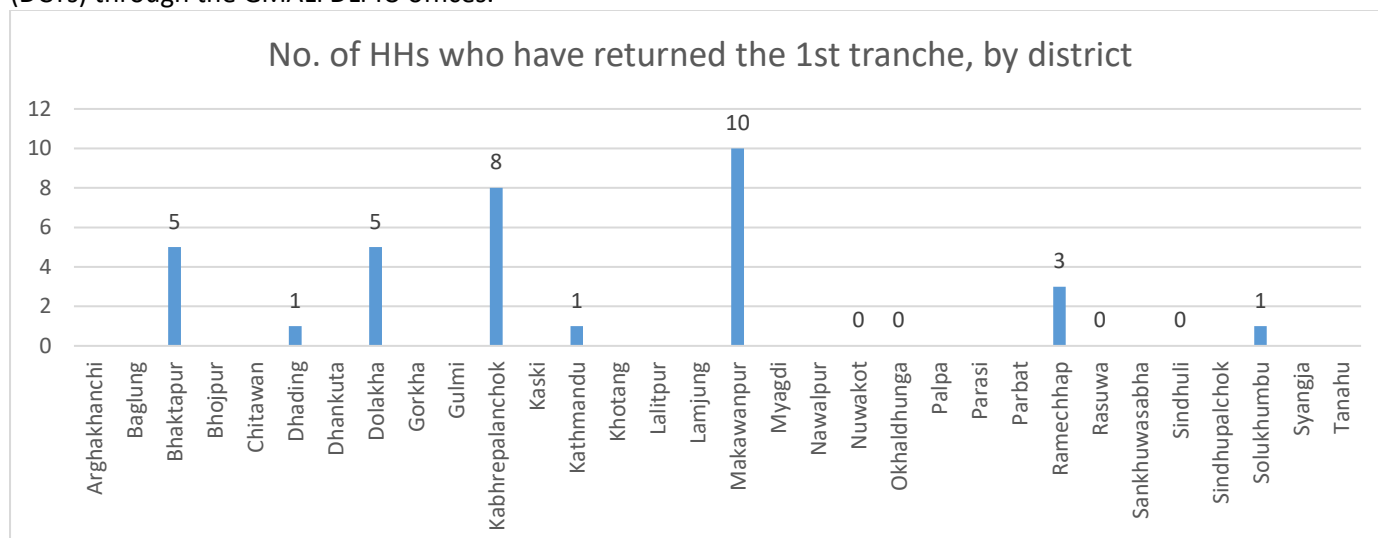

Jit Bahadur Kadel from Hetauda Municipality in Makwanpur returned the first tranche because of fears of being “blacklisted” and the impact this could have on him and his family. Jit, and his 8 family members, live in a two-storey, RC frame house which was damaged in the earthquake. Jit was advised by the engineer who designed his house that the building could be repaired. Jit felt repair was a good option as demolishing the house would be very expensive and rebuilding a two room, one storey building would not be suitable for his large family. He chose not to switch to the retrofit grant because he was worried he wouldn’t meet the deadline and would be blacklisted. Jit has applied for a loan from the bank to cover the cost of repairing his house. This story is common in Hetauda Municipality where many houses are RCC, and fear of being blacklisted and of having to demolish the relatively large houses and build something that would be too small has led to people returning the tranches. Ganesh Sunar, also from Hetauda Municipality, shared that he spent 100,000 NPRs on repairing the front of his house, but the rest of the building still has a lot of damage. He feels he did not get sufficient support from technical staff and has returned the first tranche because of fears of being blacklisted.

‘Improving Support to the most Vulnerable’, donor level meeting, 21 December: this meeting was organised by HRRP to provide reconstruction donors with an update on the status of the Vulnerable Support Working Group and to discuss current issues from the field. HRRP presented an update on the VSWG status, challenges faced, and outputs delivered. The discussion was focused on how to better support vulnerable households through government in areas where there are no Partner Organisations (POs) and effective methods to disseminate effective solutions in collaboration with government and local authorities. The VSWG will meet in the second week of January to plan for a bigger sharing session (tentatively scheduled for the first week of February) to discuss identification of vulnerable households, minimum standards, and approach to support vulnerable households in areas with POs and areas without POs. Please contact Rupa Pandey (meal@hrrpnepal.org) or Minar Thapa Magar (minar@hrrpnepal.org) for further information.

Common Feedback Project Sharing Session, 21 December, presentation and event recording: CFP used this session to share the findings from their [latest report](#) as well as showcasing some of the key trends in CFP data for the past two years. Participants discussed the findings and trends and shared their experience of how CFP data was useful for designing, evaluating, and adjusting their projects and for strengthening coordination and advocacy efforts. Unfortunately, CFP will be closing on 31 December 2018. All CFP data and reports will remain available on the [CFP website](#) for the next 6 months and then will transfer to the UNRCO’s website and will be also archived on the [humanitarian data exchange](#). During the sharing session many participants highlighted that closing CFP will lead to a gap in data regarding community perceptions and trends in reconstruction progress.

DFID Research Roundtable, 20 December: participants included representatives from the Government of Nepal, donors, Partner Organisations, research institutions, and academics. The meeting was held as part of a DFID-funded scoping study supported by their South Asia Research Hub. The aim of the study is to determine the main evidence gaps and research needs in the Nepal reconstruction context. DFID is planning to complete the scoping study by March 2019. During the roundtable the participants discussed outstanding evidence gaps in post-earthquake reconstruction, reviewed who is doing what research where, where targeted research investment would have most impact, and specific areas of technical or thematic research that require improved evidence.

Shelter Cluster Nepal Lessons Learned Workshop, 20 December: the event provided a platform to review shelter cluster inputs in terms of contingencies planning, information management as part of disaster response, and overall shelter cluster initiatives. Participants were encouraged to look back at the impacts of these initiatives and review changes in cluster performance. Participants also provided recommendations for improvements to shelter cluster coordination, particularly considering the changing government structures and how this will impact on the shelter cluster. The programme was chaired by DUDBC and attended by representatives from the National Emergency Operations Centre (NEOC), the IFRC Country Representative, and shelter cluster members.



Participants in the Shelter Cluster lessons learned workshop on 20 December.

DEC Meta-Synthesis Report Review Meeting, 18 December: the event was hosted by the Red Cross to discuss and review a meta-synthesis review undertaken for DEC based on the earthquake response programmes of 13 DEC INGO members and their partners. Participants reflected on their experiences of recovery operations and the issues and challenges that arose. They also highlighted lessons learned that could contribute to future disaster responses. The findings of the meta-synthesis review were shared and discussed, followed by a group activity where participants reviewed and formulated recommendations for a better response in future. The final report will be shared soon.

NRA Toll-free Number Sharing Event, 14 December: the event, organised with support from UNDP which also funds the toll-free number, included a presentation from one of the toll-free number operators on their experience of the role and feedback from a toll-free number user from Ramechhap. The NRA informed during the event that the toll-free numbers (NTC-16600172000 and NCELL-9801572111) have received almost 25,000 calls in total and responds to 50-60 calls per day. One of the toll-free number operators shared that the calls are recorded and transcribed and that most calls have been received from Gorkha district and very few have been received from the 18 moderately affected districts. They also shared that the majority of calls are from men with just over 10% of calls received to date having been from women. Questions are generally related to grievances, tranche disbursement process, land issues, and issues with banks. Ram Bahadur Basnet from Ramechhap shared his experience using the service and how it benefitted his community as a whole. He had found that there was a general lack of information among the local officials about reconstruction, and that often the technical staff were not available on time, so it was hard for people to get correct information. He was able to get answers through the toll-free number and shared these with the officials and his neighbours. He also shared that there are worrying trends in his area of technical staff responding to requests for inspection visits based on nepotism, favoritism, etc. In his closing remarks, Sushil Gyewali the NRA CEO, stated that the NRA will be working on developing an internal and external communication strategy and preparing a budget for both. He also shared that NRA will work on scaling up access to the toll-free numbers, particularly in the 18 moderately affected districts, and developing a consolidated set of FAQs (with HRRP) which can be printed in booklets for dissemination at local level. The CEO called for these to be priority tasks for all involved. The CEO shared his experience from the reconstruction and review workshops that are ongoing in all districts where the local authorities shared that they are unaware of NRA provisions and decisions so it's difficult for them to act accordingly. He also acknowledged the communication gap among GMAI CLPIU and DLPIUs as many decisions made at NRA central level have not been shared to them yet.

Districts & Municipalities

NRA, DLPIU Technical Staff Report from Chumsubri Rural Municipality, Northern Gorkha: Ajit Tiwari has been working in Chumsubri Rural Municipality as an NRA, Building DLPIU inspection engineer for more than 2.5 years. The area he is covering is very large, now one rural municipality but originally 7 VDCs, and it is difficult and takes a lot of time to get around (details on walking time on page four of report). Ajit shared that he often has to travel along very dangerous paths where he is at risk from rock fall and landslides.

Ajit started an awareness programme in Chumsubri RM to provide information to all households about earthquakes, the rules for tranche distribution, and how to construct stronger houses. The main problem Ajit faces is language barriers. The majority of people in Chumsubri do not understand Nepali and Ajit does not speak the local languages. To overcome this, Ajit works with a local person who can translate Ajit's messages into the local language, often one of the local elected representatives.

Ajit shares that people in Chumsubri want the deadline for second tranche disbursement to be extended by more than one year to give them the time needed to construct their homes, increased financial support to account for the added costs of building in such remote areas, and to have tranche payments disbursed by local bank branches. Most houses in the area are built using dry stone masonry with timber or RCC bands. In some cases, RC frame houses are being built but the cost of cement is very high, and rebar has to be transported by mules and then has to be straightened when it arrives on site. Ajit has also shared some videos from Chumsubri Rural Municipality including [one of timber being cut using a cross-cut saw](#) and [one of Ajit delivering an information sharing session on safer construction](#).

More information on the experience of the NRA, Building DLPIU technical staff, and the additional support they need to be able to work at scale and provide the support that households need, please refer to the report on a survey carried out with these staff in September which is available [here](#).



Mules transporting cement to Chumnubri Municipality.



Ajit providing a community orientation on safe building techniques and requirements in Shyala Village, Lho VDC, Chumnubri Rural Municipality, ward-2.



Ajit providing technical assistance to apply correction manual to provide vertical member in Shyala Village, Lho VDC, Chumnuhari Rural Municipality, ward-2.



People gathering for a community orientation in Sirdibas, Chumnuhari Rural Municipality, ward-3.



Supporting a household with site layout and planning in Saleri Village, Sirdibas, Chumnuhari Rural Municipality, ward-3.



A homeowner stands in front of their house which is being rebuilt with technical assistance from Ajit in Shyala Village, Lho VDC, Chumnuhari Rural Municipality, ward-2.

District Level Reconstruction Orientation and Review Workshops, NRA CLPIUs (Building and GMALI): these workshops have been completed in 15 districts so far and will be carried out in the remaining districts in the coming weeks ([field visit planning](#) and [event schedule](#)). The major outcomes of the workshops are NRA signing an MoU ([Nepali](#), [Unofficial English Translation](#)) with each of the municipalities and the municipalities preparing draft municipal reconstruction action plans.

- **Kavre, 25 & 26 November:** MoU signed with all 13 municipalities, [draft reconstruction action plans](#) and municipal profiles ([English](#), [Nepali](#)), presentation slides are available [here](#)
- **Dhankuta, 7 & 8 December:** MoU signed with 5 municipalities (2 were not present and will sign later), [draft reconstruction action plans](#) and [sample municipal profiles](#)
- **Solukhumbu, 7 & 8 December:** MoU signed with all 7 municipalities, [draft reconstruction action plans](#) and [sample municipal profiles](#)
- **Sankhuwasabha, 9 & 10 December:** MoU signed with 9 municipalities (Bhotkhola Rural Municipality will sign later), [draft reconstruction action plans and sample municipal profiles](#)
- **Okhaldhunga, 9 & 10 December:** MoU signed with all 8 municipalities, [draft reconstruction action plans and sample municipal profiles](#)
- **Lalitpur, 9 & 10 December:** MoU signed with 5 municipalities (Lalitpur Metropolitan City will sign later), [draft reconstruction action plans](#) and [municipal profiles](#)
- **Bhaktapur, 11 & 12 December:** MoU signed with all 4 municipalities, [draft reconstruction action plans](#) and [sample municipal profiles](#), presentation slides are available [here](#)
- **Bhojpur, 11 & 12 December:** MoU signed with all 4 municipalities, 5 remaining (Arun, Bhojpur, Hatuwagadhi, Salpasilicho, Shadananda) [draft reconstruction action plans](#) and [sample municipal profiles](#).
- **Khotang, 11 & 12 December:** MoU signed with all 10 municipalities, [draft reconstruction action plans](#) and [sample municipal profiles](#).
- **Kathmandu, 18 & 19 December:** MoU signed with all 5 municipalities, 6 remaining (Dakshinkali, Gorkarneshor, Kageshori Manahara, Kathmandu, Kirtipur, Nagarjun) [draft reconstruction action plans](#) and [sample municipal profiles](#), presentation slides are available [here](#)
- **Dolakha, 21 & 22 December:** MoU signed with all 8 municipalities, (Tamakoshi RM not present, will sign later) [draft reconstruction action plans](#) and [sample municipal profiles](#).
- **Makwanpur, 21 & 22 December:** MoU signed with all 10 municipalities, [draft reconstruction action plans](#) and [sample municipal profiles](#).
- **Palpa, 21 & 22 December:** MoU signed with all 9 municipalities, 1 remaining (Tansen Municipality) [draft reconstruction action plans](#) and [sample municipal profiles](#).
- **Sindhupalchok, 21 & 22 December:** MoU signed with all 11 municipalities, 1 remaining (Panchpokhari Thangpal) [draft reconstruction action plans](#) and [sample municipal profiles](#).
- **Gorkha, 23 & 24 December:** MoU signed with all 11 municipalities, [draft reconstruction action plans](#) and [sample municipal profiles](#).

Videos from the events are available on YouTube. Some recently uploaded videos include interviews with:

- Bhaktapur: [Deputy Mayor, Changunarayan](#), [DCC Chief](#), and [Suraj Shrestha, DLPIU/NRA Engineer](#)
- [Shiva Amatya, Branch Manager Prime Bank, Balaju Branch, Kathmandu](#)
- [Bidur Humagain, Chairperson, Makwanpurgadi Rural Municipality, Makwanpur](#)
- [Smrita, DLPIU Engineer Focal Person, Lalitpur](#)
- Dolakha: [Kalinchowk RM Chairman](#), [Kalinchowk RM Focal Engineer](#), [Mayor of Jiri Municipality](#)

For further information please contact Minar Thapa Magar, HRRP National Coordination Officer, minar@hrrpnepal.org.

HRRP District and Municipal Coordination Meetings, 7 – 20 Dec 2018: during this period district coordination meetings took place in Ramechhap (11 December), Lalitpur (18 December), Gorkha (20 December), and Sindhuli (21 December). Municipal level meetings took place in ChautaraSagachokgadhi Municipality, Sindhupalchok (7 December), Bidur Municipality, Nuwakot (11 December), Nilkantha Municipality, Dhading (7 December), Tripurasundari Rural Municipality, Dhading (11 December), Gangajamuna Rural Municipality (12 & 13 December), Doramba Rural Municipality, Ramechhap (6 & 7 December), Kageshwori Manahara Municipality, Kathmandu (13 December), Tarkeshor Municipality, Kathmandu (14 December), Gosaikunda Rural Municipality, Rasuwa (11 December), Uttargaya Rural Municipality, Rasuwa (18 & 19 December), Bhimfedi Rural Municipality (18 December), and all municipalities, Makwanpur (2- 18 December). Some of the highlights from these meetings include:

- In **Ramechhap**, there are six Partner Organisations (POs) working in recovery and reconstruction and most will complete their activities in December 2018. Additional support to the vulnerable and landless beneficiaries, gaps in construction completion and inspection, lack of information among the ward chairpersons on NRA policies and circulars, and home owner's preference for their own design especially two storey stone in mud mortar were some the challenges discussed during the meeting. Besides, challenges, working on a rotational basis (aarma parma system), selection of masons through community members, use of local and salvaged materials, Door to Door technical assistance, and masons training have been some of the good practices in the district. Special Guest, Mr. Shanti Prasad Paudel, member of Parliament, Province 3 suggested to identify the real earthquake affected people and proposed POs if possible to extend their project till July 2019 to cover this building season.
- In **Lalitpur**, DLPIU NRA GMALI requested all the POs working in reconstruction to provide winterisation support for earthquake affected families still living in temporary shelters or who are vulnerable. GMALI and Building DLPIUs will conduct a meeting to find a way forward to address the Lumanti issue in Dalchoki, that was highlighted during the review workshop. DLPIU-Education requested POs to coordinate with the DLPIU for all the activities involving school programmes. Also, POs were requested to support the construction of permanent toilets in the schools as most of the construction activities are mostly focused on the school building construction only. DLPIUs (GMALI, Building, Education) in Lalitpur will conduct a Joint Monitoring of POs work within the district to resolve issues and facilitate POs to carry out effective work.
- In **Gorkha**, households supported by POs have not been able to get the third tranche of the housing reconstruction grant due to the issue of double payment in the banking system. There has also been issues regarding the deduction of money from households' accounts by the bank, after the release of tranche payments by the POs to recompense the loan taken by the households. This has caused delay in completion of houses. Concerns were raised regarding the lack of specific information on the 50,000 NPRs top-up support for vulnerable HHs. 470 HHs in the district have been identified for relocation. So far 61 HHs have relocated and 140 HHs are in the process of relocating, with their land registration going on. Facilitation for the relocation of 235 HHs is also ongoing. Information, recommendation letters, and public inquiry forms were collected for 36 landless HHs. Regarding the completion certificate, local bodies were requested to print the certificates in coordination with DLPIU Building.
- In **Sindhuli**, it was reported that delays in providing light timber/steel frame structure manual training for technical staff are delaying third tranche inspections as most houses in the district are timber frame. This has ultimately led to a low rate of tranche disbursement in the district. Training on light timber/steel frame structure manual is scheduled for 26 and 27 December 2018 in Sindhuli. DLPIU Building recommended conducting a monitoring visit to visit non-compliant houses constructed in Ward No. 6 of Sunkoshi Rural Municipality in coordination with NRCS/ERO Sindhuli.
- In **Ward 1, ChautaraSagachokgadhi Municipality, Sindhupalchok**, the process of distributing reconstruction completion certificate was explained where the ward engineer conducts a final inspection of the houses and if the houses meet all the standards are recommended for the completion certificate signed by Ward Chief and Chief Administration Officer. It was reported that there are 5 landless people in the ward living on public land. One of them is living in a Basuki community forest and has received 50,000 NPRs

but has not started reconstruction since she does not have land. The ward chief wanted to know how to proceed with such cases.

- In **Ward 13, Bidur Municipality, Nuwakot**, there are 109 non-compliant houses and many one roomed houses have been built near these non-compliant houses. There were concerns regarding the building design approval from the Municipality. Since most of the issues were technical, Building M & E Consultant and DLPIU Engineers have agreed to address the issues by working closely together. Ward members raised concerns regarding grievance results and payments to the non-compliant houses.
- In **Ward 13, Nilkantha Municipality, Dhading**, there are still many people who have not been listed as eligible for the GoN housing reconstruction grant despite being earthquake affected. Some households have been stuck in the grievance process for a long time which has slowed their reconstruction progress. Many landless issues have been reported but ward representatives do not have information on addressing landless issues and the associated policies. They were shared some information on the process of getting 200,000 NPRs and were suggested to contact GMALI office working with landless issues for further process. Issues with banks not releasing the tranche on time were also raised in the meeting.
- In **Ward 2, Tripurasundari Rural Municipality, Dhading**, it was reported that four beneficiaries had received the third tranche of the GoN housing reconstruction grant despite continuing to live in their old, damaged house or a temporary shelter. The Ward Chief clarified that one of these houses belongs to a single woman, one belongs to an elderly man, and two belong to people who are working abroad. So, the ward representatives to meet the NRA deadlines requested the field engineers to fill up the forms and submit at the NRA District office. The ward representatives assured that reconstruction of these houses would start, and they would monitor the process by themselves.
- In **Gangajamuna Rural Municipality, Dhading**, it was reported that there has been some misunderstanding between the community and the municipality office because of the long time taken to address the grievance results by NRA. There are households who want to switch from the retrofit grant to the reconstruction grant. Ward offices conducted inspection of these houses in close collaboration with NRA field Engineers, Ward Chiefs, and municipal officers and have forwarded the list to the GMALI DLPIU office for further processing. Municipal officials were informed of the no fee policy for households that need any administrative / approval support related to the housing reconstruction and retrofit grants, e.g. change of name. Municipal officials were also informed that households that do not want to reconstruct can return the grant funds to NRA through “Rastriya Banijya Bank” account No. ॠ11004. NRA tranche disbursement deadlines and distribution of completion certificates in wards with high completion of reconstruction were also discussed.
- In **Ward 4, Gangajamuna Rural Municipality, Dhading**, suggestion was made for resurvey of houses that have not been included in the list of households eligible for GoN financial support. There were concerns regarding houses that have received the second tranche of the GoN housing reconstruction grant, but which are in landslide risk zones and need to be resettled. There was also demand for mason training in the ward. NRA tranche disbursement deadlines, distribution of completion certificates and the process of returning the GoN tranche were shared during the meeting.
- In **Ward 7, Doramba Rural Municipality, Ramechhap**, about 145 retrofit beneficiaries are not willing to do agreement as they think 100,000 NPRs is not enough for retrofitting the house. There are 85 HHs willing to switch to full reconstruction beneficiaries. It was reported that some beneficiaries have not been able to do partnership agreement due to land issues among family members. A campaign was launched by ward office with support from technical persons and Community Resource Persons (CRP) provided by HELVETAS to motivate beneficiaries to build earthquake resistant houses following NRA guideline. This seem to have worked with increase in households receiving first and second tranches as well as beneficiaries who were ready to return the tranche, starting reconstruction instead, thanks to the campaign and the regular visits by CRPs and technical persons. Ward Chief has requested CRP and technical persons to identify the

beneficiaries who are no more alive and to find the actual earthquake affected beneficiaries. The ward office has also stopped the approval of third tranche disbursement to some households with no toilets.

- In **Ward 4, Doramba Rural Municipality, Ramechhap**, 268 HHs have not started rebuilding and are still living in their old, damaged houses but have received the first tranche of the GoN housing reconstruction grant. About 10-12 houses are non-compliant. Technical persons and social mobilisers face a lot of challenges in getting around the area due to remoteness, scattered households, and poor road conditions. The irregular presence of the ward chief is also a challenge.
- In **Ward 4, Kageshwori Manahara Municipality, Kathmandu**, one of the major reconstruction issue in Danchhi is related to tenant farmers and land owners. Most of the land owners have been living abroad while the land has been occupied by the farmers as tenants for long periods. These farmers have built houses on the land without building permit and are unable to access the GoN housing reconstruction grant as they do not have land ownership certificate and without this they also cannot get building permit approval from the municipality. The ward office has been providing free service to households reconstructing up to 1,000 sqft. The ward office is also planning to do Door to Door visits to inform people about the NRA tranche disbursement deadline and to track information on households not intending to reconstruct and willing to return the first tranche.
- In **Ward 3, Kageshwori Manahara Municipality, Kathmandu**, nearly 80% of households have reconstructed through technical support (help desk) provided by NSET, Baliyo Ghar. The ward office has planned to collect the information on households who have taken the first tranche and do not intend to reconstruct houses. The list will be submitted to DLPIU Kathmandu. Additionally, the ward office is planning to conduct Door to Door visits to track reconstruction status.
- In **Ward 5, Tarkeshor Municipality, Kathmandu**, the main concern is that grievances submitted have not been addressed. 2,500 grievances were registered from Goldhunga area. Participatory Approach to Safer Shelter (PASA) has been practiced by NRCS to sensitise communities for safer reconstruction processes.
- In **Ward 5, Gosaikunda Rural Municipality, Rasuwa**, discussion focused on the NRA tranche disbursement deadline and tracking the households who have received first tranche and not started reconstruction, households on the eligible list but who have not received tranche payments, and also households not interest to reconstruct who would like to return the tranche. The ward office is planning a campaign on reconstruction in rural areas and to collect information on the types of houses with number of rooms constructed with support from field technical persons.
- In **Ward 2, Uttargaya Rural Municipality, Rasuwa**, discussion focused on the NRA tranche disbursement deadline and tracking the households who have received first tranche and not started reconstruction, households on the eligible list but who have not received tranche payments, and also households not interest to reconstruct who would like to return the tranche. The ward office is planning to collect information on the types of houses with number of rooms constructed with support from field technical persons. The distribution of completion certificates to HHs that have completed reconstruction, technical persons to collect information on HHs that that received third tranche, and the process of switching from retrofit to full reconstruction beneficiaries were also discussed.
- In **Ward 3, Uttargaya Rural Municipality, Rasuwa**, discussion focused on the NRA tranche disbursement deadline and tracking the households who have received first tranche and not started reconstruction, households on the eligible list but who have not received tranche payments, and also households not interest to reconstruct who would like to return the tranche. It was reported that there has been an absence of ward technical persons for a long time. NRCS and Build Change are providing socio-technical assistance in this ward. There was also discussion on the process of switching from retrofit to reconstruction grant.
- In **Ward 7, Bhimfedi Rural Municipality, Makwanpur**, the meeting focused on reconstruction status of beneficiaries who have signed PA and received first tranche, grievances, and retrofitting issues. It was reported that 138 HHs have signed the PA and received the first tranche, 137 have received the second

tranche, and 104 have received the third tranche. Out of them 1 HH has not completed the toilet construction so, requested for coordination and follow up for the completion of the toilet. Process of final inspection of completed houses, CS entry, and distribution of completion certificates were also discussed during the meeting. Ward office to follow up with the households that are remaining to complete reconstruction by Jan/Feb 2019.


- In **Makwanpur**, municipal level coordination meetings were held in all 10 municipalities. The main purpose of those meetings was the formulation of Environmental and Social Safeguard Management Plans. Each municipality identified the major social infrastructure scheme to be prioritised related to reconstruction. Some of the major schemes identified were plantation, maintenance of drinking water supply, landslide control, and mine management. In addition, orientation was conducted on the grievance process, with a focus on appeal of grievance results. Concerns regarding the grievance results, retrofitting especially for mud mortar masonry, landlessness, and need for clarity on the authority of the local government were raised during all the meetings.

HRRP District Coordination Team Dhading, Weekly District Report, 7 – 20 Dec 2018



Ward No. 4, Gangajamuna Rural Municipality, Dhading: two storey, hybrid structure with brick and cement mortar masonry ground floor and light weight timber frame and CGI sheet covering for the first floor. There are no lintel bands above the doors on the ground floor. The home owner has received the second tranche of the GoN housing reconstruction grant.

[HRRP District Coordination Team Kavrepalanchok, Weekly District Report, 7 – 20 Dec 2018](#)

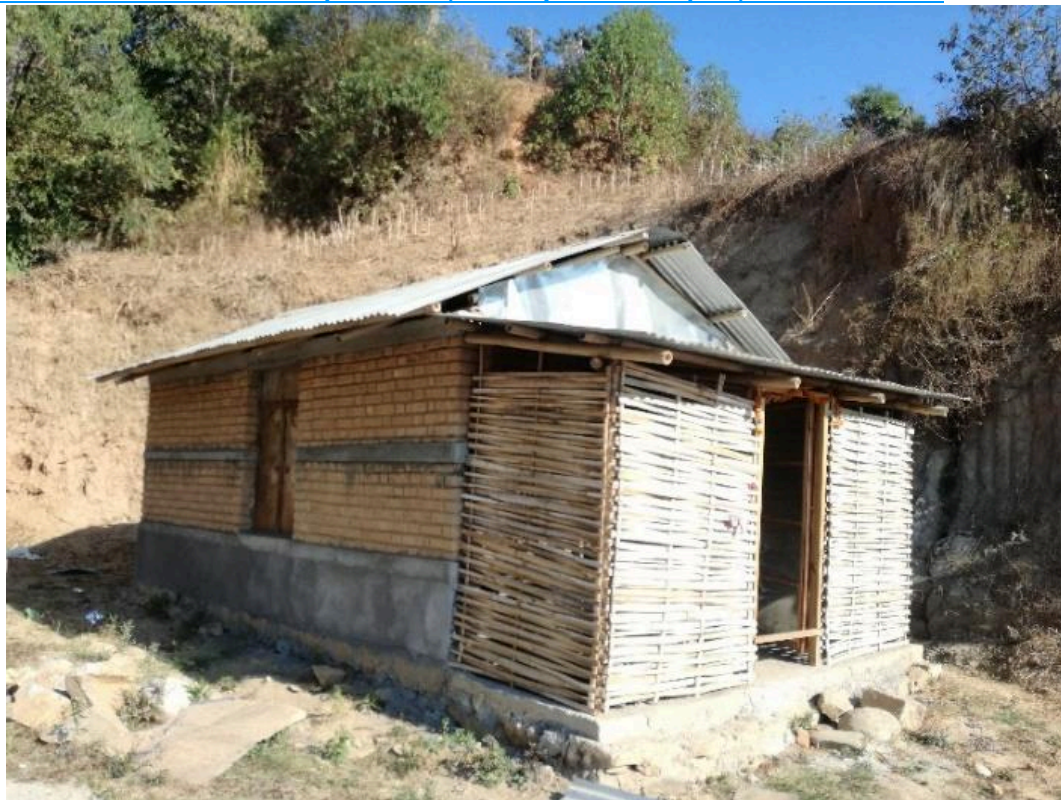

Ward No. 5, Panchkhal Municipality, Kavrepalanchok: brick and mud mortar masonry house belonging to a single woman. The home owner has received all three tranches of the GoN housing reconstruction grant. The construction was supported by Habitat for Humanity through its implementing partner ASF Nepal.

[HRRP District Coordination Team Makwanpur, Weekly District Report, 7 – 20 Dec 2018](#)



Ward No. 7, Bhimfedi Rural Municipality, Makwanpur: three room, stone and mud mortar masonry house with RCC bands. The home owners have received the first tranche of the GoN housing reconstruction grant. Around 20 - 25 of this type of house have been built in the area.

HRRP District Coordination Team Nuwakot, Weekly District Report, 7 – 20 Dec 2018



Ward No. 13, Bidur Municipality, Nuwakot: two single room, brick and cement mortar masonry houses with a shared roof. This looks like a single structure but is two structures attached, belonging to two beneficiaries. Both home owners have received the third tranche of the GoN housing reconstruction grant.

HRRP District Coordination Team Rasuwa, Weekly District Report, 7 – 20 Dec 2018



Ward No. 2, Uttargaya Rural Municipality, Rasuwa: two room, brick and cement mortar masonry with rigid roof. The home owner is a single woman and has received all three tranches of the GoN housing reconstruction grant. The total cost of construction was 1,000,000 NPRs. Build Change supported with construction materials (cement, sand, and rebars) to build up to plinth level.

HRRP District Coordination Team Sindhupalchok, Weekly District Report, 7 – 20 Dec 2018



Ward No. 9, Chautara Sagachokgadhi Municipality, Sindhupalchok: two room, load bearing, stone and mud mortar masonry with CGI roof and RCC bands. The home owner has received all three tranches of the GoN housing reconstruction grant.

Requests for Partner Support

Review of Draft Hollow Concrete Block Manual: this draft manual has been developed by a technical working group under the NRA technical committee. Please share feedback and suggestions with Kuber Bogati, HRRP National Technical Coordination Officer, techofficer1.national@hrrpnepal.org, by COB, Friday 4 January.


‘Epicentre to Aftermath: Political, social and cultural impacts of earthquakes in South Asia’, 11 and 12 January, London: this two-day conference is focused on the political and cultural impacts of earthquakes in South Asia and is hosted by the SOAS South Asia Institute as part of [SOAS’s SWAY project](#). Many of the papers presented at this conference will focus on the 2015 Nepal earthquake. The keynote speaker for the conference is Dr. Sara Shneiderman whose talk is entitled 'Restructuring Life: political, social, and material transformation in post - conflict, post-disaster Nepal' and will be delivered at SOAS on the evening of Friday 11 January. If you are interested to attend, please register [here](#).

DOCUMENTS & PRODUCTS


HRRP

Maps of Urban and Rural Tranche Disbursement, December 2018: based on GMALI-CLPIU inspection data, as of 5 December. Urban areas in earthquake affected districts were identified through consultation with GMALI DLPIU offices, municipal and ward officials, NRA, Building DLPIU technical staff, and the HRRP District Coordination Teams


(DCTs). A total of 589 wards, spread across 10 Rural Municipalities, 79 Urban Municipalities, 1 Sub-Metropolitan City, and 4 Metropolitan Cities, were identified as urban.

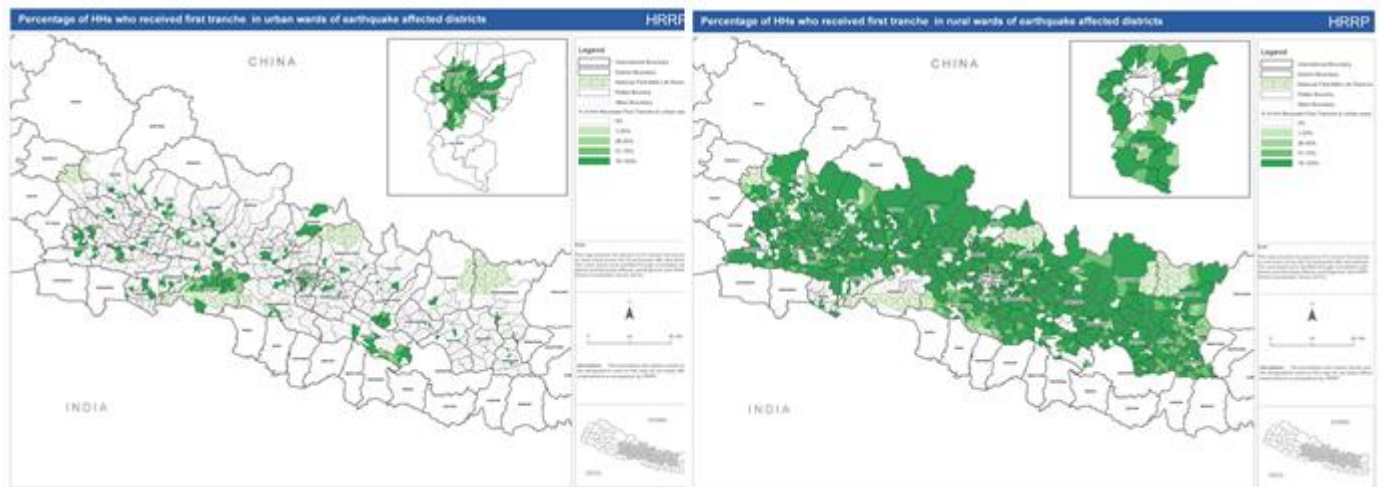

Left: [first tranche disbursement in urban wards](#). Right: [first tranche disbursement in rural wards](#).

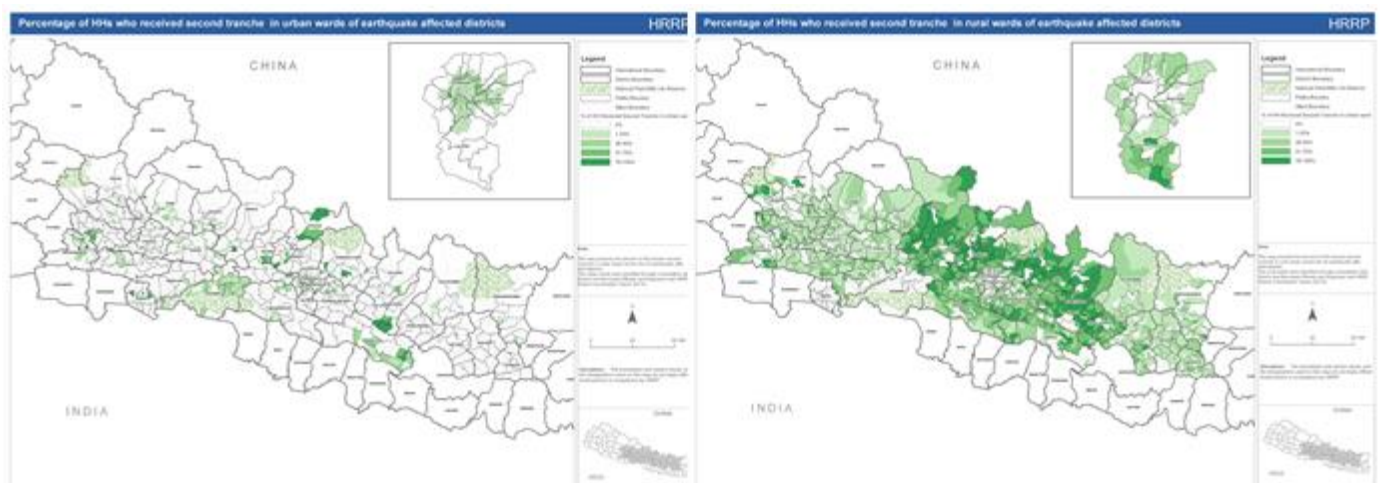

Left: [second tranche disbursement in urban wards](#). Right: [second tranche disbursement in rural wards](#).

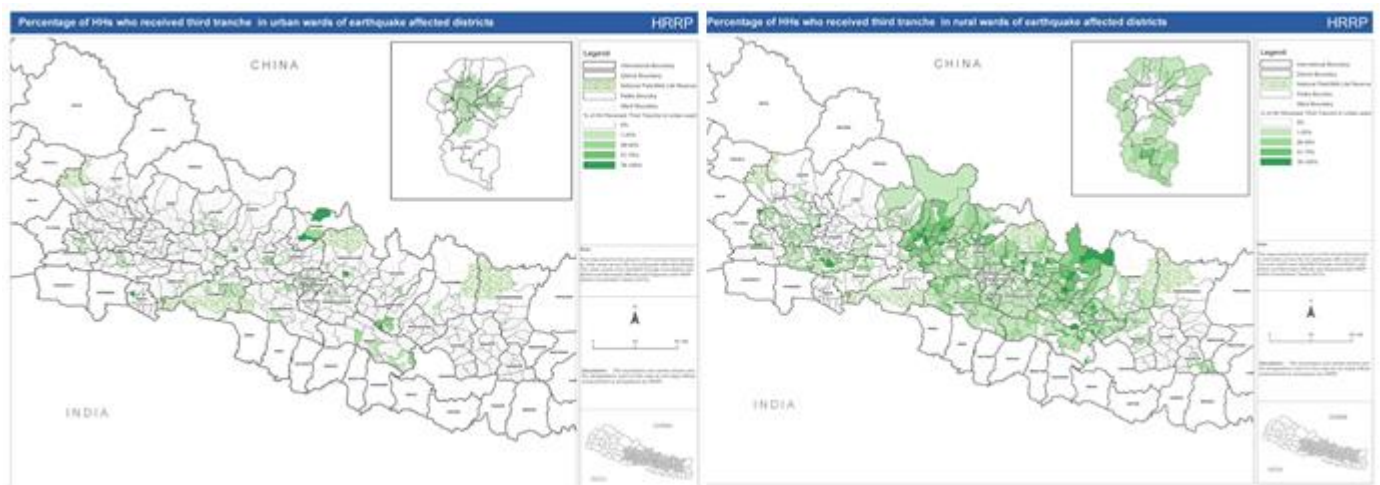

Left: [third tranche disbursement in urban wards](#). Right: [third tranche disbursement in rural wards](#).

Partners

[Community Perception Survey, Reconstruction, Food Security & Livelihood, and Protection, Common Feedback Project, November 2018](#): this is the final report from CFP which will be closing at the end of 2018. This report reflects the result of the November community perception survey and also looks back over the entire year, to examine progress made, and key gaps to be filled. The report shows positive signs of progress on reconstruction and recovery with 72% of respondents reporting that they feel they have recovered from the earthquake. The percentage of respondents taking loans to finance their reconstruction is also noteworthy – 50% of respondents reported taking a loan to finance their reconstruction, with the majority (65%) borrowing from informal sources at high interest rates. The heavy debt burden also extends to livelihood recovery. 24% of respondents reported that their debt burden is a significant constraint in their livelihood recovery. This could lead to substantial impact on the overall economic recovery of affected communities for years to come.

['Reconstructing Nepal: The 2015 Earthquakes and their aftermath', Research Guide, The University of British Columbia](#): this research guide is intended to provide an overview of English-language materials that address Nepal's series of earthquakes in April and May 2015, as well as the ongoing responses and repercussions of those events on Nepal's citizens, institutions, and environment. The resources compiled in this guide are available for reference to students, faculty, researchers, and community at UBC, and the general public.

[Milijuli Nepali, Episode 1136](#): this episode is a mix-bag programme from Sindhuli, Makwanpur, and Sindupalchok. The first story is about Ram Bahadur Biswakarma who has completed constructing his new house. He has reused the corrugated tin sheets from his damaged house to build a wall around his kitchen garden which has stopped cattle from eating the vegetables. The second story is of Dr. Abhisekh Chauhan, a physician deployed by the government at the health post in Lampantar. Dr. Abhisekh shares advice on hygiene and sanitation, ventilation, nutritious food, and warm clothes for children during winter. He says children should be immediately rushed to the health post when they fall sick and advised parents to have a doctor's number handy. The third story is of Uma Bhujel, whose house has been retrofitted. Uma Bhujel shares the joys of the living in a house that has been fortified after the earthquake.

[Improved Cook Stoves, EnDev Results-based Financing Facility \(RBFF\)](#): this is an on-going project implemented by Practical Action with funding support from DFID via GIZ EnDev. The project is providing incentives for 21 types of cook stoves, ensuring their availability and affordability. The project is being implemented in Dhading, Gorkha, Rasuwa, Nuwakot, Makwanpur, Parbat, Baglung, Myagdi, and their adjoining districts. In Nepal, more than 18,000 people (mainly women and children) die prematurely every year due to smoke generated from use of inefficient stoves. It is the third leading risk factor for ill health and also a contributing factor to greenhouse emission in the country. People also spend hours walking far distances to secure cooking fuel. The harmful effects of such practices can be minimised by using efficient cook stoves. In this context, Practical Action would like to encourage partners to support households to introduce efficient cook stoves during the reconstruction stage.

[Media Digest](#) | [FAQ](#) | [Briefing Pack](#) | [Meeting & Events](#) | [4W](#) | [Housing Progress](#) | [Housing Typologies](#)
