

Monthly District Report

Lalitpur, Bhaktapur

22 October – 21 November 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Lalitpur	World Bank Nepal in coordination with NRA CLPIU Building organized a Sharing session on curriculum development for social mobilisers and mobile masons. HRRP Lalitpur team member was also involved in documents consolidation for TOT of Social Mobilisers along with representatives from other organisations involved in shelter reconstruction.	4 Nov 2019	Royal Singi Hotel, Kathmandu	Ms. Sulochana Nepali Disaster Risk Management Analyst, World Bank Nepal snepali@worldbank.org	
	The general ward-level coordination meeting was conducted at Ward 14 of Godawari Municipality. Ward Chief in presence of Ward Members, Ward Secretary, representatives from DLPIU Building Lalitpur (M & E Consultant, Engineers) and HRRP attended the meeting. The purpose of the meeting was to find out reasons of delay in reconstruction of houses by beneficiaries to claim 2 nd tranche and 3 rd tranche.	8 Nov 2019	Thaiba, Badegaun, Ward office of Ward no. 14, Godawari Municipality	Er. Roshan Raj Giri M & E Consultant DLPIU Building Lalitpur roshanrgiri@gmail.com Contact: 9841335744	Meeting minute
	HRRP team joined engineer of Lalitpur Metropolitan City to collect housing typology survey in KoBo App and to inspect houses for 2 nd tranche	12 Nov 2019	Ward no 15, Khumaltar, Lalitpur Metropolitan City	Ms. Tilashmi Subba NRA Engineer Lalitpur Metropolitan City Contact: 9860133155	Field visit section
	DLPIU Building Lalitpur conducted Ward level interaction meeting with Ward officials in order to checked the progresses and issues of shelter reconstruction.	10 Nov 2019	Ward no 10, Lakure Bhanjyang, Mahalaxmi Municipality	Er. Sabi Shrestha Focal Engineer, DLPIU Building Lalitpur Contact: 9849366040	
	DLPIU GMALI Lalitpur organised a short interaction program for the entire banking institutions that are working in various palikas of Lalitpur district and involved in providing services related to tranche disbursement. Numerous issues related to banking processes and challenges were discussed during the event. Mr. Shivaram Gelal, Chief of DLPIU GMALI Lalitpur urged representatives from banking institutions to expedite services fairly as the reconstruction project is phasing over in nearly 1 year.	15 Nov 2019	DLPIU GMALI Lalitpur, DCC Manbawan, Lalitpur	Mr. Krishna Prasad Awasthi Finance Management Specialist EHRP-DLPIU GMALI Lalitpur Manbawan, Lalitpur	
	The team including of M & E Specialist of EHRP- GMALI Lalitpur and Durable Solutions/People in	11-13 Nov 2019	Gimdi and Ashrang areas, Bagmati Rural	Mr. Yamnath Giri M & E Specialist	

Summary of events during this period

	Need (PIN) conducted monitoring and research works for landless beneficiaries of Gimdi and Ashrang areas, Bagmati Rural Municipality, Lalitpur district		Municipality, Lalitpur district	DLPIU GMALI Lalitpur Manbhawan, Lalitpur Contact: 9851239785, yamnathgiri2014@gmail.com	
	DLPIU Building Lalitpur is engaged in conducting feasibility study of retrofitting beneficiaries in order to inspect whether is listed houses are suitable for retrofitting process or not. NRA engineers deployed in Palikas are involved in this study.		Various wards of Palikas of Lalitpur district	Prajwol Karki District Support Engineer Contact 9881498222 prazolkarki427@gmail.com	
	Palika data of Lalitpur were updated in GD	11 Nov 2019	HRRP, Jwagal, Kupondole	Mr. Sachin Malego IM Officer, HRRP and Ms. Ambika Amatya, District Coordinator HRRP	
	Tranche status of Lalitpur updated to GD sheet in Palika Profile	21 Nov 2019	HRRP, Jwagal, Kupondole	Mr. Sachin Malego IM Officer, HRRP	
	Contact list update and 5 W data update	Ongoing	HRRP, Jwagal, Kupondole	Sachin Malego, IM Officer, HRRP	
	Development of DLPIU Level MIS system	Ongoing	HRRP, Jwagal, Kupondole	Sachin Malego, IM Officer, HRRP	
	Support in Housing Cost Calculator	Ongoing	HRRP, Jwagal, Kupondole	Sachin Malego, IM Officer, HRRP	
	Support in Designing of HRRP Final Report	Ongoing	HRRP, Jwagal, Kupondole	Sachin Malego, IM Officer, HRRP	
	Support in Website maintenance	Ongoing	HRRP, Jwagal, Kupondole	Sachin Malego, IM Officer, HRRP	
	Support in Social Media Update	Ongoing	HRRP, Jwagal, Kupondole	Sachin Malego, IM Officer, HRRP	
Bhaktapur	An orientation on retrofitting measures was organised in Bhaktapur Municipality. Out of 43 beneficiaries in retrofitting list, nearly 22 of them attended the orientation. Retrofitting task group of DLPIU Building Bhaktapur organised this orientation where M & E Specialist of DLPIU GMALI Bhaktapur clarified on issues of grant processes and shifting of beneficiaries from retrofitting to reconstruction list and vice versa.	13 Nov 2019	Bhaktapur Municipality	Er. Shiva Bhandari District Support Engineer DLPIU Building Bhaktapur Contact: 9857045118	Field visit section
	Joint M & E visit was organised by a team members of DLPIU Building Bhaktapur (DSE and engineers), HRRP Bhaktapur Team and NRA engineers at Ward no 2 of Bhaktapur Municipality. The purpose of the visit was to observe the houses of beneficiaries that are in retrofitting list. Also, houses were surveyed using housing typology KoBo App tool.	13 Nov 2019	Ward no 2, Byasi, Bhaktapur Municipality	Er. Shiva Bhandari District Support Engineer DLPIU Building Bhaktapur Contact: 9857045118	Field visit section
	HRRP Bhaktapur team member was involved in sharing the key highlights of shelter reconstruction progresses taking place in Bhaktapur district with the research team of Democratic Resource Center Nepal.	17 Nov 2019	Satdobato, Lalitpur	Ms. Pallavi Payal, Democratic Resource Center Nepal Lalitpur	
	GMALI Bhaktapur in coordination and facilitation by Transparency International Nepal have organised grievances public hearing and interaction program with	18 Nov 2019	Ward no 4, Changunarayan Municipality, Bhaktapur district	Mr. Dhruva Gaida Chief, DLPIU GMALI Bhaktapur	

Summary of events during this period

beneficiaries of Ward no 4, Changunarayan Municipality, Bhaktapur district. Chief of GMALI and Building responded to the hearings from the beneficiaries.			Contact: 9851221570 dgaida022@gmail.com	
DLPIU Building Bhaktapur is engaged in conducting feasibility study of retrofitting beneficiaries in order to inspect whether is listed houses are suitable for retrofitting process or not. NRA engineers deployed in Palikas are involved in this study.		Various wards of Palikas of Bhaktapur district	Shiva Kumar Bhandari District Support Engineer Contact 957045118 Diyabhandari80@gmail.com	
Tranche status of Bhaktapur updated to GD sheet in Palika Profile	21 Nov 2019		Mr. Sachin Malego IM Officer, HRRP	Palika Profile
Update of Contact list and 5 W update	Ongoing		Mr. Sachin Malego IM Officer, HRRP and Ms. Ambika Amatya, District Coordinator HRRP	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Joint M & E visit to observe reconstruction efforts of beneficiaries in Bhaktapur and Lalitpur districts	25 November – 20 December 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	HRRP Lalitpur and Bhaktapur Cluster
General Palika level and Ward level meeting and consultation with elected ward officials over the reconstruction progress and status of the visited wards of Bhaktapur and Lalitpur district	25 November – 20 December 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	HRRP Lalitpur and Bhaktapur Cluster
Orientation and information dissemination on retrofitting measures by Retrofitting Task Group of Lalitpur and Bhaktapur	25 November – 20 December 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	HRRP Lalitpur and Bhaktapur Cluster


News & Updates

Tranche Status (Lalitpur)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	3361	3370	3142	3142	2265	2207	252	197	180	0
Godawari Nagarpalika	10950	9602	8092	8092	2975	2522	330	136	133	0
Konjyosom Gaunpalika	2580	2156	2079	2079	1871	1353	372	328	319	0
Lalitpur Mahanagarpalika	6594	7402	6357	6350	1465	976	286	125	120	0
Mahalaxmi Nagarpalika	4409	3662	3132	3107	1089	952	92	53	50	0
Mahankal Gaunpalika	2451	2271	2239	2239	1867	1414	66	58	57	0

Graph of Tranche Status:

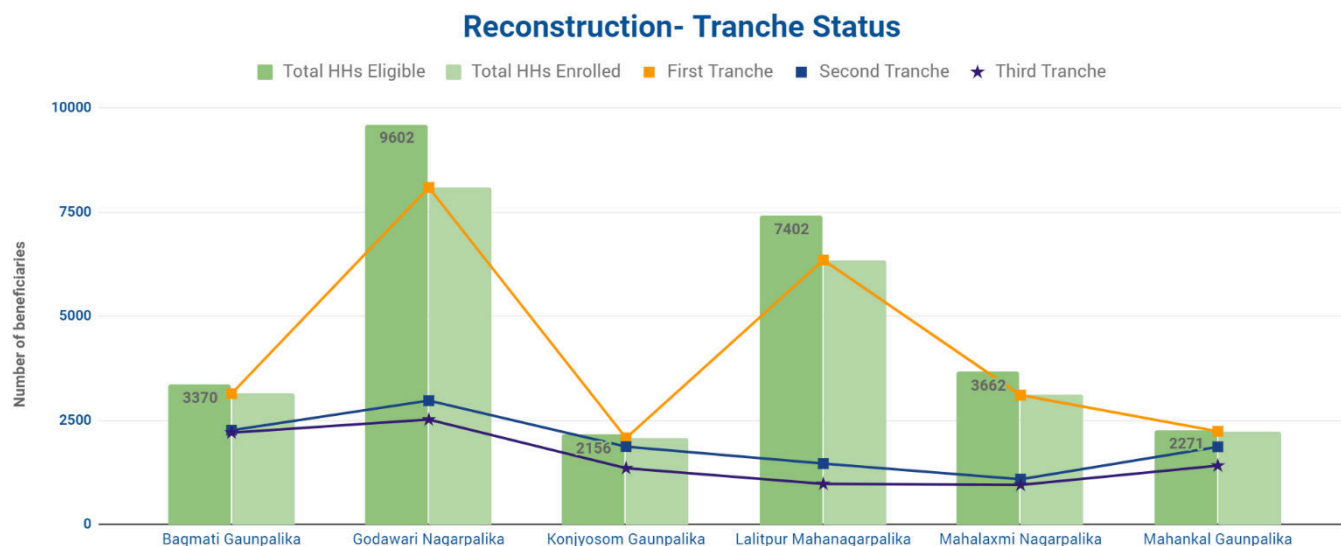

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

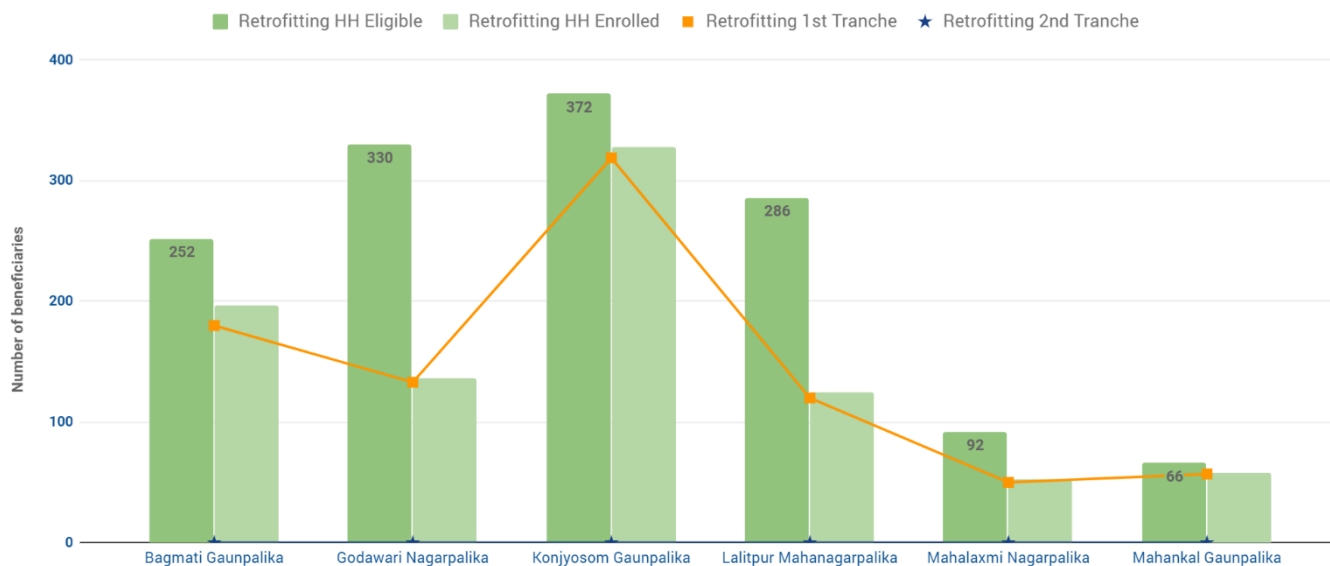

Tranche Status (Bhaktapur)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bhaktapur Nagarpalika	8175	7656	5637	5637	1874	1716	161	43	43	0
Changunarayan Nagarpalika	11059	11008	9826	9826	3887	3780	212	109	109	0
Madhyapur Thimi Nagarpalika	3015	2336	2080	2080	738	721	95	61	61	0
Suryabinayak Nagarpalika	7948	7425	6998	6998	3067	2909	234	105	105	0


Graph of Tranche Status:

Reconstruction- Tranche Status



Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

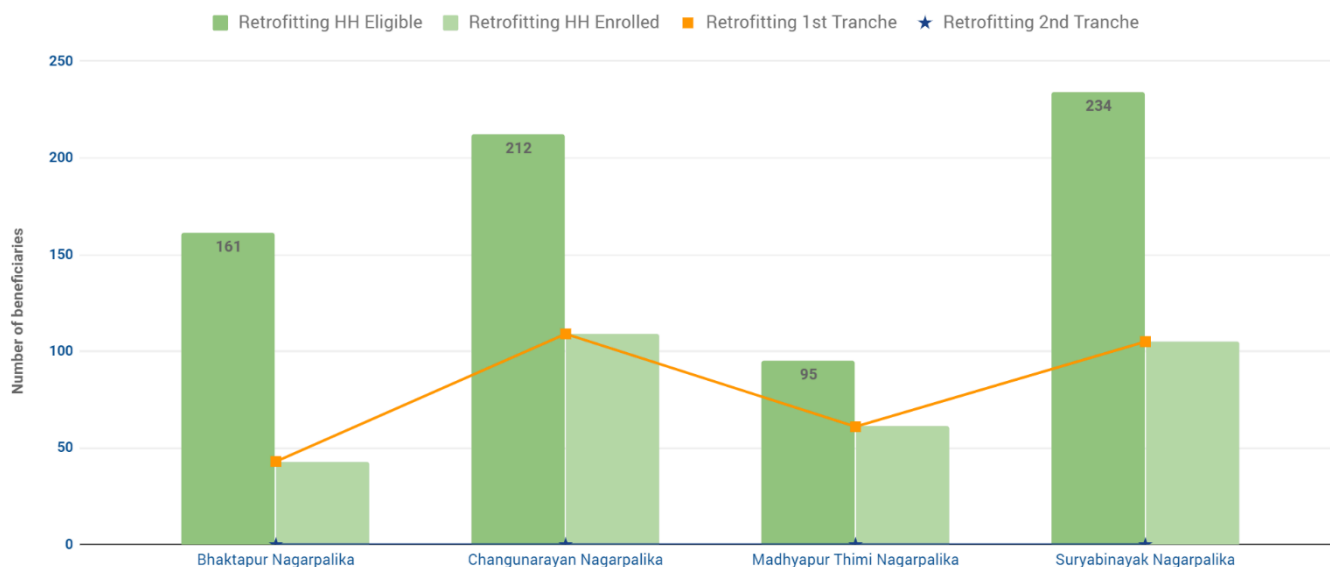

Field Visit Reports (Lalitpur)

Visit 1

Visit 1		
Date	Location	Participants
12 November 2019	Ward no. 15, Khumaltar, Lalitpur Metropolitan City, Lalitpur district	• Tilashmi Subba, Engineer, Lalitpur Metropolitan City • Ambika Amatya, District Coordinator, HRRP Lalitpur Cluster
Objective(s)	• To observe the reconstruction status of the houses and provide relevant suggestions further. • To collect housing typology survey in KoBo App	
Why was the visit carried out in this location? Priority wise, Write any other reason		

Lalitpur Metropolitan City is in P1 priority as according to HRRP's municipal targeting in shelter reconstruction. Therefore, this visit was carried out to observe reconstruction status of beneficiaries who have applied 2nd tranche and to provide way forward for the beneficiaries who have reconstructed houses soon after earthquake and before deployment of engineers.

'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.'

Previous Issues	Current Issues
-----------------	----------------

Summary

Field Visit:

- No. of HHs visited: 4
- No. of meetings/interaction with engineers:
- No. of engineers interacted with: 1
- No. of meetings/interaction with local officials: None
- No. of local officials interacted with: None

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held) - *no meetings at municipality and ward level were organised.*

HRRP Lalitpur District Coordination Team joined NRA engineer of Lalitpur Metropolitan City to observe reconstruction status of beneficiaries in Ward no 15, Khumaltar. The purpose of this visit was to observe reconstruction status of beneficiaries who have applied 2nd tranche and to provide way forward for the beneficiaries who have reconstructed houses soon after earthquake and before deployment of engineers.

Beneficiaries who have initiated reconstruction in Ward no 15 have reached to plinth level works and also upto roofing level. Such houses have applied 2nd tranche and mostly bears RCC typologies. Some beneficiaries have reconstructed the houses soon after earthquake and before deployment of engineers which were found to have missed major bands (lintel, sil, roof) and vertical reinforcement and also corner stitch too.

Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Beneficiaries have missed major elements in houses that makes houses resilient.	Beneficiaries were suggested to apply correction measures that in fact increases the resilience of the house that were rebuild without assistance and no inspection from engineers.	Beneficiaries have showed willingness to apply correction methods despite house was rebuild before deployment of engineers.	Beneficiaries	As soon as possible

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)

Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)

In the visited area, Ward no 15, it was found that some beneficiaries have immediately rebuild their houses without technical assistance that lead to missing of major technical elements that makes the houses resilient and complaint. Perpetuation of such kind of cases could challenge the urban reconstruction in face of major chunk of energy and resources and put forwarded to build the resilience capacity of the urban dwellers. This also signifies that proper information about minimum requirements of building codes hasnot been reached upto beneficiaries level.

Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)

In Ward no 15, LMC, the vulnerability issue of one beneficiary is related with non communicable disease such as cancer. The beneficiary had been living separately with her step sons before earthquake too and after earthquake too, however step sons are always there as strong support mechanism to provide her needful care and assistance.

Photos



Beneficiary name: Indira Thapa, Ward no. 15, Khumaltar, Lalitpur Metropolitan City, single storey 3 room wall system BMC house have party rigid roof and flexible roof too. The owner is a single women, accessed 1st tranche and was reconstructed soon after earthquake and before deployment of engineers.



Beneficiary name: Babu Ram Bogati, Ward no. 15, Khumaltar, Lalitpur Metropolitan City, 2.5 storey RCC house has 7 rooms in total. The house is compliant and have received 1st tranche too. The owner had earthquake damaged house at Mahankal Rural Municipality and received building drawing approval for plot at Ward no. 15, Khumaltar, Lalitpur Metropolitan City. The owner still resides in rented place at Balkhu, Kathmandu.

Field Visit Reports (Bhaktapur)

Visit 2

Date	Location	Participants
13 November 2019	Ward no. 2, Byasi, Bhaktapur Municipality, Bhaktapur district	- Prabesh Adhikari, DSE, DLPIU Building Bhaktapur - Shiva Prasad Bhandari, DSE, DLPIU Building Bhaktapur - Reeja Hathechu, Rabina, Samjhana Shrestha, Deepa Shrestha (Engineers of Bhaktapur Municipality) - Ashmita Shrestha, Engineer, DLPIU Building Bhaktapur - Ambika Amatya, District Coordinator, HRRP Lalitpur Cluster
Objective(s)	- To observe the reconstruction status of the houses and provide relevant suggestions further. - To observe the houses of retrofitting beneficiaries and to provide relevant retrofitting measures. - To collect housing typology survey in KoBo App	

Why was the visit carried out in this location?

Bhaktapur Municipality is in P1 priority as according to HRRP's municipal targeting in shelter reconstruction. There are altogether 43 beneficiaries in retrofitting list, however none of them have initiated retrofitting of their houses. Therefore, this visit was carried out to observe houses of retrofitting beneficiaries and to provide relevant retrofitting measures to be applied in the visited houses as well as to provide advises to the beneficiaries.

'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.

Previous Issues	Current Issues

Summary

Field Visit:

- No. of HHs visited: 5
- No. of meetings/interaction with engineers: 1
- No. of engineers interacted with: 3
- No. of meetings/interaction with local officials: None
- No. of local officials interacted with: None

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)- *no meetings at municipality and ward level were organised.*

HRRP Bhaktapur District Coordination Team coordinated with DLPIU Building Bhaktapur to conduct Joint M & E Visit in Ward no 2, Byasi, Bhaktapur Municipality. The field visit team observed nearly 5 houses in total. The visit was specifically targeted to cover the collection of housing typology in KoBo App as well as 2 houses were visited in order to provide suggestions to beneficiaries regarding application of suitable retrofitting measures. The houses that were visited to collect housing typology in KoBo App have already taken all three tranches from government of Nepal, however they are yet to take construction completion certificates. Those all 3 houses are compliant from technical point of view too and were reconstructed using RCC technology.

Orientation to Retrofitting Beneficiaries on Retrofitting Measures

Bhaktapur Municipality was amongst the mostly devastated municipality in Bhaktapur district by Nepal earthquake 2015. There are altogether 161 beneficiaries in retrofitting list however only 43 of them have taken 1st tranche. Reconstruction data of Bhaktapur Municipality-

Total Beneficiaries	7656
PA enrolled	5637
1st tranche	5637
2nd tranche	1855
3rd tranche	1694
Retrofitting	161
Retrofitting- enrolled beneficiary	43
Retrofitting 1 st tranche	43

It was revealed time and again from NRA engineers of Bhaktapur Municipality and from the Retrofitting Task Group Team of DLPIU Building Bhaktapur that none of the retrofitting beneficiaries have applied retrofitting procedures in their houses despite they have taken 1st tranche. It was revealed by the beneficiaries themselves that they have utilized the 1st tranche in conducting minor repair and maintenance of their houses however none of them have applied standard and certified processes of retrofitting measures.

As an important part of Retrofitting Task Group Team of DLPIU Building Bhaktapur, an orientation on retrofitting measures was co conducted at meeting hall of Bhaktapur Municipality dated 13th November 2019 from 11 AM -1 PM. Bhaktapur Municipality coordinated with DLPIU Building Bhaktapur office in informing the retrofitting beneficiaries for their compulsory presence in the orientation. Out of 43 retrofitting beneficiaries, nearly 22 of them have attended the orientation.

The main purpose of conducting orientation was to instill key messages among retrofitting beneficiaries that houses in retrofitting category can be technically retrofitted to make it technically livable again.

A brief and concise presentation about data on retrofitting beneficiaries, various kind of housing typologies in practice and needful retrofitting measures that can be applied were shared with the available beneficiaries by Shiva Kumar Bhandari and Prabesh Adhikari, District Support Engineers of DLPIU Building Bhaktapur. NRA Engineers of Bhaktapur Municipality was also present throughout the orientation along with Mr. Bibek Gautam, M & E Specialist of DLPIU GMALI Bhaktapur and HRRP Bhaktapur Team Member.

Some of the issues discussed during the orientation by beneficiaries are –

- One beneficiary revealed that in a 4 storey house with 14 inch pillar at ground level, some portion of connection were broke between wall & RCC slab. The beneficiary intended to retrofit the house unaware about the correct measures to be applied.
- 2 houses are in retrofitting category however currently the house is owned by sibling, multiple beneficiaries and the house stands on single plot but only beneficiary owns PA agreement card.
- One house is in retrofitting category, however NRA engineers have inspected it time & again during their regular site visit and have suggested the beneficiary to submit application to shift into full damage category.
- Multiple beneficiaries (siblings in relation) having SMC house with 2 storey intends to retrofit the house.
- Beneficiary had BMM house of 4 storey. 1st tranche of retrofitting grant were applied in repair and maintenance works on outer part of wall, however cracks still persists.

A short visit was carried out in Ward no 2, Byasi, Bhaktapur Municipality to observe 2 houses of retrofitting beneficiaries and to provide relevant retrofitting measures to be applied in the visited houses as well as to provide advises to the beneficiaries.

Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Retrofitting beneficiaries have poor or no knowledge on suitable retrofitting measures to be applied to make their partially damaged houses technically sound.	Technical personnel deployed in concerned municipalities should assist beneficiaries in suggesting proper retrofitting measures to be applied to the intending beneficiaries. The technical personnel had been informing beneficiaries to contact and visit DLPIU Building Bhaktapur office and meet DSE for further technical details on retrofitting.	Retrofitting Task Group under DSE and Focal Engineer will inspect the houses of intending beneficiaries in retrofitting list and cross check whether the house is suitable for retrofitting or not and also provide suitable way forward for the beneficiaries.	NRA Engineers of Palikas, DLPIU Building, DSE, Focal Engineer	As early as possible or by Magh 2076

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)

- Houses in retrofitting category are confused whether to carry retrofitting process or to shift themselves into full damaged category and conduct full reconstruction of their houses.

- Beneficiaries having SMC and BMM houses with upto 3-4 stories intends to retrofit their house however technically it was revealed from District Support Engineer that such quake damaged SMC & BMM houses are difficult to retrofit in face of its eccentric footing and degree of damage parts. If such case persists, then firstly the intending beneficiaries should reduce the stories ie. Chopping up off few stories and apply suitable correction measures. The DSE also revealed that retrofitting of SMC/BMM houses with 3-4 stories bears pretty large sum of money than expected.

Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)

Though government has provided grant amount and inspired affected communities to either rebuild or retrofit their houses, the processes has got delayed as affected people and their issues mainly of disputes over land, lack of ownership papers and reality of poor financial condition are the among the major reasons that shall challenge urban reconstruction in current condition and in forthcoming years too.

Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)

Photos



Beneficiary name: Ram Laghu, Ward no 2, Byasi, Bhaktapur Municipality. 4.5 storey RCC house is complaint and has received all three tranches from government. Cladding is done for outer finishing works.



Beneficiary name: Laxmi Das Basukala, Ward no 2, Byasi, Bhaktapur Municipality. 5 storey BMC wall system house is in retrofitting category. After observing this house by DSE, the owner was recommended to reduce the stories height (upto 2 stories) and to raise RCC wall from ground floor throughout.

Housing Typology Report (Max 4 Photos, Select best photos from each district)



Beneficiary name: Kale Bhandari, Ward no 2, Chagunarayan Municipality, Bhaktapur, RC frame structure, Non-Compliance (9"X12" column- unsafe during analysis, constructed Immediately after earthquake	Beneficiary name: Pavitra Poudel, Changunarayan Municipality, Ward no 4. Non-Compliance (Missing beam, bands, constructed immediately after earthquake
	
Beneficiary Name: Bhumi Nanda Timilsina, Ward no 4, Kaleshwor, Mahankal Rural Municipality. 1 storey plus attic SMM structure has kept RC bands. The beneficiary has requested for 3 rd tranche during time of inspection	Beneficiary Name: Bishnu Prasad Dulal, Ward no 4, Kaleshwor, Mahankal Rural Municipality. 1 storey plus attic SMM structure has kept RC bands properly. The beneficiary has requested for 3 rd tranche during time of inspection

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
My BMM house is more than 30 years old with upto 5 storey. I want to retrofit my house as it has partial cracks only. Is it possible to retrofit my house ?	Retrofitting Beneficiary	From technical point of view, partially damaged house with typology of SMM and BMM having 5 stories are often impossible to conduct retrofitting processes as it incurs huge amount of money. Therefore, if beneficiary can bear cost then full demolishing of the quake damaged house and its reconstruction is highly recommended. (District Support Engineer, DLPIU Building, Bhaktapur)
My house is a 4 storey wall system house with 14 inch pillar at ground level, however some portion of connection were broke between wall & RCC slab. The beneficiary intended to retrofit the house unaware about the correct measures to be applied.	Retrofitting Beneficiary	➤ Retrofitting Task Group under DSE and Focal Engineer will inspect the houses and cross check whether the house is suitable for retrofitting or not and also provide suitable way forward for the beneficiaries. ➤ At least 1 or 1.5 stories need to be chopped off (reduction in stories number) to reduce further threat during retrofitting process.

Questions Collected

		➤ The beneficiary should be mentally ready to bear the retrofitting cost as government provided tranche amount is only a grant amount given to inspire owners to initiate reconstruction or retrofitting by themselves. (District Support Engineer, DLPIU Building, Bhaktapur)
My house is in retrofitting category however NRA engineers of Bhaktapur Municipality who happened to inspect my house time to time have revealed that my house should go in full reconstruction list. I am totally confused, how my problem can be solved?	Beneficiary	DSE will inspect the houses and cross check whether the house is suitable for retrofitting or not and also provide suitable way forward for the beneficiaries. After the inspection by DSE, if the house is suggested technically to shift into reconstruction list then the beneficiary should request a genuine application letter to be issued from Ward office to concerned Municipality for shifting from Retrofitting category to Reconstruction Category. Once the shifting processes is kicked off, GMALI will coordinate with Building office to facilitate the concerned beneficiaries. (M & E Specialist, DLPIU GMALI, Bhaktapur)

Challenges and Way Forward

Challenge	Way Forward
Beneficiaries in retrofitting list are perplexed and in state of dilemma about retrofitting and minor repairing process and whether to go for retrofitting measures from certified agencies or not.	Responsible district government counterparts and concerned Palika offices should put effort to instill key messages of retrofitting measures among beneficiaries in retrofitting list. Proper amount of social mobilization is required to inspire and encourage beneficiaries to conduct retrofitting measures.
