

Monthly District Report

Lamjung, Tanahu, Kaski, Syangja

23 August – 27 September 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Lamjung	Sharing inspection form Design catalogue volume-2 with DLPIU-Building	05-September, 2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Meeting with DLPIU-Building, DLPIU-GMaLI for fixing date of One day Technical Orientation on NRA Guidelines and Policies along with mail sharing for invitation to the DLPIU-Building Technical, DLPIU-GMaLI, Partner Organizations and other stakeholders.	05-September, 2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Orientation to the Palika focal engineers regarding Task force implementation, working modality, process, timeline and the scheduled target reach action, procedures and strategic planning for RETROFITTING work from DLPIU building along with deployment of various level resource persons as: Coordinator-umesh dangol, DSE, NRA Member:shital babu lohani ,Focal Er Member: Biren Shah, TC, HRRP Member: Ashutosh kr.yadav ,Er	06-September, 2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Slides Preparation and Sharing of Slides for One day technical orientation program with DSE and Focal Engineer-DLPIU Building	08-September, 2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Preparation of Letter from DLPIU-GMaLI for one Day technical Orientation Program.	09-September, 2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Preparation of Orientation Schedule and sharing with DLPIU-Building, DLPIU-GMaLI	10-September, 2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	One Day Orientation Program on Technical Guidelines and Policies" completed on September 11, 2019 at Hotel Tukuhe,Besisahar,	11-September, 2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	Lamjung to NRA Technicals with 45 participants altogether: The topic of the orientation includes NRA guidelines/policies, HRRP introduction, Correctional/Exceptional Manual, Repair and Retrofitting Manual with new template format, Hollow concrete block manual. Sessions Taken By DTC- HRRP (Biren Shah), DC-HRRP (Rijan Gajurel), DSE, NRA- (Umesh Dangol) and DMT technical Coordinator- (Deepak Saud). Correctional/Exceptional manual, Repair and Retrofitting Manual, NRA guidelines/policies, HRRP introduction and Hollow concrete block manual				
	Preparation of Report for One Day Technical orientation program and sharing with HRRP Team	12-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	District contact list is updated and uploaded at district google drive.	25-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika profile of all eight municipality were uploaded at respective palika website.	25-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Tranche distribution MIS is updated for this month.	25-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Monthly meal data for the month of August is update at National level.	5-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika profile date is updated for this month.	25-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
Tanahau	Palika profile of 5 municipality were uploaded at respective palika website.	25-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Tranche distribution MIS is updated for this month.	25-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	Monthly meal data for the month of August is update at National level.	5-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika profile date is updated for this month.	25-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
Kaski	Communication with DSE and Focal Engineer for One Day Technical Orientation Program	12-September,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Preparation of Orientation Schedule and sharing with DLPIU-Building, DLPIU-GMaLI	12-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Slides Preparation and Sharing of Slides for One day technical orientation program with DSE and Focal Engineer-DLPIU Building.	12-September,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	One Day Orientation Program on Technical Guidelines and Policies" completed on September 19, 2019 to NRA Technicals with 46 participants altogether: The topic of the orientation includes NRA guidelines/policies, HRRP introduction, Correctional/Exceptional Manual, Repair and Retrofitting Manual with new template format, Hollow concrete block manual. Sessions Taken By DTC- HRRP (Biren Shah), DC-HRRP (Rijan Gajurel), DSE, NRA- (Abhishek Ghimire), DSE, NRA- (Ganesh Thapa) Correction/exception manual, Repair and Retrofitting Manual, NRA guidelines/policies, HRRP introduction, Inspection SOP and Hollow concrete block manual.	19-September,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Tranche distribution data cleaning and uploading process at newly prepared Tranche distribution MIS templet is conducted.			Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	HRRP team have worked 4 days at GMaLI kaski office. During those period we have clean tranche distribution data of			Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	individual HHs, meeting with DLPIU- Building chief, focal person, District support engineers. Apart from this support GMAI staff for data cleaning and coordination part.				
	Palika profile of all five palika is updated and uploaded on respective palika website.	20-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	District contact list is updated and uploaded in district google drive.	21-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
Syangja	Communication with DSE and Focal Engineer for One Day Technical Orientation Program	13-sep ,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Preparation of Orientation Schedule and sharing with DLPIU-Building, DLPIU-GMAI	13-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Slides Preparation and Sharing of Slides for One day technical orientation program with DSE and Focal Engineer-DLPIU Building	14-Sep ,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Sharing of retrofit inspection template.	15-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	One Day Orientation Program on Technical Guidelines and Policies" completed on September 17, 2019 to NRA Technicals with 46 participants altogether: The topic of the orientation includes NRA guidelines/policies, HRRP introduction, Correctional/Exceptional Manual, Repair and Retrofitting Manual with new template format, Hollow concrete block manual. Sessions Taken By DTC- HRRP (Biren Shah), DC-HRRP (Rijan Gajurel), DSE, NRA- (Nawaraj Sharma) Correction/exception manual, Repair and Retrofitting Manual, NRA guidelines/policies, HRRP introduction and Hollow concrete block manual.	17-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	Palika profile data of all 11 palika is updated and uploaded at respective palika website.	25-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	District contact list is updated and uploaded at respective district google drive.	23-Sep,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person

News & Updates

Lamjung

Task Force recruitment Program:

HRRP team attended the Orientation to the Palika focal engineers regarding Task force implementation, working modality, process, timeline and the scheduled target reach action, procedures and strategic planning for RETROFITTING work from DLPIU building along with deployment of various level resource. The letter from CLPIU building to deploy resource person for scaling up retrofit. On this regard DLPIU building must make a task force in district level and Palika level (Technical) to scale up retrofit. So today task force was implemented as per the letter from CLPIU building.



One Day Orientation Program on Technical Guidelines and Policies:

Upcoming Events & Meetings

One day orientation program was organized by HRRP over three district lamjung, kaski and syangja on September 11th, 17th and 19th September 2019. NRA Palika level technical person were targeted participant of that event, DLPIU's GMaLI, Building and DCC representatives also participated the program. 124 participant from three district participated orientation program. The topic of the orientation includes

- NRA guidelines/policies
- HRRP introduction, working modality and Timeline
- Correctional/Exceptional Manual
- Repair and Retrofitting Manual with new template format
- Hollow concrete block manual.

One day orientation program of technical guidelines of NRA at
Kaski District




Tranche Status (Lamjung)


Tranche Status Table: 25-Sep,2019

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Besishahar Nagarpalika	2851	1310	1235	1235	701	498	11	6	6	0
Dordi Gaunpalika	3375	2244	2254	2254	981	445	60	19	19	0
Dudhpokhari Gaunpalika	2667	2437	2356	2356	1632	490	9	4	4	0
Kwholasothar Gaunpalika	740	314	271	271	86	55	73	0	0	0
MadhyaNepal Nagarpalika	2346	1505	1444	1444	714	313	52	16	16	0
Marsyangdi Gaunpalika	1936	916	1039	1039	420	313	185	161	161	0
Rainas Nagarpalika	4362	3050	2977	2977	2111	1114	161	106	106	0
Sundarbazar Nagarpalika	4084	2257	2142	2142	1423	877	112	24	24	1

Graph of Tranche Status:

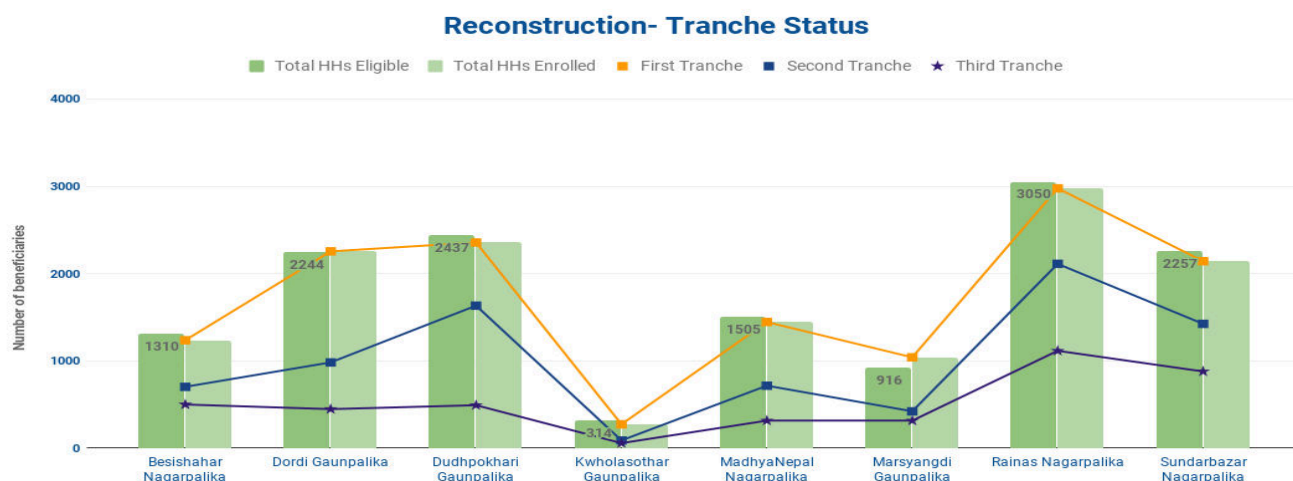

Graph for Retrofitting Status:

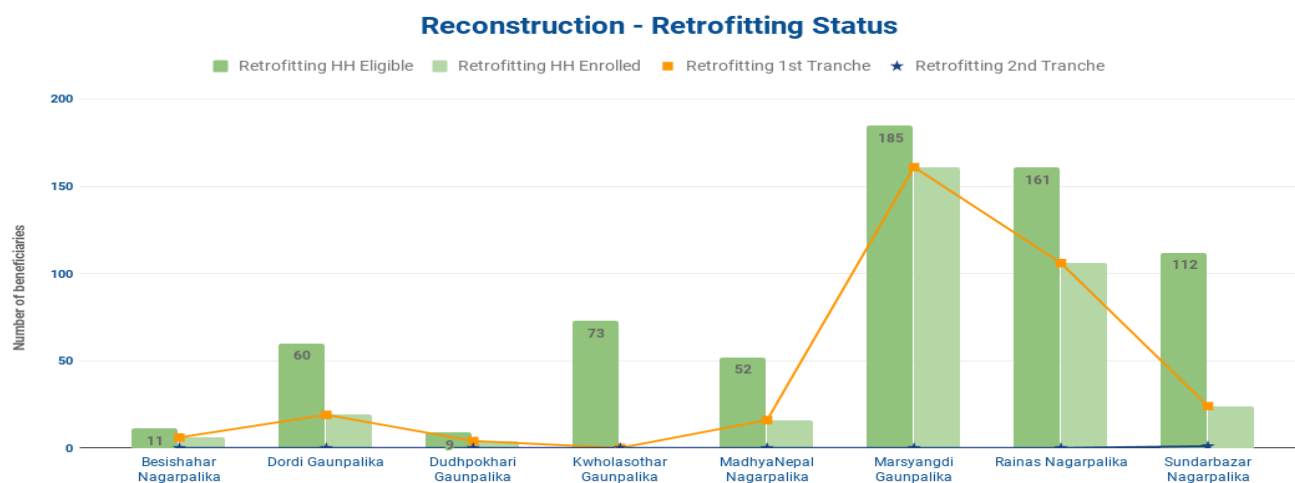


Tranche Status (Tanahau)


Tranche Status Table: 25th Sep-2019

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Anbukhaireni Gaunpalika	1050	710	760	760	434	432	21	5	5	0
Bandipur Gaunpalika	1226	609	943	943	656	428	33	32	32	0
Bhanu Nagarpalika	7540	4219	4183	4183	2358	1865	75	12	12	0
Bhimad Nagarpalika	2680	987	974	974	549	262	46	0	0	0
Byas Nagarpalika	4626	2486	1904	1904	1166	917	163	180	180	0
Devghat Gaunpalika	960	725	532	532	338	194	32	8	8	0
Ghiring Gaunpalika	969	254	235	235	133	96	0	0	0	0
Myagde Gaunpalika	1877	1292	1237	1237	661	425	38	33	33	0
Rhishing Gaunpalika	1771	680	489	489	289	216	34	0	0	0
Shuklagandaki Nagarpalika	2837	1859	1725	1725	953	571	24	1	1	0

Graph of Tranche Status:

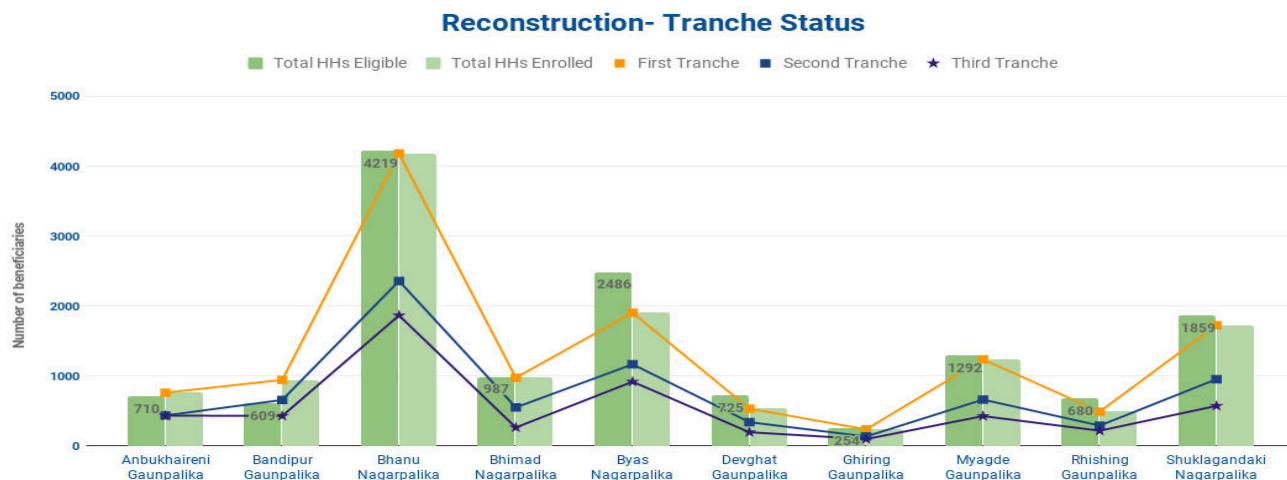

Graph for Retrofitting Status:

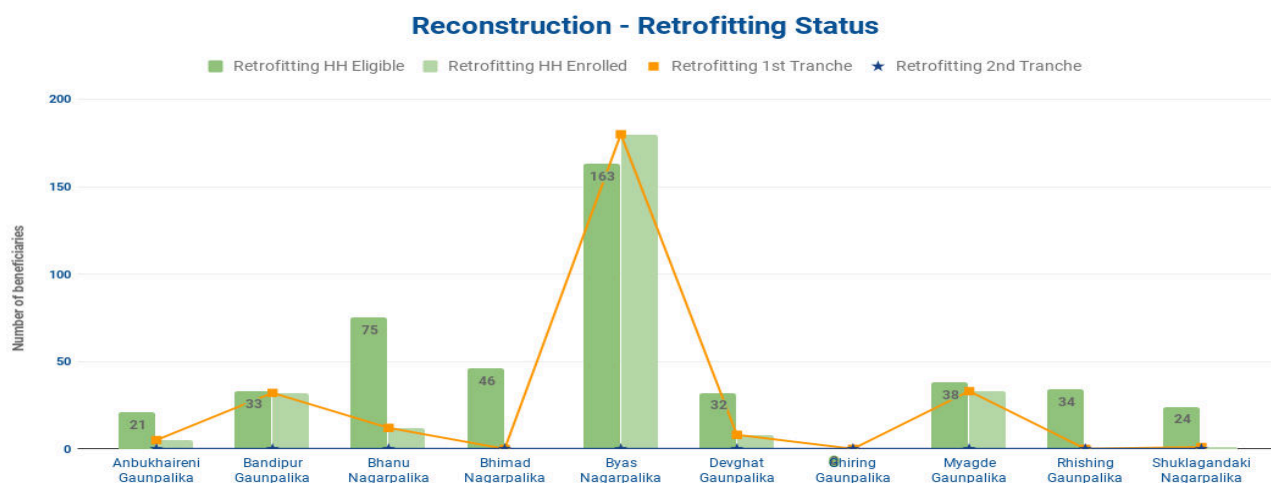


Tranche Status (Kaski)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Annapurna Gaunpalika	667	395	395	395	179	74	19	12	12	0
Machhapuchchhre Gaunpalika	781	427	427	427	265	34	30	5	5	0
Madi Gaunpalika	2296	1160	1160	1160	512	97	40	12	12	0
Pokhara Lekhnath Mahanagarपालिका	5276	2774	2421	2421	1153	281	111	84	84	0
Rupa Gaunpalika	2054	1270	1222	1222	455	238	42	26	26	0

Graph of Tranche Status:

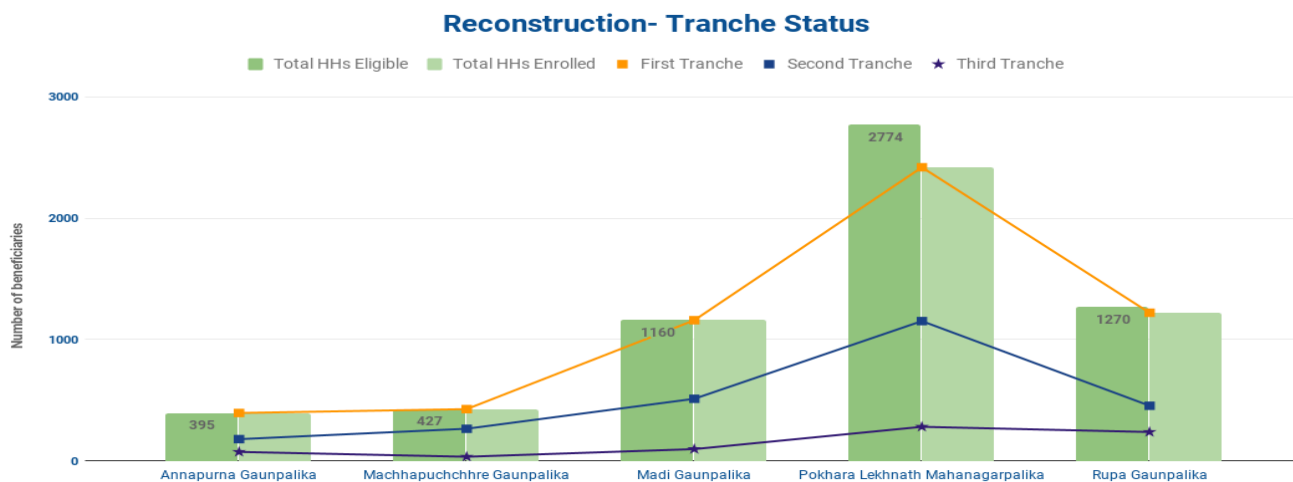

Graph for Retrofitting Status:

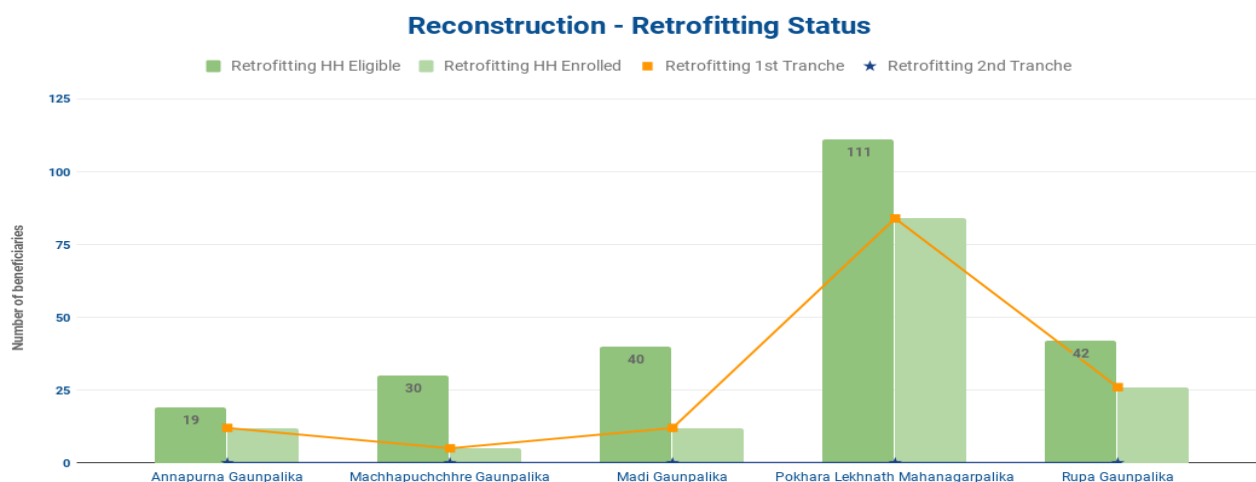


Tranche Status (Syangja)


Tranche Status Table:25-Jun,2019

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Aandhikhola Gaunpalika	1515	843	823	823	372	117	72	43	43	0
Arjunchaupari Gaunpalika	803	509	475	475	255	184	65	51	51	0
Bhirkot Nagarpalika	2099	1042	1002	1002	313	118	26	21	21	0
Biruwa Gaunpalika	1024	638	609	609	191	103	40	9	9	0
Chapakot Nagarpalika	1815	804	798	798	421	137	12	4	4	0
Galyang Nagarpalika	1294	634	621	621	323	170	101	99	99	0
Harinas Gaunpalika	912	435	405	405	176	83	1	1	1	0
Kaligandagi Gaunpalika	752	493	413	413	156	117	2	2	2	0
Phedikhola Gaunpalika	403	278	264	264	120	86	10	7	7	0
Putalibazar Nagarpalika	2798	1471	1461	1461	751	455	321	306	306	0
Waling Nagarpalika	2696	1671	1617	1617	767	352	54	33	33	0

Graph of Tranche Status:

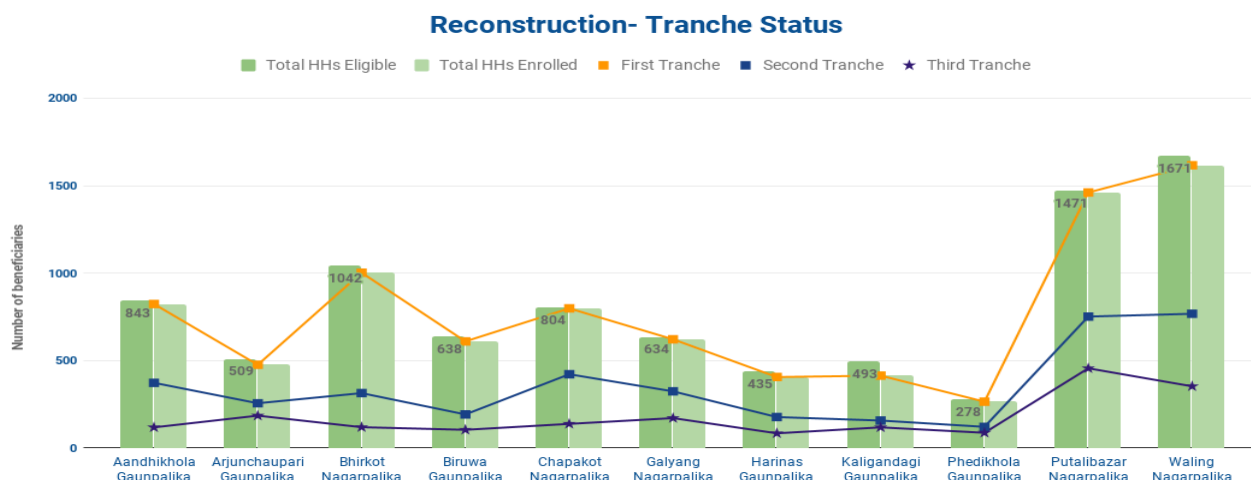

Graph for Retrofitting Status:

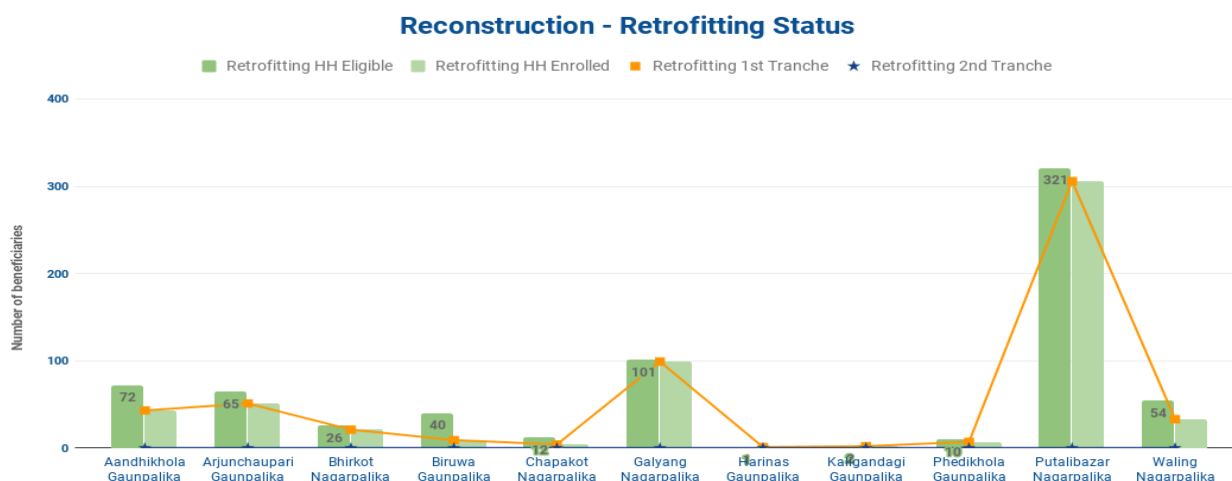

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Will there be any additional top-up for retrofitting beneficiary?	Beneficiaries	There are not any decisions made regarding additional top-up, but it has been a subject of discussion in NRA for now we could only say its not increased.

Challenges and Way Forward

Challenge	Way Forward
Most of the retrofitting beneficiaries wants to get converted to reconstruction.	Awareness and orientation program to the beneficiaries regarding the advantages, and cost parameters of retro.
Lack of masons who can implement the correction process in the district.	Mason training on retrofitting focusing those masons who have already taken training on EQ resilient housing construction.
Lack of technicals in the field for the implementation of retro.	One ward one technical (Engineer) must be implemented and these technicals must be trained on practical implementation of retrofitting.
People are not ready to adopt the concept of strong back as they feel this more costly and tedious.	Other simplified methods such as wire meshing, splint and bandage must be implemented.
