

Monthly District Report

Nuwakot

22 October – 21 November 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Nuwakot	Participate in Retrofitting Task Force		Bidur Nuwakot	Rajendra Chilwal, DSE Nuwakot, rajchi75@gmail.com	Reports
	Field Visit, Belkotgadhi-5&6, Duipipal	13 Nov 2019	Belkotgadhi 5&6, Duipipal	Badri.pyakurel@hrrp.nepal.org	Field Visit Report
	Participate in orientation to use the map of identified vulnerable area of land Slide	19 Nov 2019	Bidur	Biswas Nepali CSRC Nepal biswash@csrcnepal.org	Presentation Slides
	Participate in Meeting with GMALI and UNOPS/Gol	14 Novem ber, 2019	Bidur	Niraj Raut nirajr@unops.org	Meeting Minutes , Photo

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
District Facilitation Meeting	TBD	GMALI Nuwakot	Satyanarayan Chaudhari, satya.isha95@gmail.com

Tranche Status (Nuwakot)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Belkotgadhi Nagarpalika	10719	11037	10523	10523	9627	6491	256	51	51	0
Bidur Nagarpalika	15204	13097	12202	12202	11366	9294	264	116	116	0
Dupcheshwar Gaunpalika	5827	5884	5715	5715	5520	5087	35	1	1	0
Kakani Gaunpalika	6905	6954	6507	6507	5979	4857	175	49	49	0
Kispang Gaunpalika	4637	4788	4635	4635	4257	4071	51	1	1	0
Likhu Gaunpalika	4973	5110	4769	4769	4392	3564	155	18	18	0
Meghang Gaunpalika	4739	4520	4289	4289	4183	4003	151	1	1	0
Panchakanya Gaunpalika	4243	4566	4357	4357	4000	3341	96	19	19	0
Shivapuri Gaunpalika	6292	6524	6264	6264	5600	4745	65	1	1	0
Suryagadhi Gaunpalika	4560	5024	4913	4913	4587	3795	17	4	4	0
Tadi Gaunpalika	4476	4592	4480	4480	4299	3788	23	3	3	0
Tarkeshwar Gaunpalika	4573	4713	4397	4397	4145	3739	254	46	46	0

Graph of Tranche Status:

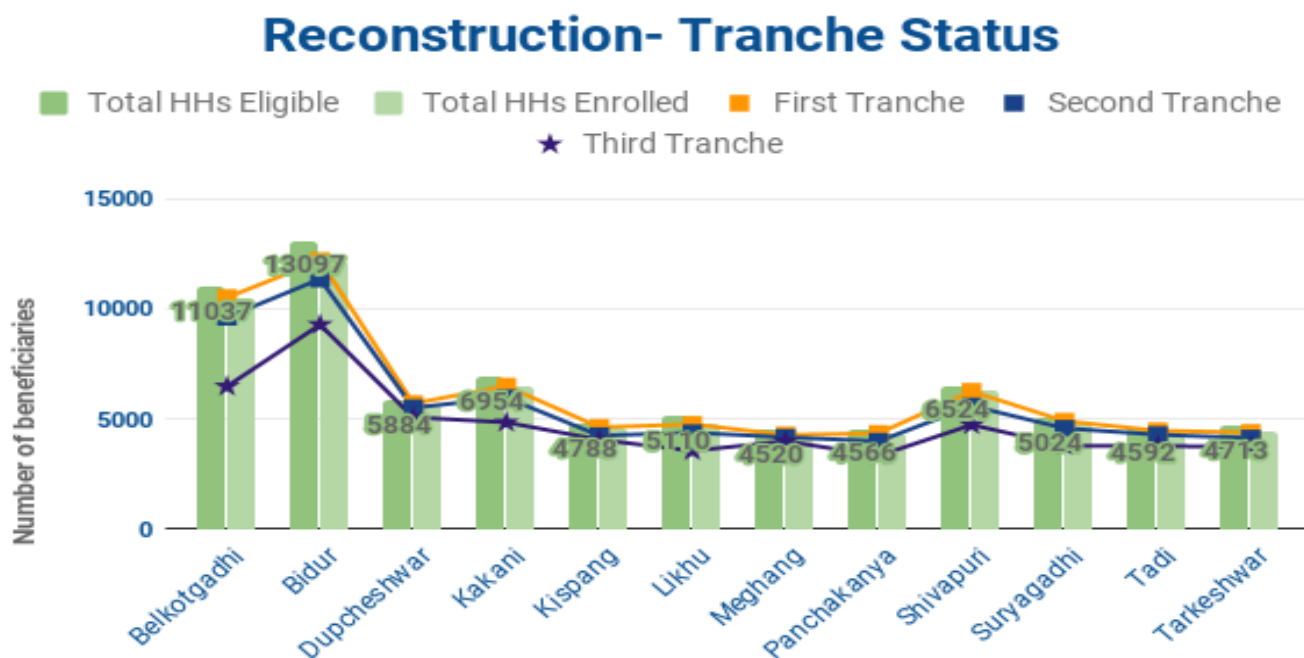

Graph for Retrofitting Status:

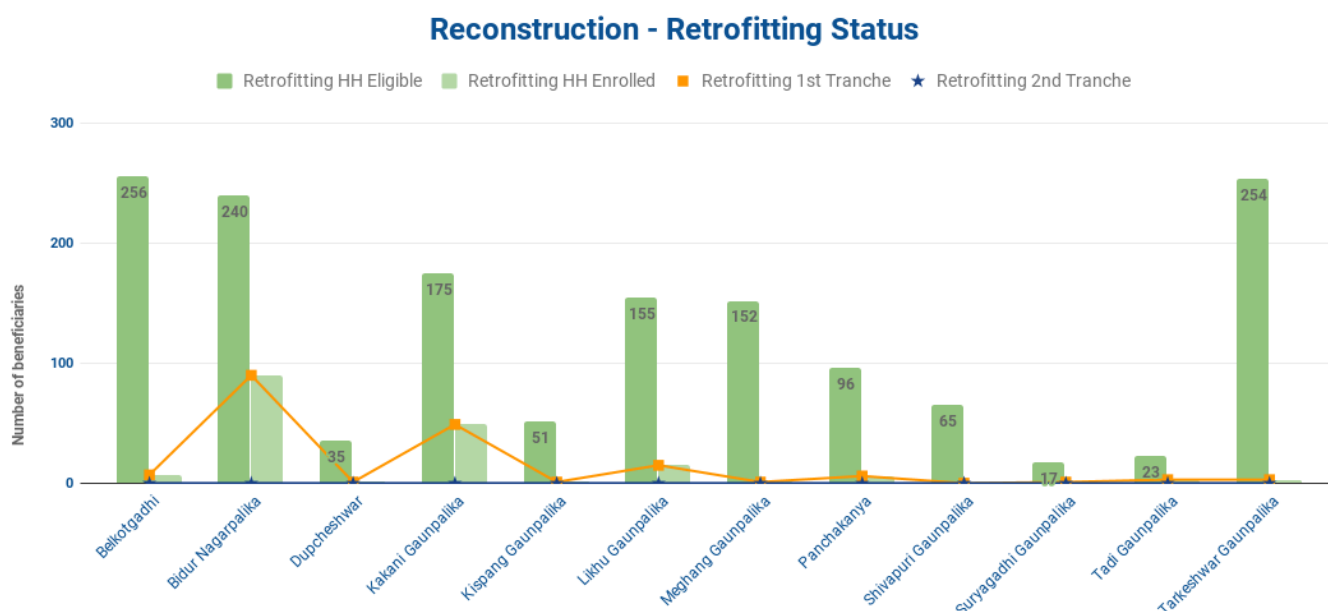

Field Visit Reports (Nuwakot)

Visit 1

Visit 1		
Date	Location	Participants
13 November 2019	Belkotgadhi 5 and 6, Duipipal	Badri Pyakurel DC, Hrrp Nepal Prabhuram Pokharel, M&E DLPIU building Rajendra Chilwal DSE Nuwakot Praksh Baral, DSE Nuwakot Milan Bhandari IM DLPIU Building Nuwakot
Objective(s)	• Joint Monitoring visit to the area. • To follow up the reconstruction and Retrofitting progress • To find out the issue and challenges to mobilize the engineers	
Why was the visit carried out in this location? Priority wise, Write any other reason		
Duipipal is previously a VDC now changed in 3 wards of Belkotgadhi Municipality. This is the ward which has least progress on Reconstruction and retrofitting. It has too less in 3rd tranche progress. There I only one beneficiary of retrofitting in ward no 6, but he is not ready to retrofit the house because he has already removed the house. As per his information his house is completely damaged. As the information of Ward Chair Ambika Tamang. It has		

146 resurveyed and re verified beneficiaries. Ward chair and other participant have showed sincere concern on its address during the meeting. Rajendra Chilwal has given emphasis on retrofitting progrees to local engineer Binod Tamang. He has confirmed his task of the month.

In ward on 5, There are 19 Retrofitting issues who are interested to be reconstruction beneficiary. Ward engineer Shaisab Mishra claimed that most beneficiaries are not convinced for the retrofitting. There are some houses not to be able to retrofit. 9 houses are started to retrofit through technical and financial support of Build change. One model house of retrofitting is being completed in the ward. After seeing the house beneficiary would convince to retrofit.

'If this municipality / ward was visited previously, what were the previous issues (specific ones) and specify the existing issues in the area.

Previous Issues	Current Issues Most of the houses are completed but some houses are not in progress after the DPC. Engineer claims the fake beneficiaries.
------------------------	--

Summary

Field Visit:

- No. of HHs visited: **10**
- No. of meetings/interaction with engineers: **2 (in ward no 6 Binod Tamang and in ward no 5 Shaisab Mishra)**
- No. of engineers interacted with: **3**
- No. of meetings/interaction with local officials: **1**
- No. of local officials interacted with: **1**

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

Challenges / Issues Identified	Solutions Provided or Possible Solutions	Decision Taken	Responsible	Timeframe (specify the time taken to decide on the issues identified)
Engineer are not regular in ward no 5, Duipipal	Regular meeting with engineers to visit beneficiaries.	Call with ward chair and engineer	Ward Chair and Engineer	As soon as possible
Not Progress in retrofitting	Meet the beneficiaries individual level	To call a meeting in ward office with beneficiaries	Ward Chair and Engineer	Regular
More Old DPCs	To follow up with beneficiaries	To visit with beneficiaries	Engineers	Regular

Retrofitting (Please write specific issues, challenges, best practices related to Retrofitting)

Most of the houses are made of stone mud masonry. Due to lack of proper information they deny for the retrofitting. Now there is started retrofitting with technical support by UKAID/ Build change. Ward chair has showed his hope on rapid progress on retrofitting.

Urban Reconstruction (Please write specific issues, challenges, best practices related to Urban Reconstruction)

Belkotgadhi is new Municipality of Nuwakot but majority of settlements are in rural. So can category it as rural area. In Nuwakot Urban Settlement more houses are not destroyed but they are NRA Beneficiaries. So they make one room or not taken 2nd tranche. We can see more RCC in Urban Settlement, rarely mud stone and other typology.

Vulnerable (Please write specific issues, challenges, best practices related to Vulnerable in Reconstruction)

7 integrated settlements have constructed for vulnerable people who are relocated from different places through the support of OXFAM. Vulnerable category is another issue, the main issue is identifying and another is distribution of vulnerable support. We can rarely see the beneficiary who are waiting to reconstruct. Remaining construction can find more on different issues. No one has supported vulnerable in official way in Nuwakot.

Photos




Ward meeting: Belkotgadhi Municipality ward no 6, ward chair Ambika Tamang




Old DPC: We can find much old DPC in this ward. Beneficiary Govinda Nepal has lived in Kathmandu has made this around two years. Due the absence of owner not more information regarding the construction.



Black Village: These all are the reconstruction beneficiary but staying in same house before the Earthquake in Belkotgadhi-6, Duipipal Dabali.

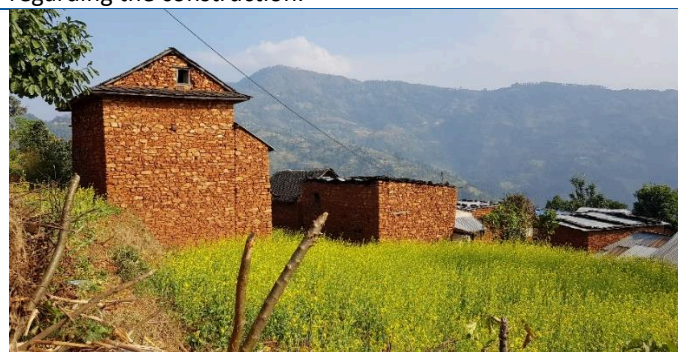

Traditional building: People seems not to worry for the disaster, staying on same unsafe building.

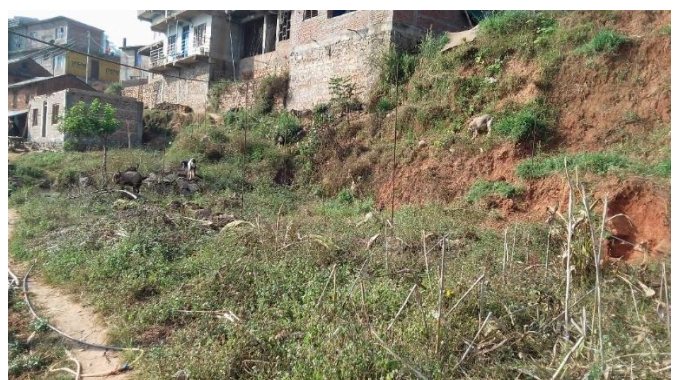

Old DPC: very hard to find DPC, Name: Ram Bdr Shrestha. 2nd tranche received, no recent plan to complete.



Retrofitting Beneficiary: Owner is not ready for retrofitting. Technically can be, socially Our team has not satisfied response to him.

Housing Typology Report (Max 4 Photos, Select best photos from each district)



Caption: **Krishna Lamichhane, Belkotgadhi Municipality, Has Received 3rd tranche Hybrid Structure**



Caption: **Akkal Tamang, Myaghang RM, Has received 3rd tranche BMC**



Caption: **Rambau Payakurel, Bidur-11, has recived 3rd tranche**



Caption: **Krishna Sapkota, Myaghang-6, Samari has received 3rd tranche, BMC**
