

# Fortnightly District Report

## Nuwakot

18 – 31 January 2019

| Summary of events during this period                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                   |                      |        |                                                                        |                                |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|----------------------|--------|------------------------------------------------------------------------|--------------------------------|
| Name of activity/event                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | Event date        | Participants summary |        | Contact Person                                                         | Reference Document             |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |                   | Male                 | Female |                                                                        |                                |
| <p>Coordination Meeting with UNOPS and GMALI.</p> <ul style="list-style-type: none"> <li>- UNOPS has been working for socio technical assistance for 23088 beneficiaries from different 19 VDCs of Nuwakot district. It has support through 20 information center. There is some more issue on non-compliances. The meeting has made common understanding share recent progress to GMALI, regular reporting and GMALI will share the tranche update to UNOPS field office.</li> <li>- There are arose some lack of coordination issue to local government and GMALI as well. Reporting to Embassy of India should be in regular level which will simplify to reimburse the tranche as soon as possible. Due to lack of reimbursement, most of the tranche from GMALI is going to stop for Nuwakot District. UNOPS will coordinate for reimbursement process as per the recent situation.</li> </ul> | 18 January , 2019 | 9                    | 2      | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a> | <a href="#">Meeting Minute</a> |
| <p>Participate in Palika level orientation and district level coordination committee meeting in Rasuwa.</p> <ul style="list-style-type: none"> <li>–5 Palikas have presented in orientation</li> <li>–coordination committee meeting and MOU signing program Completed. 5 Palika have signed the MoU of reconstruction.</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | 21 January , 2019 |                      |        | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a> |                                |

### Summary of events during this period

|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                            |                   |    |   |                                                                                                                                                  |                                          |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|----|---|--------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------|
| Field visit and ward level meeting in Bidur-12, Charghare                                                                                                                                                                                                                                                                                                                                                                                                                                  | 29 January , 2019 | 5  | 1 | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a><br><a href="mailto:im.nuwakot@hrrpnepal.org">im.nuwakot@hrrpnepal.org</a> | <i>See Detail in field visit Section</i> |
| District Level Facilitation committee meeting. The meeting has focused on 2 agendas: -Complain against bank will visit and discuss upon issues to solve. –annex 14 and its approval from ward chair not from Palika chief.                                                                                                                                                                                                                                                                 | 28 January 2019   |    |   | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a>                                                                           | Meeting Minute                           |
| Communicating and working with POS for 5W and training database update                                                                                                                                                                                                                                                                                                                                                                                                                     | 28 January 2019   |    |   |                                                                                                                                                  |                                          |
| Updated 5W on 28 Jan (EOI data for the first time update, NSET data updated)                                                                                                                                                                                                                                                                                                                                                                                                               | 28 January 2019   |    |   | <a href="mailto:im.nuwakot@hrrpnepal.org">im.nuwakot@hrrpnepal.org</a>                                                                           |                                          |
| Preparation of INFO pack and presentation for coordination meeting                                                                                                                                                                                                                                                                                                                                                                                                                         | 29 January 2019   |    |   | <a href="mailto:im.nuwakot@hrrpnepal.org">im.nuwakot@hrrpnepal.org</a>                                                                           |                                          |
| District Coordination Meeting,<br>- Oxfam has been constructing house and support to livelihood, wash to 200 hh of relocating family from Rasuwa and Nuwakot District.<br>- Nuwakot has 381 for relocation beneficiaries from geohazard survey. Among them 207 have received land. 60 have already constructed 82 have their safe land to construct and 6 has constructed.<br>- Purnima Project is working in three Palika, Shivapuri, Tadi and Dupcheswar in different Four working Area. | 30 January, 2019  | 12 | 3 | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a><br><a href="mailto:im.nuwakot@hrrpnepal.org">im.nuwakot@hrrpnepal.org</a> | Meeting Minutes                          |
| Distributing INFO pack (Booklet and Maps) to concerned stakeholders                                                                                                                                                                                                                                                                                                                                                                                                                        | 31 January 2018   |    |   | <a href="mailto:dc.nuwakot@hrrpnepal.org">dc.nuwakot@hrrpnepal.org</a><br><a href="mailto:im.nuwakot@hrrpnepal.org">im.nuwakot@hrrpnepal.org</a> |                                          |

### Upcoming Events & Meetings


| Name of activity/event | Date, Time, and Location | Organizer | Contact Person |
|------------------------|--------------------------|-----------|----------------|
|                        |                          |           |                |

| Tranche Status             |                |          |                |           |            |          |            |               |              |               |         |                |
|----------------------------|----------------|----------|----------------|-----------|------------|----------|------------|---------------|--------------|---------------|---------|----------------|
| Rural /Municipality        | Belkotgadhi NP | Bidur NP | Dupcheshwor RM | Kakani RM | Kispang RM | Likhu RM | Meghang RM | Panchkanya RM | Shivapuri RM | Suryagadhi RM | Tadi RM | Tarkeshwaor Rm |
| Total HHs Surveyed         | 9409           | 11203    | 5448           | 6157      | 1816       | 4003     | 4052       | 3692          | 5616         | 4197          | 4231    | 3760           |
| Total HHs Eligible         | 11036          | 12667    | 5873           | 6916      | 2369       | 5107     | 4500       | 4226          | 6513         | 5019          | 4604    | 4353           |
| Total HHs Enrolled         | 10326          | 11886    | 5639           | 6309      | 4267       | 4479     | 4244       | 4036          | 6008         | 4604          | 4450    | 4217           |
| First Tranche              | 10326          | 11886    | 5639           | 6309      | 4267       | 4479     | 4244       | 4036          | 6008         | 4604          | 4450    | 4217           |
| Second Tranche             | 8667           | 10223    | 5227           | 5451      | 3823       | 3686     | 3871       | 3653          | 5044         | 4097          | 4019    | 3718           |
| Third Tranche              | 1713           | 5606     | 3593           | 3020      | 2554       | 2328     | 3040       | 2178          | 3063         | 2008          | 2630    | 2818           |
| Total HH Constructed       |                |          |                |           |            |          |            |               |              |               |         |                |
| Grievance Registered       | 2271           | 1693     | 425            | 1389      | 809        | 1329     | 511        | 910           | 995          | 923           | 701     | 672            |
| Grievance Addressed        | 1627           | 1464     | 425            | 759       | 553        | 1104     | 448        | 534           | 897          | 822           | 373     | 593            |
| RF HH Eligible             | 256            | 236      | 35             | 160       | 25         | 154      | 141        | 88            | 63           | 16            | 23      | 247            |
| RF HH Enrolled             |                | 18       | 1              | 44        |            | 9        |            | 18            | 1            | 44            |         | 9              |
| RF 1 <sup>st</sup> Tranche |                | 18       | 1              | 44        |            | 9        |            | 18            | 1            | 44            |         | 9              |

as of 29<sup>th</sup> Jan 2019.


Source : GMALI Nuwakot

Graph of Tranche Status:

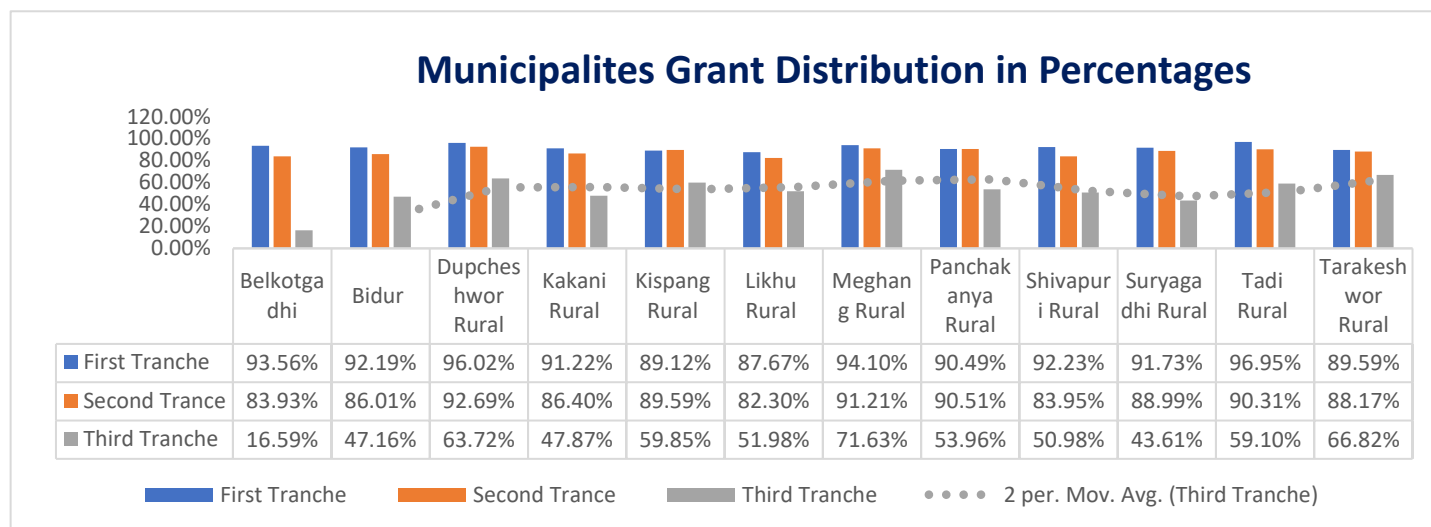

Graph for Retrofitting Status:

Graph for Grievance Status:

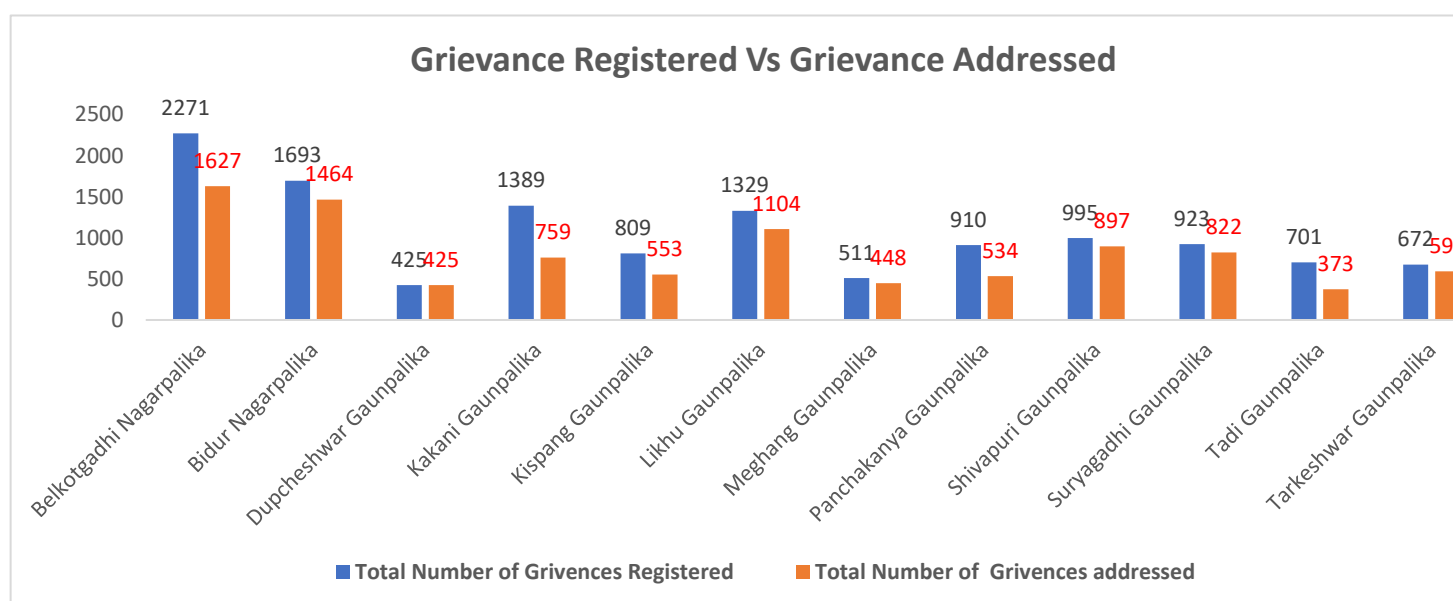


## Field Visit /Joint Field Monitoring Visit Reports

| Visit 1                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |                                            |                                                                                                                                                                                                                    |           |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------|
| Date                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          | Location                                   | Participants from HRRP and stakeholders                                                                                                                                                                            |           |
| 29 Jan, 2019                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Bidur-12<br>Charghare                      | <ul style="list-style-type: none"><li>• Badri Pyakurel, DC HRRP</li><li>• Pravuram Pokharel, DLPIU M&amp;E Expert</li><li>• Buddhasing Thakuri, HRRP</li></ul>                                                     |           |
| Objective(s)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |                                            |                                                                                                                                                                                                                    |           |
| <ul style="list-style-type: none"><li>• Objective 1: Joint Monitoring to assist on technical problem identification and Solution</li><li>• Objective 2: To know the reconstruction trend and highlighting the issues related to grant</li><li>• Objective 3: To understand the field challenges and best practice</li></ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |                                            |                                                                                                                                                                                                                    |           |
| Summary                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |                                            |                                                                                                                                                                                                                    |           |
| Charghare is now on Bidur Municipality. All wards except 1 and 2 are fallen under Bidur Municipality ward no 12. It has 1004 beneficiaries. Among them 966 has received first tranche, 918 2 <sup>nd</sup> tranche and 436 have received 3 <sup>rd</sup> tranche. There are not so many issue on reconstruction though some noncompliance issues are found in semi urban area and most of the housing typology are found stone mud mortar (SMM) and RCC frame structure can be found in lower part of the ward and some road head areas. Most of the hilly settlement has used mud mortar construction. Some of them have used brick and cement in hilly area as well. As per the saying from ward chair, Sitarama Aryal, during the ward level meeting they claimed that they have bothered from grievances. The ward has registered 68 beneficiaries but all are not settled till the date. |                                            |                                                                                                                                                                                                                    |           |
| Challenges / Issues Identified                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | Action Required                            | Responsible                                                                                                                                                                                                        | Timeframe |
| Transportation of reconstruction Materials                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | promote to use locally available materials | POs, Ward offices                                                                                                                                                                                                  | Regular   |
| Quality of reconstruction materials                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | Quality assurance to local supplier        | DCC, Rural Municipality                                                                                                                                                                                            | Regular   |
| Social Issues                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 |                                            |                                                                                                                                                                                                                    |           |
| Technical Issues on retrofitting, Vulnerable groups support                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |                                            |                                                                                                                                                                                                                    |           |
| Photos                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |                                            |                                                                                                                                                                                                                    |           |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             |                                            |                                                                                                                                |           |
| Ward level meeting was held in chairmanship with Ward chair, Sitaram Aryal. Ward secretary Ramhari Acharya, DLPIU engineer Manisha Shakya and other officials were presented in the meeting.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |                                            | Observation and suggestion during the field visit: House owner Chandra Prasad Dawadi is constructing noncompliance regarding the size, typology and construction materials. The team has suggested for correction. |           |



## Housing Typology Report

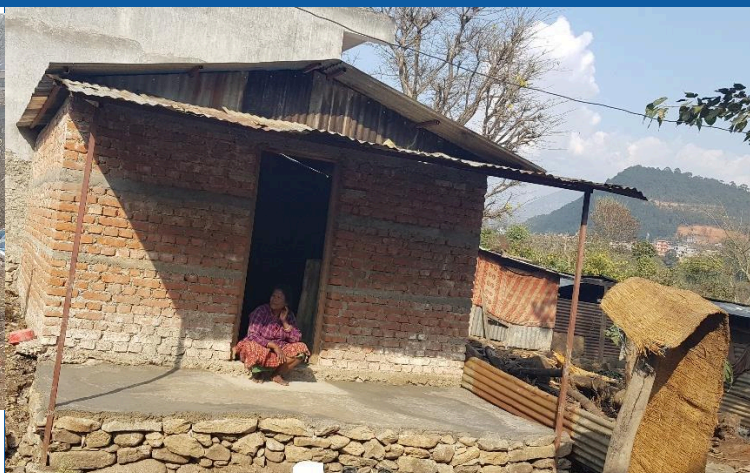

House Owner: Purna Bdr Rai (Vulnerable)  
Location: Bidur-12, Charghare  
Tranche Status: 2nd tranche received  
Typology: BMC  
The construction was supported by UNOPS,  
*Photo: Badri Pyakurel*

House Owner: Junkiri Rai  
Location: Bidur-12, Charghare  
Tranche Status: 2nd tranche received (waiting for 3<sup>rd</sup> tranche for further construction)  
Typology: BMC  
*Photo: Badri Pyakurel*



House Owner: Krishna Bdr. Rai  
Location: Bidur-12, Charghare  
Tranche Status: 3<sup>rd</sup> tranche received  
Typology: BMC  
*Photo: Badri Pyakurel*

House Owner: Thulokanchha Rai  
Location: Bidur-12, Charghare  
Tranche Status: 2nd tranche received (waiting for 3<sup>rd</sup> tranche for further construction)  
Typology: BMC  
*Photo: Badri Pyakurel*

## Challenges and Way Forward

| Challenge                                                                                                                                                                                                    | Way Forward                                                                                                      |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------|
| <b>Lack of technical assistance in the hard to reach field area.</b> NRA engineers are not in regular monitoring to the house. When they visited for the inspection, they only commented for non-compliance. | MOUD-DLPIU should monitor the engineer and instruction for regular visit.                                        |
| <b>Delayed and partial addressing of grievance.</b> Real victim from the earthquake has not addressed as                                                                                                     | NRAs should address as soon as possible by the help of local elected persons, Like ward chair and other members. |

## Challenges and Way Forward

|                                                                                                                                    |                                                                                                                         |
|------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------|
| beneficiaries. They have applied for grievance many times but not addressed.                                                       |                                                                                                                         |
| <b>When will retrofit start?</b> People don't have trained manpower for the retrofit, they are waiting the response from NRA side. | Training and other technical issue with proper communication to the common people should be done before monsoon starts. |
