



**Practical
ACTION**



Housing Recovery and
Reconstruction Platform

A Sharing Session on

Cost Benefit Analysis (CBA) research findings on Vulnerable HHs housing reconstruction support, as part of LNOB Project

10th August 2021

Live Webinar

Cost Benefit Analysis (CBA) research findings on vulnerable HHs housing reconstruction support, as part of LNOB Project

A research was carried out on cost-benefit analysis (CBA) of the shelter works performed within the UK Aid funded 'Leave No One Behind' (LNOB) project, implemented by People in Need (PIN) and Practical Action (PA) in nine Rural Municipalities of four earthquake affected districts i.e., Chitwan, Dhading, Makwanpur and Lamjung. The research has compared the two shelter models implemented by PIN (PIN model) and PA (PA model) to reconstruct the house damaged by 2015 earthquake adopting Value for Money (VfM) and CBA framework.

This virtual partner sharing session has been planned with the objective to share the research findings of the LNOB CBA research/analysis carried out by a Research Consultant on the two shelter models to support shelter construction of vulnerable HHs and provide an opportunity for cross-exchange of lessons learned from the PO's experience. The findings of this research could be useful to scale up housing reconstruction of vulnerable HHs as per the "LNOB principle in the reconstruction process."

Agenda:

10:00 - 10:05	Welcome and Introduction
10:05 - 10:15	Introduction to two models and contextual background by FCDO
10:15 - 10:25	Presentation on shelter model by PIN
10:25 - 10:35	Presentation on shelter model by PA
10:35 - 11:05	LNOB CBA Analysis research findings sharing
11:05 - 11:20	Q & A session
11:20 - 11:30	Remarks from Guests (NDRRMA, NRA, FCDO) & vote of thanks

Presenters:

- Mr. Rajesh Rai, Consortium Manager, People in Need (PIN)
- Mr. Bhim K. Shrestha, ME&L Manager, Practical Action (PA)
- Dr. Narhari Dhakal, Research Consultant, CBA research, LNOB project

Guest Speakers:

- Dr. Chandra Bahadur Shrestha, NRA Executive Member (NRA)
- Ms. Radha Verma, Senior Programme/Policy Manager (FCDO)
- Ms. Reena Chaudhary, Focal Person for Vulnerable Support (NDRRMA)

Facilitated by:

HRRP is funded by CRS and UKaid

Organizers:

UKaid

PEOPLE IN NEED

Practical ACTION

VSWG
Vulnerable Support
Working Group

10 August 2021
START 10 AM NST

Register here
<https://forms.gle/kqVbaAnKcqvA8qQZ7>

PRESENTERS

- Mr. **Rajesh Rai**, Consortium Manager, People in Need (PIN)
- Mr. **Achyut Luitel**, Regional Director, Practical Action
- Dr. **Narahari Dhakal**, Research Consultant, CBA Research, LNOB project

PANEL MEMBERS

- Dr. **Chandra Bahadur Shrestha**, NRA, Executive Committee Member
- Ms. **Radha Verma**, Senior Programme/Policy Manager, FCDO
- Ms. **Reena Chaudhary**, Focal Point, Vulnerable support, NDRRMA

FACILITATOR

- Mr. **Ruplal Aidi**, VSWG Focal Point & HRRP Team Lead-General Coordination

*Link to complete webinar recording [here](#).

COST BENEFIT ANALYSIS (CBA) RESEARCH FINDINGS ON VULNERABLE HHs HOUSING RECONSTRUCTION SUPPORT, AS PART OF LNOB PROJECT

*Subscribe to HRRP [here](#).

BACKGROUND

Introduction

A research was carried out on cost-benefit analysis (CBA) of the shelter works performed within the UK Aid funded 'Leave No One Behind' (LNOB) project, implemented by People in Need (PIN) and Practical Action (PA) in nine Rural Municipalities of four earthquake affected districts i.e., Chitwan, Dhading, Makwanpur and Lamjung. The research has compared the two shelter models implemented by PIN (PIN model) and PA (PA model) to reconstruct the house damaged by 2015 earthquake adopting Value for Money (VfM) and CBA framework.

This virtual partner sharing session was thus planned with the objective to share the research findings of the LNOB CBA research/analysis carried out by a Research Consultant on the two shelter models to support shelter construction of vulnerable HHs and provide an opportunity for cross-exchange of lessons learned from the PO's experience. The findings of this research could be useful to scale up housing reconstruction of vulnerable HHs as per the LNOB principle in the reconstruction process.

At this juncture, Housing Recovery and Reconstruction Platform (HRRP) – Nepal jointly with Practical Action, People in Need, Vulnerable Support Working Group (VSWG) with UKaid support, organized this sharing session to share the findings of the CBA research on the support to vulnerable housings reconstruction. The program was organized virtually on 10th August 2021 through zoom platform.

Objectives

The virtual partner sharing session had following objectives:

1. To share the research findings of the LNOB CBA research/analysis carried out by consultants on the two vulnerable housing shelter models to support vulnerable HH reconstruction.
2. To provide an opportunity for cross-exchange of lessons learned from the PO's experience directly from the field on the shelter model and broader vulnerable HH support issues.

Presenters and Panel Members

Presenters:

- Mr. Rajesh Rai, Consortium Manager, People in Need (PIN)

- Mr. Achyut Luitel, Regional Director, Practical Action
- Dr. Narahari Dhakal, Research Consultant, CBA Research, LNOB project

Panel Members:

- Dr. Chandra Bahadur Shrestha, NRA, Executive Committee Member
- Ms. Radha Verma, Senior Programme/Policy Manager, FCDO
- Ms Reena Chaudhary, Focal Point, Vulnerable support, NDRRMA

Facilitator:

- Mr. Ruplal Aidi, VSWG Focal Point & HRRP Team Lead-General Coordination

ZOOM WEBINAR SESSION/INTERACTION MEETING**Welcome and Opening Session/Introduction to the Webinar**

The webinar was organized through the online zoom platform given the prevailing second wave COVID-19 pandemic situation and the ongoing prohibitory order (lockdown) by the Government to curb the COVID transmission.

Mr. Ruplal Aidi, VSWG Focal Point & HRRP Team Lead-General Coordination, facilitated the whole webinar meeting by welcoming all the participants, presenters and panel members and informed of the ground rules and clarified the objectives of the sharing session. Mr. Aidi introduced the panel members and the key presenters followed by the introduction/background and presentation from the presenters.

Introduction to two models and contextual background by FCDO**Ms. Radha Verma-Senior Program/Policy Manager, FCDO**

Ms. Verma provided the contextual background to the CBA research highlighting that it was important to acknowledge how we got to where we got to ? and why we wanted to make this event more than a dissemination event. She shared that there was a lot of learning in the past 3-4 years on housing and reconstruction. It has a lot of relevance to where we want to take the housing related responses in the future and how we will approach it.

She then went on to provide some brief background to the LNOB project as a whole, including that around 2016-2017- FCDO initiated quite a few small but niche housing related interventions working closely with NRA in particular and also DUDBC.

The NRA came up with an explicit and equity-based model of conditional housing grants for

people to rebuild their houses. We then quickly realized there was a risk that there would be a certain population that would be left behind. Left behind for multiple reasons- economic reasons or criteria's related etc. such as single women, landless. We very quickly ramped up to work out a few housing reconstruction responses and for that we spread ourselves across 4 districts and a few palikas (details will be shared by colleagues), she shared.

Ms. Verma then said that the whole idea was to find out two different approaches and which approach works best in the long run for best value for money. She added that there was a twofold agenda: building safe resilient buildings made for the beneficiary or groups of people we chose to work with; but also, at a more value for money level, to make sure along with building resilient houses, what is the most cost-effective way to reach a certain group of people. She then touched briefly on the two models (which will be detailed in the presentations), one of which was working closely with the markets, respecting the overarching objective of the NRA's owner-driven reconstruction and the overall driving force as owner-driver reconstruction was a big initiative of NRA and GoN as a whole, when the housing reconstruction took off. We had the owner-drive approach, yet a strong sort of private factor supported the overall housing reconstruction and from this we have good lessons learned, she said.

She then said that from this sharing session, the hope is that some of this could be useful as we think of future responses. We can look at these two models so in the future when there are disasters, we can help the government machinery up and running quickly, she summed up.

Presentation by Speakers

Presentation By: Mr. Rajesh Rai, Project Manager, People in Need (PIN)

Key Highlights: Presentation on shelter model by PIN

Mr. Rai shared brief project overview and key highlights from the Project which is named as – *Hamro Ghar - Leave No One Behind (LNOB) Housing Project*. The project commenced from 28 June 2018 – 30 Sept. 2020 funded by UKaid with PIN, PHASE Nepal and Scott Wilson Nepal (SWN) as Consortium partners. So, almost a year since the project was closed. The project successfully managed to support 1603 households (to the total 1600 targeted ,with additions of 3 HH) through resilient shelter reconstruction. The project was implemented in three districts (Chitwan, Dhading and Makwanpur) stretched over five palikas (Icchakamana, Rapti in Chitwan; Jwalamukhi, Siddhalekh in Dhading; and Manahari in Makwanpur district). Mr Rai then went to on to share the following in his presentation:

Adopted project modality of LNOB

1. Community- led initiative - alo palo system (centuries old system of self help support from community) was revitalised in order to bring efficiency in construction.
2. Hand holding approach for Tier 5/most vulnerable households, beneficiaries.
3. Use of revolving fund and use of alternate construction materials i.e. CSEB to support Tier 5/Most Vulnerable.

Project Beneficiaries

The PIN model of the LNOB Project adopted a Tier approach based on physical, socio-economic conditions and access to services.

Tier Type	Physical ability	Socio-Economic Condition	Access to services
Tier 3	has physical ability to build and can afford unskilled labor	• has regular source of income and can purchase construction materials and skilled labor • may have access to technical support but cannot pay for the services	• resides rural to semi urban settings • has access to some basic services
Tier 4	has physical ability to build but cannot afford unskilled labor	• has intermittent source of income and partly purchase construction materials and skilled labor • lacks access to technical support and cannot pay for the services	• resides in rural setting • has limited access basic services
Tier 5	does not have capacity to build and cannot afford unskilled labor	• has no source of income and cannot purchase construction materials and skilled labor • lacks access to technical support and cannot pay for the services	• resides in rural setting • has very limited or no access to basic services

PIN Model emphasized Tier 5 approach to achieve efficiency in providing the technical support to most vulnerable beneficiaries who don't have any support system to build their houses as well as those who cannot afford unskilled labour too.

Project Support

Under project support, Mr. Rai said technical support was provided to Tier 5 (i.e., most vulnerable) beneficiaries to achieve their housing goals. Technical support were laid in terms of:

Technical support

- Access to engineers, site managers and masons – technical supervision of construction sites, preparation of design drawings and BoQs, provision of skilled masons
- Access to social mobilizers – assistance with tranche application, facilitation with local authorities

Material support and remoteness subsidy

Construction materials worth Rs 50,000/- was provided to Tier 5/most vulnerable beneficiaries. Access to transport vehicles for transportation of construction materials from source to sites for beneficiaries residing in remote areas-which was very welcomed by beneficiaries.

Beneficiaries supported

In terms of total beneficiaries supported, Mr. Rai shared:

Household type	Total household supported
Tier 5/Most Vulnerable	300
Tier 4/Less Vulnerable	503
Tier 3	800
Total	1603

PPT Presentation by: Mr. Achyut Luitel, Regional Director, Practical Action

Key Highlights: Presentation on shelter model by PA

LNOB Project- Updates and Learnings

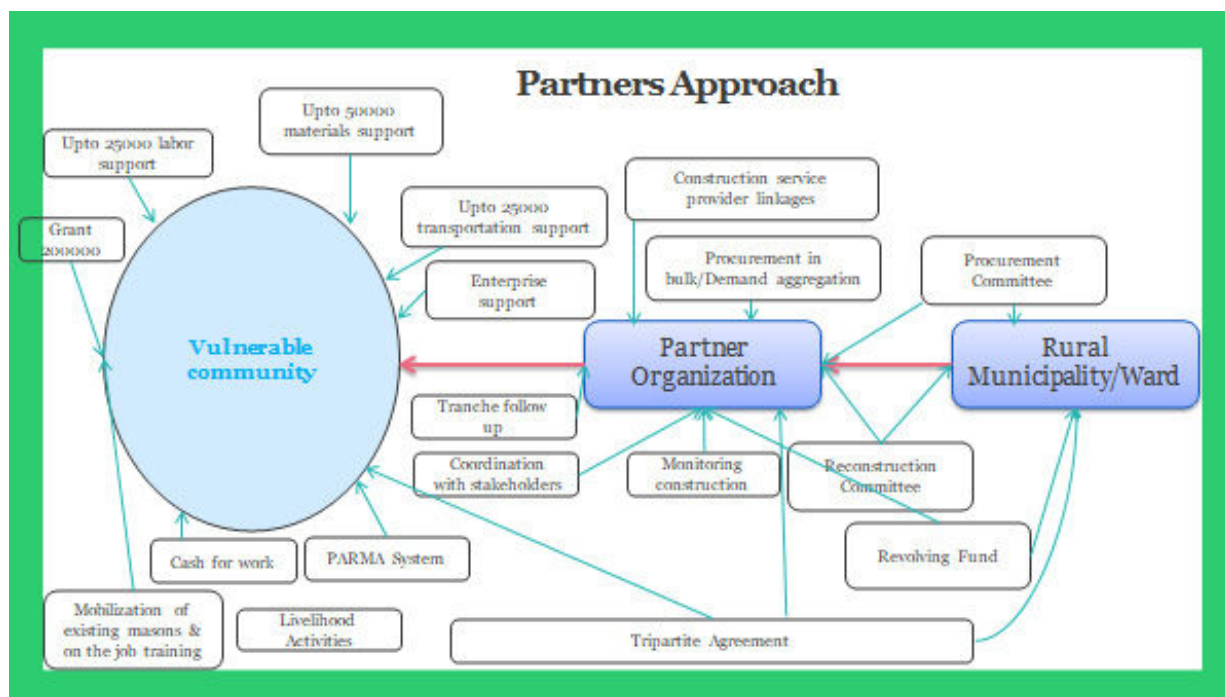
Mr. Luitel introduced the PA model and shared its objectives including of LNOB. The project/ model was implemented with joint consortium partners as: Practical Action, Action Aid and CORD. The LNOB project had two local implementing partner NGOs in two districts (Lamjung and Makwanpur) where it was implemented for a duration of 28 months (3 July 2019- 31 Dec 2020), covering the two districts and its palikas respectively: Lamjung (Dordi and Rainash) and Makwanpur (Thaha and Kailash). The project's budget was around 1.3 Million pound sterling. The outcomes achieved were 484 most vulnerable HHs (out of 560) have built earthquake resilient houses; and 819 marginalised HHs (out of 957) have built earthquake resilient houses, respectively, in the project areas/palikas.

Key Outputs

- 86% HHs fully completed with toilets
- 172 HHs under construction (up to roof and DPC) have been linked with contractors and service providers
- 42 HHs(death, migration, no land, retrofitting, financial) will not be able to construct (including 26 HHs that have not started)
- 1491 household(547 vulnerable-257 single women and 75 people living with disability households-and 944 marginalized) were directly supported

Key Enterprise Updates

- 6 CSEB, 2 Timber treatment and 2 CSEB MW enterprises have been registered with CSIO and Company Registrar
- 12 CSEB enterprises have been granted affiliation letter from respective municipalities
- 10 stone cutting machines handed over to respective entrepreneurs
- 5 mini aggregate crusher handed over to municipalities

Partners Approach

A partnership model of several committees such as procurement, reconstruction committees etc were connected with beneficiaries in order to efficiently smoothen out the shelter rebuilding processes and impart know-how to beneficiaries at community level. Implementing partners remained on regular interface with the beneficiaries for the communication process.

Presentation by Research Consultant of CBA research, LNOB Project

PPT Presentation by : Dr. Narahari Dhakal, Research Consultant, CBA Research, LNOB.

Key Highlights: LNOB CBA Analysis research findings sharing

Dr. Dhakal shared the background, objective, scope and assessment methodology of the study. This thorough research study was conducted on LNOB Project commenced by a joint consortium of partners including PIN, PA Practical Action, Action Nepal and CORD.

The objective/of the research study was to:

- Conduct a thorough Cost benefit analysis (CBA) of different shelter models used in LNOB Project
- Assess the cost effectiveness of the different approaches, or aspects of the approaches of shelter models.

The scope of the research study revolves around:

- Explore shelter models in terms of for example, overall cost effectiveness: of the intervention and its impact on poverty reduction, among others.
- Draw holistic conclusions based on qualitative and quantitative assessments.
- Conduct quantitative analysis
- Value for Money (VfM) analysis of the shelter models on 4 Es aspects (Economy, Efficiency, Effectiveness, Equity)
- CBA of the LNOB model

The research study adopted the assessment methodology of assessing primary information (such as field survey, HH visit, KII, FGDs, system & process review, information processing) along with the secondary information (such as review of literature, review of project documents, implementation manuals, information processing). Both levels of information were analyzed, interpreted and reports were prepared .

Dr. Dhakal also briefly shared in the presentation the system map of shelter ecosystem, Shelter Market value chain, as well as the results and discussion with economic analysis; efficiency analysis, effectiveness analysis, equity analysis. He also shared shelter cost and benefit for the HHs as well as shelter cost and benefits as considered from CBA approach among other details (as in the attached PPT).

LNOB Model Strategies



On the basis of documents reviewed, information collected from the field and based on the analytical results and reportings, following recommendations were suggested by the research study -

1. Replication of LNOB Shelter Model
2. Invest on market system and promote private sector participation
3. Revise flat/inform subsidy mechanism
4. Consider replicating key features of the project
5. Strengthen the shelter eco-system

REMARKS FROM PANEL MEMBERS

Ms Reena Chaudhary, Focal Point, Environment Inspector, GESI and Vulnerable, NDRRMA

Ms. Chaudhary said that NDRRMA has started to conduct risk assessment from household level and to identify and visualize the vulnerable groups such as children, single women, old-aged people at risk and many more through geo information systems. The compiled information and data will all be uploaded in BIPAD Portal so it's accessible to the public. This is the initial phase of study and NDRRMA is quite hopeful to receive support from several agencies and partners and other stakeholders in conducting risk assessment. In reconstructing the houses, we must consider people with disabilities and senior citizens to ensure that infrastructure is accessible to them or not, so they need to be reached inclusively, she added.

Dr. Chandra Bahadur Shrestha, Executive Committee Member, NRA

In his remarks, Dr. Chandra Shrestha thanked the researcher and the team for the findings of the research and said some key pointers could be extracted from the overall sharing session, presentations and from remarks too. They were -

Research studies have empirical evidence to justify the work done at community level and helpful in formulating future policies. Remarkable outcomes of interventions by consortium organizations (Practical Action and People in Need) has been the indirect cost on technical inputs provided to each household. Since its inception, NRA emphasized an owner-driven approach. In line with this, as motivating grant support, the uniform grant policy model was adopted by taking social and political viewpoints. NRA were not rationalized to adopt discriminatory grant

policies which were pointed out by this research study as recommendations. From a logical point of view to geographical differences, it was extremely difficult to formulate differentiation budgets in reconstruction for NRA. The housing grant and cost of construction for Kathmandu compared to far flung rural villages in Gorkha is obviously different, so from a logical point of view there was no question, but there has to be appreciation of the government's compulsion on taking the decision taken then from a broader perspective. There were a number of limitations of the owner driven approach, most primarily that the NRA were not able to address the interests of vulnerable and marginalized people in reconstruction. Secondly, urban housing reconstruction could not make much progress as numerous structural issues were associated that delayed the process in urban areas.

NRA in its exit plan has made its mark to transfer its learnings and footprints to NDRRMA which is not mandated for private housing reconstruction, which will most probably be implemented by local governments. The NRA still welcomes this discourse of how to support NDRRMA to move ahead in reconstruction. It's quite obvious that as future directions, local bodies will be primarily taking ownership of private housing reconstruction where central level of technical coordination and information sharing coordination will be undertaken by NDRRMA. Therefore, for further replications, local governments should take care of all these types of complexities, whether owner-drive approach was appropriate or if there is need for adjustments or other additional support that needs to be provided to vulnerable HH etc. So relevant complexities should be thoroughly discussed so that the provided recommendations by this research study become relevant to follow. The NRA will leave behind a footprint from experience we have derived. Also, he suggested the selection procedure of targeted vulnerable and marginalized beneficiaries should be systematic, well sampled and should be cautious about whether it meets the sampling requirements. There is a certain level of biasedness at local governments level which cannot be neglected, therefore a concerned federal agency should guide and handle local governments so that their decision becomes useful mainly in terms of tracking the databases of support provided. The replication of the recommended model may not be possible for the government to replicate or implementable from the government's side as it will require more qualifications. One needs to put oneself in the government's shoes.

Dr. Chandra also raised the questions from an equity perspective, as a discussion for e.g. this project/research was carried out in certain HHs in few palika's, whereas the NRA program was implemented in over 800 palikas in the earthquake affected districts. The bigger question this brings to is what does the overall aid architecture look like ?and this question remains unanswered so far ! The donors support some parts, and some people benefit but the

beneficiaries that are not included in the support architecture may feel deprived. Donor-driven NGOs go to support somewhere but those that are not included are deprived. How should we interpret equity from that paradigm?. Overall the research rightly generates a lot of important questions such as this among others, for our response in the future for the government. He stated that this is an important research and thanked the research team.

Ms. Radha Verma, Senior Program/Policy Manager, FCDO

Ms. Verma said that the research study and consortium projects built on two models of reconstruction have given the same results - One makes the houses for individuals through a community engagement model, while the other invests in micro contractors to incentivize them to rebuild for the beneficiaries of the project. The latter model really helped draw down the overall cost of construction giving the same results thus putting emphasis on value for money. The application of two models and discussions on recommendations suggested by research study drive towards some realism of where we land further. With NRA's exiting out with transfer of learning to NDRRMA's coming on board, has paved ways forward for localization of a lot of things.

Two questions is primarily important to highlight:

1. Equity basis of selection of beneficiaries and ii) observing things from private sector angle
 - Nearly 60-70% of caseloads of NRA falls in the criteria commissioned by NRA on vulnerable. There is a likely scenario of local governments making their own criteria and picking the beneficiaries. Hence defining the proper criteria of selecting the targeted beneficiaries solves many hassles and addresses the procedures in reaching out to the people in most need.
 - There is a need for appropriate mapping from the government side involving private sector angles in reconstruction and making a customized approach. Private sector angle model may be appropriate for single hundreds or thousands of beneficiaries, however that cannot address the whole of earthquake affected beneficiaries, nearly eight hundred thousand. Similarly, the recommendations provided by the research might be useful for small numbers so that customized approach can be built on.

Existence of micro-contractors in small town areas to handle small numbers of beneficiaries sounds fruitful in meeting their reconstruction needs. Therefore, regulating them through proper orientations or training could help in burdening the workloads of local governments as well as government technical staff. Taking on micro-contractors' assistance further to include vulnerable such as housing needs of people with disabilities, could reduce the burdens of local governments as well.

ANNEX A: QUESTIONS AND ANSWERS (Q&A)

Q: Was the sample stratified with geography? What were the detailed criteria for each Category? Any consideration on household capacity or investment which might be different in each category (to compare assistance with capacity)

A:

Dr Narahari Dhakal:

The Consortium Partners adopted a blanket approach to work with entire vulnerable and marginalised beneficiaries in the project areas. Random sampling was applied to reach them, in fact, the sample size was not representative therefore verification was done through physical site and door to door visit. One house model, two house model, five house model and vice versa for technology application were adopted and results and conclusions were derived thereafter. Average value addition of the technology in reconstruction was comparatively analysed through a series of verifications and studies.

Mr. Achyut Luitel:

Selection of vulnerable and marginalised households were done according to criteria set by NRA and as per palika's advice. Discrepancies were sorted out by project palikas. Site visits were done for inspection and verification of beneficiaries therefore entire vulnerable beneficiaries were reached throughout the process.

Some project areas being very remote (for example- Dordi RM, Lamjung), inclusive approaches were adopted by generating additional support of Rs 25,000 were managed from consultations with DFID/FCDO in terms of project cost. Targeted households in Dordi RM received additional grants as per eligibility to transport construction materials. Processes such as technical training, enterprise development, training of micro-contractors etc were all done as part of the project to facilitate the reconstruction process.

Mr. Minar Thapa Magar, National Coordinator, HRRP:

Mr. Thapa Magar thanked all the panel members and presenters and the researcher for the sharing of the CBA research findings and the participants for their time to attend the webinar. He stated that it was a very fruitful discussion and research findings to help ensure that no vulnerable households are left behind in the reconstruction process in the context of COVID-19 situation. Moving forward in transition, HRRP needs a collaborative approach together with like minded partner organisations in order to provide support to NDRRMA who will be taking this steering forward in future recovery and reconstruction measures through localisation initiatives. Working together through continuous learning and thorough support

would be effective in finding the optimal solution in housing recovery of disaster affected people.

ANNEX B: PARTICIPATION DETAILS

SN	Name	Affiliation
1	Achyut Luitel	Practical Action
2	Ambika Amatya	HRRP
3	Anand Sapkota	
4	Anjana Guru	
5	Anup Devkota	
6	Asal Kattel	CRS
7	B. Upadhyay	
8	Badri Pyakurel	HRRP
9	Bhubaneswari Parajuli	HRRP
10	Bijay Upadhyay	
11	Bimal Ghimire	
12	Bishan Wagle	HRRP
13	Bishnu	
14	Bishnu Raj Nepal	
15	Chandra B. Shrestha	NRA
16	Deepak Dhungel	
17	Deepak Saud	HRRP
18	Dr. Narahari Dhakal	Consultant
19	Gaurav	
20	Hikmat Adhikari	
21	Hoang Diem	
22	Indra	
23	Ishor Neupane	HRRP
24	Jennifer Gay L. Malda	
25	Kailash Shrestha	CRS
26	Kamala KC	
27	Kausal Bista	HRRP
28	Keshab Shrestha	HRRP
29	Krishna Osti	
30	Mahesh Paudel	
31	Maila E. Quiring	
32	Minar Thapa Magar	HRRP
33	Naresh K. Shrestha	
34	Netai Dey Sarker	
35	Nirmal	
36	PHASE Worldwide	

SN	Name	Affiliation
37	Phuoc Nguyen	
38	Prabin Bajracharya	
39	Prabin Gautam	HRRP
40	Practical Action	
41	Rachana Thapa	
42	Radha Verma	FCDO
43	Rahul Pratap Singh	HRRP
44	Raj Kumar Shrestha	
45	Rajesh Rai	People in Need
46	Raju Pradhan	
47	Ram Bahadur Rawat	
48	Ratan Podder	
49	RD	
50	Reena Chaudhary	NDRRMA
51	Rekha	
52	Rijan Gajurel	HRRP
53	Rudra Suwal	
54	Ruplal Aidi	HRRP
55	Sabina Bhandari	HRRP
56	Sachin Malego	HRRP
57	Sachir Maharjan	
58	Santosh Lama	Mott MacDonald
59	Shalik Ram Ghimire	
60	Shankar Pokhrel	
61	Shuva Sharma	SW Nepal
62	Stephen	
63	Sujan Rai	
64	Sulochana Nepali	WB
65	T. Ghale	
66	Udaya B. Thapa	
67	Udhab Subedi	CRS
68	Ugan Manandhar	
69	Vesh Ram Pokharel	
70	Vishma Basnet	HRRP
71	Yubaraj Bhandari	HRRP

Sharing session organized by:



**Practical
ACTION**



Housing Recovery and
Reconstruction Platform

HRRP is Primarily Funded by: CRS & UKAid
