

Employment Fund: Skills for Reconstruction progress briefing in HRRP



Mr. Ganga B. BK
Cluster Coordinator
30/03/2016

Implementation Modality

- › On- Site Training
- › Instructors – Trainees Ratio (2:10)
- › Result Based Financing
- › Skill test to only 50% of graduates
- › L2 and L3 Skill Test to Trainers




Quality Assurance

- › **Layers of Monitoring** (*Pre, During and Post Training Phase*)
- › **Full Time Engineers** (*Monitoring T&Es & Technical Team*)
- › **Technical supervision** (*one subengineer in each of the three clusters*)
- › **T&Es' Capacity Building**
- › **Training Curricula & Manual**
- › **ToT for Instructors** (*From TITI*)



Implementation Modality of EF-SR

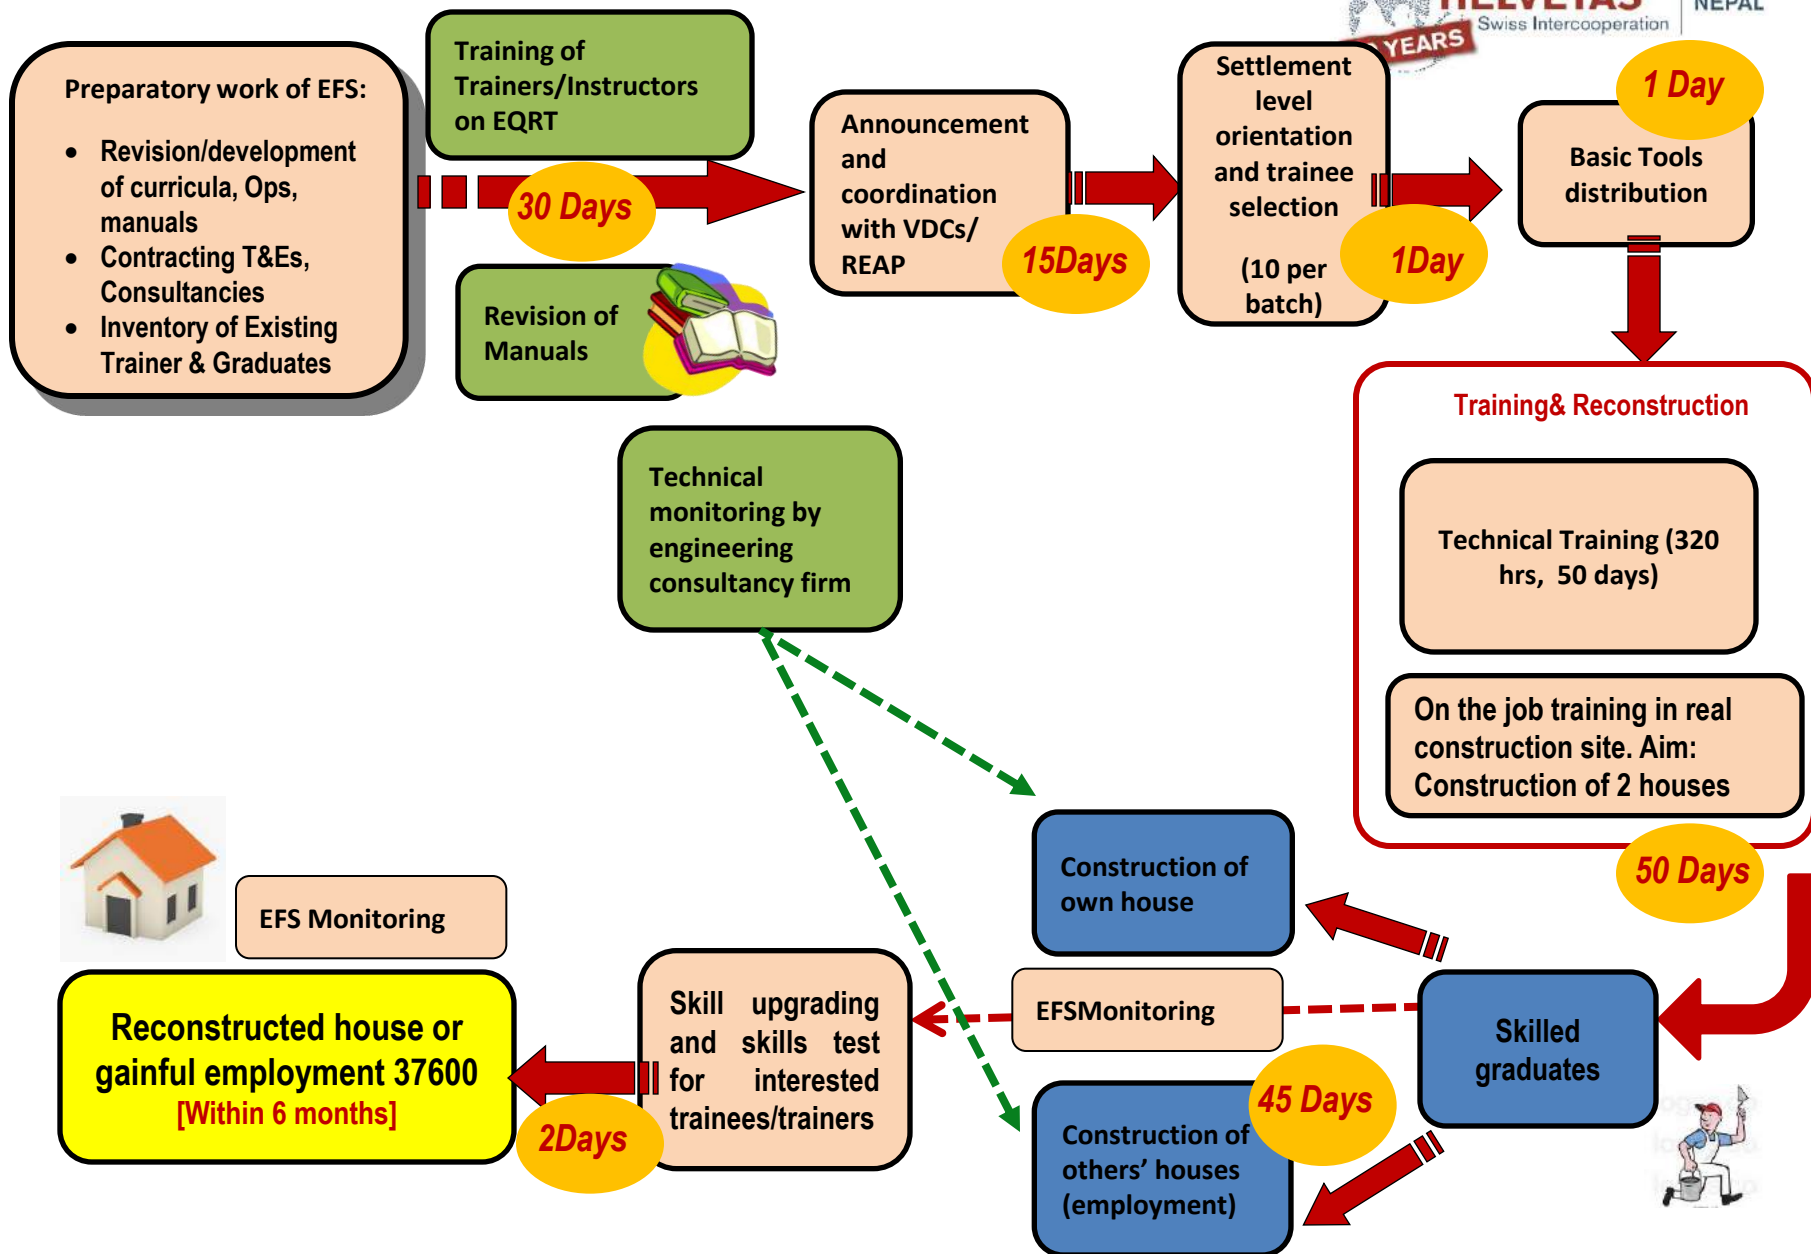

Collaboration

- › Functional Relation with DDRC
- › Working with CTEVT, NSTB for revision of curricula & manuals
- › Mapping of collaborating partners




Result Measurement

OUTPUT	IMMEDIATE OUTCOME	FINAL OUTCOME
Training Completion (400)	3-months' income NRs 18,600 Or	6-monnnths' Income NRs. 37,200 Or
House Construction (500)	Construction of Own House	Construction of 2 Houses (including own)

Financial Modality

50 Days

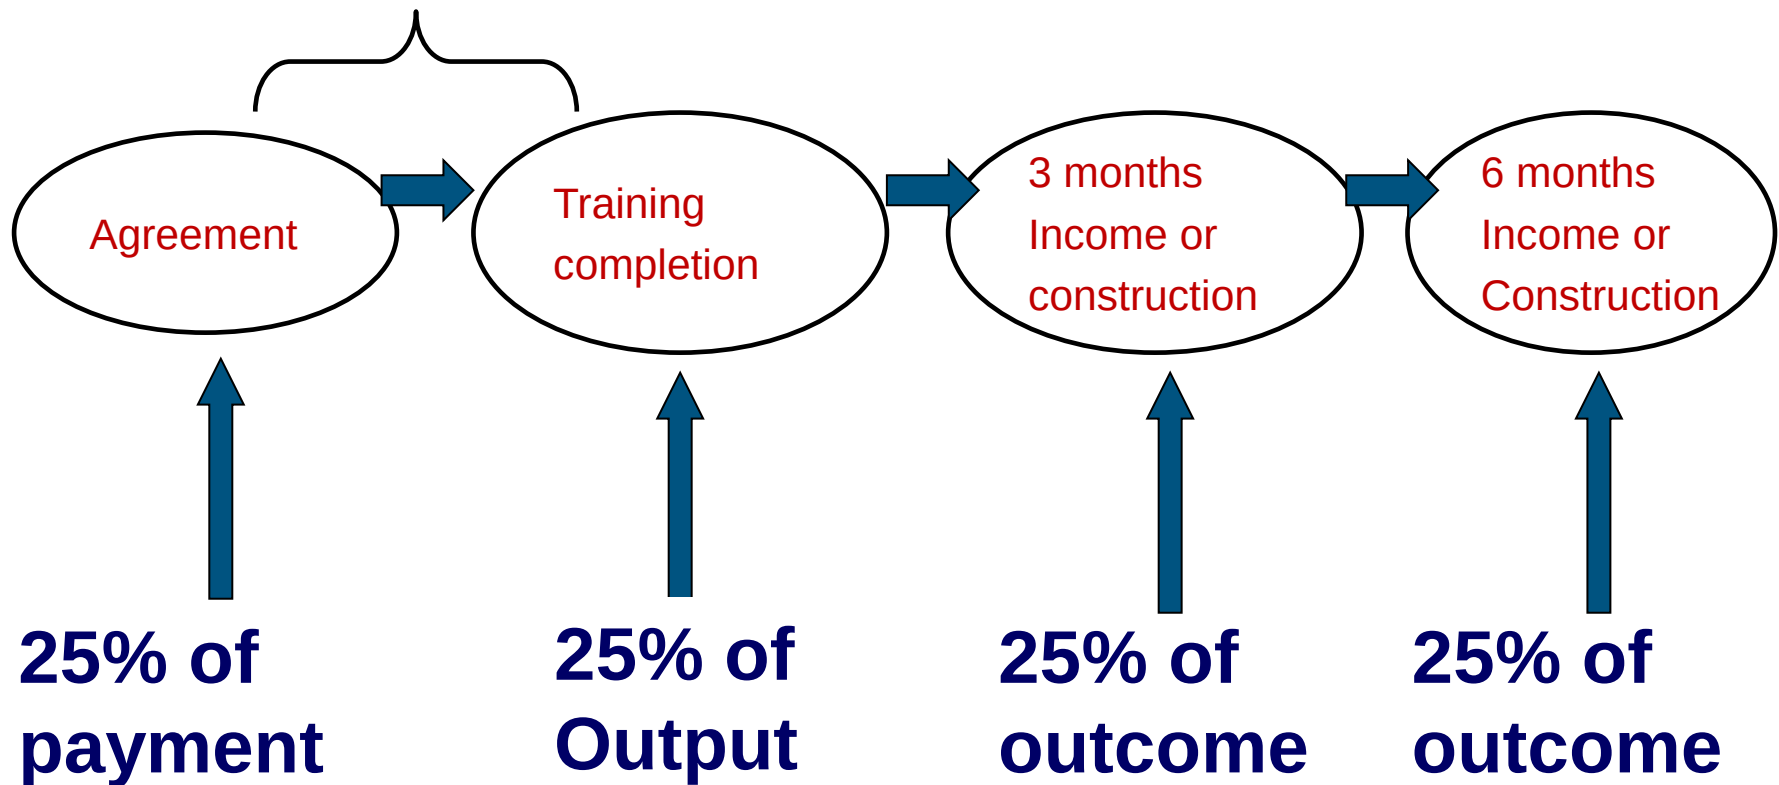

Reporting period : November, 2015 to February, 2016

Financial Progress			Physical Progress			Remarks
Plan Budget (Nrs.)	Expenditure (Nrs.)	%	Target YPO Activities	Achievement	%	
15078628	2,082,157 (as an advance)	14%	400	147	37%	

Major Input - Output - Outcome

Input	Output	Outcome	Remarks
• on Site training (50 days) • 10 Lead Trainers received ToT on EQ resilient technology • basic tools for each of participants distributed • safety tools for each of participants distributed • Stipend (200 per person) • Settlement level orientation and trainee's selection • Coordination and collaboration with like minded organisation, VDCs, DDCs, DUDBC and DDRC/NRA • CTEVT curricula, Training manuals, participants' handbook	147 persons trained (comprising of 7% Dalit, 59% Janajati and 34% from other communities, 27% Women, 67% DAGs)	18 houses completed 1 houses are in gable banding stage	

Working VDCs

1. Khimti (3 Events)
2. Pharpu (2 Events)
3. Namadi (1 Event)
4. Betali (3 Events)
5. Those (3 Events)
6. Churchure (3 Events)
7. Rasnalu
8. Bhatauli
9. Gunsibhadaure
10. Lakhanpur
11. Tokanpur
12. Dimipokhari

Weightage	<u>Trade wise</u>	Total Trade
67%	1. Stone Layer Mason	10
27%	2. Building Electrician	1
6%	3. Construction Carpenter	4
	Grand Total	15


Progress status of Ramechhap

S.N	Trade	VDC	# of Houses	Status
1	Stone Laying Mason – 10	Khimti – 1, Pharpu – 2, Churchure – 2 Those – 2 Betali – 2 Namadi - 1	19	18 Houses are completed, 1 Houses are in Gabel and roofing level
2	Construction Carpentry	Khimti – 1 Churchure – 1 Those – 1 Betali – 1	19	Working along with construction work of houses
3	Building Electrician	Khimti -1		completed


Participation

Total Trade	Dalit			Janajati			Other			Grant Total		
	Male	Female	Total	Male	Female	Total	Male	Female	Total	Male	Female	Total
10	5	4	9	45	11	56	26	9	35	76	24	100
1	0	0	0	4	3	7	3	0	3	7	3	10
4	2	2	4	22	4	26	10	0	10	34	6	40
15	7	6	13	71	18	89	39	9	48	117	33	150

Ethnicity Analysis



Gender wise Analysis

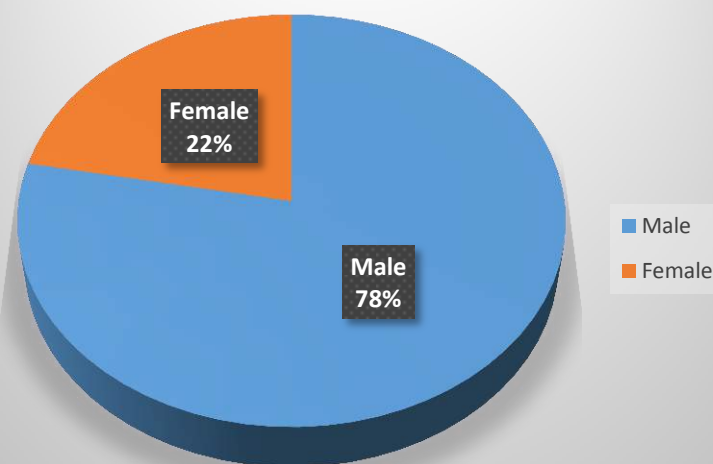

Positive Aspect	Challenges / Issues	Learnings / Experiences
• Training approach of EF-SR is highly accepted by community • A good initiator working in reconstruction • People having resources of their own can start reconstruction without waiting for government grant • 19 EQ resilient model houses constructed in the districts (example for others)	• Unavailability of quality Materials (stones and woods) at local level • Not available appropriate land as provisioned by DUDBC's design • Treatment of woods and bamboo • Very difficult to manage construction materials for the economically poor people • Delay in releasing government grant may affect to achieve the outcome of the project in time • Getting access of government grant to the owners who has already built houses • Only one design of stone and mud mortar house which is impracticable to afford due to family size and land topography in hills area • Use of forest forest materials (e.g; Timber, wood) at local without affecting the environment	 • Proper orientation and awareness to community is necessary before implementing training • Collaboration with local government (VDC level) is effective to make the program successful • Need to make all the construction materials ready before starting the training • Combination of carpenter and mason training is found effective to build house in better quality • Frequent monitoring during training and reconstruction brings quality in works



01 09 2016

Pharpu VDC, Ramechhap

Churchre VDC, Ramechhap





Churchure VDC, Ramechhap

Woman in work at Those



Churchure VDC, Ramechhap




Churchure VDC, Ramechhap



Different view of EQ resilient house



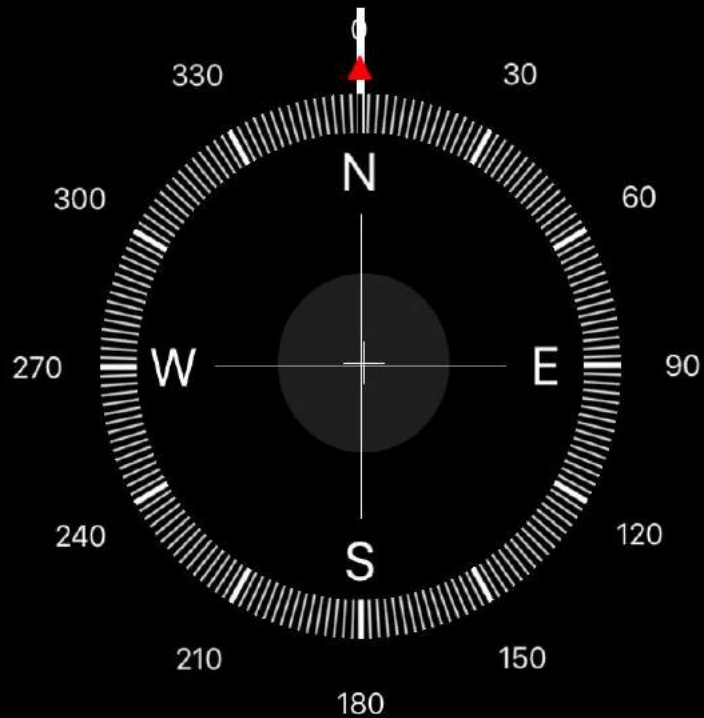

27°22'52" N 86°3'33" E
540 m Elevation



Thank you
